



Operation Number: **UR-L1094**
Year- PMR Cycle: **First period Jan-Jun 2015**
Last Update: **10/13/2015**
PMR Validation Stage: **Validated by Representative**

Chief of Operations validation date: **10/13/2015**
Division Chief validation date: **10/20/2015**
Country Representative validation date: **10/23/2015**

Inter-American Development Bank - IDB
Office of Strategic Planning and Development Effectiveness

Operation Profile

Basic Data

Operation name:	Ciudad de la Costa-west area Sanitation Project	Loan Number:	3258/OC-UR,3259/CH-UR
Executing Agency (EA):	OBRAS SANITARIAS DEL ESTADO ,OBRAS SANITARIAS DEL ESTADO		
Team Leader:	Paez Rubio,Tania	Sector/Subsector:	SANITATION URBAN
Operation Type:	Loan Operation	Overall Stage:	Disbursing (From eligibility until all the loans are closed).
Lending Instrument:	Investment Loan	Country:	URUGUAY
Borrower:	OBRAS SANITARIAS DEL ESTADO ,OBRAS SANITARIAS DEL ESTADO	Convergence related Operation(s):	

Total Cost and Source

	Original IDB	Current Active IDB	Local Counterpart	Co-Financing/Country	Total operation cost - Original Estimate
UR-L1094	\$75,000,000.00	\$75,000,000.00	\$0.00	\$0.00	\$75,000,000.00

Available Funds (US\$)

	Current IDB	Disb. Amount to Date	% Disbursed	Undisbursed Balance
UR-L1094	\$75,000,000.00	\$2,500,000.00	3.33%	\$72,500,000.00


Environmental and Social Safeguards

Main Operation	
Impacts Category:	B
Safeguard Performance Rating:	
Safeguard Performance Rating - Rationale:	


Reformulation Information

Main Operation	
Was/Were the objective(s) of this operation reformulated?	NO
Date of approval:	

Expense Categories by Loan Contract (cumulative values)

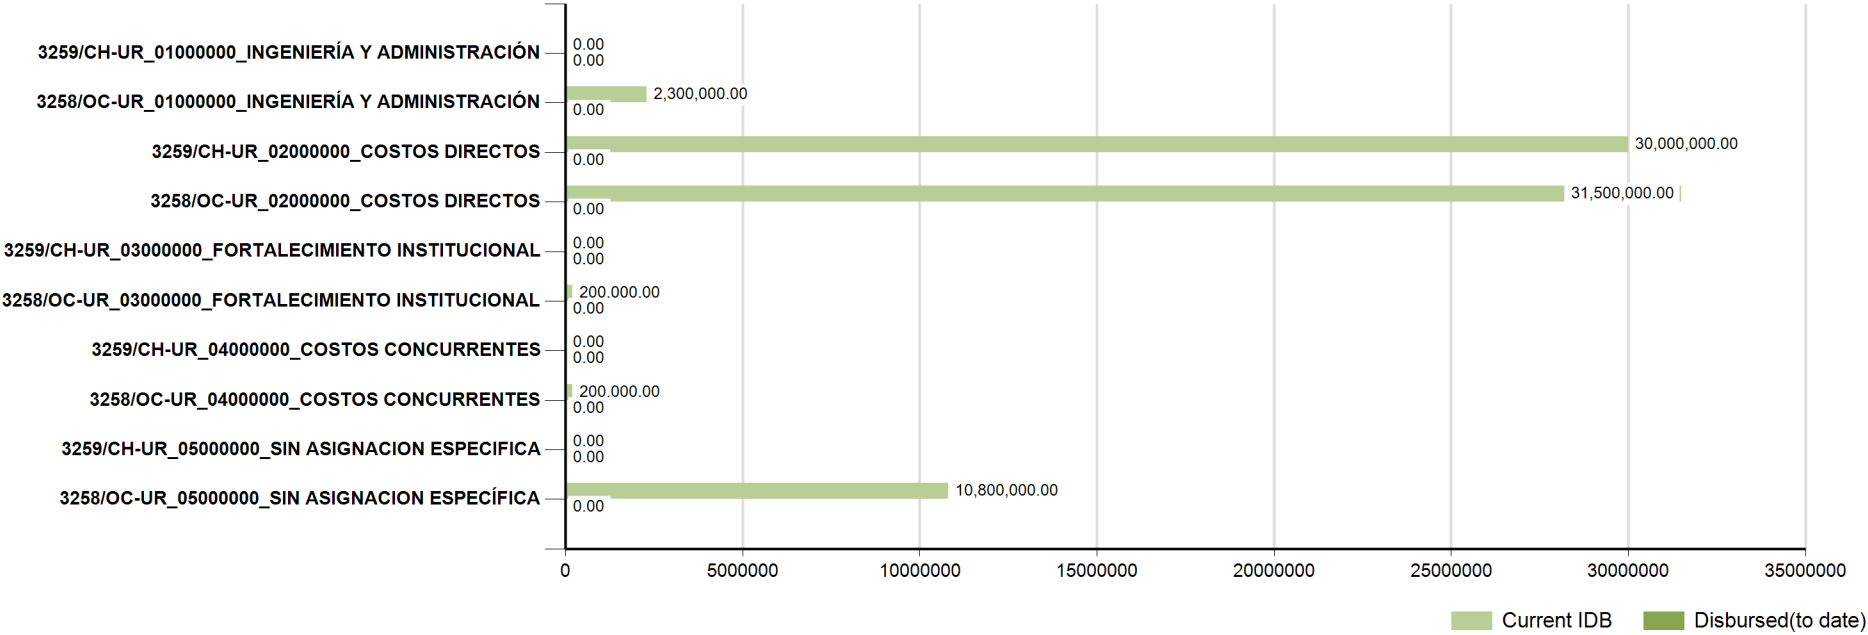

Expense Categories by Operation (cumulative values)

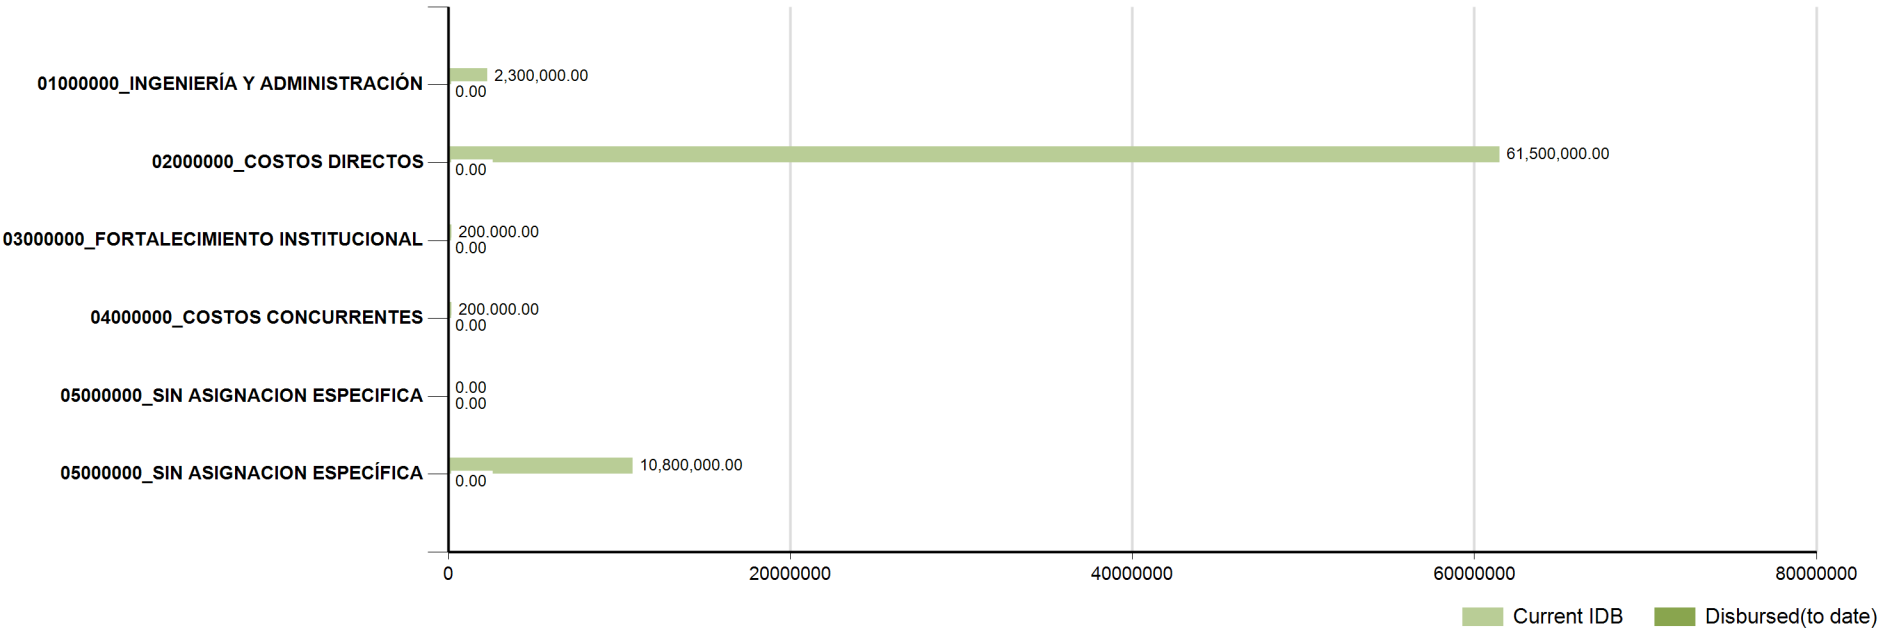

Results Matrix

Impacts

No information related to this operation.

Outcomes

[illegible]

1.2 Número de roturas de la red en la zona central y oeste de Ciudad de la Costa		numero/km /año	8.00	2014	Numero de arreglos de roturas registrados por la Gerencia del área metropolitana- OSE		P							0.90	0.90
							P(a)							0.90	0.90
							A								

Outcome:

2 Organismo ejecutor fortalecido

Observation:

Indicators	Flags*	Unit of Measure	Baseline	Baseline Year	Means of verification	Observations	2014	2015	2016	2017	2018	2019	2020	EOP
2.0 Sistemas operando y en mantenimiento según especificaciones técnicas de diseño		sistemas	0.00	2014	Cumplimiento de los niveles de tratamiento de las aguas residuales en la Planta de Tratamiento y de disposición final en el Río de la Plata		P						1.00	1.00
							P(a)						1.00	1.00
							A							

Outputs: Annual Physical and Financial Progress

Obras de saneamiento en Ciudad de la Costa – zona oeste		Physical Progress			Financial Progress		
Outputs	Unit of Measure		2015	EOP		2015	EOP
Estaciones de bombeo construidas	numero	P	0.00	7.00	P	328,000.00	7,800,000.00
		P(a)	0.00	7.00	P(a)	328,000.00	7,800,000.00
		A	0.00	0.00	A	33,138.00	33,138.00
Interceptor costero construido	metros	P	200.00	2,165.00	P	184,800.00	2,000,000.00
		P(a)	200.00	2,165.00	P(a)	184,800.00	2,000,000.00
		A	0.00	0.00	A	0.00	0.00
Redes de Saneamiento construidas	metros	P	2,763.00	97,515.00	P	1,373,000.00	41,500,000.00
		P(a)	2,763.00	97,515.00	P(a)	1,373,000.00	41,500,000.00
		A	0.00	0.00	A	0.00	0.00
Obras de agua potable en Ciudad de la Costa-zona oeste y central		Physical Progress			Financial Progress		
Outputs	Unit of Measure		2015	EOP		2015	EOP
Redes de distribución de agua potable rehabilitadas	m	P	6,618.00	122,261.00	P	670,000.00	10,200,000.00
		P(a)	6,618.00	122,261.00	P(a)	670,000.00	10,200,000.00
		A	0.00	0.00	A	0.00	0.00
Fortalecimiento institucional		Physical Progress			Financial Progress		
Outputs	Unit of Measure		2015	EOP		2015	EOP
Personal de OSE capacitado para la O & M del sistema de saneamiento de Ciudad de la Costa	personas	P	0.00	40.00	P	0.00	200,000.00
		P(a)	0.00	40.00	P(a)	0.00	200,000.00
		A	0.00	0.00	A	0.00	0.00
Other Cost					2015		Cost
Gastos de unidad ejecutora y Administrativos				P	\$0.00		\$13,300,000.00
				P(a)	\$0.00		\$13,300,000.00
				A	\$0.00		\$0.00
Total Cost					2015		Total Cost
				P	\$2,555,800.00		\$75,000,000.00
				P(a)	\$2,555,800.00		\$72,477,338.00
				A	\$33,138.00		\$33,138.00

Changes to the Matrix

No information related to this operation.

Please note that the Overall Stage represents the stage of the operation at the time of this report's publication, which might not necessarily match the stage of the operation during the PMR Cycle to which the report pertains.
