



ID	Nombre de tarea	Start	Finish	Año 1	Año 2	Año 3	Año 4	Año 5	Total	2016	2017	2018	2019	2020	2021	2022	2023	2024	2025
1	PROGRAMA DE AGUA Y SANEAMIENTO PARA CIUDADES INTERMEDIAS Y MENORES . (BO-L 1184)	Tue 5/2/17	Fri 9/6/24	\$6,246,726	\$19,524,953	\$16,496,338	\$22,515,736	\$14,216,247	\$79,000,000										
2	Preparación y Aprobación del Programa	Tue 5/2/17	Thu 1/9/20	\$0	\$0	\$0	\$0	\$0	\$0										
3	Preparación del Programa	Tue 5/2/17	Wed 11/8/17	\$0	\$0	\$0	\$0	\$0	\$0										
4	Misión de Orientación	Tue 5/2/17	Fri 5/5/17	\$0	\$0	\$0	\$0	\$0	\$0										
5	Misión de Análisis	Mon 8/14/17	Fri 8/18/17	\$0	\$0	\$0	\$0	\$0	\$0										
6	Misión de Negociación	Mon 10/9/17	Mon 10/9/17	\$0	\$0	\$0	\$0	\$0	\$0										
7	Aprobación por el Directorio Ejecutivo del BID	Wed 11/8/17	Wed 11/8/17	\$0	\$0	\$0	\$0	\$0	\$0										
8	Aprobación del Contrato de Préstamo	Wed 11/8/17	Tue 4/24/18	\$0	\$0	\$0	\$0	\$0	\$0										
9	Suscripción del Contrato de Préstamo Estado Plurinacional de Bolivia - BID	Wed 11/8/17	Tue 12/19/17	\$0	\$0	\$0	\$0	\$0	\$0										
10	Aprobación de la Asamblea y Promulgación de Ley	Wed 12/20/17	Tue 4/24/18	\$0	\$0	\$0	\$0	\$0	\$0										
11	Suscripción del Convenio Subsidiario MPD - MMAyA	Wed 4/25/18	Tue 7/17/18	\$0	\$0	\$0	\$0	\$0	\$0										
12	Suscripción del Convenio Subsidiario MMAyA - FPS	Wed 4/25/18	Tue 7/17/18	\$0	\$0	\$0	\$0	\$0	\$0										
13	Cumplimiento de Condiciones Previas al Primer Desembolso	Tue 4/24/18	Thu 7/5/18	\$0	\$0	\$0	\$0	\$0	\$0										
14	Resolución Ministerial para la Ampliación de Atribuciones UCP	Wed 4/25/18	Fri 6/8/18	\$0	\$0	\$0	\$0	\$0	\$0										
15	Informe técnico para la emisión de RM	Wed 4/25/18	Wed 4/25/18	\$0	\$0	\$0	\$0	\$0	\$0										
16	Informe jurídico para la emisión de RM	Thu 4/26/18	Mon 5/21/18	\$0	\$0	\$0	\$0	\$0	\$0										
17	Emisión de R.M.	Tue 5/22/18	Fri 6/8/18	\$0	\$0	\$0	\$0	\$0	\$0										
18	Aprobación del Reglamento Operativo del Programa UCP - FPS	Tue 4/24/18	Tue 6/5/18	\$0	\$0	\$0	\$0	\$0	\$0										
19	Elaboración del R.O.	Wed 4/25/18	Tue 6/5/18	\$0	\$0	\$0	\$0	\$0	\$0										
20	Presentación del R.O. al MMAyA	Tue 4/24/18	Tue 4/24/18	\$0	\$0	\$0	\$0	\$0	\$0										
21	Aprobación del R.O. por R.M. del MMAyA	Wed 4/25/18	Tue 5/22/18	\$0	\$0	\$0	\$0	\$0	\$0										
22	Contratación de personal mínimo	Wed 4/25/18	Thu 7/5/18	\$0	\$0	\$0	\$0	\$0	\$0										
23	Asignación Personal Clave UCP-PAAP	Wed 4/25/18	Wed 4/25/18	\$0	\$0	\$0	\$0	\$0	\$0										
24	Contratación Personal Clave FPS	Wed 4/25/18	Wed 4/25/18	\$0	\$0	\$0	\$0	\$0	\$0										
25	Designación de los responsable del Programa para la firmas autorizadas FPS	Mon 6/11/18	Fri 6/22/18	\$0	\$0	\$0	\$0	\$0	\$0										
26	Designación de los responsable del Programa para la firmas autorizadas UCP - PAAP	Mon 6/11/18	Thu 7/5/18	\$0	\$0	\$0	\$0	\$0	\$0										
27	Declaración de Elegibilidad por el BID	Wed 7/18/18	Fri 7/27/18	\$0	\$0	\$0	\$0	\$0	\$0										
28	Inscripción Presupuestaria	Wed 7/18/18	Tue 9/18/18	\$0	\$0	\$0	\$0	\$0	\$0										
29	Inscripción presupuestaria UCP-PAAP	Wed 7/18/18	Tue 9/18/18	\$0	\$0	\$0	\$0	\$0	\$0										
30	Inscripción presupuestaria FPS	Wed 7/18/18	Tue 9/18/18	\$0	\$0	\$0	\$0	\$0	\$0										
31	PRIORIZACION DE PROYECTOS FUERA DE LA MUESTRA UCP	Wed 12/5/18	Thu 1/9/20	\$0	\$0	\$0	\$0	\$0	\$0										
32	Difusión del Programa	Wed 12/5/18	Tue 1/15/19	\$0	\$0	\$0	\$0	\$0	\$0										
33	Organización del Taller y Eventos	Wed 12/5/18	Tue 1/15/19	\$0	\$0	\$0	\$0	\$0	\$0										
34	Conformación Cartera de Proyectos hasta 3000 hab.	Wed 1/16/19	Thu 7/11/19	\$0	\$0	\$0	\$0	\$0	\$0										
35	Universo de comunidades potenciales lista larga (Primera instancia)	Wed 1/16/19	Wed 4/17/19	\$0	\$0	\$0	\$0	\$0	\$0										
36	Viajes de validación (Primera instancia)	Wed 1/16/19	Tue 2/12/19	\$0	\$0	\$0	\$0	\$0	\$0										
37	Procesamiento de la información	Wed 2/13/19	Tue 3/26/19	\$0	\$0	\$0	\$0	\$0	\$0										
38	Segundo relevamiento de información	Wed 3/27/19	Thu 4/4/19	\$0	\$0	\$0	\$0	\$0	\$0										
39	Sistematización de información	Fri 4/5/19	Thu 4/11/19	\$0	\$0	\$0	\$0	\$0	\$0										
40	Toma de decisiones sobre los datos de la segunda información	Fri 4/12/19	Wed 4/17/19	\$0	\$0	\$0	\$0	\$0	\$0										
41	Universo de comunidades potenciales lista larga (Segunda instancia)	Thu 4/18/19	Wed 5/15/19	\$0	\$0	\$0	\$0	\$0	\$0										
42	Validación con los GAM	Thu 4/18/19	Wed 5/8/19	\$0	\$0	\$0	\$0	\$0	\$0										
43	Lista de comunidades elegibles validadas UCP	Thu 5/9/19	Wed 5/15/19	\$0	\$0	\$0	\$0	\$0	\$0										
44	Selección de cartera, sensibilización con Alcaldes y luego líderes comunitarios	Thu 5/16/19	Thu 7/11/19	\$0	\$0	\$0	\$0	\$0	\$0										

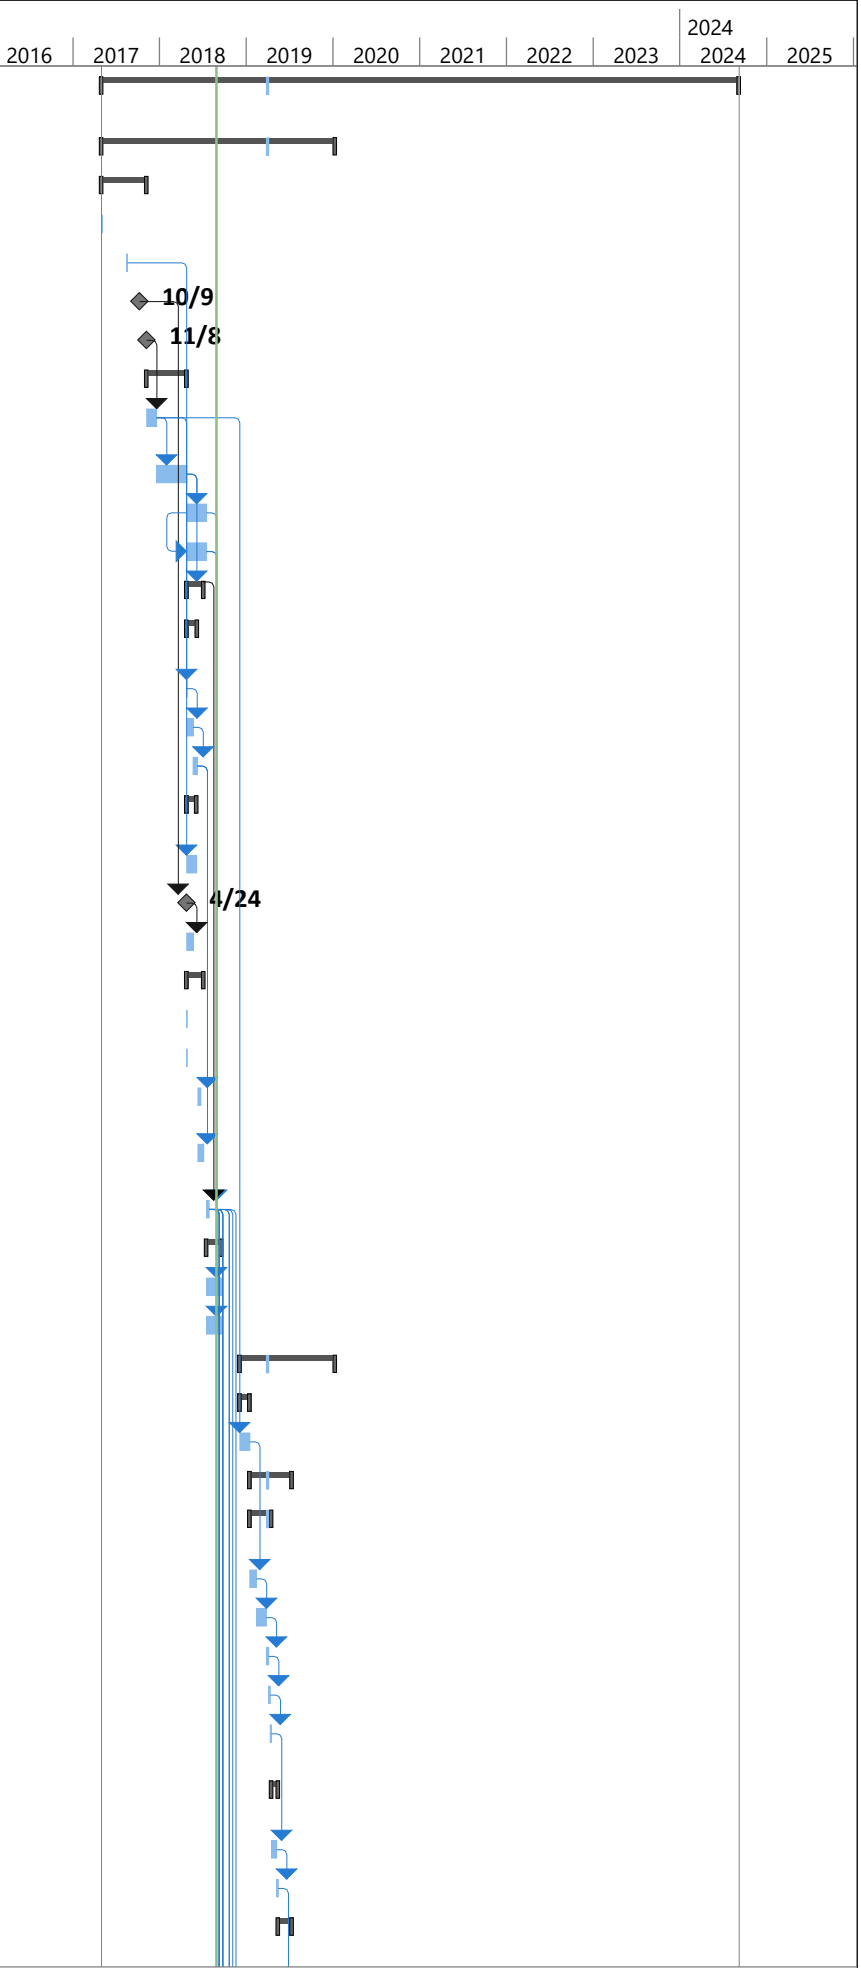

ID	Nombre de tarea	Start	Finish	Año 1	Año 2	Año 3	Año 4	Año 5	Total	2016	2017	2018	2019	2020	2021	2022	2023	2024	2025
45	Lineamientos para el Protocolo de Aleatorización	Thu 5/16/19	Tue 5/28/19	\$0	\$0	\$0	\$0	\$0	\$0										
46	Cálculo de las inversiones para el nro de comunidades por municipio	Wed 5/29/19	Thu 5/30/19	\$0	\$0	\$0	\$0	\$0	\$0										
47	<b>Aleatorización de las comunidades del Programa definición de Universo</b>	<b>Fri 5/31/19</b>	<b>Thu 7/11/19</b>	<b>\$0</b>	<b>\$0</b>	<b>\$0</b>	<b>\$0</b>	<b>\$0</b>	<b>\$0</b>										
48	<b>Suscripción de los Convenios de Participación en el Programa - CPP</b>	<b>Fri 7/12/19</b>	<b>Thu 1/9/20</b>	<b>\$0</b>	<b>\$0</b>	<b>\$0</b>	<b>\$0</b>	<b>\$0</b>	<b>\$0</b>										
49	Socialización de los convenios con GAM/GAD	Fri 7/12/19	Thu 11/14/19	\$0	\$0	\$0	\$0	\$0	\$0										
50	Firma de Convenios GAM/GAD	Fri 11/15/19	Thu 1/9/20	\$0	\$0	\$0	\$0	\$0	\$0										
51	<b>COMPONENTE I: Inversión y Apoyo a la Gestión con Operadores</b>	<b>Fri 9/1/17</b>	<b>Fri 9/6/24</b>	<b>\$5,090,353</b>	<b>\$18,377,612</b>	<b>\$15,257,895</b>	<b>\$21,313,219</b>	<b>\$12,794,701</b>	<b>\$72,833,780</b>										
52	<b>Proyectos de la Muestra Tipo E1 y E2 (UCP PAAP)</b>	<b>Fri 9/1/17</b>	<b>Thu 11/7/19</b>	<b>\$1,497,081</b>	<b>\$5,988,328</b>	<b>\$0</b>	<b>\$0</b>	<b>\$0</b>	<b>\$7,485,409</b>										
53	Elaboración de Estudios de Preinversión (Firma CES)	Fri 9/1/17	Thu 1/4/18	\$0	\$0	\$0	\$0	\$0	\$0										
54	Acompañamiento a la Elaboración de los Estudios de Preinversión (UCP)	Fri 9/1/17	Thu 1/4/18	\$0	\$0	\$0	\$0	\$0	\$0										
55	<b>Departamento de Potosi</b>	<b>Fri 1/5/18</b>	<b>Thu 11/7/19</b>	<b>\$621,561</b>	<b>\$2,486,242</b>	<b>\$0</b>	<b>\$0</b>	<b>\$0</b>	<b>\$3,107,803</b>										
56	<b>Lote 1: Municipios Colquechaca, San Pedro de Buena Vista y Lote 2: Municipio Tupiza</b>	<b>Fri 1/5/18</b>	<b>Thu 11/7/19</b>	<b>\$621,561</b>	<b>\$2,486,242</b>	<b>\$0</b>	<b>\$0</b>	<b>\$0</b>	<b>\$3,107,803</b>										
57	<b>Supervisión Obras y DESCOM-FI Lotes 1 y 2</b>	<b>Fri 1/5/18</b>	<b>Thu 11/7/19</b>	<b>\$50,034</b>	<b>\$200,133</b>	<b>\$0</b>	<b>\$0</b>	<b>\$0</b>	<b>\$250,167</b>										
58	Contratación de Firma Supervisora (SBCC)	Fri 1/5/18	Thu 7/5/18	\$0	\$0	\$0	\$0	\$0	\$0										
59	<b>Ejecución del Servicio</b>	<b>Fri 8/3/18</b>	<b>Thu 11/7/19</b>	<b>\$50,034</b>	<b>\$200,133</b>	<b>\$0</b>	<b>\$0</b>	<b>\$0</b>	<b>\$250,167</b>										
60	Municipio de San Pedro Buena Vista	Fri 8/3/18	Thu 9/26/19	\$11,321	\$45,285	\$0	\$0	\$0	\$56,606										
61	Municipio Colquechaca	Fri 8/3/18	Thu 11/7/19	\$15,908	\$63,631	\$0	\$0	\$0	\$79,539										
62	Municipio de Tupiza	Fri 8/3/18	Thu 9/12/19	\$22,805	\$91,217	\$0	\$0	\$0	\$114,022										
63	<b>Obras y DESCOM-FI</b>	<b>Fri 3/30/18</b>	<b>Thu 8/29/19</b>	<b>\$571,527</b>	<b>\$2,286,109</b>	<b>\$0</b>	<b>\$0</b>	<b>\$0</b>	<b>\$2,857,636</b>										
64	Contratación Infraestructura y DESCOM (LPN)	Fri 3/30/18	Thu 8/2/18	\$0	\$0	\$0	\$0	\$0	\$0										
65	<b>Ejecución de Obras</b>	<b>Fri 8/31/18</b>	<b>Thu 5/9/19</b>	<b>\$501,340</b>	<b>\$2,005,358</b>	<b>\$0</b>	<b>\$0</b>	<b>\$0</b>	<b>\$2,506,698</b>										
66	Municipio de San Pedro Buena Vista	Fri 8/31/18	Thu 4/11/19	\$113,439	\$453,755	\$0	\$0	\$0	\$567,194										
67	Municipio Colquechaca	Fri 8/31/18	Thu 5/9/19	\$159,396	\$637,585	\$0	\$0	\$0	\$796,981										
68	Municipio de Tupiza	Fri 8/31/18	Thu 3/14/19	\$228,505	\$914,018	\$0	\$0	\$0	\$1,142,523										
69	<b>Ejecución de DESCOM</b>	<b>Fri 8/3/18</b>	<b>Thu 8/29/19</b>	<b>\$70,187</b>	<b>\$280,751</b>	<b>\$0</b>	<b>\$0</b>	<b>\$0</b>	<b>\$350,938</b>										
70	Municipio de San Pedro Buena Vista	Fri 8/3/18	Thu 8/1/19	\$15,881	\$63,526	\$0	\$0	\$0	\$79,407										
71	Municipio Colquechaca	Fri 8/3/18	Thu 8/29/19	\$22,315	\$89,262	\$0	\$0	\$0	\$111,577										
72	Municipio de Tupiza	Fri 8/3/18	Thu 7/4/19	\$31,991	\$127,963	\$0	\$0	\$0	\$159,954										
73	<b>Departamento de Oruro</b>	<b>Fri 5/11/18</b>	<b>Thu 7/25/19</b>	<b>\$71,465</b>	<b>\$285,865</b>	<b>\$0</b>	<b>\$0</b>	<b>\$0</b>	<b>\$357,330</b>										
74	<b>Municipio Machacamarc</b>	<b>Fri 5/11/18</b>	<b>Thu 7/25/19</b>	<b>\$71,465</b>	<b>\$285,865</b>	<b>\$0</b>	<b>\$0</b>	<b>\$0</b>	<b>\$357,330</b>										
75	<b>Obras y DESCOM-FI</b>	<b>Fri 5/11/18</b>	<b>Thu 6/20/19</b>	<b>\$65,713</b>	<b>\$262,853</b>	<b>\$0</b>	<b>\$0</b>	<b>\$0</b>	<b>\$328,566</b>										
76	Contratación Infraestructura y DESCOM (LPN)	Fri 5/11/18	Thu 9/13/18	\$0	\$0	\$0	\$0	\$0	\$0										
77	Ejecución de obra	Fri 10/12/18	Thu 2/28/19	\$57,643	\$230,573	\$0	\$0	\$0	\$288,216										
78	Ejecución del DESCOM	Fri 9/14/18	Thu 6/20/19	\$8,070	\$32,280	\$0	\$0	\$0	\$40,350										
79	<b>Supervisión Obras y DESCOM-FI (CCIN)</b>	<b>Fri 6/29/18</b>	<b>Thu 7/25/19</b>	<b>\$5,752</b>	<b>\$23,012</b>	<b>\$0</b>	<b>\$0</b>	<b>\$0</b>	<b>\$28,764</b>										
80	Contratación Supervisor de Obras	Fri 6/29/18	Thu 8/30/18	\$0	\$0	\$0	\$0	\$0	\$0										
81	Ejecución de la Supervisión de Obras	Fri 8/31/18	Thu 3/28/19	\$5,188	\$20,752	\$0	\$0	\$0	\$25,940										
82	Contratación Supervisor de DESCOM	Fri 6/29/18	Thu 8/30/18	\$0	\$0	\$0	\$0	\$0	\$0										
83	Ejecución de la Supervisión DESCOM	Fri 8/31/18	Thu 7/25/19	\$564	\$2,260	\$0	\$0	\$0	\$2,824										
84	<b>Departamento de La Paz</b>	<b>Fri 3/2/18</b>	<b>Thu 10/24/19</b>	<b>\$804,055</b>	<b>\$3,216,221</b>	<b>\$0</b>	<b>\$0</b>	<b>\$0</b>	<b>\$4,020,276</b>										
85	<b>Municipio Achocalla - Marquirivi, Cañuma y Surusaya</b>	<b>Fri 3/2/18</b>	<b>Thu 8/29/19</b>	<b>\$326,109</b>	<b>\$1,304,433</b>	<b>\$0</b>	<b>\$0</b>	<b>\$0</b>	<b>\$1,630,542</b>										
86	<b>Obras y DESCOM-FI</b>	<b>Fri 5/25/18</b>	<b>Thu 8/1/19</b>	<b>\$299,858</b>	<b>\$1,199,430</b>	<b>\$0</b>	<b>\$0</b>	<b>\$0</b>	<b>\$1,499,288</b>										
87	Contratación Infraestructura y DESCOM (LPN)	Fri 5/25/18	Thu 9/27/18	\$0	\$0	\$0	\$0	\$0	\$0										
88	Ejecución de Obras	Fri 10/26/18	Thu 4/25/19	\$263,033	\$1,052,132	\$0	\$0	\$0	\$1,315,165										
89	Ejecución DESCOM	Fri 9/28/18	Thu 8/1/19	\$36,825	\$147,298	\$0	\$0	\$0	\$184,123										
90	<b>Supervisión Obras y DESCOM-FI</b>	<b>Fri 3/2/18</b>	<b>Thu 8/29/19</b>	<b>\$26,251</b>	<b>\$105,003</b>	<b>\$0</b>	<b>\$0</b>	<b>\$0</b>	<b>\$131,254</b>										
91	Contratación de Firma Supervisora (SBCC)	Fri 3/2/18	Thu 8/30/18	\$0	\$0	\$0	\$0	\$0	\$0										




ID	Nombre de tarea	Start	Finish	Año 1	Año 2	Año 3	Año 4	Año 5	Total	2016	2017	2018	2019	2020	2021	2022	2023	2024	2025
92	Ejecución del Servicio	Fri 8/31/18	Thu 8/29/19	\$26,251	\$105,003	\$0	\$0	\$0	\$131,254										
93	Municipio Tihuanaku - Huacullani	Fri 3/30/18	Thu 10/24/19	\$477,946	\$1,911,788	\$0	\$0	\$0	\$2,389,734										
94	Obras y DESCOM-FI	Fri 6/22/18	Thu 10/24/19	\$439,473	\$1,757,895	\$0	\$0	\$0	\$2,197,368										
95	Contratación Infraestructura y DESCOM (LPN)	Fri 6/22/18	Thu 10/25/18	\$0	\$0	\$0	\$0	\$0	\$0										
96	Ejecución de Obras	Fri 11/23/18	Thu 7/18/19	\$385,503	\$1,542,013	\$0	\$0	\$0	\$1,927,516										
97	Ejecución DESCOM	Fri 10/26/18	Thu 10/24/19	\$53,970	\$215,882	\$0	\$0	\$0	\$269,852										
98	Supervisión Obras y DESCOM-FI	Fri 3/30/18	Thu 10/24/19	\$38,473	\$153,893	\$0	\$0	\$0	\$192,366										
99	Contratación de Firma Supervisora (SBCC)	Fri 3/30/18	Thu 9/27/18	\$0	\$0	\$0	\$0	\$0	\$0										
100	Ejecución del Servicio	Fri 9/28/18	Thu 10/24/19	\$38,473	\$153,893	\$0	\$0	\$0	\$192,366										
101	Otros Proyectos a ser Priorizados E1 - E2 (UCP PAAP)	Mon 8/6/18	Fri 7/21/23	\$0	\$628,006	\$7,788,212	\$18,423,855	\$11,054,313	\$37,894,386										
102	Preinversión	Mon 8/6/18	Fri 7/19/19	\$0	\$598,101	\$398,733	\$0	\$0	\$996,834										
103	Contratación de Firma Consultora (SBCC)	Mon 8/6/18	Fri 2/1/19	\$0	\$0	\$0	\$0	\$0	\$0										
104	Elaboración de los Estudios de Preinversión de otros Proyectos	Mon 2/4/19	Fri 7/19/19	\$0	\$598,101	\$398,733	\$0	\$0	\$996,834										
105	Supervisión de Preinversión	Mon 10/24/22	Fri 7/21/23	\$0	\$29,905	\$19,937	\$0	\$0	\$49,842										
106	Contratación Supervisor de Preinversión (CCIN)	Mon 10/24/22	Fri 12/23/22	\$0	\$0	\$0	\$0	\$0	\$0										
107	Ejecución de la Supervisión de Preinversión	Mon 12/26/22	Fri 7/21/23	\$0	\$29,905	\$19,937	\$0	\$0	\$49,842										
108	Obras y DESCOM-FI	Mon 1/20/20	Fri 1/27/23	\$0	\$0	\$7,369,542	\$18,423,855	\$11,054,313	\$36,847,710										
109	Ejecución de proyectos	Mon 2/17/20	Fri 12/30/22	\$0	\$0	\$6,776,655	\$16,941,638	\$10,164,983	\$33,883,276										
110	Supervisión de obras	Mon 1/20/20	Fri 1/27/23	\$0	\$0	\$592,887	\$1,482,217	\$889,330	\$2,964,434										
111	Proyectos de la Muestra Tipo E3 - E4 (FPS)	Mon 5/21/18	Fri 4/2/21	\$3,473,306	\$10,769,134	\$6,063,388	\$734,825	\$0	\$21,040,653										
112	Departamento de Chuquisaca	Mon 5/21/18	Fri 10/30/20	\$618,133	\$1,545,334	\$927,201	\$0	\$0	\$3,090,668										
113	Municipio de Villaserrano - Sistema de Agua Potable y Mejoramiento y Ampliación del Sistema de Alcantarillado y PTAR	Mon 5/21/18	Fri 10/30/20	\$618,133	\$1,545,334	\$927,201	\$0	\$0	\$3,090,668										
114	Obras y DESCOM-FI	Mon 7/30/18	Fri 10/30/20	\$571,054	\$1,427,636	\$856,582	\$0	\$0	\$2,855,272										
115	Contratación Infraestructura y DESCOM (LPN)	Mon 7/30/18	Fri 11/30/18	\$0	\$0	\$0	\$0	\$0	\$0										
116	Ejecución de obra	Mon 12/31/18	Fri 6/12/20	\$544,899	\$1,362,248	\$817,349	\$0	\$0	\$2,724,496										
117	Ejecución del DESCOM	Mon 12/3/18	Fri 10/30/20	\$26,155	\$65,388	\$39,233	\$0	\$0	\$130,776										
118	Supervisión Obras y DESCOM-FI	Mon 5/21/18	Fri 10/30/20	\$47,079	\$117,698	\$70,619	\$0	\$0	\$235,396										
119	Contratación de Firma Supervisora (SBCC-LPI)	Mon 5/21/18	Fri 11/16/18	\$0	\$0	\$0	\$0	\$0	\$0										
120	Ejecución del Servicio	Mon 11/19/18	Fri 10/30/20	\$47,079	\$117,698	\$70,619	\$0	\$0	\$235,396										
121	Departamento de Santa Cruz	Mon 6/18/18	Fri 7/31/20	\$479,204	\$1,409,223	\$507,591	\$0	\$0	\$2,396,018										
122	Municipio de Pailón Centro - Adecuación y Rediseño de Estudio Técnico de Sistema de Agua Potable, Alcantarillado y PTAR	Mon 6/18/18	Fri 7/31/20	\$479,204	\$1,409,223	\$507,591	\$0	\$0	\$2,396,018										
123	Obras y DESCOM-FI	Mon 8/27/18	Fri 7/31/20	\$442,706	\$1,317,978	\$452,844	\$0	\$0	\$2,213,528										
124	Contratación Infraestructura y DESCOM (LPN)	Mon 8/27/18	Fri 12/28/18	\$0	\$0	\$0	\$0	\$0	\$0										
125	Ejecución de obra	Mon 12/31/18	Fri 3/6/20	\$422,429	\$1,267,287	\$422,429	\$0	\$0	\$2,112,145										
126	Ejecución del DESCOM	Mon 12/31/18	Fri 7/31/20	\$20,277	\$50,691	\$30,415	\$0	\$0	\$101,383										
127	Supervisión Obras y DESCOM-FI	Mon 6/18/18	Fri 7/17/20	\$36,498	\$91,245	\$54,747	\$0	\$0	\$182,490										
128	Contratación de Firma Supervisora (SBCC)	Mon 6/18/18	Fri 12/14/18	\$0	\$0	\$0	\$0	\$0	\$0										
129	Ejecución del Servicio	Mon 12/17/18	Fri 7/17/20	\$36,498	\$91,245	\$54,747	\$0	\$0	\$182,490										
130	Departamento de Oruro	Mon 7/30/18	Fri 5/29/20	\$437,314	\$1,311,943	\$437,314	\$0	\$0	\$2,186,571										
131	Municipio de Huanuni - Construcción de Sistema de Alcantarillado Sanitario y PTAR.	Mon 7/30/18	Fri 5/29/20	\$437,314	\$1,311,943	\$437,314	\$0	\$0	\$2,186,571										
132	Obras y DESCOM-FI	Mon 9/24/18	Fri 5/29/20	\$404,007	\$1,212,021	\$404,007	\$0	\$0	\$2,020,035										
133	Contratación Infraestructura y DESCOM (LPN)	Mon 9/24/18	Fri 1/25/19	\$0	\$0	\$0	\$0	\$0	\$0										
134	Ejecución de obra	Mon 2/25/19	Fri 1/24/20	\$385,503	\$1,156,509	\$385,503	\$0	\$0	\$1,927,515										
135	Ejecución del DESCOM	Mon 1/28/19	Fri 5/29/20	\$18,504	\$55,512	\$18,504	\$0	\$0	\$92,520										
136	Supervisión Obras y DESCOM-FI	Mon 7/30/18	Fri 5/29/20	\$33,307	\$99,922	\$33,307	\$0	\$0	\$166,536										
137	Contratación de Firma Supervisora (SBCC)	Mon 7/30/18	Fri 1/25/19	\$0	\$0	\$0	\$0	\$0	\$0										

ID	Nombre de tarea	Start	Finish	Año 1	Año 2	Año 3	Año 4	Año 5	Total	2016	2017	2018	2019	2020	2021	2022	2023	2024	2025
138	Ejecución del Servicio	Mon 1/28/19	Fri 5/29/20	\$33,307	\$99,922	\$33,307	\$0	\$0	\$166,536										
139	Departamento La Paz	Mon 7/30/18	Fri 4/2/21	\$1,938,655	\$6,502,634	\$4,191,282	\$734,825	\$0	\$13,367,396										
140	Municipio de Colquenchá - Construcción de Sistema de Alcantarillado Sanitario y PTAR.	Mon 7/30/18	Fri 6/26/20	\$372,697	\$1,118,090	\$372,696	\$0	\$0	\$1,863,483										
141	Obras y DESCOM-FI	Mon 10/22/18	Fri 6/26/20	\$344,311	\$1,032,932	\$344,310	\$0	\$0	\$1,721,553										
142	Contratación Infraestructura y DESCOM (LPN)	Mon 10/22/18	Fri 2/22/19	\$0	\$0	\$0	\$0	\$0	\$0										
143	Ejecución de obra	Mon 3/25/19	Fri 2/21/20	\$328,541	\$985,622	\$328,540	\$0	\$0	\$1,642,703										
144	Ejecución del DESCOM	Mon 2/25/19	Fri 6/26/20	\$15,770	\$47,310	\$15,770	\$0	\$0	\$78,850										
145	Supervisión Obras y DESCOM-FI	Mon 7/30/18	Fri 6/26/20	\$28,386	\$85,158	\$28,386	\$0	\$0	\$141,930										
146	Contratación de Firma Supervisora (SBCC)	Mon 7/30/18	Fri 1/25/19	\$0	\$0	\$0	\$0	\$0	\$0										
147	Ejecución del Servicio	Mon 1/28/19	Fri 6/26/20	\$28,386	\$85,158	\$28,386	\$0	\$0	\$141,930										
148	Municipio de Achacachi - Construcción de Sistema de Alcantarillado Sanitario y PTAR.	Mon 11/19/18	Fri 9/18/20	\$838,444	\$2,096,108	\$1,257,665	\$0	\$0	\$4,192,217										
149	Obras y DESCOM-FI	Mon 11/19/18	Fri 9/4/20	\$789,620	\$1,974,048	\$1,184,430	\$0	\$0	\$3,948,098										
150	Contratación Infraestructura y DESCOM (LPI)	Mon 11/19/18	Fri 5/3/19	\$0	\$0	\$0	\$0	\$0	\$0										
151	Ejecución de obra	Mon 6/3/19	Fri 5/1/20	\$753,454	\$1,883,634	\$1,130,181	\$0	\$0	\$3,767,269										
152	Ejecución del DESCOM	Mon 5/6/19	Fri 9/4/20	\$36,166	\$90,414	\$54,249	\$0	\$0	\$180,829										
153	Supervisión Obras y DESCOM-FI	Mon 11/19/18	Fri 9/18/20	\$48,824	\$122,060	\$73,235	\$0	\$0	\$244,119										
154	Contratación de Firma Supervisora (SBCC-LPI)	Mon 11/19/18	Fri 5/17/19	\$0	\$0	\$0	\$0	\$0	\$0										
155	Ejecución del Servicio	Mon 5/20/19	Fri 9/18/20	\$48,824	\$122,060	\$73,235	\$0	\$0	\$244,119										
156	Municipio de Distrito 2 La Laja - Construcción de Sistema de Alcantarillado Sanitario.	Mon 10/22/18	Fri 1/22/21	\$727,514	\$1,818,785	\$1,091,270	\$0	\$0	\$3,637,569										
157	Obras y DESCOM-FI	Mon 11/5/18	Fri 1/22/21	\$685,150	\$1,712,874	\$1,027,724	\$0	\$0	\$3,425,748										
158	Contratación Infraestructura y DESCOM (LPI)	Mon 11/5/18	Fri 4/19/19	\$0	\$0	\$0	\$0	\$0	\$0										
159	Ejecución de obra	Mon 5/20/19	Fri 9/18/20	\$653,769	\$1,634,422	\$980,653	\$0	\$0	\$3,268,844										
160	Ejecución del DESCOM	Mon 4/22/19	Fri 1/22/21	\$31,381	\$78,452	\$47,071	\$0	\$0	\$156,904										
161	Supervisión Obras y DESCOM-FI	Mon 10/22/18	Fri 1/8/21	\$42,364	\$105,911	\$63,546	\$0	\$0	\$211,821										
162	Contratación de Firma Supervisora (SBCC-LPI)	Mon 10/22/18	Fri 4/19/19	\$0	\$0	\$0	\$0	\$0	\$0										
163	Ejecución del Servicio	Mon 4/22/19	Fri 1/8/21	\$42,364	\$105,911	\$63,546	\$0	\$0	\$211,821										
164	Municipio de Mecapaca - Ampliación y mejoramiento del Sistema Principal de Agua Potable.	Mon 9/10/18	Fri 4/2/21	\$0	\$1,469,651	\$1,469,651	\$734,825	\$0	\$3,674,127										
165	Obras y DESCOM-FI	Mon 9/24/18	Fri 4/2/21	\$0	\$1,384,071	\$1,384,071	\$692,035	\$0	\$3,460,177										
166	Contratación Infraestructura y DESCOM (LPI)	Mon 9/24/18	Fri 3/8/19	\$0	\$0	\$0	\$0	\$0	\$0										
167	Ejecución de obra	Mon 4/8/19	Fri 12/11/20	\$0	\$1,320,678	\$1,320,678	\$660,339	\$0	\$3,301,695										
168	Ejecución del DESCOM	Mon 3/11/19	Fri 4/2/21	\$0	\$63,393	\$63,393	\$31,696	\$0	\$158,482										
169	Supervisión Obras y DESCOM-FI	Mon 9/10/18	Fri 4/2/21	\$0	\$85,580	\$85,580	\$42,790	\$0	\$213,950										
170	Contratación de Firma Supervisora (SBCC-LPI)	Mon 9/10/18	Fri 3/8/19	\$0	\$0	\$0	\$0	\$0	\$0										
171	Ejecución del Servicio	Mon 3/11/19	Fri 4/2/21	\$0	\$85,580	\$85,580	\$42,790	\$0	\$213,950										
172	Otros Proyectos a ser Priorizados E3 - E4 (FPS)	Mon 10/24/22	Fri 9/6/24	\$0	\$0	\$813,829	\$2,034,573	\$1,220,744	\$4,069,146										
173	Ejecución de Obras, DESCOM-FI y Susprevisión	Mon 10/24/22	Fri 9/6/24	\$0	\$0	\$813,829	\$2,034,573	\$1,220,744	\$4,069,146										
174	Medidas de Rápido Impacto (UCP-PAAP)	Mon 9/24/18	Fri 12/9/22	\$0	\$472,500	\$472,500	\$0	\$0	\$945,000										
175	Implementación	Mon 9/24/18	Fri 12/9/22	\$0	\$472,500	\$472,500	\$0	\$0	\$945,000										
176	FI Operadores E3 - E4 (FPS)	Mon 10/22/18	Fri 1/6/23	\$119,966	\$119,966	\$119,966	\$119,966	\$119,966	\$599,830										
177	Implementación - Muestra	Mon 10/22/18	Fri 9/18/20	\$119,966	\$119,966	\$119,966	\$119,966	\$0	\$479,864										
178	Implementación - Otros proyectos de la cartera	Mon 9/21/20	Fri 1/6/23	\$0	\$0	\$0	\$0	\$119,966	\$119,966										
179	Implementación del SIASAR	Mon 8/6/18	Tue 8/23/22	\$0	\$399,678	\$0	\$0	\$399,678	\$799,356										
180	Primera Fase - 750 comunidades	Mon 8/6/18	Fri 6/21/19	\$0	\$399,678	\$0	\$0	\$0	\$399,678										
181	Proceso de contratación	Mon 8/6/18	Fri 2/1/19	\$0	\$0	\$0	\$0	\$0	\$0										
182	Implementación	Mon 2/4/19	Fri 6/21/19	\$0	\$399,678	\$0	\$0	\$0	\$399,678										
183	Segunda Fase - 750 comunidades	Wed 10/6/21	Tue 8/23/22	\$0	\$0	\$0	\$0	\$399,678	\$399,678										
184	Proceso de contratación	Wed 10/6/21	Tue 4/5/22	\$0	\$0	\$0	\$0	\$0	\$0										



ID	Nombre de tarea	Start	Finish	Año 1	Año 2	Año 3	Año 4	Año 5	Total	2016	2017	2018	2019	2020	2021	2022	2023	2024	2025
185	Implementación	Wed 4/6/22	Tue 8/23/22	\$0	\$0	\$0	\$0	\$399,678	\$399,678										
186	Monitoreo, Evaluación y Auditoria	Mon 7/30/18	Fri 3/10/23	\$80,112	\$80,112	\$160,112	\$80,112	\$280,113	\$680,561										
187	Auditoria Contable	Mon 7/30/18	Fri 3/10/23	\$50,000	\$50,000	\$50,000	\$50,000	\$50,000	\$250,000										
188	Proceso de contratación	Mon 7/30/18	Fri 9/28/18	\$0	\$0	\$0	\$0	\$0	\$0										
189	Implementación	Mon 10/1/18	Fri 3/10/23	\$50,000	\$50,000	\$50,000	\$50,000	\$50,000	\$250,000										
190	Evaluación Intermedia	Fri 4/3/20	Thu 11/19/20	\$0	\$0	\$80,000	\$0	\$0	\$80,000										
191	Contratación de consultor individual (CCIN)	Fri 4/3/20	Thu 6/4/20	\$0	\$0	\$0	\$0	\$0	\$0										
192	Ejecución de la consultoria	Fri 6/5/20	Thu 11/19/20	\$0	\$0	\$80,000	\$0	\$0	\$80,000										
193	Evaluación Final	Wed 2/2/22	Tue 1/17/23	\$0	\$0	\$0	\$0	\$200,000	\$200,000										
194	Contratación de Firma Supervisora (SBCC)	Wed 2/2/22	Tue 8/2/22	\$0	\$0	\$0	\$0	\$0	\$0										
195	Ejecución de la consultoria	Wed 8/3/22	Tue 1/17/23	\$0	\$0	\$0	\$0	\$200,000	\$200,000										
196	Seguimiento y Monitoreo del Programa por el VAPSB	Mon 7/30/18	Fri 3/3/23	\$30,112	\$30,112	\$30,112	\$30,112	\$30,113	\$150,561										
197	Contratación de Consultores	Mon 7/30/18	Fri 3/3/23	\$30,112	\$30,112	\$30,112	\$30,112	\$30,113	\$150,561										
198	Administración	Mon 7/30/18	Fri 3/3/23	\$1,076,261	\$1,067,229	\$1,078,331	\$1,122,405	\$1,141,433	\$5,485,659										
199	Contratación del Personal de la UCP-PAAP	Mon 7/30/18	Fri 3/3/23	\$514,196	\$547,764	\$608,866	\$652,940	\$671,968	\$2,995,734										
200	Gastos Operativos UCP-PAAP	Mon 7/30/18	Fri 3/3/23	\$202,130	\$159,530	\$109,530	\$109,530	\$109,530	\$690,250										
201	Gastos Operativos FPS	Mon 7/30/18	Fri 3/3/23	\$359,935	\$359,935	\$359,935	\$359,935	\$359,935	\$1,799,675										
202		Mon 7/30/18	Mon 7/30/18	\$0	\$0	\$0	\$0	\$0	\$0										

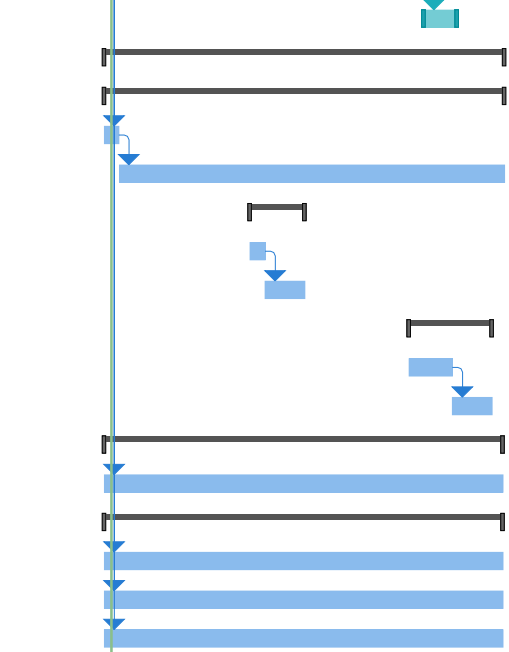



Id	Nombre de tarea	Comienzo	Fin	Año 1	Año 2	2017				2018				2019				2020				2021				2022				2023	
						tri 1	tri 2	tri 3	tri 4	tri 1	tri 2	tri 3	tri 4	tri 1	tri 2	tri 3	tri 4	tri 1	tri 2	tri 3	tri 4	tri 1	tri 2	tri 3	tri 4	tri 1	tri 2	tri 3	tri 4	tri 1	tri 2
72	Municipio de Tupiza	vie 03/08/18	jue 04/07/19	\$31,991	\$127,963																										
73	Departamento de Oruro	vie 11/05/18	jue 25/07/19	\$71,465	\$285,865																										
74	Municipio Machacamarca	vie 11/05/18	jue 25/07/19	\$71,465	\$285,865																										
75	Obras y DESCOM-FI	vie 11/05/18	jue 20/06/19	\$65,713	\$262,853																										
76	Contratación Infraestructura y DESCOM (LPN)	vie 11/05/18	jue 13/09/18	\$0	\$0																										
77	Ejecución de obra	vie 12/10/18	jue 28/02/19	\$57,643	\$230,573																										
78	Ejecución del DESCOM	vie 14/09/18	jue 20/06/19	\$8,070	\$32,280																										
79	Supervisión Obras y DESCOM-FI (CCIN)	vie 29/06/18	jue 25/07/19	\$5,752	\$23,012																										
80	Contratación Supervisor de Obras	vie 29/06/18	jue 30/08/18	\$0	\$0																										
81	Ejecución de la Supervisión de Obras	vie 31/08/18	jue 28/03/19	\$5,188	\$20,752																										
82	Contratación Supervisor de DESCOM	vie 29/06/18	jue 30/08/18	\$0	\$0																										
83	Ejecución de la Supervisión DESCOM	vie 31/08/18	jue 25/07/19	\$564	\$2,260																										
84	Departamento de La Paz	vie 02/03/18	jue 24/10/19	\$804,055	\$3,216,221																										
85	Municipio Achocalla - Marquirivi, Cañuma y Surusaya	vie 02/03/18	jue 29/08/19	\$326,109	\$1,304,433																										
86	Obras y DESCOM-FI	vie 25/05/18	jue 01/08/19	\$299,858	\$1,199,430																										
87	Contratación Infraestructura y DESCOM (LPN)	vie 25/05/18	jue 27/09/18	\$0	\$0																										
88	Ejecución de Obras	vie 26/10/18	jue 25/04/19	\$263,033	\$1,052,132																										
89	Ejecución DESCOM	vie 28/09/18	jue 01/08/19	\$36,825	\$147,298																										
90	Supervisión Obras y DESCOM-FI	vie 02/03/18	jue 29/08/19	\$26,251	\$105,003																										
91	Contratación de Firma Supervisora (SBCC)	vie 02/03/18	jue 30/08/18	\$0	\$0																										
92	Ejecución del Servicio	vie 31/08/18	jue 29/08/19	\$26,251	\$105,003																										
93	Municipio Tihuanaku - Huacullani	vie 30/03/18	jue 24/10/19	\$477,946	\$1,911,788																										
94	Obras y DESCOM-FI	vie 22/06/18	jue 24/10/19	\$439,473	\$1,757,895																										
95	Contratación Infraestructura y DESCOM (LPN)	vie 22/06/18	jue 25/10/18	\$0	\$0																										
96	Ejecución de Obras	vie 23/11/18	jue 18/07/19	\$385,503	\$1,542,013																										

Id	Nombre de tarea	Comienzo	Fin	Año 1	Año 2	2017				2018				2019				2020				2021				2022				2023	
						tri 1	tri 2	tri 3	tri 4	tri 1	tri 2	tri 3	tri 4	tri 1	tri 2	tri 3	tri 4	tri 1	tri 2	tri 3	tri 4	tri 1	tri 2	tri 3	tri 4	tri 1	tri 2	tri 3	tri 4	tri 1	tri 2
97	Ejecución DESCOM	vie 26/10/18	jue 24/10/19	\$53,970	\$215,882																										
98	Supervisión Obras y DESCOM-FI	vie 30/03/18	jue 24/10/19	\$38,473	\$153,893																										
99	Contratación de Firma Supervisora (SBCC)	vie 30/03/18	jue 27/09/18	\$0	\$0																										
100	Ejecución del Servicio	vie 28/09/18	jue 24/10/19	\$38,473	\$153,893																										
101	Otros Proyectos a ser Priorizados E1 - E2 (UCP PAAP)	lun 06/08/18	vie 23/08/19	\$0	\$628,006																										
102	Preinversión	lun 06/08/18	vie 19/07/19	\$0	\$598,101																										
103	Contratación de Firma Consultora (SBCC)	lun 06/08/18	vie 01/02/19	\$0	\$0																										
104	Elaboración de los Estudios de Preinversión de otros Proyectos	lun 04/02/19	vie 19/07/19	\$0	\$598,101																										
105	Supervisión de Preinversión	lun 26/11/18	vie 23/08/19	\$0	\$29,905																										
106	Contratación Supervisor de Preinversión (CCIN)	lun 26/11/18	vie 25/01/19	\$0	\$0																										
107	Ejecución de la Supervisión de Preinversión	lun 28/01/19	vie 23/08/19	\$0	\$29,905																										
108	Proyectos de la Muestra Tipo E3 - E4 (FPS)	lun 21/05/18	vie 02/04/21	\$3,473,306	\$10,769,134																										
109	Departamento de Chuquisaca	lun 21/05/18	vie 30/10/20	\$618,133	\$1,545,334																										
110	Municipio de Villaserrano - Sistema de Agua Potable y Mejoramiento y Ampliación del Sistema de Alcantarillado y PTAR	lun 21/05/18	vie 30/10/20	\$618,133	\$1,545,334																										
111	Obras y DESCOM-FI	lun 30/07/18	vie 30/10/20	\$571,054	\$1,427,636																										
112	Contratación Infraestructura y DESCOM (LPN)	lun 30/07/18	vie 30/11/18	\$0	\$0																										
113	Ejecución de obra	lun 31/12/18	vie 12/06/20	\$544,899	\$1,362,248																										
114	Ejecución del DESCOM	lun 03/12/18	vie 30/10/20	\$26,155	\$65,388																										
115	Supervisión Obras y DESCOM-FI	lun 21/05/18	vie 30/10/20	\$47,079	\$117,698																										
116	Contratación de Firma Supervisora (SBCC-LPI)	lun 21/05/18	vie 16/11/18	\$0	\$0																										
117	Ejecución del Servicio	lun 19/11/18	vie 30/10/20	\$47,079	\$117,698																										
118	Departamento de Santa Cruz	lun 18/06/18	vie 31/07/20	\$479,204	\$1,409,223																										



Id	Nombre de tarea	Comienzo	Fin	Año 1	Año 2	2017				2018				2019				2020				2021				2022				2023	
						tri 1	tri 2	tri 3	tri 4	tri 1	tri 2	tri 3	tri 4	tri 1	tri 2	tri 3	tri 4	tri 1	tri 2	tri 3	tri 4	tri 1	tri 2	tri 3	tri 4	tri 1	tri 2	tri 3	tri 4	tri 1	tri 2
119	Municipio de Pailón Centro - Adecuación y Rediseño de Estudio Técnico de Sistema de Agua Potable, Alcantarillado y PTAR	lun 18/06/18	vie 31/07/20	\$479,204	\$1,409,223																										
120	Obras y DESCOM-FI	lun 27/08/18	vie 31/07/20	\$442,706	\$1,317,978																										
121	Contratación Infraestructura y DESCOM (LPN)	lun 27/08/18	vie 28/12/18	\$0	\$0																										
122	Ejecución de obra	lun 31/12/18	vie 06/03/20	\$422,429	\$1,267,287																										
123	Ejecución del DESCOM	lun 31/12/18	vie 31/07/20	\$20,277	\$50,691																										
124	Supervisión Obras y DESCOM-FI	lun 18/06/18	vie 17/07/20	\$36,498	\$91,245																										
125	Contratación de Firma Supervisora (SBCC)	lun 18/06/18	vie 14/12/18	\$0	\$0																										
126	Ejecución del Servicio	lun 17/12/18	vie 17/07/20	\$36,498	\$91,245																										
127	Departamento de Oruro	lun 30/07/18	vie 29/05/20	\$437,314	\$1,311,943																										
128	Municipio de Huanuni - Construcción de Sistema de Alcantarillado Sanitario y PTAR.	lun 30/07/18	vie 29/05/20	\$437,314	\$1,311,943																										
129	Obras y DESCOM-FI	lun 24/09/18	vie 29/05/20	\$404,007	\$1,212,021																										
130	Contratación Infraestructura y DESCOM (LPN)	lun 24/09/18	vie 25/01/19	\$0	\$0																										
131	Ejecución de obra	lun 25/02/19	vie 24/01/20	\$385,503	\$1,156,509																										
132	Ejecución del DESCOM	lun 28/01/19	vie 29/05/20	\$18,504	\$55,512																										
133	Supervisión Obras y DESCOM-FI	lun 30/07/18	vie 29/05/20	\$33,307	\$99,922																										
134	Contratación de Firma Supervisora (SBCC)	lun 30/07/18	vie 25/01/19	\$0	\$0																										
135	Ejecución del Servicio	lun 28/01/19	vie 29/05/20	\$33,307	\$99,922																										
136	Departamento La Paz	lun 30/07/18	vie 02/04/21	\$1,938,655	\$6,502,634																										
137	Municipio de Colquencha - Construcción de Sistema de Alcantarillado Sanitario y PTAR.	lun 30/07/18	vie 26/06/20	\$372,697	\$1,118,090																										
138	Obras y DESCOM-FI	lun 22/10/18	vie 26/06/20	\$344,311	\$1,032,932																										
139	Contratación Infraestructura y DESCOM (LPN)	lun 22/10/18	vie 22/02/19	\$0	\$0																										
140	Ejecución de obra	lun 25/03/19	vie 21/02/20	\$328,541	\$985,622																										

Id	Nombre de tarea	Comienzo	Fin	Año 1	Año 2	2017				2018				2019				2020				2021				2022				2023	
						tri 1	tri 2	tri 3	tri 4	tri 1	tri 2	tri 3	tri 4	tri 1	tri 2	tri 3	tri 4	tri 1	tri 2	tri 3	tri 4	tri 1	tri 2	tri 3	tri 4	tri 1	tri 2	tri 3	tri 4	tri 1	tri 2
141	Ejecución del DESCOM	lun 25/02/19	vie 26/06/20	\$15,770	\$47,310																										
142	Supervisión Obras y DESCOM-FI	lun 30/07/18	vie 26/06/20	\$28,386	\$85,158																										
143	Contratación de Firma Supervisora (SBCC)	lun 30/07/18	vie 25/01/19	\$0	\$0																										
144	Ejecución del Servicio	lun 28/01/19	vie 26/06/20	\$28,386	\$85,158																										
145	Municipio de Achacachi - Construcción de Sistema de Alcantarillado Sanitario y PTAR.	lun 19/11/18	vie 18/09/20	\$838,444	\$2,096,108																										
146	Obras y DESCOM-FI	lun 19/11/18	vie 04/09/20	\$789,620	\$1,974,048																										
147	Contratación Infraestructura y DESCOM (LPI)	lun 19/11/18	vie 03/05/19	\$0	\$0																										
148	Ejecución de obra	lun 03/06/19	vie 01/05/20	\$753,454	\$1,883,634																										
149	Ejecución del DESCOM	lun 06/05/19	vie 04/09/20	\$36,166	\$90,414																										
150	Supervisión Obras y DESCOM-FI	lun 19/11/18	vie 18/09/20	\$48,824	\$122,060																										
151	Contratación de Firma Supervisora (SBCC-LPI)	lun 19/11/18	vie 17/05/19	\$0	\$0																										
152	Ejecución del Servicio	lun 20/05/19	vie 18/09/20	\$48,824	\$122,060																										
153	Municipio de Distrito 2 La Laja - Construcción de Sistema de Alcantarillado Sanitario.	lun 22/10/18	vie 22/01/21	\$727,514	\$1,818,785																										
154	Obras y DESCOM-FI	lun 05/11/18	vie 22/01/21	\$685,150	\$1,712,874																										
155	Contratación Infraestructura y DESCOM (LPI)	lun 05/11/18	vie 19/04/19	\$0	\$0																										
156	Ejecución de obra	lun 20/05/19	vie 18/09/20	\$653,769	\$1,634,422																										
157	Ejecución del DESCOM	lun 22/04/19	vie 22/01/21	\$31,381	\$78,452																										
158	Supervisión Obras y DESCOM-FI	lun 22/10/18	vie 08/01/21	\$42,364	\$105,911																										
159	Contratación de Firma Supervisora (SBCC-LPI)	lun 22/10/18	vie 19/04/19	\$0	\$0																										
160	Ejecución del Servicio	lun 22/04/19	vie 08/01/21	\$42,364	\$105,911																										
161	Municipio de Mecapaca - Ampliación y mejoramiento del Sistema Principal de Agua Potable.	lun 10/09/18	vie 02/04/21	\$0	\$1,469,651																										
162	Obras y DESCOM-FI	lun 24/09/18	vie 02/04/21	\$0	\$1,384,071																										
163	Contratación Infraestructura y DESCOM (LPI)	lun 24/09/18	vie 08/03/19	\$0	\$0																										

Id	Nombre de tarea	Comienzo	Fin	Año 1	Año 2	2017				2018				2019				2020				2021				2022				2023	
						tri 1	tri 2	tri 3	tri 4	tri 1	tri 2	tri 3	tri 4	tri 1	tri 2	tri 3	tri 4	tri 1	tri 2	tri 3	tri 4	tri 1	tri 2	tri 3	tri 4	tri 1	tri 2	tri 3	tri 4	tri 1	tri 2
164	Ejecución de obra	lun 08/04/19	vie 11/12/20	\$0	\$1,320,678																										
165	Ejecución del DESCOM	lun 11/03/19	vie 02/04/21	\$0	\$63,393																										
166	Supervisión Obras y DESCOM-FI	lun 10/09/18	vie 02/04/21	\$0	\$85,580																										
167	Contratación de Firma Supervisora (SBCC-LPI)	lun 10/09/18	vie 08/03/19	\$0	\$0																										
168	Ejecución del Servicio	lun 11/03/19	vie 02/04/21	\$0	\$85,580																										
169	Otros Proyectos a ser Priorizados E3 - E4 (FPS)	lun 26/11/18	vie 09/10/20	\$0	\$0																										
170	Ejecución de Obras, DESCOM-FI y Susprevisión	lun 26/11/18	vie 09/10/20	\$0	\$0																										
171	Medidas de Rápido Impacto (UCP-PAAP)	lun 24/09/18	vie 09/12/22	\$0	\$472,500																										
172	Implementación	lun 24/09/18	vie 09/12/22	\$0	\$472,500																										
173	FI Operadores E3 - E4 (FPS)	lun 22/10/18	vie 06/01/23	\$119,966	\$119,966																										
174	Implementación - Muestra	lun 22/10/18	vie 18/09/20	\$119,966	\$119,966																										
175	Implementación - Otros proyectos de la cartera	lun 21/09/20	vie 06/01/23	\$0	\$0																										
176	Implementación del SIASAR	lun 06/08/18	vie 21/06/19	\$0	\$399,678																										
177	Primera Fase - 750 comunidades	lun 06/08/18	vie 21/06/19	\$0	\$399,678																										
178	Proceso de contratación	lun 06/08/18	vie 01/02/19	\$0	\$0																										
179	Implementación	lun 04/02/19	vie 21/06/19	\$0	\$399,678																										
180	Monitoreo, Evaluación y Auditoria	lun 30/07/18	vie 10/03/23	\$80,112	\$80,112																										
181	Auditoria Contable	lun 30/07/18	vie 10/03/23	\$50,000	\$50,000																										
182	Proceso de contratación	lun 30/07/18	vie 28/09/18	\$0	\$0																										
183	Implementación	lun 01/10/18	vie 10/03/23	\$50,000	\$50,000																										
184	Seguimiento y Monitoreo del Programa por el VAPSB	lun 30/07/18	vie 03/03/23	\$30,112	\$30,112																										
185	Contratación de Consultores	lun 30/07/18	vie 03/03/23	\$30,112	\$30,112																										
186	Administración	lun 30/07/18	vie 03/03/23	\$1,080,461	\$1,071,429																										
187	Contratación del Personal de la UCP-PAAP	lun 30/07/18	vie 03/03/23	\$514,196	\$547,764																										
188	Gastos Operativos UCP-PAAP	lun 30/07/18	vie 03/03/23	\$202,130	\$159,530																										

