
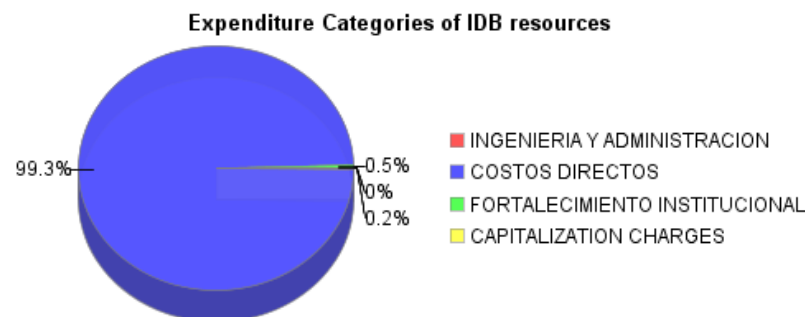
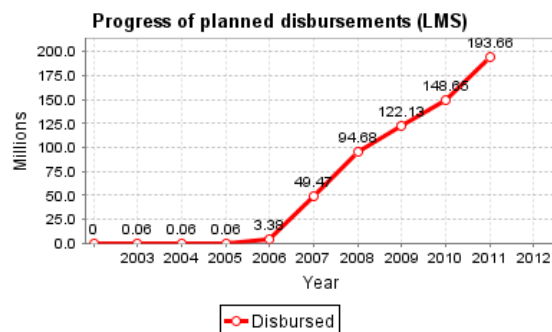



## Summary Report

Basic Data		Available Funds (US\$)		Total Cost and Source	
Executing Agency (EA):	MINISTERIO DE ECONOMIA, HACIENDA Y FINANZAS				
Sector:	TRANSPORT				
Loan Number(s):	1294/OC-AR	Current Approved Amount:	200.000.000,00	Original IDB:	200.000.000,00
Stage:	Approved	Disbursed Amount to Date:	199.999.999,97	Current IDB:	200.000.000,00
Operation Type:	INV - Investment	% Disbursed:	100,00	Pari-passu:	50,00
Related Operation(s):	TC9803504	Balance:	0,03	Co-Financing/Country:	80.000.000,00
Operation Subtype:	GOM - Global of Multiple Works Operation			Original Estimate:	280.000.000,00
				Amortization Period (months):	162

Project Environmental and Social Impact Category	Reformulation	Validation
Project Environmental and Social Impact Category: B(R)	( ) Was the objective(s) of this project reformulated?	Validated by Division Chief: 23-abr-2012 Validated by Country Representative: 25-abr-2012

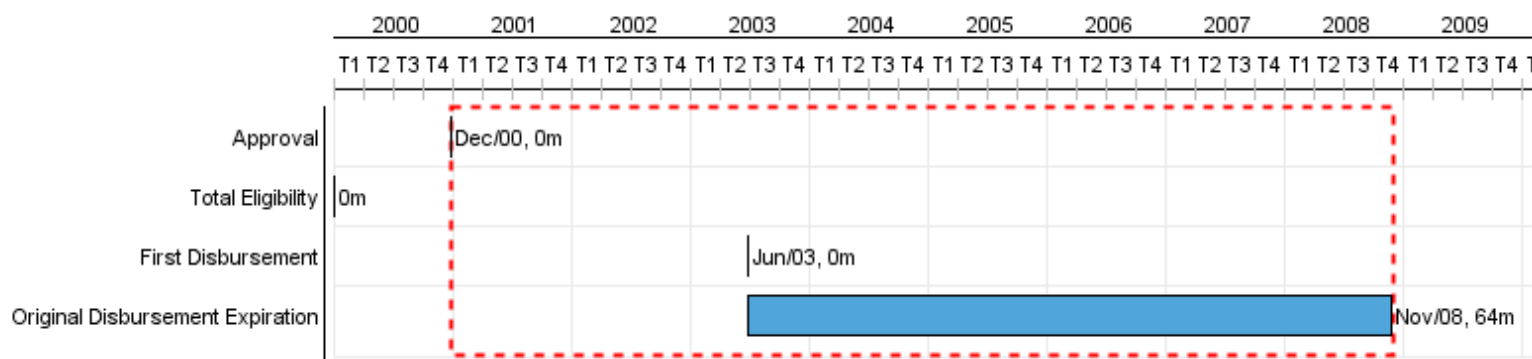

## Accumulated Progress as of 2011

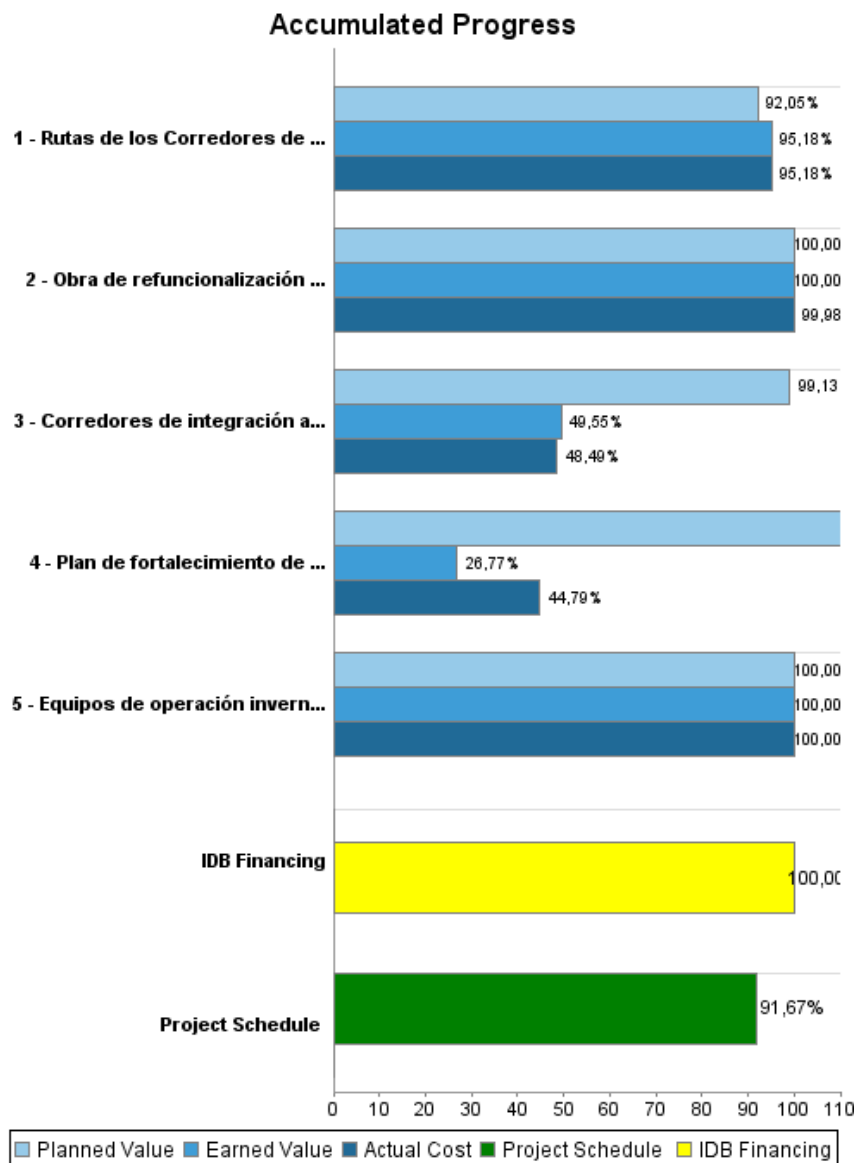

## Outcomes

<b>Outcome:</b>	Nivel de servicio de las rutas y pasos fronterizos intervenidos mejorado.
-----------------	---

Indicator	Unit of Measure	Baseline	Baseline Year		End of project
Costos de Transporte Reducidos	\$/km	1.42		P A	1,01
Tiempo de Viaje Reducido	\$/km	1.30		P A	1,00
Condiciones de Seguridad Mejoradas	Alertas			P A	3,00

## Outputs: Annual Physical and Financial Progress 2011

Description	Unit of Measure	Physical				Financial			
		Planned	Actual	Accumulated units	EOP units	Planned	Actual	Accumulated costs	EOP costs
<b>1. Mejoramiento y Rehabilitación de Corredores Viales de Integración.</b>									
Corredores de integración ampliados	Kilómetros	97,00	5,00		242,00	273.311.000,00	8.653.000,00		513.800.000,00
Rutas de los Corredores de integración rehabilitados	Kilómetros				68,00	4.441.000,00	3.072.000,00		28.400.000,00
<b>2. Fortalecimiento Institucional</b>									
Plan de fortalecimiento de la capacidad de la Dirección Nacional de Vialidad implementado	Plan	1,00			1,00	1.394.200,00	343.000,00		1.904.000,00
Obra de refuncionalización del campamento de la DNV en Uspallata, Ruta Nacional 7 terminada	Obra				1,00				1.754.000,00
<b>3. Adquisición de equipos de operación</b>									
Equipos de operación invernal adquiridos	equipos				9,00				5.152.391,00
<b>4. Ingeniería y Administración</b>									
<b>TOTAL</b>						<b>279.146.200,00</b>	<b>12.068.000,00</b>		<b>551.010.391,00</b>
