
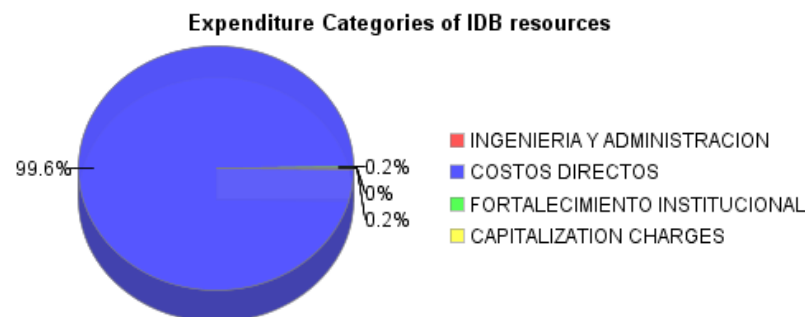
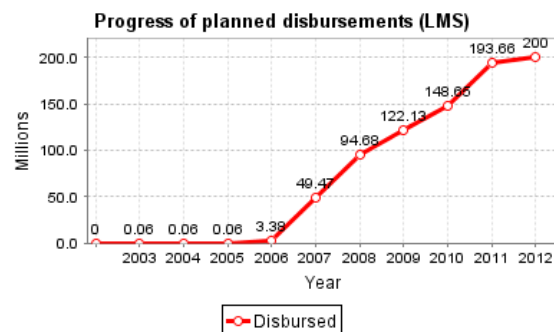



## Summary Report

Basic Data		Available Funds (US\$)		Total Cost and Source	
Executing Agency (EA):	MINISTERIO DE ECONOMIA, HACIENDA Y FINANZAS				
Sector:	TRANSPORT				
Loan Number(s):	1294/OC-AR	Current Approved Amount:	200.000.000,00	Original IDB:	200.000.000,00
Stage:	Approved	Disbursed Amount to Date:	199.999.999,97	Current IDB:	200.000.000,00
Operation Type:	INV - Investment	% Disbursed:	100,00	Pari-passu:	50,00
Related Operation(s):	TC9803504	Balance:	0,03	Co-Financing/Country:	80.000.000,00
Operation Subtype:	GOM - Global of Multiple Works Operation			Original Estimate:	280.000.000,00
				Amortization Period (months):	162

Project Environmental and Social Impact Category	Reformulation	Validation
Project Environmental and Social Impact Category: B(R)	( ) Was the objective(s) of this project reformulated?	Validated by Division Chief: 28-sep-2012 Validated by Country Representative: 15-oct-2012

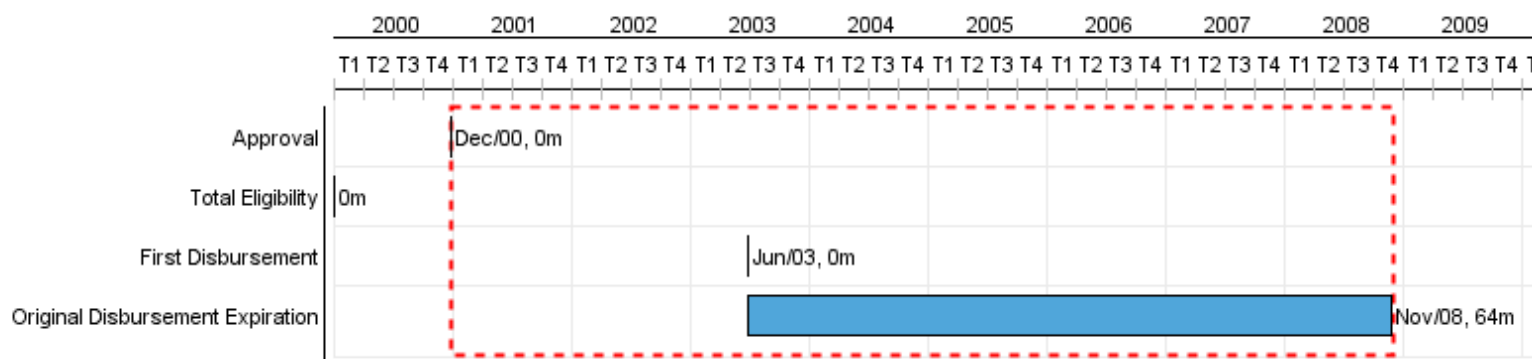

## Accumulated Progress as of 2012

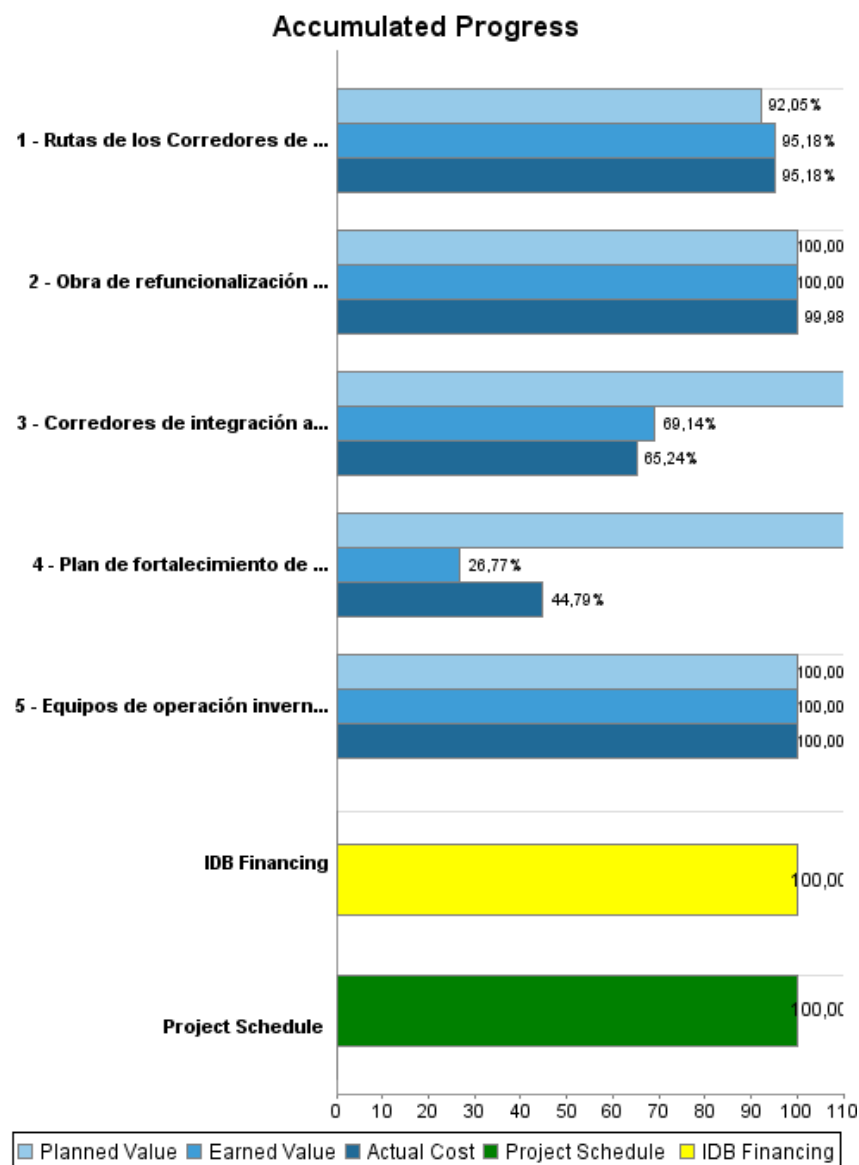

## Outcomes

<b>Outcome:</b>	Nivel de servicio de las rutas y pasos fronterizos intervenidos mejorado.
-----------------	---

Indicator	Unit of Measure	Baseline	Baseline Year		End of project
Costos de Transporte Reducidos	\$/km	1.42		P A	1.01
Tiempo de Viaje Reducido	\$/km	1.30		P A	1.00
Condiciones de Seguridad Mejoradas	Alertas			P A	3.00

## Outputs: Annual Physical and Financial Progress 2012

Description	Unit of Measure	Physical				Financial			
		Planned	Actual	Accumulated units	EOP units	Planned	Actual	Accumulated costs	EOP costs
<b>1. Mejoramiento y Rehabilitación de Corredores Viales de Integración.</b>									
Corredores de integración ampliados	Kilómetros	92,00	35,00		242,00	264.658.000,00	86.050.284,00		513.800.000,00
Rutas de los Corredores de integración rehabilitados	Kilómetros				68,00				28.400.000,00
<b>2. Fortalecimiento Institucional</b>									
Plan de fortalecimiento de la capacidad de la Dirección Nacional de Vialidad implementado	Plan				1,00				1.904.000,00
Obra de refuncionalización del campamento de la DNV en Uspallata, Ruta Nacional 7 terminada	Obra				1,00				1.754.000,00
<b>3. Adquisición de equipos de operación</b>									
Equipos de operación invernal adquiridos	equipos				9,00				5.152.391,00
<b>4. Ingeniería y Administración</b>									
Ingeniería y Administración	N/A								19.500.000,00
<b>TOTAL</b>						<b>264.658.000,00</b>	<b>86.050.284,00</b>		<b>570.510.391,00</b>
