

PMR Operational Report

Operation Number	UR-L1069	Chief of Operations Validation Date	04/15/19
Year- PMR Cycle	Second period Jan-Dec 2018	Division Chief Validation Date	04/15/19
Last Update	04/03/19	Country Representative Validation Date	05/02/19
PMR Validation Stage	Validated by Representative		

Basic Data

Operation Profile

Operation Name	Drainage and Environmental Sanitation	Loan Number	2647/OC-UR
Executing Agency	INTENDENCIA MUNICIPAL DE MONTEVIDEO	Sector/Subsector	AS - WATER AND SANITATION
Team Leader	PAEZ RUBIO, TANIA	Overall Stage	Disbursing (From eligibility until all the Operations are closed)
Operation Type	Loan Operation	Country	URUGUAY
Lending Instrument	Investment Loan	Convergence related Operation(s)	
Borrower	REPUBLICA ORIENTAL DE URUGUAY		


Environmental and Social Safeguards

Impacts Category	B	Was/Were the objective(s) of this operation reformulated?	NO
Safeguard Performance Rating	Satisfactory	Date of approval	
Safeguard Performance Rating - Rationale	Satisfactory		

Financial Data

Item	Total Cost and Source					Available Funds (US\$)			
	Original IDB	Current IDB	Local Counterpart	Co-Financing / Country	Total Original Cost	Current IDB	Disb. Amount to Date	% Disb	Undisbursed Amount
UR-L1069	20,500,000	20,500,000	10,000,000	0	30,500,000	20,500,000	20,500,000	100.00%	0
Aggregated	20,500,000	20,500,000	10,000,000	0	30,500,000	20,500,000	20,500,000	100.00%	0

Expense Categories by Loan Contract (cumulative values)

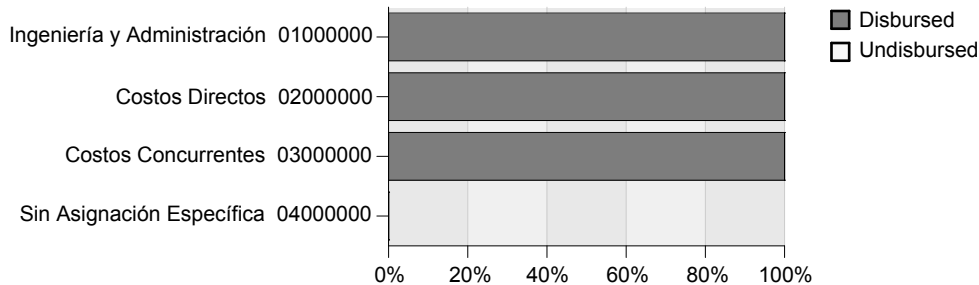

Please note that inactive indicators and outputs are not displayed; totals in the actual cost table may not match the sum of the cost of the outputs displayed, due to the cost of inactive outputs.

PMR Operational Report

RESULTS MATRIX

IMPACTS

No information available for this section

PMR Operational Report

RESULTS MATRIX

OUTCOMES

Outcome Nbr. 1: Sistema de drenaje y saneamiento ambiental mejorado

Observation:

Indicator	Unit of Measure	Baseline	Baseline Year		2012	2013	2014	2015	2016	2017	2018	2019	EOP 2019
1.0	Hogares protegidos de riesgo de inundación	Households (#)	0.00	2012	P								
					P(a)				0.00	0.00	911.00		1,510.00
					A			359.00	240.00	0.00	911.00		

Details

Means of verification: relevamiento de las viviendas luego de un evento de lluvias que originalmente estuvieron afectadas por las inundaciones

Observations: Período de retorno de 10 años

Pro-Gender	No	Pro-Ethnicity	No
-------------------	----	----------------------	----

Indicator	Unit of Measure	Baseline	Baseline Year		2012	2013	2014	2015	2016	2017	2018	2019	EOP 2019
1.1	Áreas inundables en Montevideo con un período de retorno de 10 años.	Áreas	11.00	2011	P								8.00
					P(a)			10.00	10.00	10.00	8.00		8.00
					A			10.00	10.00	10.00	8.00		

Details

Means of verification: Certificaciones de obra

Pro-Gender	No	Pro-Ethnicity	No
-------------------	----	----------------------	----

Indicator	Unit of Measure	Baseline	Baseline Year		2012	2013	2014	2015	2016	2017	2018	2019	EOP 2019
1.2	Número de Conexiones irregulares a las redes de agua y saneamiento en el PTI	Conexiones irregulares	67.00	2011	P								
					P(a)								0.00
					A								0.00

Details

Pro-Gender	No	Pro-Ethnicity	No
-------------------	----	----------------------	----

RESULTS MATRIX

OUTPUTS: ANNUAL PHYSICAL AND FINANCIAL PROGRESS

Component Nbr. 1 Componente I. Obras de drenaje pluvial en la cuenca de Arroyo Seco

	Output	Unit of Measure		PHYSICAL PROGRESS		FINANCIAL PROGRESS	
				2018	EOP 2019	2018	EOP 2019
1.1	1.1 Obras de control de inundaciones	Tanques	P		2		6,843,900
			P(a)	1	2	1,762,282.67	7,840,264.73
			A	1	2	1,503,500.02	7,581,482.08

Component Nbr. 2 Componente II. Obras de drenaje pluvial en la cuenca del Arroyo Quitacalzones

	Output	Unit of Measure		PHYSICAL PROGRESS		FINANCIAL PROGRESS	
				2018	EOP 2019	2018	EOP 2019
2.1	2.1 Obras de control de inundaciones	Tanques	P		3		10,129,100
			P(a)	1	2	1,067,981.06	9,370,788.71
			A	1	2	1,045,592.48	9,348,400.13

Component Nbr. 3 Componente III. Obras de drenaje pluvial en la cuenca de la Cañada Peabody

	Output	Unit of Measure		PHYSICAL PROGRESS		FINANCIAL PROGRESS	
				2018	EOP 2019	2018	EOP 2019
3.1	3.1 Redes de alcantarillado pluvial construidas o ampliadas	km	P		4.6		4,746,000
			P(a)		4.6		6,894,694.96
			A		4.5		6,625,693
3.2	3.2 Obras de control de inundaciones	Tanques	P		1		340,000
			P(a)		1		290,514.04
			A		1		260,608.69

Component Nbr. 4 Componente IV. Saneamiento ambiental para el PTI

	Output	Unit of Measure		PHYSICAL PROGRESS		FINANCIAL PROGRESS	
				2018	EOP 2019	2018	EOP 2019
4.1	4.1 Sistema de Saneamiento Ambiental y microdrenaje construido	Sistemas	P		1		1,083,000
			P(a)		1		1,424,579.72
			A		1		1,423,731.72

Component Nbr. 5 Componente V. Estaciones hidrometereológicas

	Output	Unit of Measure		PHYSICAL PROGRESS		FINANCIAL PROGRESS	
				2018	EOP 2019	2018	EOP 2019
5.1	5.1 Estaciones Hidrometeorológicas	Estaciones	P		12		50,000
			P(a)		12		43,651.92
			A		15		43,651.92

Component Nbr. 6 Compra Terrenos

	Output	Unit of Measure		PHYSICAL PROGRESS		FINANCIAL PROGRESS	
					EOP	EOP	
6.			P				
			P(a)				
			A				

RESULTS MATRIX

OUTPUTS: ANNUAL PHYSICAL AND FINANCIAL PROGRESS

Component Nbr. 7 Costos administrativos y financieros

				PHYSICAL PROGRESS	FINANCIAL PROGRESS
	Output	Unit of Measure		EOP	EOP
7.			P		
			P(a)		
			A		

Other Cost

	Adquisición de Terrenos	P				671,000
		P(a)				661,158
		A				661,158
	Costos Administrativos y Financieros	P				6,637,000
		P(a)			1,897,844.81	7,804,656.17
		A			1,324,929.82	7,231,741.18

Total Cost

	Total Cost	P				30,500,000
		P(a)			4,728,108.54	34,330,308.25
		A			3,874,022.32	33,176,466.72

CHANGES TO THE MATRIX

Section	Name	Reasons	Type of Change	Subtype	Modified By	Entered in the System
Outcome	Número de Conexiones irregulares a las redes de agua y saneamiento en el PTI	<p>En el marco del trabajo sobre la evaluación final del Programa, se acordó con la Unidad Ejecutora la inclusión de un indicador de resultado que de cuenta de los trabajos realizados en cuanto a las conexiones de agua y saneamiento en el Parque Tecnológico Industrial (PTI) de la Intendencia de Montevideo.</p> <p>Los valores de la línea de base son los que aparecen en los documentos del Préstamo.</p> <p>La Intendencia de Montevideo solicitó este ajuste por nota Siscor CSC/CUR-2260.</p>	Create Outcome Indicator	N/A	FBACHINO	12/18/2018
Output	1.1 Obras de control de inundaciones	Los ajustes responden a los datos definitivos de ejecución remitidos por la Unidad Ejecutora en su informe final. (Entrada Siscor CSC/CUR-345/2019)	Modify Output	Modify Financial Historical Actual	FBACHINO	03/22/2019
				Modify Financial P(a) value	FBACHINO	03/22/2019
	2.1 Obras de control de inundaciones	Los ajustes responden a los datos definitivos de ejecución remitidos por la Unidad Ejecutora en su informe final. (Entrada Siscor CSC/CUR-345/2019)	Modify Output	Modify Financial Historical Actual	FBACHINO	03/22/2019
				Modify Financial P(a) value	FBACHINO	03/22/2019
	3.1 Redes de alcantarillado pluvial construidas o ampliadas	Los ajustes responden a los datos definitivos de ejecución remitidos por la Unidad Ejecutora en su informe final. (Entrada Siscor CSC/CUR-345/2019)	Modify Output	Modify Financial Historical Actual	FBACHINO	03/22/2019
				Modify Financial P(a) value	FBACHINO	03/22/2019
	3.2 Obras de control de inundaciones	Los ajustes responden a los datos definitivos de ejecución remitidos por la Unidad Ejecutora en su informe final. (Entrada Siscor CSC/CUR-345/2019)	Modify Output	Modify Financial Historical Actual	FBACHINO	03/22/2019
				Modify Financial P(a) value	FBACHINO	03/22/2019
	4.1 Sistema de Saneamiento Ambiental y microdrenaje construido	Los ajustes responden a los datos definitivos de ejecución remitidos por la Unidad Ejecutora en su informe final. (Entrada Siscor CSC/CUR-345/2019)	Modify Output	Modify Financial Historical Actual	FBACHINO	03/22/2019
				Modify Financial P(a) value	FBACHINO	03/22/2019
	5.1 Estaciones Hidrometeorológicas	Los ajustes responden a los datos definitivos de ejecución remitidos por la Unidad Ejecutora en su informe final. (Entrada Siscor CSC/CUR-345/2019)	Modify Output	Modify Financial Historical Actual	FBACHINO	03/22/2019
				Modify Financial P(a) value	FBACHINO	03/22/2019

PMR Operational Report

IMPLEMENTATION STATUS AND LEARNING

Lesson Learned - Categories
Intra/Inter Coordination
Others - Dimensions Related to Public Processes/ Actors
Others - Fiduciary Dimensions
Others - Technical-Sectorial Dimensions
Project Management Capacity
Stakeholder Priorities
