

PMR Operational Report

Operation Number	BA-L1025	Chief of Operations Validation Date	03/24/20
Year- PMR Cycle	Second period Jan-Dec 2019	Division Chief Validation Date	03/24/20
Last Update	03/23/20	Country Representative Validation Date	03/26/20
PMR Validation Stage	Validated by Representative		

Basic Data

Operation Profile

Operation Name	Public Sector Smart Energy (PSSE) Program	Loan Number	2748/OC-BA
Executing Agency	INTER-AMERICAN DEVELOPMENT BANK	Sector/Subsector	EN-EEC - ENERGY-ENERGY EFFICIENCY AND RENEWABLE ENERGY IN END USE
Team Leader	PRADO, VERONICA	Overall Stage	Disbursing (From eligibility until all the Operations are closed)
Operation Type	Loan Operation	Country	Barbados
Lending Instrument	Investment Loan	Convergence related Operation(s)	BA-X1003
Borrower	BARBADOS		


Environmental and Social Safeguards

Impacts Category	A	Was/Were the objective(s) of this operation reformulated?	NO
Safeguard Performance Rating	Satisfactory	Date of approval	
Safeguard Performance Rating - Rationale	Currently the program in the process of identifying the contractor for the management of hazardous waste coming from the retrofitting of buildings, to ensure it follows International Standards. Once identified, the waste management plan should be put into place. The project is also starting the assess the thematic associated with the OTEC technology, even though still in early stages.		

Financial Data

Item	Total Cost and Source					Available Funds (US\$)			
	Original IDB	Current IDB	Local Counterpart	Co-Financing / Country	Total Original Cost	Current IDB	Disb. Amount to Date	% Disb	Undisbursed Amount
BA-L1025	17,000,000	17,000,000	0	7,664,000	24,664,000	17,000,000	10,337,003.25	60.81%	6,662,996.75
BA-X1003	0	7,626,493.47	0	0	5,810,000	7,626,493.47	5,537,191.84	72.60%	2,089,301.63
Aggregated	17,000,000	24,626,493.47	0	7,664,000	30,474,000	24,626,493.47	15,874,195.09	64.46%	8,752,298.38

Expense Categories by Loan Contract (cumulative values)

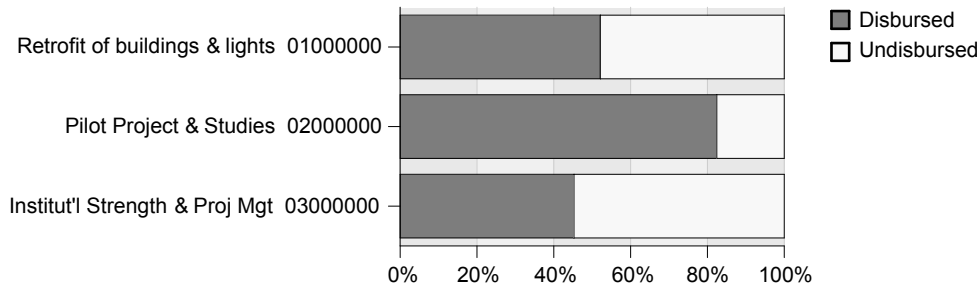

Please note that inactive indicators and outputs are not displayed; totals in the actual cost table may not match the sum of the cost of the outputs displayed, due to the cost of inactive outputs.

PMR Operational Report

RESULTS MATRIX

IMPACTS

Impact Nbr. 1: PSSE Financial savings cumulative to date (real 2012 US\$).

Observation: Financial savings from the reduction in electricity purchased from BL&P by the GOBA, as well as the sale of electricity produced by the solar PV systems to BL&P, and reduction in fuel purchased for the GOBA vehicle fleet.

No information available for this section

Details

Means of verification: Power consumption Information provided by the Government and by the utility (BL&P)

Pro-Gender	No	Pro-Ethnicity	No
-------------------	----	----------------------	----

Impact Nbr. 2: Avoided CO2 emissions by the PSSE Program (cumulative to date).

Observation:

No information available for this section

Details

Means of verification: Reports prepared by Government of Barbados - Energy Division

Pro-Gender	No	Pro-Ethnicity	No
-------------------	----	----------------------	----

PMR Operational Report

RESULTS MATRIX

OUTCOMES

Outcome Nbr. 1: RE capacity installed in government buildings

Observation:

Indicator		Unit of Measure	Baseline	Baseline Year		2018	2020	EOP 2020
1.1	Electricity Generated from Solar PV Systems (MWh/year, MWh to date generated).	MWh	0.00	2012	P			6,073.00
					P(a)			6,073.00
					A			
Details								
Means of verification: Reports prepared by Government of Barbados- Energy Division								
Observations: Assuming an output of 1,700/kW/year for solar PV. Note: this includes the 50kW PV system installed for charging the Electric Vehicles in Component 2.								
Pro-Gender		No	Pro-Ethnicity		No			

Outcome Nbr. 2: Energy saving with EE technologies in public lighting and buildings

Observation:

Indicator		Unit of Measure	Baseline	Baseline Year		2018	2020	EOP 2020
2.1	Electricity Saved through retrofits (energy efficient public lights and energy efficient equipment in public buildings) (MWh/year, MWh to date saved).	MWh	0.00	2012	P			28,608.00
					P(a)			28,608.00
					A			
Details								
Means of verification: Reports prepared by Government of Barbados Energy Division								
Pro-Gender		No	Pro-Ethnicity			No		

Outcome Nbr. 3: Fossil Fuels Saved from the implementation of the pilot projects (barrels of oil equivalent).

Observation:

Indicator		Unit of Measure	Baseline	Baseline Year		2018	2020	EOP 2020
3.1	Fossil Fuels Saved from the implementation of the pilot projects (barrels of oil	barrels of oil	0.00	2012	P			240.00
					P(a)			240.00

PMR Operational Report

RESULTS MATRIX

OUTCOMES

3.1	equivalent).	barrels of oil	0.00	2012	A			
Details								
Means of verification: Reports prepared by Government of Barbados - Energy Division								
Pro-Gender			No			Pro-Ethnicity		
						No		

Outcome Nbr. 4: public awareness increased in public sector for RE and EE

Observation:

Indicator		Unit of Measure	Baseline	Baseline Year		2018	2020	EOP 2020
4.1	Percentage of survey respondents participating at events that report high awareness and support of sustainable energy practices (Number of respondents that answered ?high awareness and support of sustainable energy?/ Total number of survey res	%	0.00	2012	P			80.00
					P(a)			80.00
					A			
Details								
Means of verification: Reports prepared by Government of Barbados - Energy Division								
Pro-Gender		No	Pro-Ethnicity		No			

RESULTS MATRIX

OUTPUTS: ANNUAL PHYSICAL AND FINANCIAL PROGRESS

Component Nbr. 1 RE and EE in public buildings

	Output	Unit of Measure		PHYSICAL PROGRESS		FINANCIAL PROGRESS	
				2019	EOP 2020	2019	EOP 2020
1.1	Streetlight installation completed	%	P		85		9,977,800
			P(a)	60	85	5,293,250	7,560,464.05
			A	51	51	7,379,264	7,450,418.05
1.2	Number of public buildings retrofitted with EE	Buildings	P		12		4,150,000
			P(a)	3	14	375,661	3,545,000
			A	0	0	0	0
1.3	PV in Public Buildings Installed	kW	P		1,190		5,500,000
			P(a)	500	3,965	2,306,710	6,150,464.49
			A	1,755	2,600	1,597,509	4,630,319.49

Component Nbr. 2 Pilot projects

	Output	Unit of Measure		PHYSICAL PROGRESS		FINANCIAL PROGRESS	
				2019	EOP 2020	2019	EOP 2020
2.1	Public Electric Vehicles with Solar PV installed and pilot completed	Electric vehicles	P		8		300,000
			P(a)	2	10	670,200	1,573,389.4
			A	0	8	0	423,291.4
2.2	Ocean studies completed	Studies	P		1		1,000,000
			P(a)	0	1	100,364	1,077,382.09
			A	0	0	14,632	98,608.09

Component Nbr. 3 capacity building

	Output	Unit of Measure		PHYSICAL PROGRESS		FINANCIAL PROGRESS	
				2019	EOP 2020	2019	EOP 2020
3.1	Capacity Building training/activities completed	numbr of people	P		0		1,395,000
			P(a)	10	18	202,798	841,864.2
			A	3	13	25,620	151,741.2
3.2	Public awareness events completed	number of people	P		100		305,000
			P(a)	50	250	66,000	918,002
			A	200	200	13,910	13,910
3.3	Monitoring and evaluation activities completed	activities	P		4		500,000
			P(a)	1	4	77,000	477,879
			A	1	2	52,965	305,844
3.4	Number of Jobs created in ETD for implementing the PSSE Program	Positions	P		4		1,153,000
			P(a)	0	9	325,463	1,483,525.74
			A	0	9	146,223	1,342,078.74

Other Cost

	Administrative fees expended	P				383,200
		P(a)				383,200
		A				0

Total Cost

	Total Cost	P				24,664,000
		P(a)			9,417,446	24,011,170.97
		A			9,230,123	14,416,210.97

PMR Operational Report

CHANGES TO THE MATRIX

Section	Name	Reasons	Type of Change	Subtype	Modified By	Entered in the System
Output	Capacity Building training/activities completed	The project has experienced delays as a result of lengthy procurement processes, difficulty related to stakeholders engagement, delays in contract preparation, registration of international firms, and consequently, timelines and related costs had to adjusted accordingly.	Modify Output	Modify Financial EOP P(a) value - caused by a change in the Financial P(a).	ROCHELLEF	03/20/2020
				Modify Physical EOP P(a) value - caused by a change in the Physical P(a).	ROCHELLEF	03/20/2020
	Monitoring and evaluation activities completed	The project has experienced delays as a result of lengthy procurement processes, difficulty related to stakeholders engagement, delays in contract preparation, registration of international firms, and consequently, timelines and related costs had to adjusted accordingly.	Modify Output	Modify Financial EOP P(a) value - caused by a change in the Financial P(a).	ROCHELLEF	03/20/2020
	Number of Jobs created in ETD for implementing the PSSE Program	The project has experienced delays as a result of lengthy procurement processes, difficulty related to stakeholders engagement, delays in contract preparation, registration of international firms, and consequently, timelines and related costs had to adjusted accordingly.	Modify Output	Modify Financial EOP P(a) value - caused by a change in the Financial P(a).	ROCHELLEF	03/20/2020
	Number of public buildings retrofitted with EE	The project has experienced delays as a result of lengthy procurement processes, difficulty related to stakeholders engagement, delays in contract preparation, registration of international firms, and consequently, timelines and related costs had to adjusted accordingly.	Modify Output	Modify Financial EOP P(a) value - caused by a change in the Financial P(a).	ROCHELLEF	03/20/2020
				Modify Physical EOP P(a) value - caused by a change in the Physical P(a).	ROCHELLEF	03/19/2020
	Ocean studies completed	The project has experienced delays as a result of lengthy procurement processes, difficulty related to stakeholders engagement, delays in contract preparation, registration of international firms, and consequently, timelines and related costs had to adjusted accordingly.	Modify Output	Modify Financial EOP P(a) value - caused by a change in the Financial P(a).	ROCHELLEF	03/20/2020
	PV in Public Buildings Installed	The project has experienced delays as a result of lengthy procurement processes, difficulty related to stakeholders engagement, delays in contract preparation, registration of international firms, and consequently, timelines and related costs had to adjusted accordingly.	Modify Output	Modify Financial EOP P(a) value - caused by a change in the Financial P(a).	ROCHELLEF	03/20/2020
				Modify Physical EOP P(a) value - caused by a change in the Physical P(a).	VPRADO	03/20/2020
				Modify Physical Historical Actual	VPRADO	03/20/2020
	Public Electric Vehicles with Solar PV installed and pilot completed	The project has experienced delays as a result of lengthy procurement processes, difficulty related to stakeholders engagement, delays in contract preparation, registration of international firms, and consequently, timelines and related costs had to adjusted accordingly.	Modify Output	Modify Financial EOP P(a) value - caused by a change in the Financial P(a).	ROCHELLEF	03/20/2020
	Public awareness events completed	The project has experienced delays as a result of lengthy procurement processes, difficulty related to stakeholders engagement, delays in contract preparation, registration of international firms, and consequently, timelines and related costs had to adjusted accordingly.	Modify Output	Modify Financial EOP P(a) value - caused by a change in the Financial P(a).	ROCHELLEF	03/20/2020
				Modify Physical EOP P(a) value - caused by a change in the Physical P(a).	ROCHELLEF	03/20/2020
	Streetlight installation completed	The project has experienced delays as a result of lengthy procurement processes, difficulty related to stakeholders engagement, delays in contract preparation, registration of international firms, and consequently, timelines and related costs had to adjusted accordingly.	Modify Output	Modify Financial EOP P(a) value - caused by a change in the Financial P(a).	ROCHELLEF	03/20/2020

PMR Operational Report

IMPLEMENTATION STATUS AND LEARNING

Lesson Learned - Categories

Acquisitions and Procurement - Bidding Stage
