



Operation Number: **BR-L1099**  
Year- PMR Cycle: **Segundo período enero-diciembre 2013**  
Last Update: **5/29/2014**  
PMR Validation Stage: **Validada por el Representante de País**

Chief of Operations validation date: **06/18/2014**  
Division Chief validation date: **06/24/2014**  
Country Representative validation date: **07/11/2014**

Inter-American Development Bank - IDB  
Office of Strategic Planning and Development Effectiveness

## Operation Profile

### Basic Data

Operation name:	PROCIDADES-Programa Mejoramiento Infraestructura Urbana Municipio Ponta Grossa	Loan Number:	2054/OC-BR
Executing Agency (EA):	PREFEITURA MUNICIPAL DE PONTA GROSSA		
Team Leader:	Hobbs,Jason Anthony	Sector/Subsector:	NEIGHBORHOOD UPGRADING
Operation Type:	Loan Operation	Overall Stage:	Cerrado (Todos los préstamos están cerrados)
Lending Instrument:	Investment Loan	Country:	BRAZIL
Borrower:	PREFEITURA MUNICIPAL DE PONTA GROSSA	Convergence related Operation(s):	

### Total Cost and Source

	Original IDB	Current Active IDB	Local Counterpart	Co-Financing/Country	Total operation cost - Original Estimate
BR-L1099	\$7,500,000.00	\$7,500,000.00	\$7,500,000.00	\$0.00	\$15,000,000.00

### Available Funds (US\$)

	Current IDB	Disb. Amount to Date	% Disbursed	Undisbursed Balance
BR-L1099	\$7,500,000.00	\$7,500,000.00	100.00%	\$0.00


### Environmental and Social Safeguards

Main Operation	
Impacts Category:	B
Safeguard Performance Rating:	
Safeguard Performance Rating - Rationale:	

### Reformulation Information

Main Operation	
Was/Were the objective(s) of this operation reformulated?	NO
Date of approval:	

Expense Categories by Loan Contract (cumulative values)

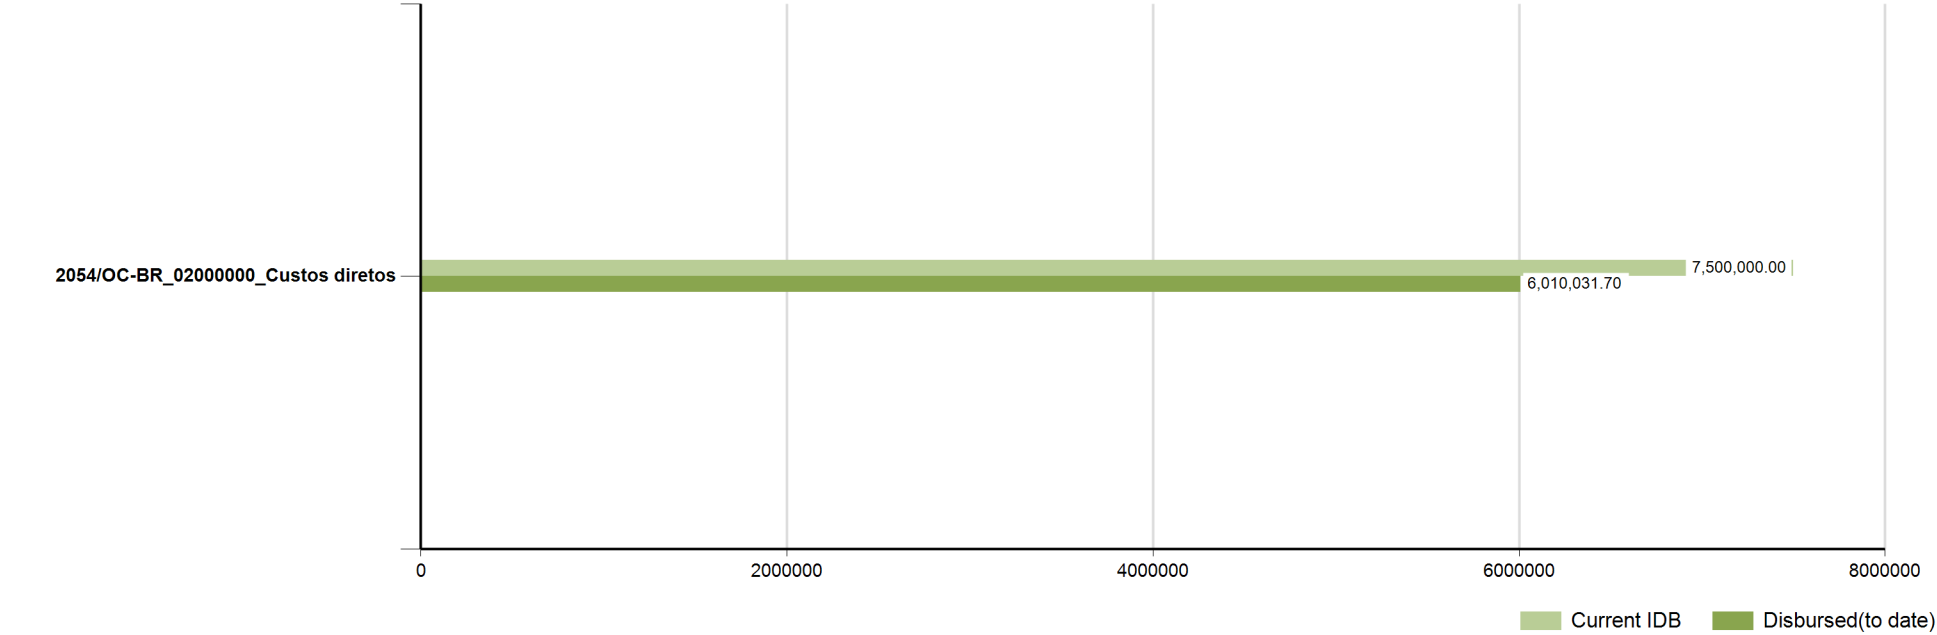

Results Matrix

Impacts

Impact:	1 Calidad de vida de la población del municipio de Ponta Grossa mejorada							
Observation:								
Indicators	Flags*	Unit of Measure	Baseline	Baseline Year	Means of verification	Observations	EOP	
1.1 Indice de Oferta de Servicios Publicos (IOSP) de Ponta Grossa		Valor indice IOSP	0.40	2005	Informe de Evaluacion Final del Programa	El IOSP ya no esta siendo medido por PARANACIDA DE por lo tanto durante el inicio de ejecucion del programa se propondra un indicador valido.	P	0.44
							P(a)	0.44
							A	

 RF - RF Indicator

 SI - Sector Indicator

 CI - Country Indicator

 PG - Pro-Gender

 PE - Pro-Ethnicity

Outcomes

Outcome:	1 Movilidad del municipio de Ponta Grossa mejorada							
Observation:								
Indicators	Flags*	Unit of Measure	Baseline	Baseline Year	Means of verification	Observations	EOP	
1.1 Tiempo de viaje de autobuses que circulan en los tramos pavimentados		Minutos/viaje	40.00	2007	Estudio de Speed Delay.		P	38.00
							P(a)	38.00
							A	30.08
Outcome:	2 Red de infraestructura escolar basica (tanto educación fundamental como educación infantil) mejorada							
Observation:								
Indicators	Flags*	Unit of Measure	Baseline	Baseline Year	Means of verification	Observations	EOP	
2.1 Alumnos de educación básica beneficiados con las mejoras de infraestructura escolar		Estudiantes	0.00	2007	Informes anuales de la Secretaría Municipal de Educación e Informe Final del Programa.		P	10,420.00
							P(a)	10,420.00
							A	7,477.00

2.2 Vagas de educação infantil		Estudiantes	3,285.00	2007	Informes anuales de la Secretaría Municipal de Educación e Informe Final del Programa.		P	3,876.00
							P(a)	3,876.00
							A	7,021.00
Outcome:	3 Eficiencia de la gestión municipal de Ponta Grossa mejorada							
Observation:								
Indicators	Flags*	Unit of Measure	Baseline	Baseline Year	Means of verification	Observations	EOP	
3.1 Tiempo medio de los procesos de licitación de la Prefeitura		Dias	65.00	2007	Informe de la Secretaría Municipal de Finanzas e Informe Final del Programa.		P	45.00
							P(a)	45.00
							A	30.00
3.2 Media de procesos de licitación de la Prefeitura realizados por año		Procesos por año	840.00	2007	Informe de la Secretaría Municipal de Finanzas e Informe Final del Programa.		P	798.00
							P(a)	798.00
							A	449.00

## Outputs: Annual Physical and Financial Progress

Educación		Physical Progress			Financial Progress		
Outputs	Unit of Measure	2013		EOP	2013		EOP
Escuelas de educación básica remodeladas	Escuela	P	0.00	26.00	P	0.00	5,330,000.00
		P(a)	0.00	26.00	P(a)	0.00	6,123,904.00
		A	0.00	26.00	A	793,904.00	6,123,904.00
Centros de Educación Infantil (CEMEIs) remodelados	Escuela	P	0.00	5.00	P	0.00	1,065,000.00
		P(a)	0.00	5.00	P(a)	0.00	2,741,614.00
		A	0.00	5.00	A	1,676,614.00	2,741,614.00
Movilidad y Transporte		Physical Progress			Financial Progress		
Outputs	Unit of Measure	2013		EOP	2013		EOP
Vías en barrios de bajos ingresos pavimentadas	kilometer	P	13.00	36.00	P	2,133,000.00	7,613,000.00
		P(a)	3.90	23.76	P(a)	2,133,000.00	10,162,349.00
		A	15.26	23.76	A	5,962,349.00	10,162,349.00
Fortalecimiento Institucional		Physical Progress			Financial Progress		
Outputs	Unit of Measure	2013		EOP	2013		EOP
Consultoría de revisión y racionalización de procesos y procedimientos de la PMPG realizada	relatorio	P	0.00	0.00	P	0.00	0.00
		P(a)	0.00	1.00	P(a)	0.00	0.00
		A	1.00	1.00	A	0.00	0.00
Equipos de computación para a unidad ejecutora adquiridos	equipamentos	P	0.00	0.00	P	0.00	0.00
		P(a)	0.00	1.00	P(a)	0.00	50,000.00
		A	1.00	1.00	A	50,000.00	50,000.00
Plan de Acción para la Modernización del Catastro Inmobiliario elaborado	Plan	P	0.00	1.00	P	0.00	210,000.00
		P(a)	0.00	1.00	P(a)	0.00	0.00
		A		1.00	A	0.00	0.00
Plan de capacitación desarrollado	Plan	P	0.00	1.00	P	0.00	0.00
		P(a)	0.00	1.00	P(a)	0.00	0.00
		A		1.00	A	0.00	0.00
Otros							

Other Cost		2013	Cost
Administración del programa	P	\$100,000.00	\$254,000.00
	P(a)	\$100,000.00	\$114,000.00
	A	\$114,000.00	\$114,000.00
Total Cost		2013	Total Cost
	P	\$2,233,000.00	\$14,472,000.00
	P(a)	\$2,233,000.00	\$12,828,000.00
	A	\$8,596,867.00	\$19,191,867.00

## Changes to the Matrix

No information related to this operation.

Please note that the Overall Stage represents the stage of the operation at the time of this report's publication, which might not necessarily match the stage of the operation during the PMR Cycle to which the report pertains.
