



Operation Number: **BR-L1057**  
Year- PMR Cycle: **Segundo período enero-diciembre 2013**  
Last Update: **6/25/2014**  
PMR Validation Stage: **Validada por el Representante de País**

Chief of Operations validation date: **06/27/2014**  
Division Chief validation date: **06/30/2014**  
Country Representative validation date: **07/06/2014**

Inter-American Development Bank - IDB  
Office of Strategic Planning and Development Effectiveness

## Operation Profile

### Basic Data

Operation name:	PROCIDADES - Programa de Desarrollo Urbano e Inclusión Social de Vitoria	Loan Number:	1986/OC-BR
Executing Agency (EA):	Prefeitura Municipal de Vitoria		
Team Leader:	Curvelo,Aderbal Jose	Sector/Subsector:	NEIGHBORHOOD UPGRADING
Operation Type:	Loan Operation	Overall Stage:	Desembolso (De la elegibilidad hasta que todos los préstamos están cerrados).
Lending Instrument:	Investment Loan	Country:	BRAZIL
Borrower:	Prefeitura Municipal de Vitoria	Convergence related Operation(s):	

### Total Cost and Source

	Original IDB	Current Active IDB	Local Counterpart	Co-Financing/Country	Total operation cost - Original Estimate
BR-L1057	\$39,100,000.00	\$39,100,000.00	\$26,100,000.00	\$0.00	\$65,200,000.00

### Available Funds (US\$)

	Current IDB	Disb. Amount to Date	% Disbursed	Undisbursed Balance
BR-L1057	\$39,100,000.00	\$32,455,645.87	83.01%	\$6,644,354.13


### Environmental and Social Safeguards

Main Operation	
Impacts Category:	B(R)
Safeguard Performance Rating:	
Safeguard Performance Rating - Rationale:	

### Reformulation Information

Main Operation	
Was/Were the objective(s) of this operation reformulated?	NO
Date of approval:	

Expense Categories by Loan Contract (cumulative values)

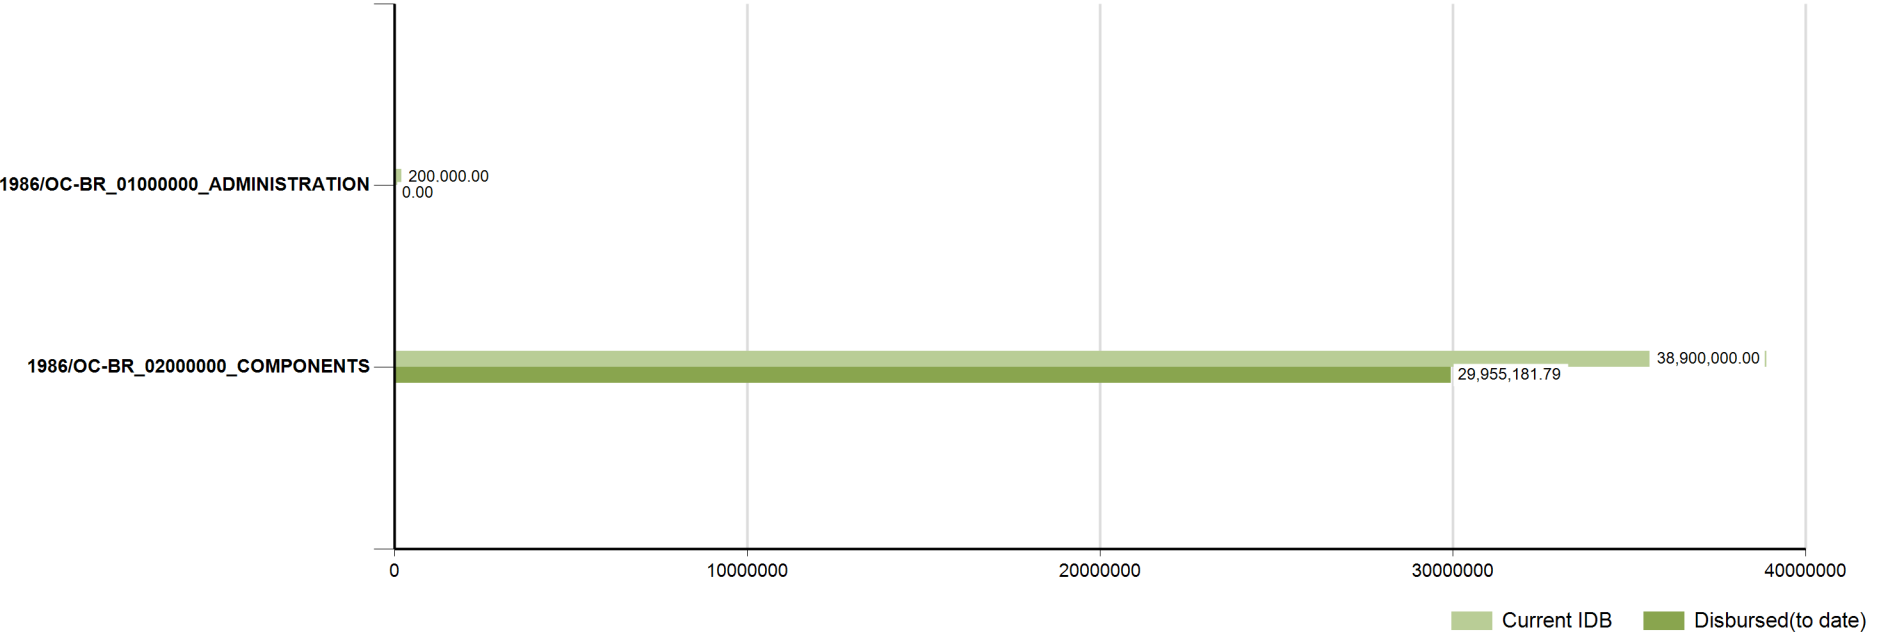

Results Matrix

Impacts

Impact:	1 Satisfação dos moradores com as melhorias realizadas pelo projeto Terra Mais Igual incrementada								
Observation:	Esse item somente será aferido ao final das intervenções.								
Indicators		Flags*	Unit of Measure	Baseline	Baseline Year	Means of verification	Observations	EOP	
1.0 Satisfação dos moradores com as melhorias realizadas pelo projeto Terra Mais Igual incrementada			%	0.00	2014			P	
								P(a)	0.00
								A	
Impact:	2 Valorização imobiliária na área de intervenção da ação de drenagem urbana aumentada								
Observation:	Esse item somente será aferido ao final das intervenções.								
Indicators		Flags*	Unit of Measure	Baseline	Baseline Year	Means of verification	Observations	EOP	
2.0 Valorização imobiliária na área de intervenção da ação de drenagem urbana aumentada			RS/m2	0.00	2014			P	
								P(a)	0.00
								A	

 RF - RF Indicator     SI - Sector Indicator     CI - Country Indicator     PG - Pro-Gender     PE - Pro-Ethnicity

Outcomes

Outcome:	2 Infraestrutura urbana y las condiciones ambientales del municipio mejorada y el acceso de su población a servicios sociales básicos ampliados.												
Observation:													
Indicators	Flags*	Unit of Measure	Baseline	Baseline Year	Means of verification	Observations	2009	2010	2011	2012	2013	EOP	
2.1 Domicílios interligados ao sistema de abastecimento de água e com atendimento regular aumentado		domicílio	453.00	2006	Levantamento de campo da Secretaria de Obras		P	613.00	1,186.00	1,532.00	3,260.00	115.00	6,706.00
							P(a)	613.00	1,186.00	1,532.00	3,260.00	115.00	6,706.00
							A	613.00	1,186.00	1,532.00			
2.2 Domicílios interligados ao sistema de esgoto aumentado		domicilio	425.00	2006	Levantamento de campo da Secretaria de Obras		P	737.00	1,467.00	1,090.00	3,070.00		6,364.00
							P(a)	737.00	1,467.00	1,090.00	3,070.00		6,364.00
							A	737.00	1,467.00	1,090.00			
2.2 Tempo de percurso entre a moradia e o ponto de ônibus (via 2 ligando os morros de Romão ao Forte de São João) reduzido		Minutos	25.00	2006	Levantamento de campo da Secretaria de Obras	Esse item somente será aferido ao término das intervenções na poligonal.	P						1.00
							P(a)						1.00
							A						

2.3 Restauração e melhoria de Imóveis de interesse histórico-cultural no entorno imediato da Praça Costa Pereira incrementado		Unidade	3.00	2006	Esse item somente será aferido ao final do Programa	Esse item somente será aferido ao final do Programa	P						0.00
							P(a)						3.00
							A						
2.4 Área inundável na área de intervenção reduzida		metro	100.00	2006	Levantamento realizado pela Secretaria de Obras	metro quadrado	P	80.00	60.00	10.00			10.00
							P(a)	80.00	60.00	10.00			10.00
							A	80.00	60.00	10.00			
2.6 Satisfação dos moradores na área de intervenção incrementada		%	0.00	2006	Levantamento de campo da Secretaria de Obras		P						0.00
							P(a)						0.00
							A						
2.7 Tempo médio de licenciamento ambiental reduzido		Dias	60.00	2011	Levantamento realizado pela Secretaria de Obras		P						2.00
							P(a)						2.00
							A						

Outputs: Annual Physical and Financial Progress

Apoyo al proyecto ¿Terra Mais Igual¿		Physical Progress			Financial Progress		
Outputs	Unit of Measure		2013	EOP		2013	EOP
Obra do Projeto Terra realizada	obra	P		0.00	P		16,610,573.00
		P(a)		0.00	P(a)		16,610,573.00
		A		0.00	A		16,610,573.00
Programa Gerenciamento Social Projeto Terra implementado	programa	P			P		1,234,360.56
		P(a)		0.00	P(a)		1,234,360.56
		A			A		1,234,360.56
1.1 Extensão de rede de abastecimento de água implantada	Metro	P	5,500.00	20,524.00	P	820,000.00	2,511,000.00
		P(a)	5,500.00	38,779.00	P(a)	820,000.00	4,748,000.00
		A	21,399.00	30,225.00	A	2,338,000.00	3,392,000.00
1.2 Extensão de rede de esgoto implantada	Metro	P	4,000.00	14,784.00	P	512,000.00	1,328,000.00
		P(a)	4,000.00	41,399.00	P(a)	512,000.00	6,829,000.00
		A	29,744.00	35,105.00	A	5,811,000.00	6,122,000.00
1.3 Domicílios construídos ou recuperados	Domicílio	P	80.00	392.00	P	1,449,000.00	9,036,000.00
		P(a)	80.00	411.00	P(a)	1,449,000.00	9,035,000.00
		A	16.00	303.00	A		6,966,000.00
1.4 Pontos de contenção implantados	Ponto	P	1.00	18.00	P	30,000.00	218,000.00
		P(a)	1.00	7.00	P(a)	30,000.00	2,332,000.00
		A		6.00	A	2,114,000.00	2,232,000.00
1.5 Extensão da pavimentação / rede de drenagem implantada	Metro	P	4,233.00	14,780.00	P	1,808,000.00	5,297,000.00
		P(a)	4,233.00	52,288.00	P(a)	1,808,000.00	22,542,000.00
		A	38,993.00	47,726.00	A	18,739,000.00	21,453,000.00
1.6 Equipamentos públicos construídos	Equipamento	P	2.00	8.00	P	706,000.00	1,009,000.00
		P(a)	2.00	5.00	P(a)	706,000.00	1,012,000.00
		A		1.00	A	3.00	3.00
1.7 Gerenciamento Social implantado	Gerenciamento	P	0.00	0.00	P		
		P(a)	0.00	1.00	P(a)		2,341,540.07
		A	1.00	1.00	A	2,341,540.07	2,341,540.07
Recalificación del centro		Physical Progress			Financial Progress		
Outputs	Unit of Measure		2013	EOP		2013	EOP
2.1 - Obra de recalificación del centro realizada - Praça Costa Pereira	Obra	P		1.00	P		498,450.00
		P(a)		1.00	P(a)		529,411.76
		A		1.00	A		498,450.00
Drenaje Urbano		Physical Progress			Financial Progress		
Outputs	Unit of Measure		2013	EOP		2013	EOP
3.1 - Obra de drenaje urbana realizada - Bacia de Bairro República	Obra	P		1.00	P		21,052,800.00
		P(a)		1.00	P(a)		21,052,800.00
		A		1.00	A		21,052,800.00
Fortalecimiento Institucional		Physical Progress			Financial Progress		
Outputs	Unit of Measure		2013	EOP		2013	EOP
4.1 Sistema Integrado de Licenciamento Ambiental desenvolvido.	Sistema	P	1.00	1.00	P	300,000.00	300,000.00
		P(a)	1.00	1.00	P(a)	300,000.00	400,000.00
		A			A		
4.2 Participações em capacitações em monitoramento e fiscalização ambiental	Capacitação	P	75.00	150.00	P	50,000.00	100,000.00
		P(a)	75.00	150.00	P(a)	50,000.00	150,000.00
		A			A		

4.3 Equipamentos adquiridos	Equipamento	P	28.00	56.00	P	50,000.00	100,000.00
		P(a)	28.00	56.00	P(a)	50,000.00	150,000.00
		A			A		
4.4 Estudos e consultorias realizados	Estudo	P		1.00	P	900,000.00	2,747,000.00
		P(a)		1.00	P(a)	900,000.00	2,747,000.00
		A			A		
4.5 Plano Diretor de Drenagem Urbana realizado	Plano	P	1.00	1.00	P	1,353,000.00	1,353,000.00
		P(a)	1.00	1.00	P(a)	1,353,000.00	1,353,000.00
		A	1.00	1.00	A		
Administracion del programa							
others							

Other Cost		2013	Cost
avaliacao e monitoramento	P	\$250,000.00	\$549,812.00
	P(a)	\$250,000.00	\$550,000.00
	A		\$31,812.00
Servicos Tecnicos especializados - Auditoria	P	\$50,000.00	\$200,000.00
	P(a)	\$50,000.00	\$200,000.00
	A		\$0.00
supervisao de obras	P		\$684,920.00
	P(a)		\$685,294.12
	A	\$374.12	\$685,294.12
Unidade Gerenciadora	P	\$190,000.00	\$465,000.00
	P(a)	\$190,000.00	\$465,000.00
	A		\$0.00
others - comissão de crédito	P	\$80,000.00	\$239,926.58
	P(a)	\$80,000.00	\$240,000.00
	A		\$97,926.58
Total Cost		2013	Total Cost
	P	\$8,548,000.00	\$65,534,842.14
	P(a)	\$8,548,000.00	\$95,206,979.51
	A	\$31,343,917.19	\$82,717,759.33

## Changes to the Matrix

No information related to this operation.

Please note that the Overall Stage represents the stage of the operation at the time of this report's publication, which might not necessarily match the stage of the operation during the PMR Cycle to which the report pertains.
