

[illegible]

Project Execution Plan (PEP) - Improving Transport Logistics and Competitiveness un Suriname Project SU-L1057

ID	WBS	Prod/ Req	Components / Products / Activities	Duration	Start	Finish	TOTAL USD	Responsable	ly	B	M	E	April	B	M	E	January	B	M	E	October	B	M	E	July	B	April	M	E	January	B	M	E	October	B	July	M	E	April	B	
38	1.1.1.2.12		Elaboration of the contract draft	3 days	Wed 2/12/20	Fri 4/12/20	\$0.00	PS																																	
39	1.1.1.2.13		Contract Subscription	15 days	Mon 7/12/20	Fri 25/12/20	\$0.00	PSPWTC;HF																																	
40	1.1.1.2.14		Signed contract	0 days	Fri 25/12/20	Fri 25/12/20	\$0.00																																		
41	1.1.1.2.15		Remission to the Bank a copy of the contract and requests the contract code	1 day	Mon 28/12/20	Mon 28/12/20	\$0.00	PS																																	
42	1.1.1.3		Execution of the contract	264 days	Tue 29/12/20	Fri 31/12/21	\$537,537.00																																		
43	1.1.1.3.1		Urbanization of the Logistics Center	264 days	Tue 29/12/20	Fri 31/12/21	\$537,537.00	HF																																	
44	1.1.2	PRM-A # 3.3	Define requirements of experience and capacity of companies for the execution of works	132 days	Thu 25/6/20	Fri 25/12/20	\$0.00	TC-P																																	
45	1.1.3	PRM-A # 4.2	Implement an adequate penalty fee mechanism in the supervision contract	396 days	Thu 25/6/20	Thu 30/12/21	\$0.00	TC-P																																	
46	1.1.4		ICB_1. Design and Construction of the Logistics Center's Building	264 days	Tue 29/12/20	Fri 31/12/21	\$1,461,889.00																																		
47	1.1.4.1		Execution of the contract	264 days	Tue 29/12/20	Fri 31/12/21	\$1,461,889.00																																		
48	1.1.4.1.1		Elaborating of the designs	66 days	Tue 29/12/20	Tue 30/3/21	\$58,476.00	HF																																	
49	1.1.4.1.2		Works for construction of the Logistics Center	198 days	Wed 31/3/21	Fri 31/12/21	\$1,403,413.00	HF																																	
50	1.1.5		CQS_5. Supervision of Construction of the Logistics Center	428 days	Thu 11/6/20	Mon 31/1/22	\$49,986.00																																		
51	1.1.5.1		Expression of Interest	44 days	Thu 11/6/20	Tue 11/8/20	\$0.00																																		
52	1.1.5.1.1		Preparation of the Expression of Interest announcement	5 days	Thu 11/6/20	Wed 17/6/20	\$0.00	PS																																	
53	1.1.5.1.2		Publication of the Expression of Interest announcement (minimum 14 running days)	10 days	Thu 18/6/20	Wed 1/7/20	\$0.00	PS																																	
54	1.1.5.1.3		Present Expression of Interest	1 day	Thu 2/7/20	Thu 2/7/20	\$0.00	PF																																	
55	1.1.5.1.4		Selection of short list	5 days	Fri 3/7/20	Thu 9/7/20	\$0.00	PS																																	
56	1.1.5.1.5		Preparation of the RP proposal request that includes the draft contract	38 days	Thu 11/6/20	Mon 3/8/20	\$0.00	PS																																	
57	1.1.5.1.6		Request Non Objection from the Bank of the short list and RP	1 day	Tue 4/8/20	Tue 4/8/20	\$0.00	PD																																	
58	1.1.5.1.7		Issuance Non Objection of short list and RP	5 days	Wed 5/8/20	Tue 11/8/20	\$0.00	IDB																																	
59	1.1.5.1.8		Conformed short list and Request for Proposal with NO	0 days	Tue 11/8/20	Tue 11/8/20	\$0.00																																		
60	1.1.5.2		Hiring Process	77 days	Wed 12/8/20	Thu 26/11/20	\$0.00																																		
61	1.1.5.2.1		Publication of the process in the media (UNDB; Executing Agency Web pages, etc)	3 days	Wed 12/8/20	Fri 14/8/20	\$0.00	PS																																	
62	1.1.5.2.2		Forward the request for proposals from short list companies	1 day	Mon 17/8/20	Mon 17/8/20	\$0.00	PS																																	
63	1.1.5.2.3		Period for preparing technical and economic proposals	22 days	Tue 18/8/20	Wed 16/9/20	\$0.00	PS																																	
64	1.1.5.2.4		Addendum to the publication deadline	10 days	Thu 17/9/20	Wed 30/9/20	\$0.00	PF																																	
65	1.1.5.2.5		Evaluation of technical and the economical proposals (combined evaluation)	22 days	Thu 1/10/20	Fri 30/10/20	\$0.00	EC																																	
66	1.1.5.2.6		Negociation of contract and finalization of the contract text	10 days	Mon 2/11/20	Fri 13/11/20	\$0.00	PD;PS;PF																																	
67	1.1.5.2.7		Request of Non Objection from the Bank to the combined evaluation and the negotiated contract	1 day	Mon 16/11/20	Mon 16/11/20	\$0.00	PD																																	

[illegible]

Project Execution Plan (PEP) – Improving Transport Logistics and Competitiveness un Suriname Project SU-L1057																											
ID	WBS	Prod/ Req	Components / Products / Activities	Duration	Start	Finish	TOTAL USD	Responsible	ly	B	M	E	B	January	October	July	April	January	October	July	April	January	October	July	April		
103	1.2.2		Access control system equipped and installed	0 days	Fri 29/4/22	Fri 29/4/22	\$0.00																				
104	1.2.3		Rounding amount	1 day	Fri 29/4/22	Fri 29/4/22	\$3,000.00																				
105	1.3	P3	Product 3: Port Community System implemented	672 days	Fri 13/3/20	Mon 10/10/22	\$2,200,000.00																				
106	1.3.1		QCBS_6. Contracting of Firm for the Implementation of a Port Community System software, set up and supply materials	672 days	Fri 13/3/20	Mon 10/10/22	\$2,200,000.00																				
107	1.3.1.1		Expression of Interest	44 days	Fri 13/3/20	Wed 13/5/20	\$0.00																				
108	1.3.1.1.1		Preparation of the Expression of Interest announcement	5 days	Fri 13/3/20	Thu 19/3/20	\$0.00	PS																			
109	1.3.1.1.2		Publication of the Expression of Interest announcement (minimum 14 running days)	10 days	Fri 20/3/20	Thu 2/4/20	\$0.00	PS																			
110	1.3.1.1.3		Present Expression of Interest	1 day	Fri 3/4/20	Fri 3/4/20	\$0.00	PF																			
111	1.3.1.1.4		Selection of short list	5 days	Mon 6/4/20	Fri 10/4/20	\$0.00	PS																			
112	1.3.1.1.5		Preparation of the RP proposal request that includes the draft contract	38 days	Fri 13/3/20	Tue 5/5/20	\$0.00	PS																			
113	1.3.1.1.6		Request Non Objection from the Bank of the short list and RP	1 day	Wed 6/5/20	Wed 6/5/20	\$0.00	PD																			
114	1.3.1.1.7		Issuance Non Objection of short list and RP	5 days	Thu 7/5/20	Wed 13/5/20	\$0.00	IDB																			
115	1.3.1.1.8		Conformed short list and Request for Proposal with NO	0 days	Wed 13/5/20	Wed 13/5/20	\$0.00																				
116	1.3.1.2		Hiring Process	100 days	Thu 14/5/20	Wed 30/9/20	\$0.00																				
117	1.3.1.2.1		Publication of the process in the media (UNDB; Executing Agency Web pages, etc)	3 days	Thu 14/5/20	Mon 18/5/20	\$0.00	PS																			
118	1.3.1.2.2		Forward the request for proposals from short list companies	1 day	Tue 19/5/20	Tue 19/5/20	\$0.00	PS																			
119	1.3.1.2.3		Period for preparing technical and economic proposals	22 days	Wed 20/5/20	Thu 18/6/20	\$0.00	PS																			
120	1.3.1.2.4		Addendum to the publication deadline	10 days	Fri 19/6/20	Thu 2/7/20	\$0.00																				
121	1.3.1.2.5		Evaluation of technical proposals	22 days	Fri 3/7/20	Mon 3/8/20	\$0.00	EC																			
122	1.3.1.2.6		Request Non Objection from the Bank to the evaluation of technical proposals	1 day	Tue 4/8/20	Tue 4/8/20	\$0.00	PD																			
123	1.3.1.2.7		Issuance of Non Objection from the Bank	5 days	Wed 5/8/20	Tue 11/8/20	\$0.00	IDB																			
124	1.3.1.2.8		Notification of results, technical evaluation, call for the opening act	1 day	Wed 12/8/20	Wed 12/8/20	\$0.00	PS																			
125	1.3.1.2.9		Opening act of Economical Offers	1 day	Thu 13/8/20	Thu 13/8/20	\$0.00	PS																			
126	1.3.1.2.10		Combined Evaluation	10 days	Fri 14/8/20	Thu 27/8/20	\$0.00	EC																			
127	1.3.1.2.11		Negotiation of contract and finalization of the contract text	10 days	Fri 28/8/20	Thu 10/9/20	\$0.00	PD;PS;PF																			
128	1.3.1.2.12		Request of Non Objection from the Bank to the combined evaluation and the negotiated contract	1 day	Fri 11/9/20	Fri 11/9/20	\$0.00	PD																			
129	1.3.1.2.13		Issuance NO to the combined evaluation for the draft of the contract	5 days	Mon 14/9/20	Fri 18/9/20	\$0.00	IDB																			
130	1.3.1.2.14		Preparation of the Award Resolution	2 days	Fri 11/9/20	Mon 14/9/20	\$0.00	PS																			
131	1.3.1.2.15		Issuance of the Award Resolution	1 day	Tue 15/9/20	Tue 15/9/20	\$0.00	PSPWTC																			
Página 4																											

Project Execution Plan (PEP) – Improving Transport Logistics and Competitiveness un Suriname Project SU-L1057																																			
ID	WBS	Prod/ Req	Components / Products / Activities	Duration	Start	Finish	TOTAL USD	Responsible	ly	B	M	E	B	M	E	October	B	M	E	B	April	M	E	B	January	B	M	E	B	July	M	E	B	April	
132	1.3.1.2.16		Subscribe the contract	10 days	Wed 16/9/20	Tue 29/9/20	\$0.00	PSPWTC;HF																											
133	1.3.1.2.17		Remission to the Bank a copy of the contract and requests the contract code	1 day	Wed 30/9/20	Wed 30/9/20	\$0.00	PS																											
134	1.3.1.3		Execution of the contract	528 days	Thu 1/10/20	Mon 10/10/22	\$2,200,000.00																												
135	1.3.1.3.1		Execution of the contract	528 days	Thu 1/10/20	Mon 10/10/22	\$2,200,000.00	HF																											
136	1.3.2		Port Community System implemented	0 days	Mon 10/10/22	Mon 10/10/22	\$0.00																												
137	2		Component 2: Road interventions	828 days	Tue 15/9/20	Thu 16/11/23	\$36,200,000.00																												
138	2.1	P4	Product 4: Primary urban roads rehabilitated	828 days	Tue 15/9/20	Thu 16/11/23	\$26,600,000.00																												
139	2.1.1		QCBS_7. Contracting of Firm for elaborating the Executive Project for the rehabilitation of de roads	276 days	Tue 15/9/20	Tue 5/10/21	\$2,350,384.00																												
140	2.1.1.1		Expression of Interest	44 days	Tue 15/9/20	Fri 13/11/20	\$0.00																												
141	2.1.1.1.1		Preparation of the Expression of Interest announcement	5 days	Tue 15/9/20	Mon 21/9/20	\$0.00	PS																											
142	2.1.1.1.2		Publication of the Expression of Interest announcement (minimum 14 running days)	10 days	Tue 22/9/20	Mon 5/10/20	\$0.00	PS																											
143	2.1.1.1.3		Present Expression of Interest	1 day	Tue 6/10/20	Tue 6/10/20	\$0.00	PF																											
144	2.1.1.1.4		Selection of short list	5 days	Wed 7/10/20	Tue 13/10/20	\$0.00	PS																											
145	2.1.1.1.5		Preparation of the RP proposal request that includes the draft contract	38 days	Tue 15/9/20	Thu 5/11/20	\$0.00	PS																											
146	2.1.1.1.6		Request Non Objection from the Bank of the short list and RP	1 day	Fri 6/11/20	Fri 6/11/20	\$0.00	PD																											
147	2.1.1.1.7		Issuance Non Objection of short list and RP	5 days	Mon 9/11/20	Fri 13/11/20	\$0.00	IDB																											
148	2.1.1.1.8		Conformed short list and Request for Proposal with NO	0 days	Fri 13/11/20	Fri 13/11/20	\$0.00																												
149	2.1.1.2		Hiring Process	100 days	Mon 16/11/20	Fri 2/4/21	\$0.00																												
150	2.1.1.2.1		Publication of the process in the media (UNDB; Executing Agency Web pages, etc)	3 days	Mon 16/11/20	Wed 18/11/20	\$0.00	PS																											
151	2.1.1.2.2		Forward the request for proposals from short list companies	1 day	Thu 19/11/20	Thu 19/11/20	\$0.00	PS																											
152	2.1.1.2.3		Period for preparing technical and economic proposals	22 days	Fri 20/11/20	Mon 21/12/20	\$0.00	PS																											
153	2.1.1.2.4		Addendum to the publication deadline	10 days	Tue 22/12/20	Mon 4/1/21	\$0.00																												
154	2.1.1.2.5		Evaluation of technical proposals	22 days	Tue 5/1/21	Wed 3/2/21	\$0.00	EC																											
155	2.1.1.2.6		Request Non Objection from the Bank to the evaluation of technical proposals	1 day	Thu 4/2/21	Thu 4/2/21	\$0.00	PD																											
156	2.1.1.2.7		Issuance of Non Objection from the Bank	5 days	Fri 5/2/21	Thu 11/2/21	\$0.00	IDB																											
157	2.1.1.2.8		Notification of results, technical evaluation, call for the opening act	1 day	Fri 12/2/21	Fri 12/2/21	\$0.00	PS																											
158	2.1.1.2.9		Opening act of Economical Offers	1 day	Mon 15/2/21	Mon 15/2/21	\$0.00	PS																											
159	2.1.1.2.10		Combined Evaluation	10 days	Tue 16/2/21	Mon 1/3/21	\$0.00	EC																											
160	2.1.1.2.11		Negotiation of contract and finalization of the contract text	10 days	Tue 2/3/21	Mon 15/3/21	\$0.00	PD;PS;PF																											
161	2.1.1.2.12		Request of Non Objection from the Bank to the combined evaluation and the negotiated contract	1 day	Tue 16/3/21	Tue 16/3/21	\$0.00	PD																											
Página 5																																			

Project Execution Plan (PEP) - Improving Transport Logistics and Competitiveness un Suriname Project SU-L1057																									
ID	WBS	Prod/ Req	Components / Products / Activities	Duration	Start	Finish	TOTAL USD	Responsible	ly	B	M	E	B	M	E	B	M	E	B	M	E	B	M	E	B
162	2.1.1.2.13		Issuance NO to the combined evaluation for the draft of the contract	5 days	Wed 17/3/21	Tue 23/3/21	\$0.00	IDB																	
163	2.1.1.2.14		Preparation of the Award Resolution	2 days	Tue 16/3/21	Wed 17/3/21	\$0.00	PS																	
164	2.1.1.2.15		Issuance of the Award Resolution	1 day	Thu 18/3/21	Thu 18/3/21	\$0.00	PSPWTC																	
165	2.1.1.2.16		Subscribe the contract	10 days	Fri 19/3/21	Thu 1/4/21	\$0.00	PSPWTC;HF																	
166	2.1.1.2.17		Remission to the Bank a copy of the contract and requests the contract code	1 day	Fri 2/4/21	Fri 2/4/21	\$0.00	PS																	
167	2.1.1.3		Execution of the contract	132 days	Mon 5/4/21	Tue 5/10/21	\$2,350,384.00																		
168	2.1.1.3.1		Execution of the contract	132 days	Mon 5/4/21	Tue 5/10/21	\$2,350,384.00	HF																	
169	2.1.1.4		a) Designs approved by Project Executing Unit	0 days	Tue 5/10/21	Tue 5/10/21	\$0.00																		
170	2.1.2	PRM-A # 2.2	Implementation of a traffic management plan, construction management plan (including areas for heavy equipment, noise and dust control, etc.) and pedestrian circulation in construction sites	805 days	Tue 15/9/20	Mon 16/10/23	\$0.00	ESS																	
171	2.1.3	PRM-A # 3.2	Close and timely coordination with utility companies	805 days	Tue 15/9/20	Mon 16/10/23	\$0.00	TC-R																	
172	2.1.4	PRM-A # 3.3	Define requirements of experience and capacity of companies for the execution of works	132 days	Wed 6/10/21	Thu 7/4/22	\$0.00	TC-R																	
173	2.1.5	PRM-A # 4.2	Implement an adequate penalty fee mechanism in the supervision contract	529 days	Wed 6/10/21	Mon 16/10/23	\$0.00	TC-R																	
174	2.1.6		Road rehabilitation and additional lanes construction	529 days	Wed 6/10/21	Mon 16/10/23	\$15,047,615.00																		
175	2.1.6.1		ICB_2. Construction and/or rehabilitation of roads and additional lanes	529 days	Wed 6/10/21	Mon 16/10/23	\$15,047,615.00																		
176	2.1.6.1.1		Previous Stage	33 days	Wed 6/10/21	Fri 19/11/21	\$0.00																		
177	2.1.6.1.1.1		Review and final adjustments to executive designs	25 days	Wed 6/10/21	Tue 9/11/21	\$0.00	TC-R																	
178	2.1.6.1.1.2		Validation of tender documents prepared by the design firm	2 days	Wed 10/11/21	Thu 11/11/21	\$0.00	PD																	
179	2.1.6.1.1.3		Request of Non Objection from the Bank to the tender documents	1 day	Fri 12/11/21	Fri 12/11/21	\$0.00	PD																	
180	2.1.6.1.1.4		Issuance of Non Objection to the tender documents or comments, communicatin the PEU	5 days	Mon 15/11/21	Fri 19/11/21	\$0.00	IDB																	
181	2.1.6.1.1.5		Tender Documents with Non Objection	0 days	Fri 19/11/21	Fri 19/11/21	\$0.00																		
182	2.1.6.1.2		Hiring Process	100 days	Mon 22/11/21	Fri 8/4/22	\$0.00																		
183	2.1.6.1.2.1		Management of publication of the call in the corresponding advertising media	1 day	Mon 22/11/21	Mon 22/11/21	\$0.00	PS																	
184	2.1.6.1.2.2		Period of preparation of proposals (minimum)	42 days	Tue 23/11/21	Wed 19/1/22	\$0.00	PF																	
185	2.1.6.1.2.3		Addendum to the publication deadline	12 days	Thu 20/1/22	Fri 4/2/22	\$0.00																		
186	2.1.6.1.2.4		Receipt of proposals	1 day	Mon 7/2/22	Mon 7/2/22	\$0.00	PS																	
187	2.1.6.1.2.5		Opening of proposals	0 days	Mon 7/2/22	Mon 7/2/22	\$0.00																		
188	2.1.6.1.2.6		Evaluation of proposals	15 days	Tue 8/2/22	Mon 28/2/22	\$0.00	EC																	
189	2.1.6.1.2.7		Request Non Objection from the Bank to the evaluation	1 day	Tue 1/3/22	Tue 1/3/22	\$0.00	PD																	
190	2.1.6.1.2.8		Issuance of Non Objection to the evaluation	5 days	Wed 2/3/22	Tue 8/3/22	\$0.00	IDB																	
191	2.1.6.1.2.9		Preparation of the Award Resolution	2 days	Wed 9/3/22	Thu 10/3/22	\$0.00	PS																	
192	2.1.6.1.2.10		Issuance of the Award Resolution	1 day	Fri 11/3/22	Fri 11/3/22	\$0.00	PSPWTC																	
193	2.1.6.1.2.11		Communication of the process results	1 day	Mon 14/3/22	Mon 14/3/22	\$0.00	PS																	

Project Execution Plan (PEP) - Improving Transport Logistics and Competitiveness un Suriname Project SU-L1057																						
ID	WBS	Prod/ Req	Components / Products / Activities	Duration	Start	Finish	TOTAL USD	Responsible	ly	B	M	E	B	M	E	B	M	E	B	M	E	B
194	2.1.6.1.2.12		Elaboration of the contract draft	3 days	Tue 15/3/22	Thu 17/3/22	\$0.00	PS														
195	2.1.6.1.2.13		Contract Subscription	15 days	Fri 18/3/22	Thu 7/4/22	\$0.00	PSPWTC;HF														
196	2.1.6.1.2.14		Signed contract	0 days	Thu 7/4/22	Thu 7/4/22	\$0.00															
197	2.1.6.1.2.15		Remission to the Bank a copy of the contract and re	1 day	Fri 8/4/22	Fri 8/4/22	\$0.00	PS														
198	2.1.6.1.3		Execution of the contract	396 days	Mon 11/4/22	Mon 16/10/23	\$15,047,615.00															
199	2.1.6.1.3.1		Execution of the contract	396 days	Mon 11/4/22	Mon 16/10/23	\$15,047,615.00	HF														
200	2.1.6.1.4		b) Primary roads widened and paved	0 days	Mon 16/10/23	Mon 16/10/23	\$0.00															
201	2.1.7		Installation of traffic lights and signaling	396 days	Mon 11/4/22	Mon 16/10/23	\$2,025,572.00															
202	2.1.7.1		ICB_2. Installation of traffic lights	396 days	Mon 11/4/22	Mon 16/10/23	\$2,025,572.00															
203	2.1.7.1.1		Execution of the contract	396 days	Mon 11/4/22	Mon 16/10/23	\$2,025,572.00	HF														
204	2.1.7.1.2		e) Intelligent Traffic System installed	0 days	Mon 16/10/23	Mon 16/10/23	\$0.00															
205	2.1.8		Drainage and street lighting	396 days	Mon 11/4/22	Mon 16/10/23	\$1,551,063.00															
206	2.1.8.1		ICB_2. Construction of drainage systems and instalation of street lighting	396 days	Mon 11/4/22	Mon 16/10/23	\$1,551,063.00															
207	2.1.8.1.1		Execution of the contract	396 days	Mon 11/4/22	Mon 16/10/23	\$1,551,063.00	HF														
208	2.1.8.1.2		c) Drainage systems with design considerations for climate change constructed	0 days	Mon 16/10/23	Mon 16/10/23	\$0.00															
209	2.1.9		Bikeline	396 days	Mon 11/4/22	Mon 16/10/23	\$2,023,951.00															
210	2.1.9.1		ICB_2. Construction and/or rehabilitation of pedestrians and bicycles paths	396 days	Mon 11/4/22	Mon 16/10/23	\$2,023,951.00															
211	2.1.9.1.1		Execution of the contract	396 days	Mon 11/4/22	Mon 16/10/23	\$2,023,951.00	HF														
212	2.1.9.1.2		d) Dedicated lanes for pedestrians and bikes constructed	0 days	Mon 16/10/23	Mon 16/10/23	\$0.00															
213	2.1.10		Minor induced works	396 days	Mon 11/4/22	Mon 16/10/23	\$2,550,998.00															
214	2.1.10.1		ICB_2. Minor works	396 days	Mon 11/4/22	Mon 16/10/23	\$2,550,998.00															
215	2.1.10.1.1		Execution of the contract	396 days	Mon 11/4/22	Mon 16/10/23	\$2,550,998.00	HF														
216	2.1.10.1.2		f) Signalization and road safety measures installed	0 days	Mon 16/10/23	Mon 16/10/23	\$0.00															
217	2.1.11		QCBS_8. Contracting of Firm for the Supervision of the rehabilitation of roads, lanes, drainage systems, pedestrians and bikes paths	650 days	Fri 21/5/21	Thu 16/11/23	\$579,980.00															
218	2.1.11.1		Expression of Interest	44 days	Fri 21/5/21	Wed 21/7/21	\$0.00															
219	2.1.11.1.1		Preparation of the Expression of Interest announcement	5 days	Fri 21/5/21	Thu 27/5/21	\$0.00	PS														
220	2.1.11.1.2		Publication of the Expression of Interest announcement (minimum 14 running days)	10 days	Fri 28/5/21	Thu 10/6/21	\$0.00	PS														
221	2.1.11.1.3		Present Expression of Interest	1 day	Fri 11/6/21	Fri 11/6/21	\$0.00	PF														
222	2.1.11.1.4		Selection of short list	5 days	Mon 14/6/21	Fri 18/6/21	\$0.00	PS														
223	2.1.11.1.5		Preparation of the RP proposal request that includes the draft contract	38 days	Fri 21/5/21	Tue 13/7/21	\$0.00	PS														
224	2.1.11.1.6		Request Non Objection from the Bank of the short list and RP	1 day	Wed 14/7/21	Wed 14/7/21	\$0.00	PD														
225	2.1.11.1.7		Issuance Non Objection of short list and RP	5 days	Thu 15/7/21	Wed 21/7/21	\$0.00	IDB														
226	2.1.11.1.8		Conformed short list and Request for Proposal with NO	0 days	Wed 21/7/21	Wed 21/7/21	\$0.00															
227	2.1.11.2		Hiring Process	100 days	Thu 22/7/21	Wed 8/12/21	\$0.00															

Project Execution Plan (PEP) – Improving Transport Logistics and Competitiveness un Suriname Project SU-L1057																									
ID	WBS	Prod/ Req	Components / Products / Activities	Duration	Start	Finish	TOTAL USD	Responsible	ly	B	M	E	B	M	E	B	M	E	B	M	E	B	M	E	B
228	2.1.11.2.1		Publication of the process in the media (UNDB; Executing Agency Web pages, etc)	3 days	Thu 22/7/21	Mon 26/7/21	\$0.00	PS																	
229	2.1.11.2.2		Forward the request for proposals from short list companies	1 day	Tue 27/7/21	Tue 27/7/21	\$0.00	PS																	
230	2.1.11.2.3		Period for preparing technical and economic proposals	22 days	Wed 28/7/21	Thu 26/8/21	\$0.00	PS																	
231	2.1.11.2.4		Addendum to the publication deadline	10 days	Fri 27/8/21	Thu 9/9/21	\$0.00																		
232	2.1.11.2.5		Evaluation of technical proposals	22 days	Fri 10/9/21	Mon 11/10/21	\$0.00	EC																	
233	2.1.11.2.6		Request Non Objection from the Bank to the evaluation of technical proposals	1 day	Tue 12/10/21	Tue 12/10/21	\$0.00	PD																	
234	2.1.11.2.7		Issuance of Non Objection from the Bank	5 days	Wed 13/10/21	Tue 19/10/21	\$0.00	IDB																	
235	2.1.11.2.8		Notification of results, technical evaluation, call for the opening act	1 day	Wed 20/10/21	Wed 20/10/21	\$0.00	PS																	
236	2.1.11.2.9		Opening act of Economical Offers	1 day	Thu 21/10/21	Thu 21/10/21	\$0.00	PS																	
237	2.1.11.2.10		Combined Evaluation	10 days	Fri 22/10/21	Thu 4/11/21	\$0.00	EC																	
238	2.1.11.2.11		Negotiation of contract and finalization of the contract text	10 days	Fri 5/11/21	Thu 18/11/21	\$0.00	PD;PS;PF																	
239	2.1.11.2.12		Request of Non Objection from the Bank to the combined evaluation and the negociated contract	1 day	Fri 19/11/21	Fri 19/11/21	\$0.00	PD																	
240	2.1.11.2.13		Issuance NO to the combined evaluation for the draft of the contract	5 days	Mon 22/11/21	Fri 26/11/21	\$0.00	IDB																	
241	2.1.11.2.14		Preparation of the Award Resolution	2 days	Fri 19/11/21	Mon 22/11/21	\$0.00	PS																	
242	2.1.11.2.15		Issuance of the Award Resolution	1 day	Tue 23/11/21	Tue 23/11/21	\$0.00	PSPWTC																	
243	2.1.11.2.16		Subscribe the contract	10 days	Wed 24/11/21	Tue 7/12/21	\$0.00	PSPWTC;HF																	
244	2.1.11.2.17		Remission to the Bank a copy of the contract and requests the contract code	1 day	Wed 8/12/21	Wed 8/12/21	\$0.00	PS																	
245	2.1.11.3		Execution of the contract	440 days	Fri 11/3/22	Thu 16/11/23	\$579,980.00																		
246	2.1.11.3.1		Execution of the contract	440 days	Fri 11/3/22	Thu 16/11/23	\$579,980.00	HF																	
247	2.1.12		Rounding amount	1 day	Thu 16/11/23	Thu 16/11/23	\$470,437.00																		
248	2.2	P5	Product 5: Bridge over Saramacca channel at Van’t Hogerhuysstraat built	684 days	Mon 5/4/21	Thu 16/11/23	\$9,600,000.00																		
249	2.2.1		QCBS_7. Contracting of Firm for elaborating the Executive Project for the Saramacca channel's bridge	661 days	Mon 5/4/21	Mon 16/10/23	\$730,454.00																		
250	2.2.1.1		Execution of the contract	132 days	Mon 5/4/21	Tue 5/10/21	\$730,454.00	HF																	
251	2.2.1.2	PRM-A # 3.3	Define requirements of experience and capacity of companies for the execution of works	132 days	Mon 5/4/21	Tue 5/10/21	\$0.00	TC-R																	
252	2.2.1.3	PRM-A # 4.2	Implement an adequate penalty fee mechanism in the supervision contract	264 days	Wed 12/10/22	Mon 16/10/23	\$0.00	TC-R																	
253	2.2.2		ICB_3. Construction of the bridge over the Saramacca channel	397 days	Fri 8/4/22	Mon 16/10/23	\$8,570,354.00																		
254	2.2.2.1		Previous Stage	33 days	Fri 8/4/22	Tue 24/5/22	\$0.00																		
255	2.2.2.1.1		Review and final adjustments to executive designs	25 days	Fri 8/4/22	Thu 12/5/22	\$0.00	TC																	
Página 8																									

[illegible]


Project Execution Plan (PEP) - Improving Transport Logistics and Competitiveness un Suriname Project SU-L1057

ID	WBS	Prod/ Req	Components / Products / Activities	Duration	Start	Finish	TOTAL USD	Responsible	ly	B	M	E	April	B	M	E	October	B	M	E	July	B	April	M	E	January	B	M	E	October	B	July	M	E	April	B
291	3.1.1.1.6		Request Non Objection from the Bank of the short list and RP	1 day	Fri 6/11/20	Fri 6/11/20	\$0.00	PD									PD																			
292	3.1.1.1.7		Issuance Non Objection of short list and RP	5 days	Mon 9/11/20	Fri 13/11/20	\$0.00	IDB									IDB																			
293	3.1.1.1.8		Conformed short list and Request for Proposal with NO	0 days	Fri 13/11/20	Fri 13/11/20	\$0.00										13/11																			
294	3.1.1.2		Hiring Process	100 days	Mon 16/11/20	Fri 2/4/21	\$0.00																													
295	3.1.1.2.1		Publication of the process in the media (UNDB; Executing Agency Web pages, etc)	3 days	Mon 16/11/20	Wed 18/11/20	\$0.00	PS									PS																			
296	3.1.1.2.2		Forward the request for proposals from short list companies	1 day	Thu 19/11/20	Thu 19/11/20	\$0.00	PS									PS																			
297	3.1.1.2.3		Period for preparing technical and economic proposals	22 days	Fri 20/11/20	Mon 21/12/20	\$0.00	PS									PS																			
298	3.1.1.2.4		Addendum to the publication deadline	10 days	Tue 22/12/20	Mon 4/1/21	\$0.00																													
299	3.1.1.2.5		Evaluation of technical proposals	22 days	Tue 5/1/21	Wed 3/2/21	\$0.00	EC									EC																			
300	3.1.1.2.6		Request Non Objection from the Bank to the evaluation of technical proposals	1 day	Thu 4/2/21	Thu 4/2/21	\$0.00	PD									PD																			
301	3.1.1.2.7		Issuance of Non Objection from the Bank	5 days	Fri 5/2/21	Thu 11/2/21	\$0.00	IDB									IDB																			
302	3.1.1.2.8		Notification of results, technical evaluation, call for the opening act	1 day	Fri 12/2/21	Fri 12/2/21	\$0.00	PS									PS																			
303	3.1.1.2.9		Opening act of Economical Offers	1 day	Mon 15/2/21	Mon 15/2/21	\$0.00	PS									PS																			
304	3.1.1.2.10		Combined Evaluation	10 days	Tue 16/2/21	Mon 1/3/21	\$0.00	EC									EC																			
305	3.1.1.2.11		Negociation of contract and finalization of the contract text	10 days	Tue 2/3/21	Mon 15/3/21	\$0.00	PD;PS;PF									PD;PS;PF																			
306	3.1.1.2.12		Request of Non Objection from the Bank to the combi	1 day	Tue 16/3/21	Tue 16/3/21	\$0.00	PD									PD																			
307	3.1.1.2.13		Issuance NO to the combined evaluation for the draft of the contract	5 days	Wed 17/3/21	Tue 23/3/21	\$0.00	IDB									IDB																			
308	3.1.1.2.14		Preparation of the Award Resolution	2 days	Tue 16/3/21	Wed 17/3/21	\$0.00	PS									PS																			
309	3.1.1.2.15		Issuance of the Award Resolution	1 day	Thu 18/3/21	Thu 18/3/21	\$0.00	PSPWTC									PSPWTC																			
310	3.1.1.2.16		Subscribe the contract	10 days	Fri 19/3/21	Thu 1/4/21	\$0.00	PSPWTC;HF									PSPWTC;HF																			
311	3.1.1.2.17		Remission to the Bank a copy of the contract and requests the contract code	1 day	Fri 2/4/21	Fri 2/4/21	\$0.00	PS									PS																			
312	3.1.1.3		Execution of the contract	396 days	Mon 5/4/21	Mon 10/10/22	\$200,000.00																													
313	3.1.1.3.1		Execution of the contract	396 days	Mon 5/4/21	Mon 10/10/22	\$200,000.00	HF																												
314	3.1.2		Road asset management system implemented	0 days	Mon 10/10/22	Mon 10/10/22	\$0.00																													
315	3.2	P7	Product 7: Technical Training implemented	1120 days	Tue 15/9/20	Mon 30/12/24	\$400,000.00																													
316	3.2.1		QCBS_21. Activities for training in Road Design and Maintenance, Project Management and in Port Community System and new port processes	1120 days	Tue 15/9/20	Mon 30/12/24	\$400,000.00																													
317	3.2.1.1		Expression of Interest	44 days	Tue 15/9/20	Fri 13/11/20	\$0.00																													
318	3.2.1.1.1		Preparation of the Expression of Interest announcement	5 days	Tue 15/9/20	Mon 21/9/20	\$0.00	PS									PS																			
319	3.2.1.1.2		Publication of the Expression of Interest announcement (minimum 14 running days)	10 days	Tue 22/9/20	Mon 5/10/20	\$0.00	PS									PS																			

Project Execution Plan (PEP) - Improving Transport Logistics and Competitiveness un Suriname Project SU-L1057																																		
ID	WBS	Prod/ Req	Components / Products / Activities	Duration	Start	Finish	TOTAL USD	Responsible	ly	B	M	E	B	M	E	October	B	M	E	B	April	M	E	January	B	M	E	B	July	April	January	October	July	April
320	3.2.1.1.3		Present Expression of Interest	1 day	Tue 6/10/20	Tue 6/10/20	\$0.00	PF																										
321	3.2.1.1.4		Selection of short list	5 days	Wed 7/10/20	Tue 13/10/20	\$0.00	PS																										
322	3.2.1.1.5		Preparation of the RP proposal request that includes the draft contract	38 days	Tue 15/9/20	Thu 5/11/20	\$0.00	PS																										
323	3.2.1.1.6		Request Non Objection from the Bank of the short list and RP	1 day	Fri 6/11/20	Fri 6/11/20	\$0.00	PD																										
324	3.2.1.1.7		Issuance Non Objection of short list and RP	5 days	Mon 9/11/20	Fri 13/11/20	\$0.00	IDB																										
325	3.2.1.1.8		Conformed short list and Request for Proposal with NO	0 days	Fri 13/11/20	Fri 13/11/20	\$0.00																											
326	3.2.1.2		Hiring Process	100 days	Mon 16/11/20	Fri 2/4/21	\$0.00																											
327	3.2.1.2.1		Publication of the process in the media (UNDB; Executing Agency Web pages, etc)	3 days	Mon 16/11/20	Wed 18/11/20	\$0.00	PS																										
328	3.2.1.2.2		Forward the request for proposals from short list companies	1 day	Thu 19/11/20	Thu 19/11/20	\$0.00	PS																										
329	3.2.1.2.3		Period for preparing technical and economic proposals	22 days	Fri 20/11/20	Mon 21/12/20	\$0.00	PS																										
330	3.2.1.2.4		Addendum to the publication deadline	10 days	Tue 22/12/20	Mon 4/1/21	\$0.00	PF																										
331	3.2.1.2.5		Evaluation of technical proposals	22 days	Tue 5/1/21	Wed 3/2/21	\$0.00	EC																										
332	3.2.1.2.6		Request Non Objection from the Bank to the evaluation of technical proposals	1 day	Thu 4/2/21	Thu 4/2/21	\$0.00	PD																										
333	3.2.1.2.7		Issuance of Non Objection from the Bank	5 days	Fri 5/2/21	Thu 11/2/21	\$0.00	IDB																										
334	3.2.1.2.8		Notification of results, technical evaluation, call for the opening act	1 day	Fri 12/2/21	Fri 12/2/21	\$0.00	PS																										
335	3.2.1.2.9		Opening act of Economical Offers	1 day	Mon 15/2/21	Mon 15/2/21	\$0.00	PS																										
336	3.2.1.2.10		Combined Evaluation	10 days	Tue 16/2/21	Mon 1/3/21	\$0.00	EC																										
337	3.2.1.2.11		Negotiation of contract and finalization of the contract text	10 days	Tue 2/3/21	Mon 15/3/21	\$0.00	PD;PS;PF																										
338	3.2.1.2.12		Request of Non Objection from the Bank to the combined evaluation and the negociated contract	1 day	Tue 16/3/21	Tue 16/3/21	\$0.00	PD																										
339	3.2.1.2.13		Issuance NO to the combined evaluation for the draft of the contract	5 days	Wed 17/3/21	Tue 23/																												

Project Execution Plan (PEP) - Improving Transport Logistics and Competitiveness un Suriname Project SU-L1057

ID	WBS	Prod/ Req	Components / Products / Activities	Duration	Start	Finish	TOTAL USD	Responsible	ly	B	M	E	April	B	M	E	January	B	M	E	October	B	M	E	July	B	April	B	January	B	October	B	July	B	April	B
349	3.3	P8	Product 8: Programs to improve the participation of women in logistics services, implemented	922 days	Fri 18/6/21	Mon 30/12/24	\$100,000.00																													
350	3.3.1		3CV_11. Contracting of Consultant for developing a Program to improve the employability and working conditions of women in logistic activities in the port, including training events to empower women in specialized logistic services	139 days	Fri 18/6/21	Wed 29/12/21	\$20,000.00																													
351	3.3.1.1		Previous Stage	11 days	Fri 18/6/21	Fri 2/7/21	\$0.00																													
352	3.3.1.1.1		Elaboration of the Terms of Reference	5 days	Fri 18/6/21	Thu 24/6/21	\$0.00	PS																												
353	3.3.1.1.2		Request of Non Objection to the TORs and contract proforma	1 day	Fri 25/6/21	Fri 25/6/21	\$0.00	PD																												
354	3.3.1.1.3		Issuance of Non Objection	5 days	Mon 28/6/21	Fri 2/7/21	\$0.00	IDB																												
355	3.3.1.1.4		TORs with Non Objection	0 days	Fri 2/7/21	Fri 2/7/21	\$0.00																													
356	3.3.1.2		Hiring Process	40 days	Mon 5/7/21	Fri 27/8/21	\$0.00																													
357	3.3.1.2.1		Publication of the call	3 days	Mon 5/7/21	Wed 7/7/21	\$0.00	PS																												
358	3.3.1.2.2		Reception of the closed envelopes of the applications until the deadline indicated in the letter of invitation or notice of publication	15 days	Thu 8/7/21	Wed 28/7/21	\$0.00	PS																												
359	3.3.1.2.3		Closing Act of the applications	0 days	Wed 28/7/21	Wed 28/7/21	\$0.00																													
360	3.3.1.2.4		Evaluation of the candidates and preparation of the qualification and selection report, recommending the contracting of consultant	5 days	Thu 29/7/21	Wed 4/8/21	\$0.00	EC																												
361	3.3.1.2.5		Request Non Objection from the Bank for the evaluation	1 day	Thu 5/8/21	Thu 5/8/21	\$0.00	PD																												
362	3.3.1.2.6		Verification and Issuance of Non Objection or demur	5 days	Fri 6/8/21	Thu 12/8/21	\$0.00	IDB																												
363	3.3.1.2.7		Preparation of the contract, based on the established model that has the Non Objection from the Bank	2 days	Fri 13/8/21	Mon 16/8/21	\$0.00	PS																												
364	3.3.1.2.8		Notification of competition results to applicants (can be by email) and publish the contract award on the corresponding website	1 day	Tue 17/8/21	Tue 17/8/21	\$0.00	PS																												
365	3.3.1.2.9		Call the first qualified professional to sign the contract (if the contract is not signed, the following will be invited and so on)	2 days	Wed 18/8/21	Thu 19/8/21	\$0.00	PS																												
366	3.3.1.2.10		Signature of the contract with the individual consultant selected	5 days	Fri 20/8/21	Thu 26/8/21	\$0.00	PSPWTC;CH																												
367	3.3.1.2.11		Remission to the Bank a copy of the contract and requests the contract code	1 day	Fri 27/8/21	Fri 27/8/21	\$0.00	PS																												
368	3.3.1.3		Execution of the contract	88 days	Mon 30/8/21	Wed 29/12/21	\$20,000.00																													
369	3.3.1.3.1		Execution of the contract	88 days	Mon 30/8/21	Wed 29/12/21	\$20,000.00	CH																												
370	3.3.2		Implementation of the Program	783 days	Thu 30/12/21	Mon 30/12/24	\$80,000.00	CH																												
371	3.3.3		Program's activities realized	0 days	Mon 30/12/24	Mon 30/12/24	\$0.00																													
372	4		Administration, Monitoring, Evaluation and Audit	1378 days	Wed 23/10/19	Fri 31/1/25	\$2,000,000.00																													
373	4.1	Adm	Program Administration	1378 days	Wed 23/10/19	Fri 31/1/25	\$1,895,000.00																													
374	4.1.1		Project Excecution Unit (PEU)	1378 days	Wed 23/10/19	Fri 31/1/25	\$1,895,000.00																													
375	4.1.1.1	PRM-A # 1.2	3CV_12. Contracting of Project Director	1378 days	Wed 23/10/19	Fri 31/1/25	\$270,000.00																													

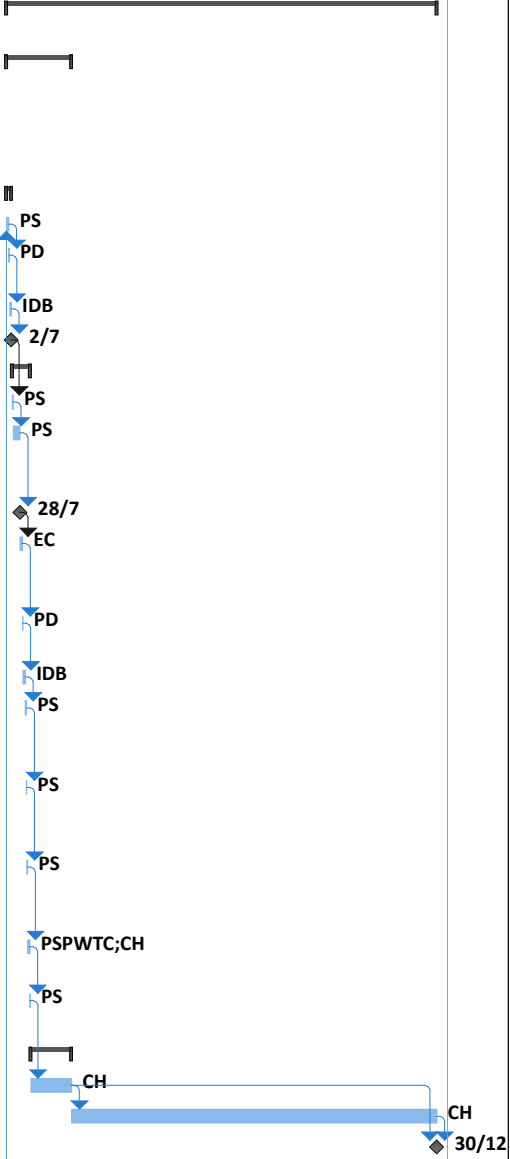

[illegible]

Project Execution Plan (PEP) – Improving Transport Logistics and Competitiveness un Suriname Project SU-L1057																															
ID	WBS	Prod/ Req	Components / Products / Activities	Duration	Start	Finish	TOTAL USD	Responsible	ly	B	M	E	April	B	January	E	October	B	M	July	E	April	B	January	E	October	B	M	July	E	April
403	4.1.1.2.2.2		Reception of the closed envelopes of the applications until the deadline indicated in the letter of invitation or notice of publication	15 days	Wed 22/1/20	Tue 11/2/20	\$0.00	PS																							
404	4.1.1.2.2.3		Closing Act of the applications	0 days	Tue 11/2/20	Tue 11/2/20	\$0.00																								
405	4.1.1.2.2.4		Evaluation of the candidates and preparation of the qualification and selection report, recommending the contracting of consultant	5 days	Wed 12/2/20	Tue 18/2/20	\$0.00	EC																							
406	4.1.1.2.2.5		Request Non Objection from the Bank for the evaluation	1 day	Wed 19/2/20	Wed 19/2/20	\$0.00	PD																							
407	4.1.1.2.2.6		Verification and Issuance of Non Objection or demur	5 days	Thu 20/2/20	Wed 26/2/20	\$0.00	IDB																							
408	4.1.1.2.2.7		Preparation of the contract, based on the established model that has the Non Objection from the Bank	2 days	Thu 27/2/20	Fri 28/2/20	\$0.00	PS																							
409	4.1.1.2.2.8		Notification of competition results to applicants (can be by email) and publish the contract award on the corresponding website	1 day	Mon 2/3/20	Mon 2/3/20	\$0.00	PS																							
410	4.1.1.2.2.9		Call the first qualified professional to sign the contract (if the contract is not signed, the following will be invited and so on)	2 days	Tue 3/3/20	Wed 4/3/20	\$0.00	PS																							
411	4.1.1.2.2.10		Signature of the contract with the individual consultant selected	5 days	Thu 5/3/20	Wed 11/3/20	\$0.00	PSPWTC;CH																							
412	4.1.1.2.2.11		Remission to the Bank a copy of the contract and requests the contract code	1 day	Thu 12/3/20	Thu 12/3/20	\$0.00	PS																							
413	4.1.1.2.3		Execution of the contract	1276 days	Fri 13/3/20	Fri 31/1/25	\$240,000.00																								
414	4.1.1.2.3.1		Execution of activities according to TORs	1276 days	Fri 13/3/20	Fri 31/1/25	\$240,000.00	TC-P																							
415	4.1.1.3	PRM-A # 3.1	3CV_14. Contracting of Technical Coordinator for Road Component	1327 days	Thu 2/1/20	Fri 31/1/25	\$240,000.00																								
416	4.1.1.3.1		Previous Stage	11 days	Thu 2/1/20	Thu 16/1/20	\$0.00																								
417	4.1.1.3.1.1		Elaboration of the Terms of Reference	5 days	Thu 2/1/20	Wed 8/1/20	\$0.00	PS																							
418	4.1.1.3.1.2		Request of Non Objection to the TORs and contract	1 day	Thu 9/1/20	Thu 9/1/20	\$0.00	PD																							
419	4.1.1.3.1.3		Issuance of Non Objection	5 days	Fri 10/1/20	Thu 16/1/20	\$0.00	IDB																							
420	4.1.1.3.1.4		TORs with Non Objection	0 days	Thu 16/1/20	Thu 16/1/20	\$0.00																								
421	4.1.1.3.2		Hiring Process	40 days	Fri 17/1/20	Thu 12/3/20	\$0.00																								
422	4.1.1.3.2.1		Publication of the call	3 days	Fri 17/1/20	Tue 21/1/20	\$0.00	PS																							
423	4.1.1.3.2.2		Reception of the closed envelopes of the application	15 days																											

Project Execution Plan (PEP) – Improving Transport Logistics and Competitiveness un Suriname Project SU-L1057																												
ID	WBS	Prod/ Req	Components / Products / Activities	Duration	Start	Finish	TOTAL USD	Responsible	ly	B	M	E	B	M	E	B	M	E	B	M	E	B	M	E	B	M	E	B
433	4.1.1.3.3		Execution of the contract	1276 days	Fri 13/3/20	Fri 31/1/25	\$240,000.00																					
434	4.1.1.3.3.1		Execution of activities according to TORs	1276 days	Fri 13/3/20	Fri 31/1/25	\$240,000.00	TC-R																				
435	4.1.1.4	PRM-A # 7.1	3CV_15. Contracting of Financial Management Specialist	1378 days	Wed 23/10/19	Fri 31/1/25	\$210,000.00																					
436	4.1.1.4.1		Previous Stage	11 days	Wed 23/10/19	Wed 6/11/19	\$0.00																					
437	4.1.1.4.1.1		Elaboration of the Terms of Reference	5 days	Wed 23/10/19	Tue 29/10/19	\$0.00	Designated MPWTC Staff																				
438	4.1.1.4.1.2		Request of Non Objection to the TORs and contract proforma	1 day	Wed 30/10/19	Wed 30/10/19	\$0.00	Designated MPWTC Staff																				
439	4.1.1.4.1.3		Issuance of Non Objection	5 days	Thu 31/10/19	Wed 6/11/19	\$0.00	IDB																				
440	4.1.1.4.1.4		TORs with Non Objection	0 days	Wed 6/11/19	Wed 6/11/19	\$0.00																					
441	4.1.1.4.2		Hiring Process	40 days	Thu 7/11/19	Wed 1/1/20	\$0.00																					
442	4.1.1.4.2.1		Publication of the call	3 days	Thu 7/11/19	Mon 11/11/19	\$0.00	Designated MPWTC Staff																				
443	4.1.1.4.2.2		Reception of the closed envelopes of the applications until the deadline indicated in the letter of invitation or notice of publication	15 days	Tue 12/11/19	Mon 2/12/19	\$0.00	Designated MPWTC Staff																				
444	4.1.1.4.2.3		Closing Act of the applications	0 days	Mon 2/12/19	Mon 2/12/19	\$0.00																					
445	4.1.1.4.2.4		Evaluation of the candidates and preparation of the qualification and selection report, recommending the contracting of consultant	5 days	Tue 3/12/19	Mon 9/12/19	\$0.00	EC																				
446	4.1.1.4.2.5		Request Non Objection from the Bank for the evaluation	1 day	Tue 10/12/19	Tue 10/12/19	\$0.00	Designated MPWTC Staff																				
447	4.1.1.4.2.6		Verification and Issuance of Non Objection or demur	5 days	Wed 11/12/19	Tue 17/12/19	\$0.00	IDB																				
448	4.1.1.4.2.7		Preparation of the contract, based on the established model that has the Non Objection from the Bank	2 days	Wed 18/12/19	Thu 19/12/19	\$0.00	Designated MPWTC Staff																				
449	4.1.1.4.2.8		Notification of competition results to applicants (can be by email) and publish the contract award on the corresponding website	1 day	Fri 20/12/19	Fri 20/12/19	\$0.00	Designated MPWTC Staff																				
450	4.1.1.4.2.9		Call the first qualified professional to sign the contract (if the contract is not signed, the following will be invited and so on)	2 days	Mon 23/12/19	Tue 24/12/19	\$0.00	Designated MPWTC Staff																				
451	4.1.1.4.2.10		Signature of the contract with the individual consultant selected	5 days	Wed 25/12/19	Tue 31/12/19	\$0.00	PSPWTC;CH																				
452	4.1.1.4.2.11		Remission to the Bank a copy of the contract and requests the contract code	1 day	Wed 1/1/20	Wed 1/1/20	\$0.00	PD																				
453	4.1.1.4.3		Execution of the contract	1327 days	Thu 2/1/20	Fri 31/1/25	\$210,000.00																					
454	4.1.1.4.3.1		Execution of activities according to TORs	1327 days	Thu 2/1/20	Fri																						


Project Execution Plan (PEP) - Improving Transport Logistics and Competitiveness un Suriname Project SU-L1057

ID	WBS	Prod/ Req	Components / Products / Activities	Duration	Start	Finish	TOTAL USD	Responsible	July	April	January	October	July	April	January	October	July	April
									B	M	E	B	M	E	B	M	E	B
461	4.1.1.5.2		Hiring Process	40 days	Thu 7/11/19	Wed 1/1/20	\$0.00											
462	4.1.1.5.2.1		Publication of the call	3 days	Thu 7/11/19	Mon 11/11/19	\$0.00	Designated MPWTC Staff										
463	4.1.1.5.2.2		Reception of the closed envelopes of the applications until the deadline indicated in the letter of invitation or notice of publication	15 days	Tue 12/11/19	Mon 2/12/19	\$0.00	Designated MPWTC Staff										
464	4.1.1.5.2.3		Closing Act of the applications	0 days	Mon 2/12/19	Mon 2/12/19	\$0.00											
465	4.1.1.5.2.4		Evaluation of the candidates and preparation of the qualification and selection report, recommending the contracting of consultant	5 days	Tue 3/12/19	Mon 9/12/19	\$0.00	EC										
466	4.1.1.5.2.5		Request Non Objection from the Bank for the evaluation	1 day	Tue 10/12/19	Tue 10/12/19	\$0.00	Designated MPWTC Staff										
467	4.1.1.5.2.6		Verification and Issuance of Non Objection or demur	5 days	Wed 11/12/19	Tue 17/12/19	\$0.00	IDB										
468	4.1.1.5.2.7		Preparation of the contract, based on the established model that has the Non Objection from the Bank	2 days	Wed 18/12/19	Thu 19/12/19	\$0.00	Designated MPWTC Staff										
469	4.1.1.5.2.8		Notification of competition results to applicants (can be by email) and publish the contract award on the corresponding website	1 day	Fri 20/12/19	Fri 20/12/19	\$0.00	Designated MPWTC Staff										
470	4.1.1.5.2.9		Call the first qualified professional to sign the contract (if the contract is not signed, the following will be invited and so on)	2 days	Mon 23/12/19	Tue 24/12/19	\$0.00	Designated MPWTC Staff										
471	4.1.1.5.2.10		Signature of the contract with the individual consultant selected	5 days	Wed 25/12/19	Tue 31/12/19	\$0.00	PSPWTC;CH										
472	4.1.1.5.2.11		Remission to the Bank a copy of the contract and requests the contract code	1 day	Wed 1/1/20	Wed 1/1/20	\$0.00	PD										
473	4.1.1.5.3		Execution of the contract	1327 days	Thu 2/1/20	Fri 31/1/25	\$210,000.00											
474	4.1.1.5.3.1		Execution of activities according to TORs	1327 days	Thu 2/1/20	Fri 31/1/25	\$210,000.00	PS										
475	4.1.1.6	PRM-A # 4.1	3CV_17. Contracting of Environmental and Social Specialist	1327 days	Thu 2/1/20	Fri 31/1/25	\$210,000.00											
476	4.1.1.6.1		Previous Stage	11 days	Thu 2/1/20	Thu 16/1/20	\$0.00											
477	4.1.1.6.1.1		Elaboration of the Terms of Reference	5 days	Thu 2/1/20	Wed 8/1/20	\$0.00	PS										
478	4.1.1.6.1.2		Request of Non Objection to the TORs and contract proforma	1 day	Thu 9/1/20	Thu 9/1/20	\$0.00	PD										
479	4.1.1.6.1.3		Issuance of Non Objection	5 days	Fri 10/1/20	Thu 16/1/20	\$0.00	IDB										
480	4.1.1.6.1.4		TORs with Non Objection	0 days	Thu 16/1/20	Thu 16/1/20	\$0.00											
481	4.1.1.6.2		Hiring Process	40 days	Fri 17/1/20	Thu 12/3/20	\$0.00											
482	4.1.1.6.2.1		Publication of the call	3 days	Fri 17/1/20	Tue 21/1/20	\$0.00	PS										
483	4.1.1.6.2.2		Reception of the closed envelopes of the applications until the deadline indicated in the letter of invitation or notice of publication	15 days	Wed 22/1/20	Tue 11/2/20	\$0.00	PS										
484	4.1.1.6.2.3		Closing Act of the applications	0 days	Tue 11/2/20	Tue 11/2/20	\$0.00											
485	4.1.1.6.2.4		Evaluation of the candidates and preparation of the qualification and selection report, recommending the contracting of consultant	5 days	Wed 12/2/20	Tue 18/2/20	\$0.00	EC										

Project Execution Plan (PEP) – Improving Transport Logistics and Competitiveness un Suriname Project SU-L1057																						
ID	WBS	Prod/ Req	Components / Products / Activities	Duration	Start	Finish	TOTAL USD	Responsible	ly	B	M	E	B	January	October	July	April	January	October	July	April	ly
486	4.1.1.6.2.5		Request Non Objection from the Bank for the evaluation	1 day	Wed 19/2/20	Wed 19/2/20	\$0.00	PD														
487	4.1.1.6.2.6		Verification and Issuance of Non Objection or demur	5 days	Thu 20/2/20	Wed 26/2/20	\$0.00	IDB														
488	4.1.1.6.2.7		Preparation of the contract, based on the established model that has the Non Objection from the Bank	2 days	Thu 27/2/20	Fri 28/2/20	\$0.00	PS														
489	4.1.1.6.2.8		Notification of competition results to applicants (can be by email) and publish the contract award on the corresponding website	1 day	Mon 2/3/20	Mon 2/3/20	\$0.00	PS														
490	4.1.1.6.2.9		Call the first qualified professional to sign the contract (if the contract is not signed, the following will be invited and so on)	2 days	Tue 3/3/20	Wed 4/3/20	\$0.00	PS														
491	4.1.1.6.2.10		Signature of the contract with the individual consultant selected	5 days	Thu 5/3/20	Wed 11/3/20	\$0.00	PSPWTC;CH														
492	4.1.1.6.2.11		Remission to the Bank a copy of the contract and requests the contract code	1 day	Thu 12/3/20	Thu 12/3/20	\$0.00	PS														
493	4.1.1.6.3		Execution of the contract	1276 days	Fri 13/3/20	Fri 31/1/25	\$210,000.00															
494	4.1.1.6.3.1		Execution of activities according to TORs	1276 days	Fri 13/3/20	Fri 31/1/25	\$210,000.00	ESS														
495	4.1.1.7 PRM-A # 6.2		Other supporting personal	1327 days	Thu 2/1/20	Fri 31/1/25	\$515,000.00															
496	4.2		Monitoring and Evaluations of the Program	160 days	Wed 22/5/24	Tue 31/12/24	\$25,000.00															
497	4.2.1		3CV_18. Contracting of Consultant for Final Evaluation of the Program	117 days	Wed 22/5/24	Thu 31/10/24	\$10,000.00															
498	4.2.1.1		Previous Stage	11 days	Wed 22/5/24	Wed 5/6/24	\$0.00															
499	4.2.1.1.1		Elaboration of the Terms of Reference	5 days	Wed 22/5/24	Tue 28/5/24	\$0.00	PS														
500	4.2.1.1.2		Request of Non Objection to the TORs and contract proforma	1 day	Wed 29/5/24	Wed 29/5/24	\$0.00	PD														
501	4.2.1.1.3		Issuance of Non Objection	5 days	Thu 30/5/24	Wed 5/6/24	\$0.00	IDB														
502	4.2.1.1.4		TORs with Non Objection	0 days	Wed 5/6/24	Wed 5/6/24	\$0.00															
503	4.2.1.2		Hiring Process	40 days	Thu 6/6/24	Wed 31/7/24	\$0.00															
504	4.2.1.2.1		Publication of the call	3 days	Thu 6/6/24	Mon 10/6/24	\$0.00	PS														
505	4.2.1.2.2		Reception of the closed envelopes of the applications until the deadline indicated in the letter of invitation or notice of publication	15 days	Tue 11/6/24	Mon 1/7/24	\$0.00	PS														
506	4.2.1.2.3		Closing Act of the applications	0 days	Mon 1/7/24	Mon 1/7/24	\$0.00															
507	4.2.1.2.4		Evaluation of the candidates and preparation of the qualification and selection report, recommending the contracting of consultant	5 days	Tue 2/7/24	Mon 8/7/24	\$0.00	EC														
508	4.2.1.2.5		Request Non Objection from the Bank for the evaluation	1 day	Tue 9/7/24	Tue 9/7/24	\$0.00	PD														
509	4.2.1.2.6		Verification and Issuance of Non Objection or demur	5 days	Wed 10/7/24	Tue 16/7/24	\$0.00	IDB														
510	4.2.1.2.7		Preparation of the contract, based on the established model that has the Non Objection from the Bank	2 days	Wed 17/7/24	Thu 18/7/24	\$0.00	PS														
Página 17																						

Project Execution Plan (PEP) - Improving Transport Logistics and Competitiveness un Suriname Project SU-L1057

ID	WBS	Prod/ Req	Components / Products / Activities	Duration	Start	Finish	TOTAL USD	Responsible	ly	B	M	E	B	January	October	July	April	January	October	July	April
511	4.2.1.2.8		Notification of competition results to applicants (can be by email) and publish the contract award on the corresponding website	1 day	Fri 19/7/24	Fri 19/7/24	\$0.00	PS													
512	4.2.1.2.9		Call the first qualified professional to sign the contract (if the contract is not signed, the following will be invited and so on)	2 days	Mon 22/7/24	Tue 23/7/24	\$0.00	PS													
513	4.2.1.2.10		Signature of the contract with the individual consultant selected	5 days	Wed 24/7/24	Tue 30/7/24	\$0.00	PSPWTC;CH													
514	4.2.1.2.11		Remission to the Bank a copy of the contract and requests the contract code	1 day	Wed 31/7/24	Wed 31/7/24	\$0.00	PS													
515	4.2.1.3		Execution of the contract	66 days	Thu 1/8/24	Thu 31/10/24	\$10,000.00														
516	4.2.1.3.1		Execution of the contract	66 days	Thu 1/8/24	Thu 31/10/24	\$10,000.00	CH													
517	4.2.2		3CV_19. Contracting of Consultant for Impact Evaluation of the Program	117 days	Wed 22/5/24	Thu 31/10/24	\$10,000.00														
518	4.2.2.1		Previous Stage	11 days	Wed 22/5/24	Wed 5/6/24	\$0.00														
519	4.2.2.1.1		Elaboration of the Terms of Reference	5 days	Wed 22/5/24	Tue 28/5/24	\$0.00	PS													
520	4.2.2.1.2		Request of Non Objection to the TORs and contract proforma	1 day	Wed 29/5/24	Wed 29/5/24	\$0.00	PD													
521	4.2.2.1.3		Issuance of Non Objection	5 days	Thu 30/5/24	Wed 5/6/24	\$0.00	IDB													
522	4.2.2.1.4		TORs with Non Objection	0 days	Wed 5/6/24	Wed 5/6/24	\$0.00														
523	4.2.2.2		Hiring Process	40 days	Thu 6/6/24	Wed 31/7/24	\$0.00														
524	4.2.2.2.1		Publication of the call	3 days	Thu 6/6/24	Mon 10/6/24	\$0.00	PS													
525	4.2.2.2.2		Reception of the closed envelopes of the applications until the deadline indicated in the letter of invitation or notice of publication	15 days	Tue 11/6/24	Mon 1/7/24	\$0.00	PS													
526	4.2.2.2.3		Closing Act of the applications	0 days	Mon 1/7/24	Mon 1/7/24	\$0.00														
527	4.2.2.2.4		Evaluation of the candidates and preparation of the qualification and selection report, recommending the contracting of consultant	5 days	Tue 2/7/24	Mon 8/7/24	\$0.00	EC													
528	4.2.2.2.5		Request Non Objection from the Bank for the evaluation	1 day	Tue 9/7/24	Tue 9/7/24	\$0.00	PD													
529	4.2.2.2.6		Verification and Issuance of Non Objection or demur	5 days	Wed 10/7/24	Tue 16/7/24	\$0.00	IDB													
530	4.2.2.2.7		Preparation of the contract, based on the established model that has the Non Objection from the Bank	2 days	Wed 17/7/24	Thu 18/7/24	\$0.00	PS													
531	4.2.2.2.8		Notification of competition results to applicants (can be by email) and publish the contract award on the corresponding website	1 day	Fri 19/7/24	Fri 19/7/24	\$0.00	PS													
532	4.2.2.2.9		Call the first qualified professional to sign the contract (if the contract is not signed, the following will be invited and so on)	2 days	Mon 22/7/24	Tue 23/7/24	\$0.00	PS													
533	4.2.2.2.10		Signature of the contract with the individual consultant selected	5 days	Wed 24/7/24	Tue 30/7/24	\$0.00	PSPWTC;CH													
534	4.2.2.2.11		Remission to the Bank a copy of the contract and requests the contract code	1 day	Wed 31/7/24	Wed 31/7/24	\$0.00	PS													
535	4.2.2.3		Execution of the contract	66 days	Thu 1/8/24	Thu 31/10/24	\$10,000.00														
536	4.2.2.3.1		Execution of the contract	66 days	Thu 1/8/24	Thu 31/10/24	\$10,000.00	CH													





















[illegible]

[illegible]

Project Execution Plan (PEP) - Improving Transport Logistics and Competitiveness un Suriname Project SU-L1057

ID	WBS	Prod/ Req	Components / Products / Activities	Duration	Start	Finish	TOTAL USD	Responsible	ly	B	M	E	April	B	M	E	January	B	M	E	October	B	M	E	July	B	April	B	M	E	January	B	M	E	October	B	July	B	M	E	April	B	M	E	
594	6.4	PRM-A # 5.2 y 7.2	Develop a project operations manual that determines the functions and responsibilities for procurement and financial management	75 days	Tue 22/10/19	Mon 3/2/20	\$0.00	DR;PD																																					
595	6.5	PRM-A # 5.3	Procurement training provided by the IDB	1379 days	Tue 22/10/19	Fri 31/1/25	\$0.00	IDB PS																																					
596	6.6	PRM-A # 5.4	Implement an ex-ante review methodology of purchasing processes	264 days	Tue 4/2/20	Fri 5/2/21	\$0.00	IDB PS																																					
597	6.7	PRM-A # 6.1	Monitoring and control of payment processes	1304 days	Tue 4/2/20	Fri 31/1/25	\$0.00	FMS																																					
598	6.8	PRM-A # 7.3	Financial management training provided by the IDB	1379 days	Tue 22/10/19	Fri 31/1/25	\$0.00	IDB FS																																					
599	6.9	PRM-A # 7.4	IDB Fiduciary supervision of the project	1304 days	Tue 4/2/20	Fri 31/1/25	\$0.00	IDB FS																																					
600	6.10	PRM-A # 8.1	Implement an accounting system for the project's financial management in accordance with the requirements of the bank	1379 days	Tue 22/10/19	Fri 31/1/25	\$0.00	IDB TLP																																					

Proyecto: Project Execution Plan (
Fecha: Thu 21/3/19

Tarea		Tarea inactiva		Informe de resumen manual		Hito externo	
División		Hito inactivo		Resumen manual		Fecha límite	
Hito		Resumen inactivo		solo el comienzo		Progreso	
Resumen		Tarea manual		solo fin		Progreso manual	
Resumen del proyecto		solo duración		Tareas externas	
