
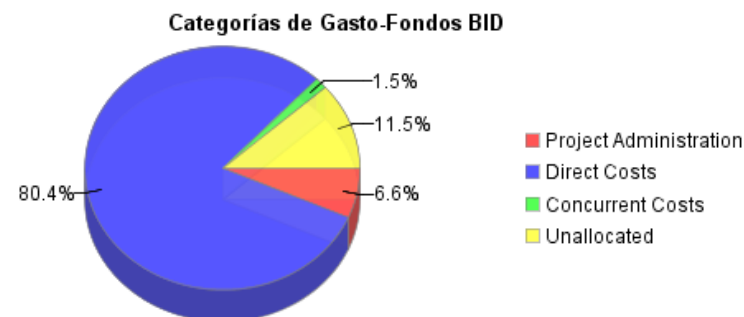
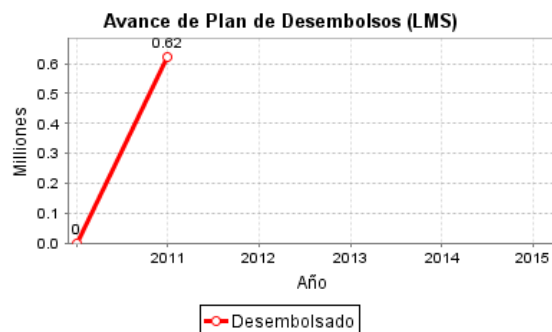



Informe Resumido

Datos Básicos del Proyecto		Fondos Disponibles (US\$)	Costo total y Fuente
Agencia Ejecutora (AE):	Surinaamsche Waterleiding Maatschappij		
Sector:	WATER AND SANITATION-WATER SUPPLY		
Número(s) de Préstamo:	2451/OC-SU	Monto Aprobado Actual:	12.000.000,00
Etapas:	Approved	Monto Desembolsado a la fecha:	625.000,00
Tipo de Operación:	INV - Inversión	% Desembolsado:	5,21
Operación(es) Relacionada(s):	RG-P1400	Saldo:	11.375.000,00
Subtipo de Operación:	ESP - Inversión Específica		
		BID Original:	12.000.000,00
		Actual BID:	12.000.000,00
		Pari-passu:	96,00
		Co-financiamiento/País:	500.000,00
		Estimado Original:	12.500.000,00
		Período de Amortización (meses):	234

Categoría de Impacto Ambiental y Social del Proyecto	Reformulación	Validación
Categoría de Impacto Ambiental y Social del Proyecto: B	() ¿El objetivo (s) del proyecto fue reformulado?	Validado por el Jefe de División: 23-abr-2012 Validado por Representante de País: 23-abr-2012

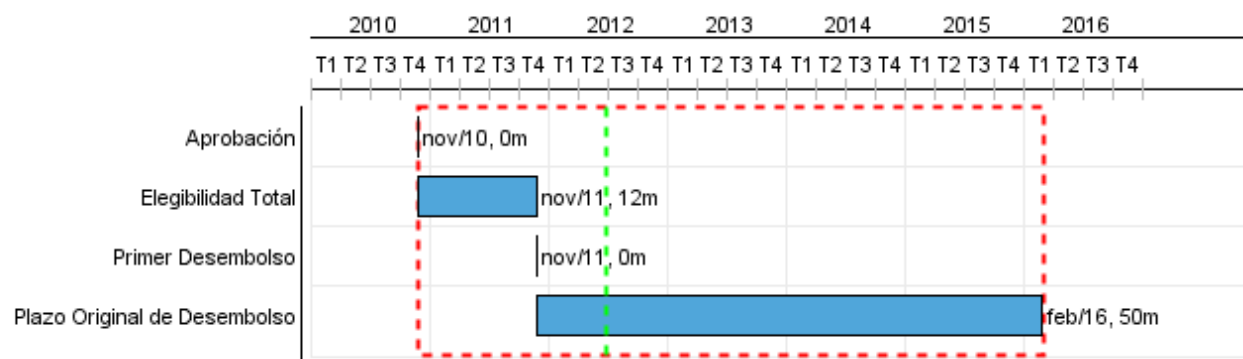

Progreso Acumulado al 2011

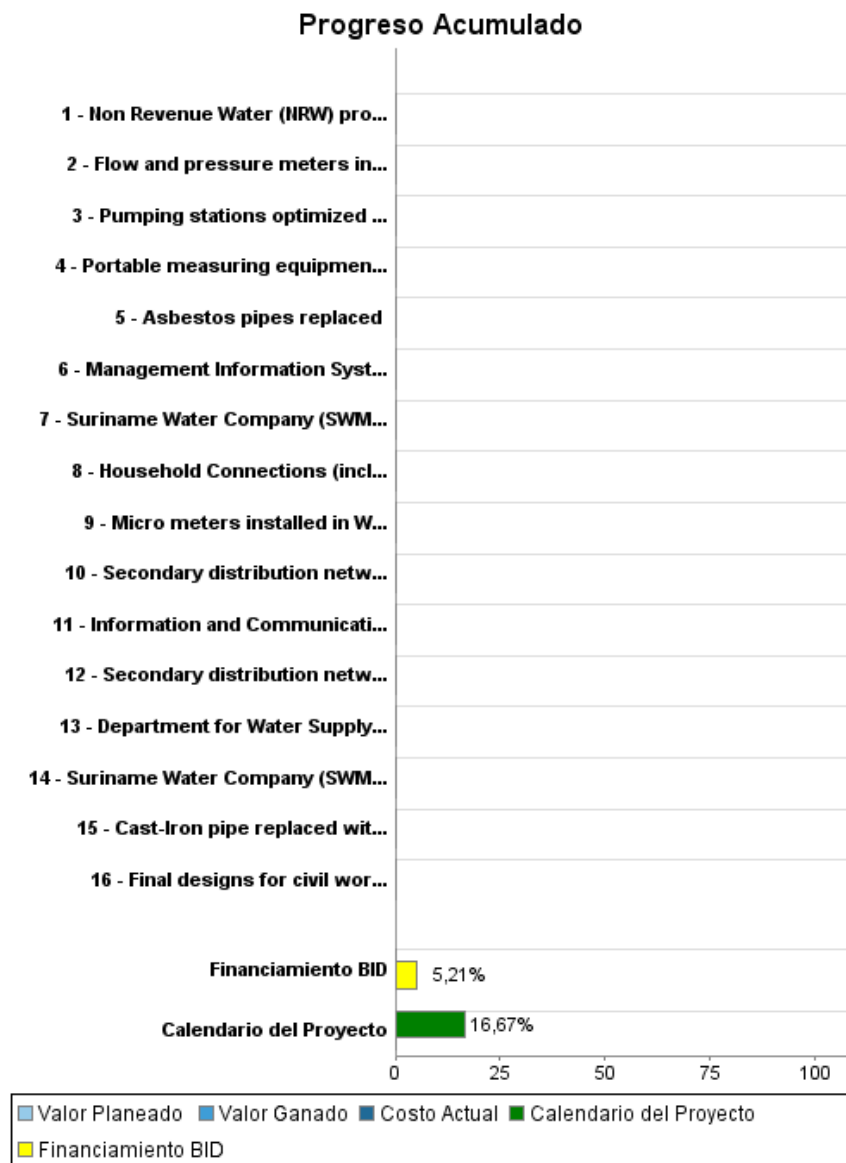

Resultados

Resultado: Water supply network in Greater Paramaribo improved

Indicador	Unidad de Medida	Línea de base	Año Línea de base		2012	2013	2014	2015	2016	Fin de Proyecto
Households connected to an upgraded water supply network	Households		2010	P A		2,560.00	6,560.00	10,120.00	11,600.00	11,600.00

Resultado: Level of Non Revenue Water (NRW) decreased

Indicador	Unidad de Medida	Línea de base	Año Línea de base		2012	2013	2014	2015	2016	Fin de Proyecto
Volume of potable water billed	mill m3/year	16.70	2010	P A					18.45	18.45
Level of Non Revenue Water (NRW) in areas targeted by the project through the Non Revenue Water (NRW) program	percentage points	45.00	2010	P A		43.00	41.00	38.00	35.00	35.00

Resultado: Energy use in SWM improved

Indicador	Unidad de Medida	Línea de base	Año Línea de base		2012	2013	2014	2015	2016	Fin de Proyecto
Energy Consumption in the 8 pilot facilities	MWh/year	13,000.00	2009	P A		12,500.00	12,000.00	11,000.00	10,000.00	10,000.00

Resultado: Water supply agencies capacity (in O&M and water quality monitoring) improved

Indicador	Unidad de Medida	Línea de base	Año Línea de base		2012	2013	2014	2015	2016	Fin de Proyecto
Time response to complains	Days	10.00	2010	P A		9.00	8.00	7.00	5.00	5.00

Productos: Progreso Físico y Financiero Anual 2011

Descripción	Unidad de medida	Físico				Financiero			
		Planeado	Actual	Unidades Acumuladas	Unidades FDP	Planeado	Actual	Costos Acumulados	Costos FDP
Water Supply System Rehabilitation									
Asbestos pipes replaced	Km				16,00				2.200.000,00
Secondary distribution network pipes replaced	Km				35,00				987.000,00
Secondary distribution network pipes re-laid	Km				70,00				1.435.000,00
Micro meters installed in Wanica and Para	Micro Meters				3.000,00				240.000,00
Household Connections (including micro meters) in Leidingen replaced	Connections				5.000,00				487.000,00
Cast-Iron pipe replaced with Polyvinyl chloride (PVC) pipe	Km				7,00				650.000,00
Non Revenue Water Program									
Flow and pressure meters installed	Meters				80,00				1.000.000,00
Suriname Water Company (SWM) Staff trained on Non Revenue Water (NRW)	People				10,00				50.000,00
Final designs for civil works (on network rehabilitation and interventions related to Non Revenue Water reduction) completed	Designs				1,00				640.000,00
Non Revenue Water (NRW) program implemented by the Suriname Water Company (SWM)	Program				1,00				500.000,00
Energy efficiency pilot project									
Portable measuring equipment purchased	Equipment				5,00				40.000,00
Pumping stations optimized (rehabilitated, calibrated, etc.)	Pumping stations				8,00				450.000,00
Institutional strengthening									
Suriname Water Company (SWM) Staff trained on Operation and Maintenance (O&M) and energy efficiency	People				15,00				115.000,00
Department for Water Supply under the Ministry of Natural Resources (NH/DWC) Staff trained on water quality	People				5,00				30.000,00
Management Information System integration completed	Systems				1,00				220.000,00
Information and Communication Technology (ICT) Servers upgraded	Servers				2,00				300.000,00
Management, contingencies and others									
TOTAL									9.344.000,00
