
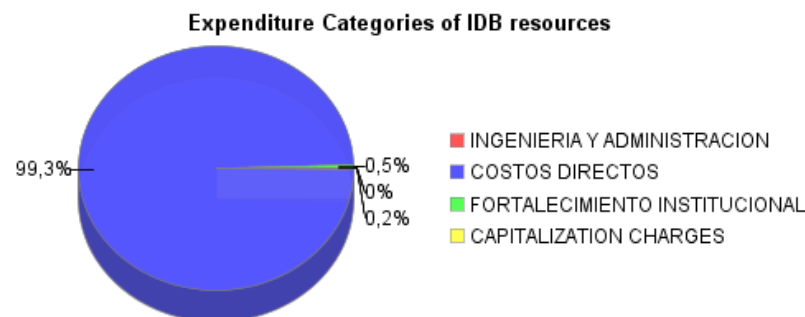
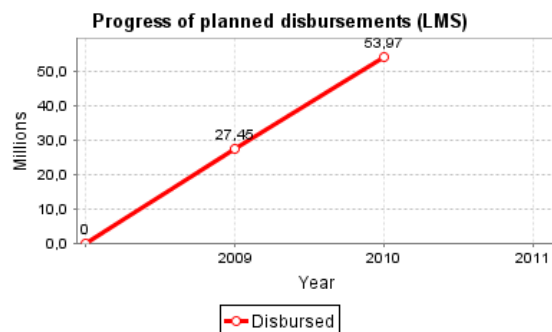



## Summary Report

Basic Data		Available Funds (US\$)		Total Cost and Source	
Executing Agency (EA):	MINISTERIO DE ECONOMIA, HACIENDA Y FINANZAS				
Sector:	TRANSPORTATION				
Loan Number(s):	1294/OC-AR	Current Approved Amount:	200.000.000,00	Original IDB:	200.000.000,00
Stage:	Approved	Disbursed Amount to Date:	148.647.308,78	Current IDB:	200.000.000,00
Operation Type:	INV - Investment	% Disbursed:	74,32	Pari-passu:	28,70
Related Operation(s):	TC9803504	Balance:	51.352.691,22	Co-Financing/Country:	80.000.000,00
Operation Subtype:	GOM - Global of Multiple Works Operation			Original Estimate:	280.000.000,00
				Amortization Period (months):	162

Project Environmental and Social Impact Category	Reformulation	Validation
Project Environmental and Social Impact Category: B	( ) Was the objective(s) of this project reformulated?	Validated by Division Chief: Mar 31, 2011 Validated by Country Representative: Apr 28, 2011

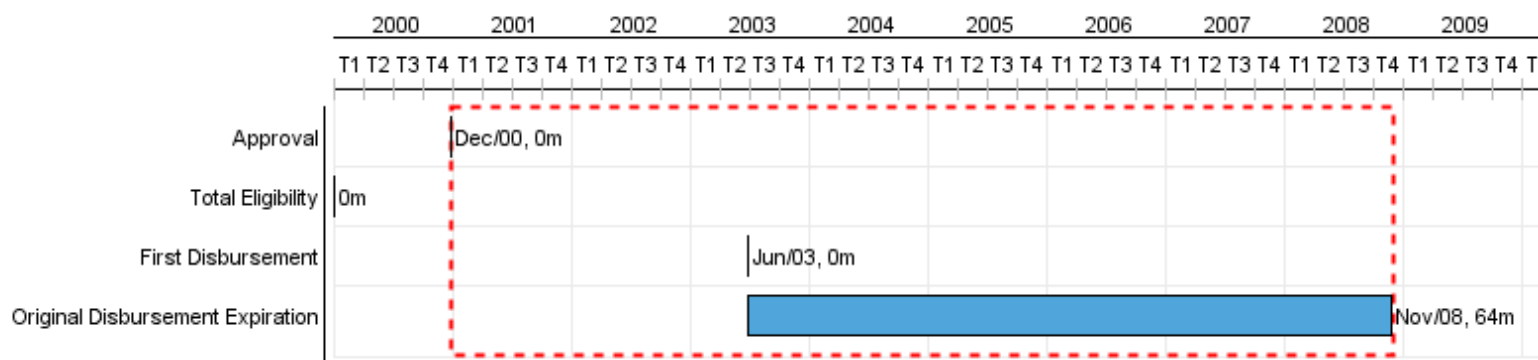

## Accumulated Progress as of 2010

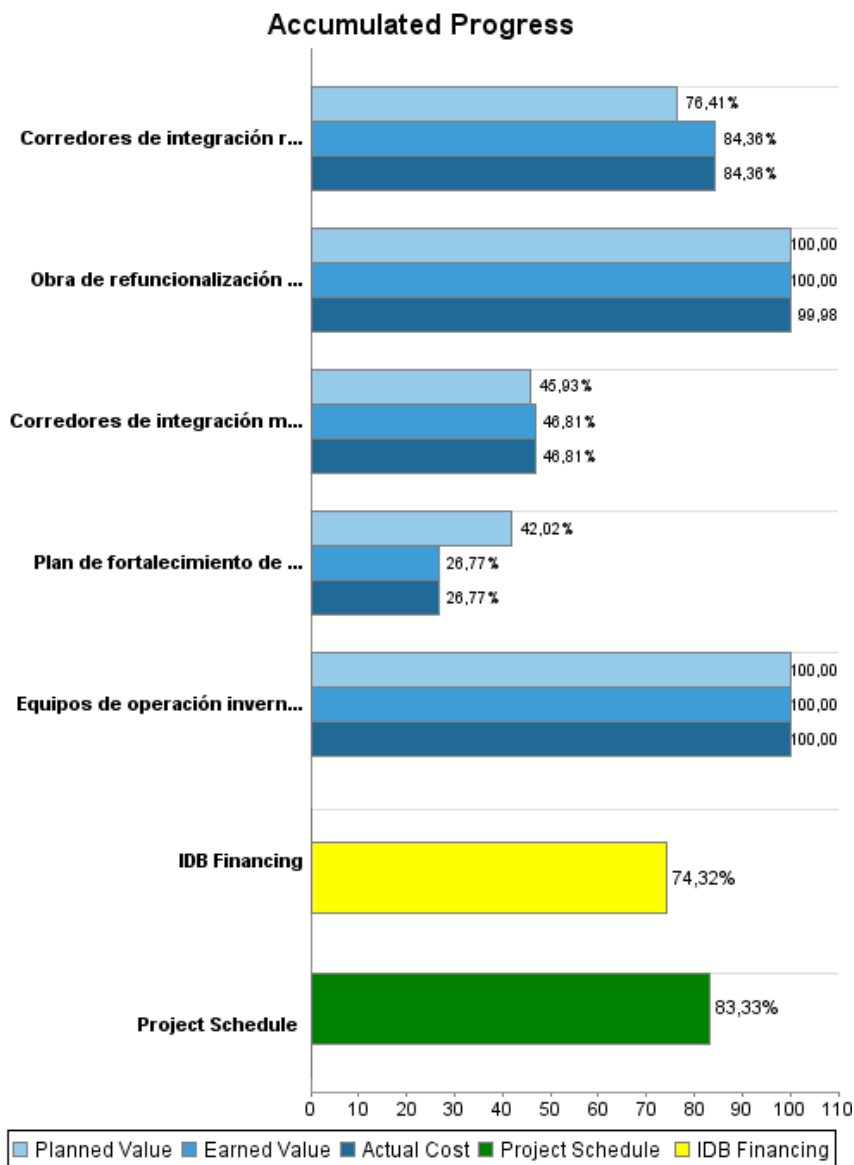

## Outcomes

<b>Outcome:</b>	Nivel de servicio de las rutas y pasos fronterizos intervenidos mejorado.
-----------------	---

Indicator	Unit of Measure	Baseline	Baseline Year		End of project
Costos de operación de un camión tipo en pasos fronterizos (Ruta Nacional 14)	\$/km	1,42		P A	1,01
Tránsito con Chile por pasos mejorados (paso Cristo Redentor)	veh/año	1.300,00		P A	2.700,00
Costos de operación de un camión tipo en corredores mejorados (Ruta Nacional 16)	\$/km	1,30		P A	1,00
Alertas por avalanchas de nieve atendidas por el sistema en el Paso Cristo Redentor (a Chile)	Alertas			P A	3,00

## Outputs: 2010 Annual Physical and Financial Progress 2010

Description	Unit of Measure	Physical				Financial			
		Planned	Actual	Accumulated units	EOP units	Planned	Actual	Accumulated costs	EOP costs
<b>1. Mejoramiento y Rehabilitación de Corredores Viales de Integración.</b>									
Corredores de integración mejorados	Kilómetros		145,00		242,00	60.000.000,00	64.489.000,00		513.800.000,00
Corredores de integración rehabilitados	Kilómetros		68,00		68,00	3.500.000,00	5.759.000,00		28.400.000,00
<b>2. Fortalecimiento Institucional</b>									
Plan de fortalecimiento de la capacidad de la Dirección Nacional de Vialidad implementado	Plan				1,00	300.000,00	10.290,00		1.904.000,00
Obra de refuncionalización del campamento de la DNV en Uspallata, Ruta Nacional 7 terminada	Obra				1,00				1.754.000,00
<b>3. Adquisición de equipos de operación</b>									
Equipos de operación invernal adquiridos	equipos				9,00				5.152.391,00
<b>4. Ingeniería y Administración</b>									
<b>TOTAL</b>						<b>63.800.000,00</b>	<b>70.258.290,00</b>		<b>551.010.391,00</b>
