
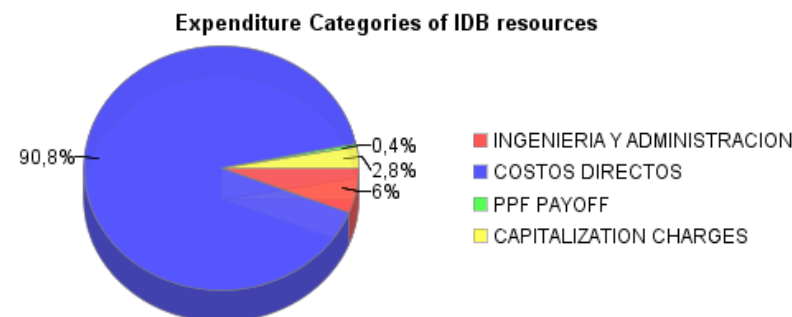
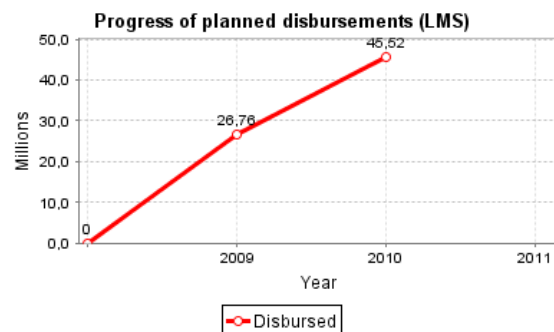



Summary Report

Basic Data		Available Funds (US\$)		Total Cost and Source	
Executing Agency (EA):	Administradora Boliviana de Carreteras				
Sector:	TRANSPORTATION				
Loan Number(s):	1101/SF-BO	Current Approved Amount:	75.000.000,00	Original IDB:	75.000.000,00
Stage:	Approved	Disbursed Amount to Date:	74.167.579,56	Current IDB:	75.000.000,00
Operation Type:	INV - Investment	% Disbursed:	98,89	Pari-passu:	80,94
Related Operation(s):		Balance:	832.420,44	Co-Financing/Country:	45.000.000,00
Operation Subtype:	PFM - Multi-Phase Lending Project			Original Estimate:	120.000.000,00
				Amortization Period (months):	354

Project Environmental and Social Impact Category	Reformulation	Validation
Project Environmental and Social Impact Category: B	() Was the objective(s) of this project reformulated?	Validated by Division Chief: Mar 28, 2011 Validated by Country Representative: Apr 19, 2011

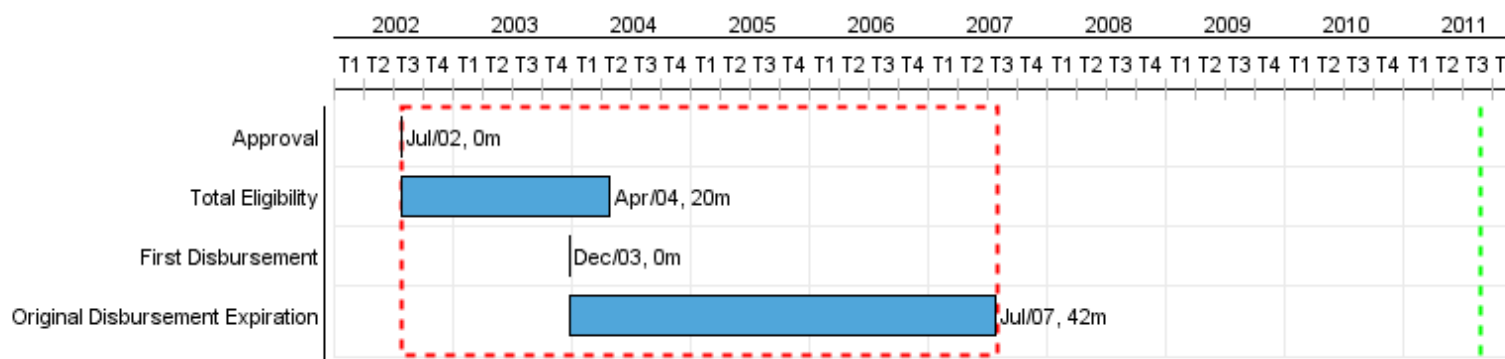

Accumulated Progress as of 2010

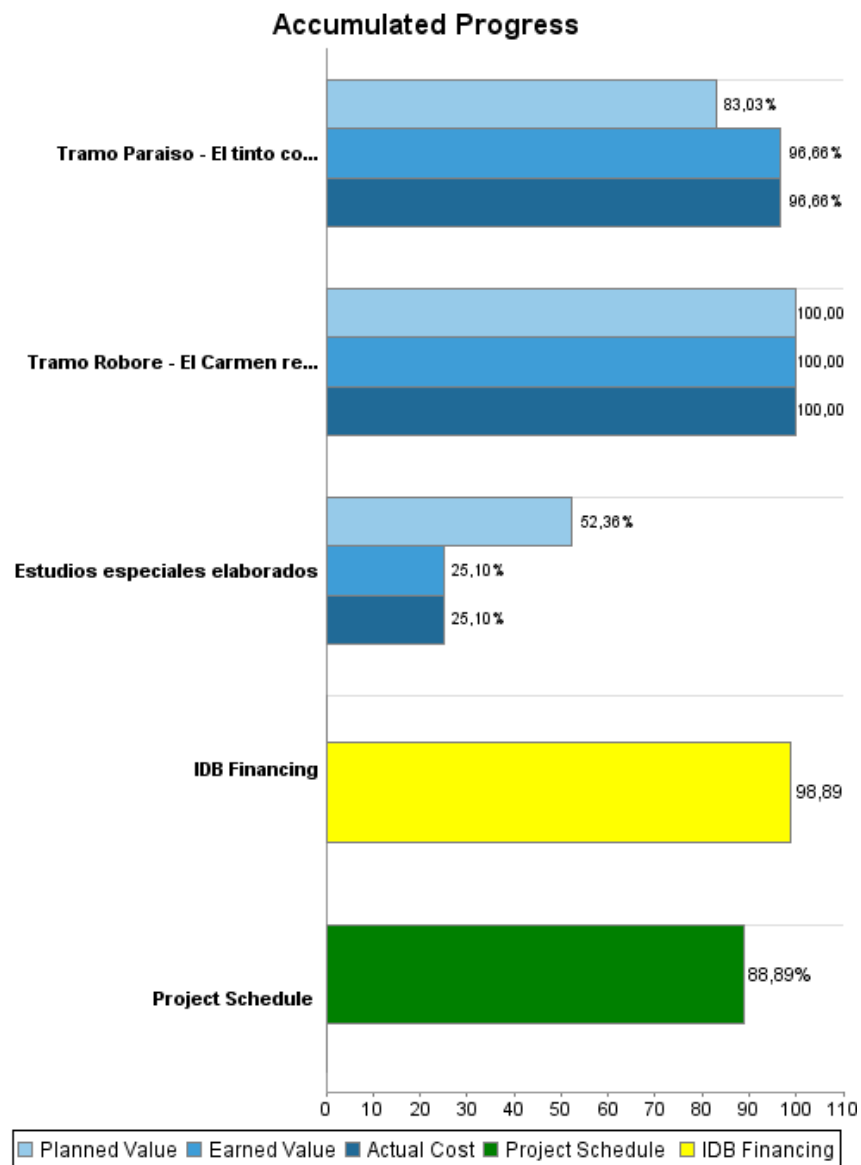

Outcomes

Outcome:	Condiciones de integración entre Santa Cruz y Puerto Suárez mejoradas
-----------------	---

Indicator	Unit of Measure	Baseline	Baseline Year		End of project
Tiempo de viaje para vehículos pesados en el corredor Santa Cruz-Puerto Suarez	Días	7,00	2002	P A	1,00
Transito de vehículos comerciales y particulares en el tramo Paraiso-El Tinto	Vehículos/día	87,00	2002	P A	1.130,00

Outputs: 2010 Annual Physical and Financial Progress 2010

Description	Unit of Measure	Physical				Financial			
		Planned	Actual	Accumulated units	EOP units	Planned	Actual	Accumulated costs	EOP costs
COMPONENTE 1: CONSTRUCCION, REHABILITACION, MANTENIMIENTO y SUPERVISION TECNICA.									
Tramo Paraiso - El tinto contruido y pavimentado	Kilómetros				125,00	17.459.920,00	29.270.440,00		86.695.720,00
Tramo Robore - El Carmen rehabilitado en Ripio	Kilómetros				139,00				2.575.260,00
COMPONENTE 2: FORTALECIMIENTO INSTITUCIONAL									
Estudios especiales elaborados	Estudios				3,00	224.290,00	33.470,00		700.000,00
TOTAL						17.684.210,00	29.303.910,00		89.970.980,00
