
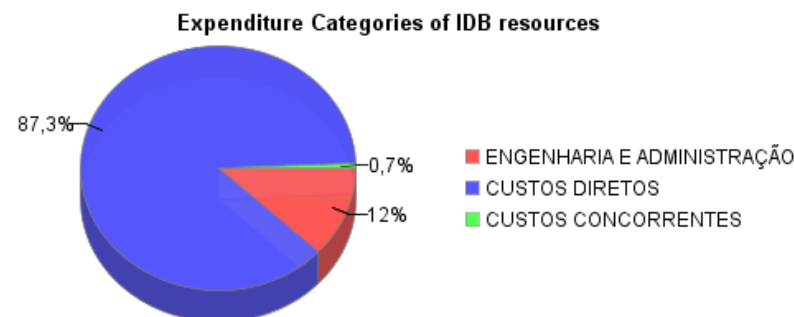
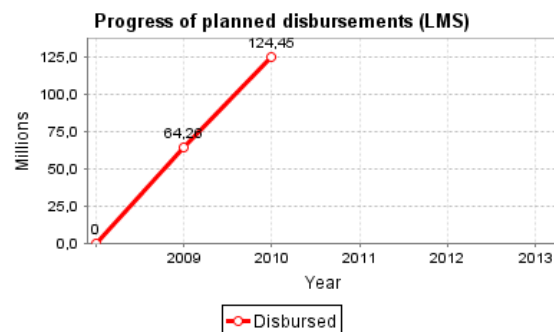



Summary Report

Basic Data		Available Funds (US\$)		Total Cost and Source	
Executing Agency (EA):	Estado de Amazonas				
Sector:	WATER AND SANITATION-SEWERAGE				
Loan Number(s):	2006/OC-BR	Current Approved Amount:	154.000.000,00	Original IDB:	154.000.000,00
Stage:	Approved	Disbursed Amount to Date:	124.453.667,53	Current IDB:	154.000.000,00
Operation Type:	INV - Investment	% Disbursed:	80,81	Pari-passu:	6,86
Related Operation(s):	BR-L1005	Balance:	29.546.332,47	Co-Financing/Country:	66.000.000,00
Operation Subtype:	PFM - Multi-Phase Lending Project			Original Estimate:	220.000.000,00
				Amortization Period (months):	234

Project Environmental and Social Impact Category	Reformulation	Validation
Project Environmental and Social Impact Category: B	() Was the objective(s) of this project reformulated?	Validated by Division Chief: Mar 24, 2011 Validated by Country Representative: Apr 20, 2011

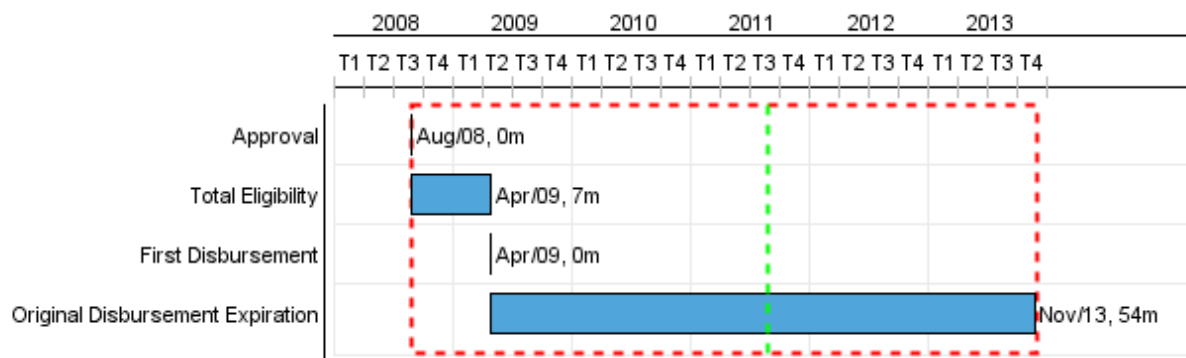

Accumulated Progress as of 2010

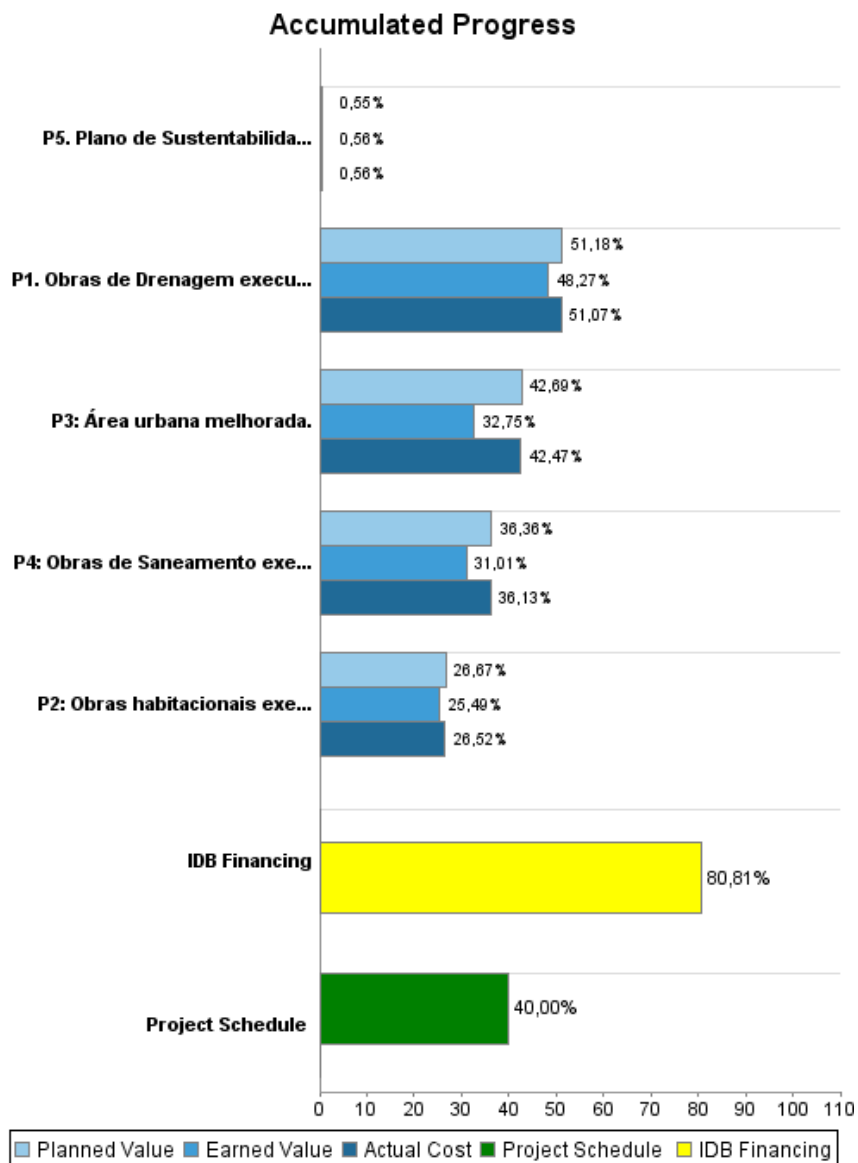

Outcomes

Outcome:	Ocorrências de contaminação das águas nos igarapés da cidade de Manaus-AM.
-----------------	--

Indicator	Unit of Measure	Baseline	Baseline Year		End of project
Quantidade de coliformes fecais reduzidos, parte por milhão.	NMP/100ml	2.400,00	2009	P A	1.000,00
Oxigênio dissolvido nas águas aumentado, parte por 100 milhões.	mgO2/l	3,10	2009	P A	4,20
Demanda Bioquímica de Oxígeno (DBO).	mgO2/l	240,00	2009	P A	20,00
Quantidade de nitrogênio amoniacal.	mgN/l	20,00	2009	P A	10,00
Demanda Química de Oxigênio (DQO).	mgO2/l	152,30	2009	P A	75,00

Outcome:	Ocorrências de inundações dos igarapés na cidade de Manaus-AM.
-----------------	--

Indicator	Unit of Measure	Baseline	Baseline Year		End of project
Pessoas afetadas por inundações dos igarapés.	Pessoas	21.760,00	2009	P A	0,00
Casas construídas nas margens dos igarapés.	Casas	4.352,00	2009	P A	0,00

Outputs: 2010 Annual Physical and Financial Progress 2010

Description	Unit of Measure	Physical				Financial			
		Planned	Actual	Accumulated units	EOP units	Planned	Actual	Accumulated costs	EOP costs
COMPONENTE1: Melhoria Ambiental, Urbanística e Habitacional									
P1. Obras de Drenagem executadas.	Metros	2.575,00	2.096,00		9.488,00	4.722.560,11	4.687.895,56		30.148.264,48
P2: Obras habitacionais executadas.	Un	168,00	158,00		1.038,00	8.248.232,48	8.185.943,98		41.405.212,28
P3: Área urbana melhorada.	Ha	3,00	2,00		40,00	20.973.961,17	20.819.771,44		70.299.996,77
P4: Obras de Saneamento executadas.	Metros	42.900,00	35.907,00		142.734,00	17.499.118,51	17.372.789,41		53.287.526,47
COMPONENE 2: Sustentabilidade Social e Institucional									
P5. Plano de Sustentabilidade Comunitário Social , implementado.	Plano		0,01		1,00	23.474,54	24.201,78		4.284.000,00
COMPONENTE 3: OUTROS									
TOTAL						51.467.346,81	51.090.602,17		199.425.000,00
