
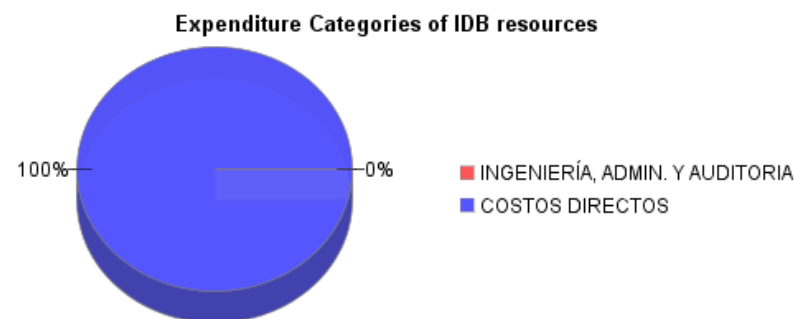
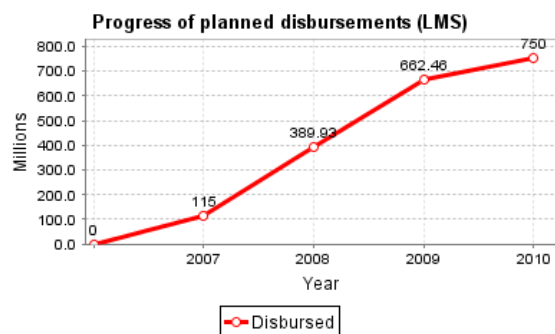


Summary Report


| Basic Data | | Available Funds (US\$) | | Total Cost and Source | |
|------------------------|--|---------------------------|----------------|-------------------------------|------------------|
| Executing Agency (EA): | C.V.G. ELECTRIFICACION DEL CARONI, S.A. (EDELCA) | | | | |
| Sector: | ENERGY-HYDROELECTRIC ENERGY | | | | |
| Loan Number(s): | 1686/OC-VE | Current Approved Amount: | 750.000.000,00 | Original IDB: | 750.000.000,00 |
| Stage: | Approved | Disbursed Amount to Date: | 750.000.000,00 | Current IDB: | 750.000.000,00 |
| Operation Type: | INV - Investment | % Disbursed: | 100,00 | Pari-passu: | 25,00 |
| Related Operation(s): | VE-L1006, VE-L1026 | Balance: | | Co-Financing/Country: | 2.311.000.000,00 |
| Operation Subtype: | ESP - Specific Investment Operation | | | Original Estimate: | 3.061.000.000,00 |
| | | | | Amortization Period (months): | 126 |

| Project Environmental and Social Impact Category | | Reformulation | Validation |
|---|------|--|--|
| Project Environmental and Social Impact Category: | A(R) | () Was the objective(s) of this project reformulated? | Validated by Division Chief: 18-abr-2012 Validated by Country Representative: 30-abr-2012 |

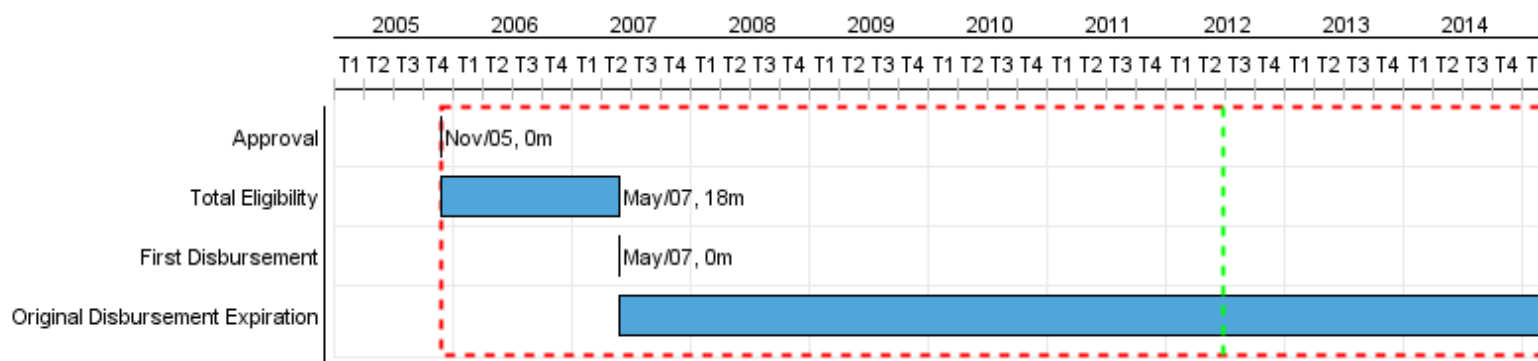

Accumulated Progress as of 2011

Accumulated Progress

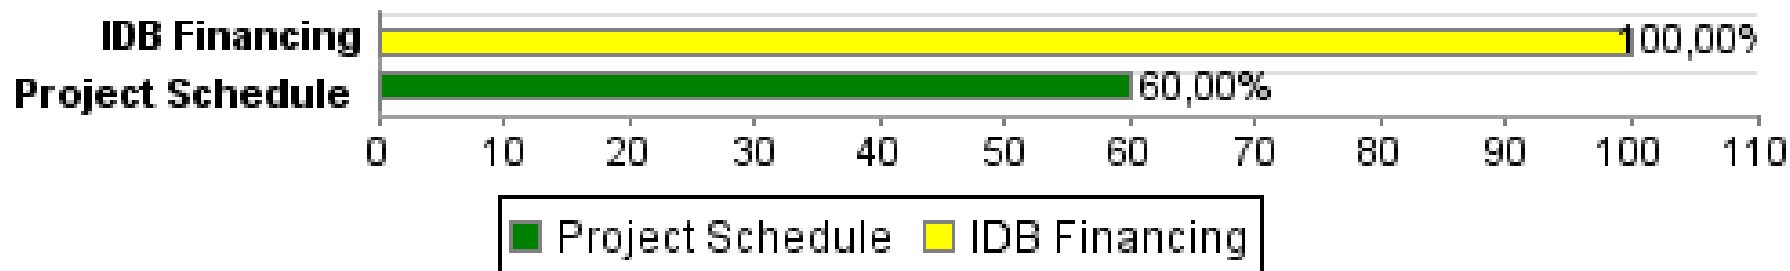



PROGRESS MONITORING REPORT

VE-L1003 - Tocomá Hydroelectric Power Plant
2011 2nd period with closure up to (31-Mar-2012)

Inter-American Development Bank - IDB

Office of Strategic Planning and Development Effectiveness

Last Update: 18/11/2011

Outcomes

- No information available

PROGRESS MONITORING REPORT

VE-L1003 - Tocomá Hydroelectric Power Plant
2011 2nd period with closure up to (31-Mar-2012)

Inter-American Development Bank - IDB

Office of Strategic Planning and Development Effectiveness

Last Update: 18/11/2011

Outputs: Annual Physical and Financial Progress 2011

| Description | Unit of Measure | Physical | | | | Financial | | | |
|------------------------|-----------------|----------|--------|-------------------|-----------|-----------|--------|-------------------|-----------|
| | | Planned | Actual | Accumulated units | EOP units | Planned | Actual | Accumulated costs | EOP costs |
| Central Hidroeléctrica | | | | | | | | | |
| Protección Ambiental | | | | | | | | | |
| Presa derecha | | | | | | | | | |
| TOTAL | | | | | | | | | |
