
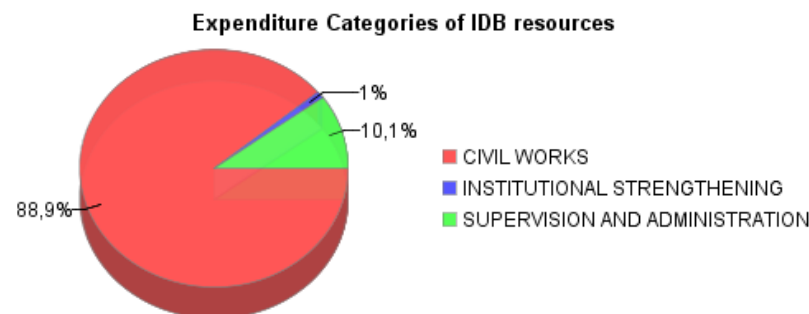
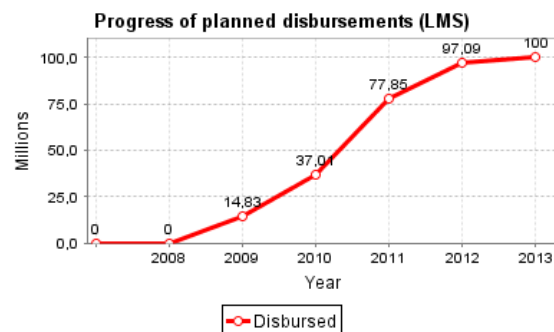



## Summary Report

Basic Data		Available Funds (US\$)		Total Cost and Source	
Executing Agency (EA):	MINISTRY OF PUBLIC WORKS AND TRANSPORTATION				
Sector:	TRANSPORT-MAJOR HIGHWAYS				
Loan Number(s):	1988/OC-BH	Current Approved Amount:	100.000.000,00	Original IDB:	100.000.000,00
Stage:	Approved	Disbursed Amount to Date:	100.000.000,00	Current IDB:	100.000.000,00
Operation Type:	INV - Investment	% Disbursed:	100,00	Pari-passu:	100,00
Related Operation(s):	BH0029, BH-L1029	Balance:		Co-Financing/Country:	
Operation Subtype:	SUP - Supplementary Financing			Original Estimate:	100.000.000,00
				Amortization Period (months):	246

Project Environmental and Social Impact Category	Reformulation	Validation
Project Environmental and Social Impact Category: B	( ) Was the objective(s) of this project reformulated?	Validated by Division Chief: 25-sep-2013 Validated by Country Representative: 07-oct-2013

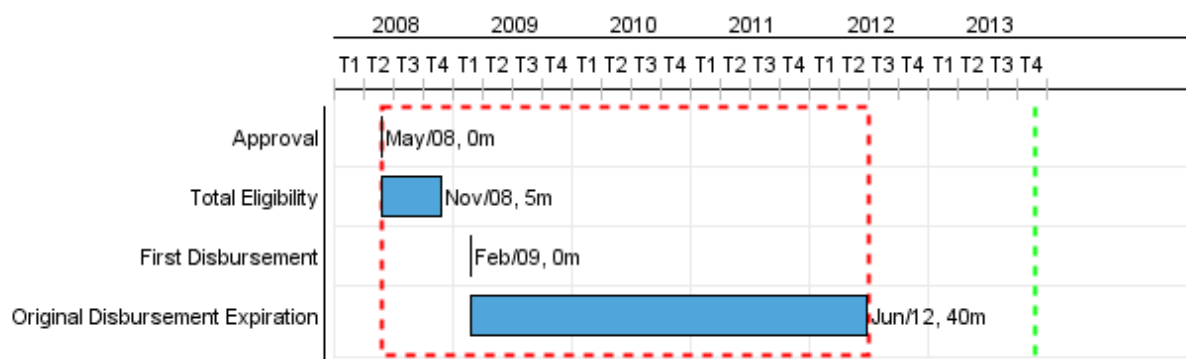

**Accumulated Progress as of 2013**

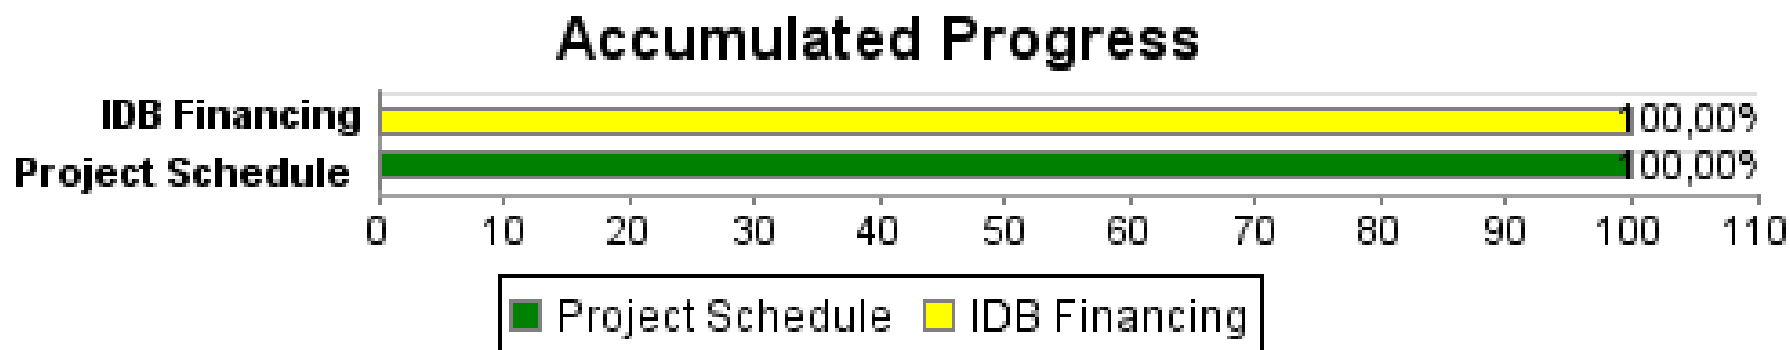

# PROGRESS MONITORING REPORT

BH-L1024 - Supplementary Financing for New Providence Transport Program  
2013 1º period closed in (31-Oct-2013)

Inter-American Development Bank - IDB

Office of Strategic Planning and Development Effectiveness  
Last Update: 20/09/2013

## Outcomes

<b>Outcome:</b>	Transport costs for road users reduced.
<b>Suppositions:</b>	Automobile ownership growth rates remain at 2008 predicted levels and policy actions to reduce automobile use are implemented.

Indicator	Unit of Measure	Baseline	Baseline Year		2008	2009	2010	2011	2012	2013	End of project
Volume/capacity ratio of major road network	Number	0,90	2008	P		0,90			0,85	0,85	0,85
				A		0,90			0,85		
Annual total number of crash incidents	Incidents	10.320,00	2008	P		9.768,00			8.772,00	8.772,00	8.772,00
				A		9.768,00			8.772,00		
Public bus ridership versus private car transport (mode split)	Ratio	0,35	2008	P					0,45	0,45	0,45
				A					0,45		

## Outputs: Annual Physical and Financial Progress 2013

Description	Unit of Measure	Physical			
		Planned	Actual	Accumulated units	EOP units
<b>Roadway Development</b>					
Major Roads constructed and upgraded to Florida Dept of Transport (FDOT) specifications	Kilometers	9,60	4,80		25,60
Big Pond Park Developed (Phase 1)	Park				1,00
<b>Institutional Development</b>					
Public Bus service unified	Service				1,00
Major road network maintained under a routine road Management System	Miles				600,00
Action Plan for Strengthening of the MOWT/DPW into an effective and efficient results-oriented organization	Action Plan				1,00
Surface Transport Development Plan (2005-2015) substantially implemented	Plan				1,00
<b>Administrative Costs</b>					
Consulting firm supervised construction/upgrade of road corridors	N/A				
Consultant Project Coordinator support provided to MOWT-PEU	N/A				
Evaluations	N/A				
