



Operation Number: **JA-L1016**
Year- PMR Cycle: **First period Jan-Jun 2016**
Last Update: **10/14/2016**
PMR Validation Stage: **Validated by Chief of Operations**

Chief of Operations validation date: **10/18/2016**
Division Chief validation date:
Country Representative validation date:

Inter-American Development Bank - IDB
Office of Strategic Planning and Development Effectiveness

Operation Profile

Basic Data

Operation name:	Transportation Infrastructure Rehabilitation Program	Loan Number:	2026/OC-JA
Executing Agency (EA):	MINISTRY OF TRANSPORT AND WORKS		
Team Leader:	Persaud,Christopher	Sector/Subsector:	TR
Operation Type:	Loan Operation	Overall Stage:	Closed (all the Operations are closed)
Lending Instrument:	Investment Loan	Country:	JAMAICA
Borrower:	JAMAICA	Convergence related Operation(s):	

Total Cost and Source

	Original IDB	Current Active IDB	Local Counterpart	Co-Financing/Country	Total operation cost - Original Estimate
JA-L1016	\$50,000,000.00	\$50,000,000.00	\$0.00		\$50,000,000.00

Available Funds (US\$)

	Current IDB	Disb. Amount to Date	% Disbursed	Undisbursed Balance
JA-L1016	\$49,934,013.41	\$49,934,013.41	100.00%	\$0.00


Environmental and Social Safeguards

Main Operation	
Impacts Category:	B
Safeguard Performance Rating:	
Safeguard Performance Rating - Rationale:	

Reformulation Information

Main Operation	
Was/Were the objective(s) of this operation reformulated?	NO
Date of approval:	

Expense Categories by Loan Contract (cumulative values)

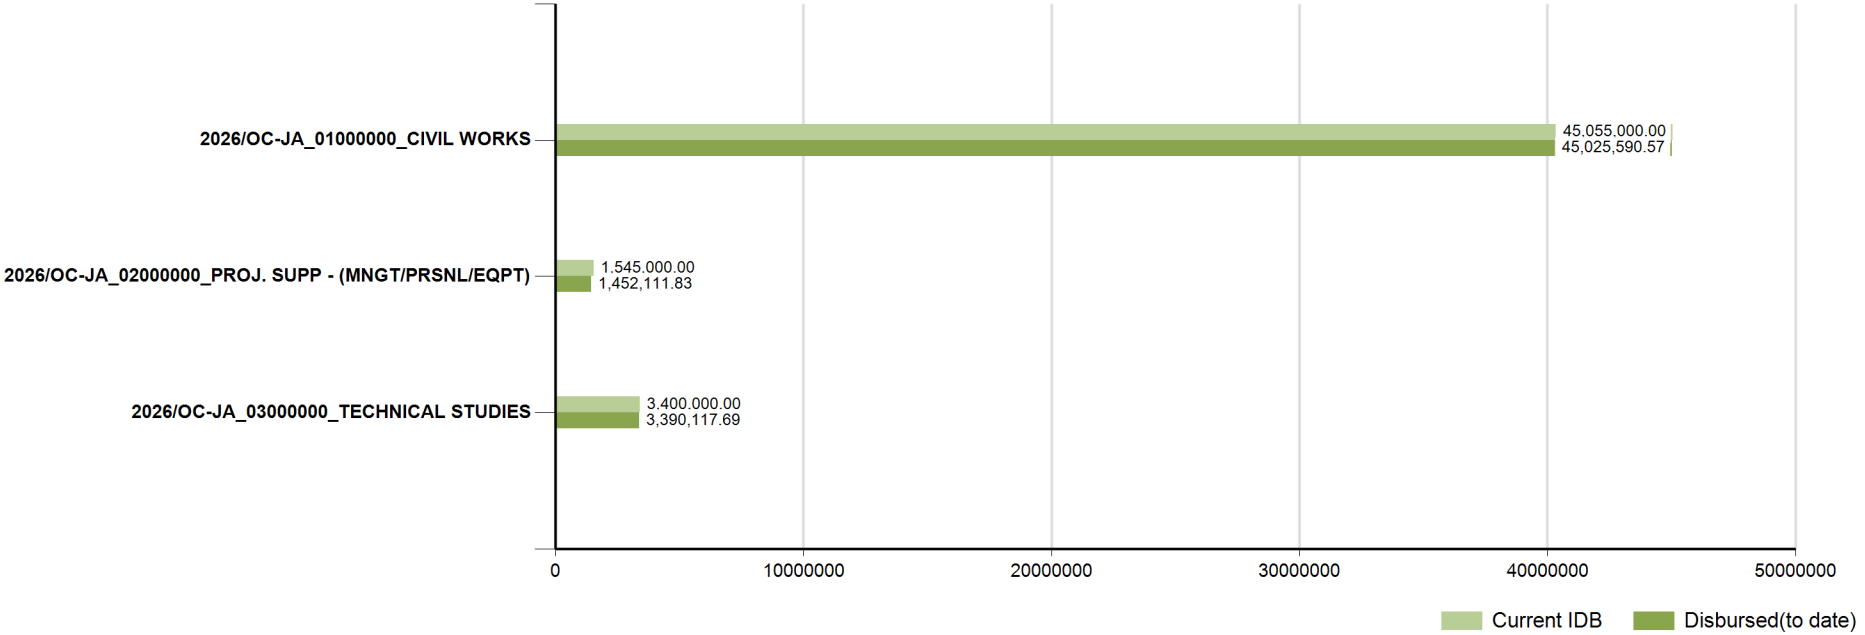

Indicators	Flags*	Unit of Measure	Baseline	Baseline Year	Means of verification	Observations	2009		2010	2011	2012	2013	EOP
2.1 Average Vehicle Operating Cost		Base	100.00	2008	Semi-Annual progress reports		P	100.00	99.00	93.00	87.00	78.00	75.00
							P(a)	100.00	99.00	93.00	87.00	78.00	75.00
							A	100.00	100.00	93.00	87.00	78.00	78.00
2.2 Accidents due to bad roads		Base	100.00	2008	Semi-Annual Progress reports		P	100.00	95.00	90.00	80.00	60.00	50.00
							P(a)	100.00	95.00	90.00	95.00	60.00	50.00
							A	100.00	100.00	90.00	90.00	60.00	60.00

-  RF - Contribution
-  RF - Alignment
-  RF - Strategic Alignment
-  RF - Strategic Alignment during Execution
-  SI - Sector Indicator
-  CI - Country Indicator
-  PG - Pro-Gender
-  PE - Pro-Ethnicity

Outputs: Annual Physical and Financial Progress

1. Civil Works		Physical Progress			Financial Progress		
Outputs	Unit of Measure	2016		EOP	2016		EOP
Length of Road Rehabilitated	Kilometers	P		50.00	P		44,372,700.00
		P(a)	0.00	50.00	P(a)	262,029.37	45,000,000.00
		A	0.00	50.00	A	287,619.97	45,025,590.60
2 Project Implementation Support (US\$2 million)							
3 Technical Studies (US\$ 4 million).		Physical Progress			Financial Progress		
Outputs	Unit of Measure	2016		EOP	2016		EOP
Technical Studies completed	Studies	P		2.00	P		4,000,000.00
		P(a)	0.00	2.00	P(a)		2,868,451.72
		A	0.00	2.00	A	20,553.69	3,390,117.69
Other Cost					2016	Cost	
Project Implementation Support				P		\$1,999,998.00	
				P(a)	\$198,133.17	\$1,600,000.00	
				A	\$50,245.00	\$1,452,111.83	
Total Cost					2016	Total Cost	
				P		\$50,372,698.00	
				P(a)	\$460,162.54	\$49,969,564.00	
				A	\$358,418.66	\$49,867,820.12	

Changes to the Matrix

No information related to this operation.

Please note that the Overall Stage represents the stage of the operation at the time of this report’s publication, which might not necessarily match the stage of the operation during the PMR Cycle to which the report pertains.
