

PMR Operational Report

Operation Number	PE-L1226	Chief of Operations Validation Date	10/01/19
Year- PMR Cycle	First period Jan-Jun 2019	Division Chief Validation Date	
Last Update	09/30/19	Country Representative Validation Date	
PMR Validation Stage	Validated by Chief of Operations		

Basic Data

Operation Profile

Operation Name	Comprehensive Rural Water and Sanitation Program (PIASAR)	Loan Number	4442/OC-PE
Executing Agency	MINISTERIO DE VIVIENDA CONSTRUCCION Y SANEAMIENTO	Sector/Subsector	AS - WATER AND SANITATION
Team Leader	PAEZ RUBIO, TANIA	Overall Stage	Disbursing (From eligibility until all the Operations are closed)
Operation Type	Loan Operation	Country	PERU
Lending Instrument	Investment Loan	Convergence related Operation(s)	
Borrower	REPUBLICA DEL PERU		


Environmental and Social Safeguards

Impacts Category	B	Was/Were the objective(s) of this operation reformulated?	NO
Safeguard Performance Rating		Date of approval	
Safeguard Performance Rating - Rationale			

Financial Data

Item	Total Cost and Source					Available Funds (US\$)			
	Original IDB	Current IDB	Local Counterpart	Co-Financing / Country	Total Original Cost	Current IDB	Disb. Amount to Date	% Disb	Undisbursed Amount
PE-L1226	100,000,000	100,000,000	26,000,000	0	126,000,000	100,000,000	15,110,556	15.11%	84,889,444
Aggregated	100,000,000	100,000,000	26,000,000	0	126,000,000	100,000,000	15,110,556	15.11%	84,889,444

Expense Categories by Loan Contract (cumulative values)

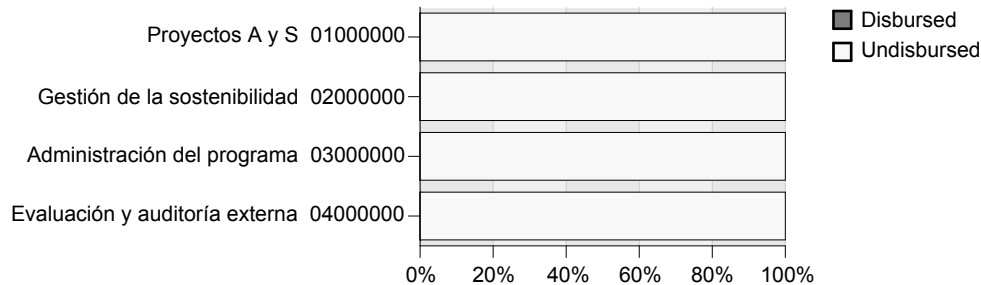

Please note that inactive indicators and outputs are not displayed; totals in the actual cost table may not match the sum of the cost of the outputs displayed, due to the cost of inactive outputs.

PMR Operational Report

RESULTS MATRIX

IMPACTS

No information available for this section

PMR Operational Report

RESULTS MATRIX

OUTCOMES

Outcome Nbr. 0: Resultado 1. Mayor acceso a agua segura en centros poblados rurales

Observation:

Indicator		Unit of Measure	Baseline	Baseline Year		2018	2019	2020	2021	2022	EOP 2022
0.0	Hogares en centros poblados rurales con acceso a agua segura	Hogar	0.00	2017	P	0.00	0.00	0.00	5,000.00	10,000.00	15,000.00
					P(a)	0.00	0.00	0.00	5,000.00	10,000.00	15,000.00
					A	0.00	0.00				
Details											
Pro-Gender		No			Pro-Ethnicity		No				

Outcome Nbr. 1: Resultado 2. Mayor acceso a saneamiento seguro en centros poblados rurales

Observation:

Indicator		Unit of Measure	Baseline	Baseline Year		2018	2019	2020	2021	2022	EOP 2022
1.0	Hogares en centros poblados rurales con acceso a saneamiento seguro	Hogar	0.00	2017	P	0.00	0.00	0.00	5,000.00	10,000.00	15,000.00
					P(a)	0.00	0.00	0.00	5,000.00	10,000.00	15,000.00
					A	0.00	0.00				
Details											
Pro-Gender		No			Pro-Ethnicity		No				

Indicator		Unit of Measure	Baseline	Baseline Year		2018	2019	2020	2021	2022	EOP 2022
1.1	Hogares en centros poblados rurales que utilizan las UBS construidas por el programa	%	0.00	2017	P	0.00	0.00	0.00	60.00	80.00	80.00
					P(a)	0.00	0.00	0.00	60.00	80.00	80.00
					A	0.00	0.00				
Details											
Pro-Gender		No	Pro-Ethnicity		No						

Outcome Nbr. 2: Resultado 3. Prestadores e Instituciones del sector AyS fortalecidas para la gestión sostenible de los sistemas de AyS

Observation:

Indicator		Unit of Measure	Baseline	Baseline Year		2018	2019	2020	2021	2022	EOP 2022
2.0	Sistemas de agua funcionando según especificaciones técnicas de diseño	%	0.00	2017	P	0.00	0.00	0.00	90.00	90.00	90.00
					P(a)	0.00	0.00	0.00	90.00	90.00	90.00
					A	0.00	0.00				

PMR Operational Report

RESULTS MATRIX

OUTCOMES

Details											
Means of verification: Informe de firma consultora para el fortalecimiento de la sostenibilidad a partir del reporte de operación de las JASS											
Observations: Se incluyen sólo los sistemas del Programa											
Pro-Gender		No			Pro-Ethnicity			No			
Indicator		Unit of Measure	Baseline	Baseline Year		2018	2019	2020	2021	2022	EOP 2022
2.1	JASS cuyos ingresos operativos cubren los costos de AOM	%	0.00	2017	P	0.00	0.00	0.00	70.00	90.00	90.00
					P(a)	0.00	0.00	0.00	70.00	90.00	90.00
					A	0.00	0.00				
Details											
Means of verification: Informes financieros de las JASS											
Observations: Sobre el total de JASS del Programa.											
Pro-Gender		No			Pro-Ethnicity			No			
Indicator		Unit of Measure	Baseline	Baseline Year		2018	2019	2020	2021	2022	EOP 2022
2.2	Sistemas rurales construidos por el programa con seguimiento anual de indicadores de prestación por parte del MVCS	%	0.00	2017	P	0.00	0.00	0.00	80.00	80.00	80.00
					P(a)	0.00	0.00	0.00	80.00	80.00	80.00
					A	0.00	0.00				
Details											
Pro-Gender		No			Pro-Ethnicity			No			
Indicator		Unit of Measure	Baseline	Baseline Year		2018	2019	2020	2021	2022	EOP 2022
2.3	JASS con al menos dos mujeres en su Consejo Directivo	%	0.00	2017	P	0.00	0.00	0.00	0.00	50.00	50.00
					P(a)	0.00	0.00	0.00	0.00	50.00	50.00
					A	0.00	0.00				
Details											
Means of verification: Actas de conformación de las JASS											
Observations: Sobre el total de las JASS que se conformen durante la ejecución del Programa.											
Pro-Gender		No			Pro-Ethnicity			No			
Indicator		Unit of Measure	Baseline	Baseline Year		2018	2019	2020	2021	2022	EOP 2022
2.4	Núcleos Ejecutores con al menos una mujer en su	%	0.00	2017	P	0.00	25.00	60.00			60.00

PMR Operational Report

RESULTS MATRIX

OUTCOMES

2.4	estructura organizativa	%	0.00	2017	P(a)	0.00	25.00	60.00			60.00
					A	0.00	0.00				
Details											
Means of verification: Actas de conformación de los Núcleos Ejecutores											
Observations: Sobre el total de los Núcleos Ejecutores del Programa.											
Pro-Gender		No			Pro-Ethnicity		No				

RESULTS MATRIX

OUTPUTS: ANNUAL PHYSICAL AND FINANCIAL PROGRESS

Component Nbr. 1 Componente I: Proyectos de Agua Potable y Saneamiento

	Output	Unit of Measure		PHYSICAL PROGRESS		FINANCIAL PROGRESS	
				2019	EOP 2022	2019	EOP 2022
1.1	Estudios definitivos de proyectos de AyS actualizados	Estudios	P	80	100	179,373.6	1,596,808
			P(a)	80	100	179,373.6	1,596,808
			A	42	42	0	0
1.2	Sistemas de agua potable en entros poblados rurales construidos o mejorados	Sistemas	P	25	100	7,728,618.6	43,204,617
			P(a)	25	100	7,728,618.6	43,204,617
			A	0	0	0	0
1.3	Unidades Básicas Sanitarias (UBS) en centros poblados rurales construidas	UBS	P	1,825	10,000	10,942,296.6	61,924,291.8
			P(a)	1,825	10,000	10,942,296.6	61,924,291.8
			A	0	0	0	0
1.4	JASS capacitadas para administrar, operar y mantener los servicios de AyS durante la operación asistida en la gestión del servicio	JAAS	P	20	100	254,166	1,510,386
			P(a)	20	100	254,166	1,510,386
			A	0	0	0	0
1.5	ATM capacitadas para brindar asistencia técnica a las JASS durante la operación asistida en la gestión del servicio	ATM	P	20	62	173,904	1,006,924
			P(a)	20	62	173,904	1,006,924
			A	0	0	0	0
1.6	Personas capacitadas en educación sanitaria y ambiental y uso de los servicios de AyS	Personas	P	3,000	15,000	300,000	4,776,757
			P(a)	3,000	15,000	300,000	4,776,757
			A	0	0	0	0
1.7	Núcleos Ejecutores capacitados en gestión y administración de proyectos	Núcleos Ejecutores	P	14	30	80,262.6	455,801
			P(a)	14	30	80,262.6	455,801
			A	0	0	0	0

RESULTS MATRIX

OUTPUTS: ANNUAL PHYSICAL AND FINANCIAL PROGRESS

Component Nbr. 2 Componente II: Gestión de la Sostenibilidad de los Servicios y Fortalecimiento de las Entidades del Sector

	Output	Unit of Measure		PHYSICAL PROGRESS		FINANCIAL PROGRESS	
				2019	EOP 2022	2019	EOP 2022
2.1	JASS equipadas para la adecuada AOM	JASS	P	0	100	38,813.6	492,691
			P(a)	0	100	38,813.6	492,691
			A	0	0	0	0
2.2	ATMs fortalecidas para brindar asistencia técnica a las JASS	ATM	P	0	62	115,409.6	1,454,300
			P(a)	0	62	115,409.6	1,454,300
			A	0	0	0	0
2.3	DRVCS fortalecidas para brindar asistencia técnica a las ATMs	Institución	P	0	9	12,895.2	350,858.2
			P(a)	0	9	12,895.2	350,858.2
			A	0	0	0	0
2.4	PNSR fortalecido para brindar asistencia técnica a las DRVCS y ATMs	Institución	P	0	1	0	303,660
			P(a)	0	1	0	303,660
			A	0	0	0	0
2.5	Personal del PNSR capacitado para brindar asistencia técnica a las ATMs y las DRVCS	Personas	P	0	85	0	539,839
			P(a)	0	85	0	539,839
			A	0	0	0	0
2.6	Sistemas de agua potable con operación técnica asistida concluida	Sistemas	P	0	100	27,860	788,319
			P(a)	0	100	27,860	788,319
			A	0	0	0	0
2.7	Sistemas de agua potable con reforzamiento de la AOM post construcción	Sistemas	P	0	80	57,336	2,000,000
			P(a)	0	80	57,336	2,000,000
			A	0	0	0	0
2.8	Diseño e implementación del plan de comunicación del programa	Plan	P	0	1	14,817.6	345,076
			P(a)	0	1	14,817.6	345,076
			A	0	0	0	0

Other Cost

	Seguimiento, Evaluación, Auditoria	P			39,969	627,797
		P(a)			39,969	627,797
		A			0	0
	Administración del Programa	P			1,246,876	4,621,875
		P(a)			1,246,876	4,621,875
		A			416,964	497,267

Total Cost

	Total Cost	P			21,212,598.4	126,000,000
		P(a)			21,212,598.4	126,000,000
		A			416,964	497,267

CHANGES TO THE MATRIX

No information available for this section

PMR Operational Report

IMPLEMENTATION STATUS AND LEARNING

Lesson Learned - Categories
