

PMR Operational Report

Operation Number	UR-L1149	Chief of Operations Validation Date	04/02/20
Year- PMR Cycle	Second period Jan-Dec 2019	Division Chief Validation Date	04/02/20
Last Update	03/23/20	Country Representative Validation Date	04/03/20
PMR Validation Stage	Validated by Representative		

Basic Data

Operation Profile

Operation Name	Ciudad del Plata Sanitation Program, Stage I	Loan Number	4642/OC-UR
Executing Agency	OFICINA DE PLANEAMIENTO Y PRESUPUESTO DE LA PRESIDENCIA DE LA REPUBLICA	Sector/Subsector	AS-SAU - WATER AND SANITATION-SANITATION URBAN
Team Leader	BASANI, MARCELLO	Overall Stage	Disbursing (From eligibility until all the Operations are closed)
Operation Type	Loan Operation	Country	Uruguay
Lending Instrument	Investment Loan	Convergence related Operation(s)	
Borrower	REPUBLICA ORIENTAL DE URUGUAY		


Environmental and Social Safeguards

Impacts Category	B	Was/Were the objective(s) of this operation reformulated?	NO
Safeguard Performance Rating		Date of approval	
Safeguard Performance Rating - Rationale			

Financial Data

Item	Total Cost and Source					Available Funds (US\$)			
	Original IDB	Current IDB	Local Counterpart	Co-Financing / Country	Total Original Cost	Current IDB	Disb. Amount to Date	% Disb	Undisbursed Amount
UR-L1149	20,000,000	20,000,000	0	0	20,000,000	20,000,000	1,000,000	5.00%	19,000,000
Aggregated	20,000,000	20,000,000	0	0	20,000,000	20,000,000	1,000,000	5.00%	19,000,000

Expense Categories by Loan Contract (cumulative values)

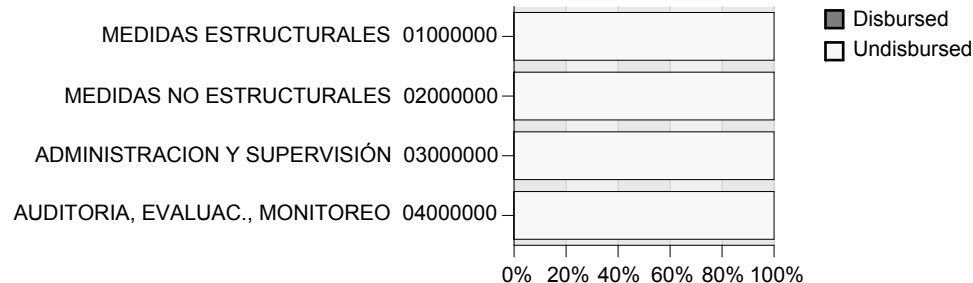

PMR Operational Report

RESULTS MATRIX

IMPACTS

No information available for this section

PMR Operational Report

RESULTS MATRIX

OUTCOMES

Outcome Nbr. 1: Hogares con aguas residuales tratadas en el área de influencia del proyecto

Observation:

Indicator		Unit of Measure	Baseline	Baseline Year		2019	2020	2021	2022	2023	2024	EOP 2024
1.1	Nuevos hogares cuyas aguas residuales son tratadas en la Planta de ciudad del Plata en el área de intervención del proyecto	Número de hogares	0.00	2018	P			348.00	697.00	738.00		1,783.00
					P(a)			348.00	697.00	738.00		1,783.00
					A							
Details												
Pro-Gender		No			Pro-Ethnicity		No					

Outcome Nbr. 2: Hogares con conexión habilitada a redes de saneamiento en el área de influencia del proyecto

Observation:

Indicator		Unit of Measure	Baseline	Baseline Year		2019	2020	2021	2022	2023	2024	EOP 2024
2.1	Porcentaje de hogares con conexión habilitada a redes de saneamiento en el área de intervención del proyecto	% de hogares	0.00	2018	P			29.00	33.00	38.00		60.00
					P(a)			29.00	33.00	38.00		60.00
					A							
Details												
Pro-Gender		No			Pro-Ethnicity		No					

Outcome Nbr. 3: Hogares con acceso a redes de saneamiento en el área de influencia del proyecto

Observation:

Indicator		Unit of Measure	Baseline	Baseline Year		2019	2020	2021	2022	2023	2024	EOP 2024
3.1	Nuevos hogares con acceso a la red de saneamiento en el área de intervención del proyecto	Número de hogares	0.00	2018	P		600.00	390.00	1,500.00	500.00		2,990.00
					P(a)		600.00	390.00	1,500.00	500.00		2,990.00
					A							
Details												
Pro-Gender		No			Pro-Ethnicity		No					

Outcome Nbr. 4: Mejora en la capacidad de tratamiento de la planta de aguas residuales de Ciudad del Plata

Observation:

Indicator		Unit of Measure	Baseline	Baseline Year		2019	2020	2021	2022	2023	2024	EOP 2024
4.1	DBO5 removido en la planta de tratamiento de Ciudad del Plata	KgDBO /día	82.00	2018	P					337.00		337.00

PMR Operational Report

RESULTS MATRIX

OUTCOMES

4.1	DBO5 removido en la planta de tratamiento de Ciudad del Plata	KgDBO /dia	82.00	2018	P(a)					337.00		337.00
					A							
Details												
Pro-Gender		No		Pro-Ethnicity		No						

Outcome Nbr. 5: Mejora de las familias con jefas de hogar al acceso a los servicios de saneamiento

Observation:

Indicator		Unit of Measure	Baseline	Baseline Year		2019	2020	2021	2022	2023	2024	EOP 2024
5.1	Porcentaje de subsidios entregados a jefas de hogar	%	0.00	2018	P			15.00	15.00	20.00		50.00
					P(a)			15.00	15.00	20.00		50.00
					A							
Details												
Pro-Gender		No		Pro-Ethnicity		No						

RESULTS MATRIX

OUTPUTS: ANNUAL PHYSICAL AND FINANCIAL PROGRESS

Component Nbr. 1 Componente I. Medidas estructurales

	Output	Unit of Measure		PHYSICAL PROGRESS		FINANCIAL PROGRESS	
				2019	EOP 2024	2019	EOP 2024
1.1	Proyectos ejecutivos finalizados	Proyectos ejecutivos	P	0	2	50,000	500,000
			P(a)	0	2	50,000	500,000
			A	0	0	0	0
1.2	Sistema de saneamiento construido y operando	Sistema	P	0	1	499,348	16,200,000
			P(a)	0	1	499,348	16,200,000
			A	0	0	403,676	403,676

Component Nbr. 2 Componente II. Medidas no estructurales

	Output	Unit of Measure		PHYSICAL PROGRESS		FINANCIAL PROGRESS	
				2019	EOP 2024	2019	EOP 2024
2.1	Plan de conexiones ejecutado	Plan	P	0	1	58,065	2,000,000
			P(a)	0	1	58,065	2,000,000
			A	0	0	0	0

Other Cost

	Administración del Programa	P			89,906	724,840
		P(a)			89,906	724,840
		A			0	0
	Supervisión de obras	P			35,032	175,160
		P(a)			35,032	175,160
		A			0	0
	Auditoría externa	P				25,000
		P(a)				25,000
		A			0	0
	Evaluación y monitoreo	P				375,000
		P(a)				375,000
		A			0	0

Total Cost

	Total Cost	P			732,351	20,000,000
		P(a)			732,351	20,000,000
		A			403,676	403,676

CHANGES TO THE MATRIX

No information available for this section

IMPLEMENTATION STATUS AND LEARNING

No information available for this section
