


PMR Public Report

Operation Number	BR-L1445	Chief of Operations Validation Date	10/18/22
Year- PMR Cycle	First period Jan-Jun 2022	Division Chief Validation Date	
Last Update	09/30/22	Country Representative Validation Date	
PMR Validation Stage	Validated by Chief of Operations		
Basic Data			
Operation Profile			
Operation Name	Maracanaú Transportation and Urban Logistics Program	Loan Number	4445/OC-BR
Executing Agency	PREFEITURA DE MARACANAÚ	Sector/Subsector	TRANSPORT-URBAN TRANSPORT INFRASTRUCTURE
Team Leader	TORRES GRACIA, DANIEL	Overall Stage	Disbursing (From eligibility until all the Operations are closed)
Operation Type	Loan Operation	Country	Brazil
Lending Instrument	Investment Loan	Convergence related Operation(s)	
Borrower	PREFEITURA DE MARACANAÚ		
Environmental and Social Safeguards			
Impacts Category	B	Was/Were the objective(s) of this operation reformulated?	NO
Safeguard Performance Rating	Satisfactory	Date of approval	
Safeguard Performance Rating - Rationale	Durante a missão, foi possível evidenciar que a Agência Executora está cumprindo as diretrizes das políticas ambientais e sociais do BID, tendo apresentado evidências de cumprimento através da implementação do PGAS. O quadro técnico da UCP é adequado e capacitado para desenvolvimento das atividades e ainda conta com equipe de supervisão de obras para apoio aos processos de licenciamento, monitoramento e produção de relatórios mensais relativos aos controles dos programas de obras. Com relação a questões específicas sociais, a UCP possui plano de comunicação, que permanece sendo adequadamente implementado, mantém o MQR ativo e funcionando com celeridade no atendimento à população.		

Financial Data									
	Total Cost and Source					Available Funds (US\$)			
Operations	Original IDB	Current IDB	Local Counterpart	Co-Financing / Country	Total Original Cost	Current IDB	Disb. Amount to Date	% Disbursed	Undisbursed Amount
BR-L1445	31,784,500	31,784,500	31,784,500	0	63,569,000	31,784,500	14,200,000	44.68%	17,584,500
Aggregated	31,784,500	31,784,500	31,784,500	0	63,569,000	31,784,500	14,200,000	44.68%	17,584,500

Expense Categories by Loan Contract (cumulative values)

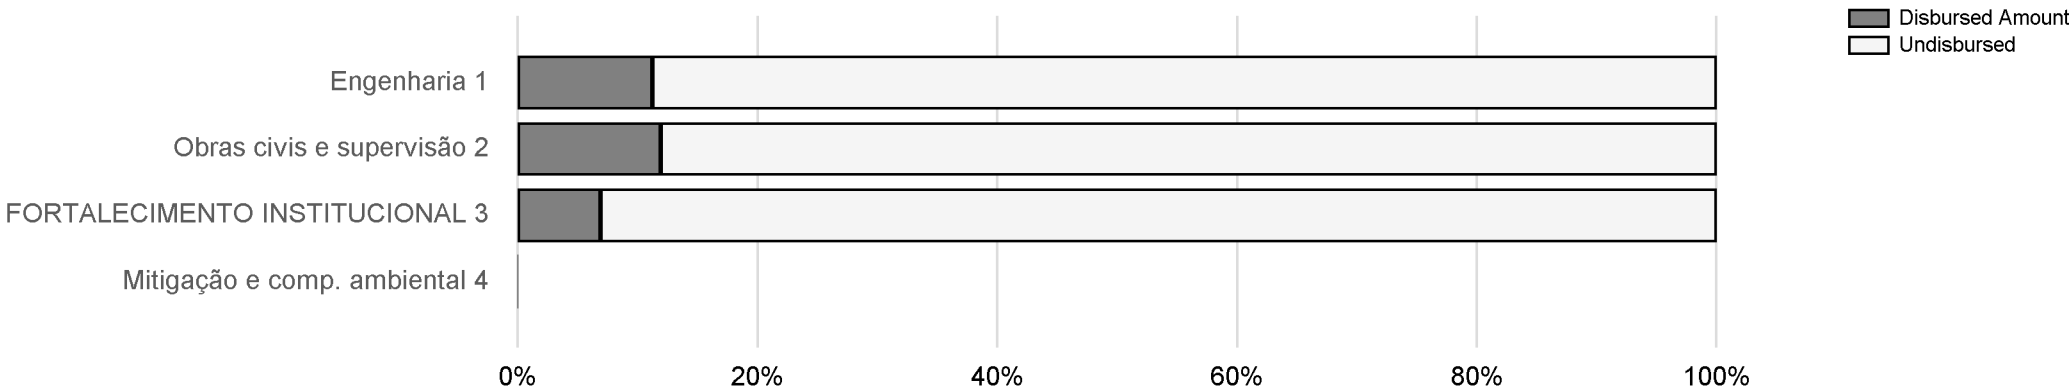

Please note that inactive indicators and outputs are not displayed; totals in the actual cost table may not match the sum of the cost of the outputs displayed, due to the cost of inactive outputs.

RESULTS MATRIX
General Development Objectives

RESULTS MATRIX

Specific Development Objectives

Specific Development Objectives Nbr. 0: Tempo médio de viagem reduzido

Observation:

	Indicator	Unit of Measure	Baseline	Baseline Year		2023	EOP 2023
0.0	Tempo médio de viagem dos veículos particulares	Minutos	15.9	2017	P	9.3	9.3
					A	-	-

Details

Means of Verification: Pesquisa de campo. Relatório Semestral de Progresso - UGP.

Observations:

Evaluation Methodology: -

Pro-Gender	No	Pro-Ethnicity	No	CRF indicator	

	Indicator	Unit of Measure	Baseline	Baseline Year		2023	EOP 2023
0.1	Tempo médio de viagem dos ônibus	Minutos	28.7	2017	P	16.4	16.4
					A	-	-

Details

Means of Verification: Pesquisa de campo. Relatório Semestral de Progresso - UGP.

Observations:

Evaluation Methodology: -

Pro-Gender	No	Pro-Ethnicity	No	CRF indicator	

	Indicator	Unit of Measure	Baseline	Baseline Year		2023	EOP 2023
0.2	Tempo médio de viagem dos caminhões	Minutos	20.7	2017	P	12	12
					A	-	-

Details

Means of Verification: Pesquisa de campo. Relatório Semestral de Progresso - UGP.

Observations:

Evaluation Methodology: -

Pro-Gender	No	Pro-Ethnicity	No	CRF indicator	

Specific Development Objectives Nbr. 1: Velocidade média do transporte coletivo na Avenida Manoel Moreira Lima aumentada

Observation:										
	Indicator			Unit of Measure	Baseline	Baseline Year		2023	EOP 2023	
1.0	Tempo médio de viagem do transporte público coletivo na Avenida Manoel Moreira Lima (corredor de ônibus)			Minutos	19.9	2016		P	8.6	8.6
								A	-	-
Details										
Means of Verification: Pesquisa de campo. Relatório Semestral de Progresso - UGP.										
Observations:										
Evaluation Methodology: -										
Pro-Gender	No	Pro-Ethnicity	No	CRF indicator						

Specific Development Objectives Nbr. 2: Emissão de CO2 reduzida

Observation:

	Indicator	Unit of Measure	Baseline	Baseline Year		2023	EOP 2023
2.0	Emissão média de CO2	Ton	6210	2017	P	5,387	5,387
					A	-	-
Details							

Means of Verification: Relatório de Encerramento do Projeto (PCR) - UGP.

Observations:

Evaluation Methodology: -

Pro-Gender	No	Pro-Ethnicity	No	CRF indicator			

Specific Development Objectives Nbr. 3: Custo operacional reduzido

Observation:

	Indicator	Unit of Measure	Baseline	Baseline Year		2023	EOP 2023
3.0	Custo operacional dos veículos de passeio em Maracanaú	US\$ milhões	375.9	2017	P	335.4	335.4
					A	-	-
Details							

Means of Verification: Relatório de avaliação econômica ex-ante e ex-post. Relatório de Encerramento do Projeto - PCR.

Observations:

Evaluation Methodology: -

Pro-Gender	No	Pro-Ethnicity	No	CRF indicator			

RESULTS MATRIX

OUTPUTS: ANNUAL PHYSICAL AND FINANCIAL PROGRESS

Component Nbr. 1 Engenharia

				PHYSICAL PROGRESS		FINANCIAL PROGRESS	
	Output	Unit of Measure		2022	EOP 2023	2022	EOP 2023
1.01	Projetos de engenharia de detalhe das vias principais elaborados	Projetos	P	-	6	600,000	2,320,000
			P (a)	-	8	92,366.39	2,320,000
			A	-	8	-	280,047.52
1.02	Projeto da obra de implantação do corredor de ônibus elaborado	Projetos	P	-	1	-	180,000
			P (a)	-	1	-	180,000
			A	-	-	-	-

Component Nbr. 2 Obras Civas

				PHYSICAL PROGRESS		FINANCIAL PROGRESS	
	Output	Unit of Measure		2022	EOP 2023	2022	EOP 2023
2.01	Vias pavimentadas	km	P	10	30	3,627,503	13,969,000
			P (a)	15	30	4,735,454.43	13,969,000
			A	-	-	-	-
2.02	Vias duplicadas	km	P	8.75	18.75	13,125,000	28,100,000
			P (a)	3.1	9.7	5,243,498	28,099,999.37
			A	-	-	-	4,806,592
2.03	Vias reabilitadas	km	P	2	4.5	1,000,000	2,500,000
			P (a)	1.9	1.9	3,464,933.96	3,924,316.88
			A	-	-	-	459,382.92
2.04	Via de transporte coletivo implantada	km	P	1.15	3.15	2,500,000	6,500,000
			P (a)	-	3.15	-	6,500,000
			A	-	-	-	-

Component Nbr. 3 Fortalecimento institucional

				PHYSICAL PROGRESS		FINANCIAL PROGRESS	
	Output	Unit of Measure		2022	EOP 2023	2022	EOP 2023
3.01	Unidades operacionais de transporte fortalecidas	Unidade Operacional	P	1	3	138,158	552,632
			P (a)	-	3	184,210.66	552,632
			A	-	-	-	-
3.02	Plano logístico e de cargas do município elaborado	Plano	P	-	1	-	550,000
			P (a)	1	1	220,703.25	340,968.81
			A	-	-	-	120,265.56
3.03	Plano de mobilidade urbana atualizado	Plano	P	-	1	-	550,000
			P (a)	1	1	220,703.25	340,968.82
			A	-	-	-	120,265.57
3.04	Plano de ação para o desenvolvimento de uma economia de de baixo carbono elaborado	Plano	P	-	1	-	552,632
			P (a)	-	1	150,267.52	207,110.63
			A	-	-	-	-
3.05	Plano municipal para a redução dos riscos de mudanças climáticas elaborado	Plano	P	-	1	-	552,632
			P (a)	-	1	150,267.52	207,110.63
			A	-	-	-	-
3.06	Plano estratégico para a promoção de ações fiscais com o objetivo de atrair novas empresas elaborado	Plano	P	1	1	200,000	400,000
			P (a)	-	1	133,333.34	400,000
			A	-	-	-	-
3.07	Medição sobre a percepção de segurança e conforto das mulheres no transporte público	Medição	P	-	1	171,052	342,104
			P (a)	-	1	175,023.51	342,104
			A	-	-	-	-

Other Cost				
	Supervisão de Obras	P	1,125,000	2,500,000
		P (a)	962,073.4	2,500,000
		A	0	483,995.38
	Ações de mitigação ambiental	P	400,000	1,000,000
		P (a)	300,000	1,000,000
		A	0	0
	Administração do Programa	P	598,000	2,750,000
		P (a)	590,269.86	2,749,703.04
		A	0	1,541,182.51
	Auditoria	P	62,500	250,000

	Auditoria	P (a)	41,595.18	249,260
		A	0	42,506.02
Total Cost				
	Total Cost	P	23,547,213	63,569,000
		P (a)	16,664,700.27	63,883,174.18
		A	0	7,854,237.48

No information available for this section

RISKS AND PLANNED RESPONSES

Risk ID	Risk Status		Risk Taxonomy
3	Active		Natural Environment
	Response Actions		
	3.1	Management Strategy	Status
		MITIGATE	ACTIVE

Risk ID	Risk Status		Risk Taxonomy
6	Inactive		Planning
	Response Actions		
	6.0	Management Strategy	Status
		-	

Risk ID	Risk Status		Risk Taxonomy
9	Inactive		Economic and Financial Environment
	Response Actions		
	9.0	Management Strategy	Status
		-	

Risk ID	Risk Status		Risk Taxonomy
12	Active		Economic and Financial Environment
	Response Actions		
	12.1	Management Strategy	Status
		ACCEPT	ACTIVE

Risk ID	Risk Status		Risk Taxonomy
15	Active		Organizational Structure
	Response Actions		
	15.0	Management Strategy	Status
		-	

Risk ID	Risk Status		Risk Taxonomy
18	Active		Technical Design
	Response Actions		
	18.1	Management Strategy	Status
		MITIGATE	ACTIVE

Risk ID	Risk Status		Risk Taxonomy
20	Active		Planning
	Response Actions		
	20.1	Management Strategy	Status
		MITIGATE	ACTIVE

IMPLEMENTATION STATUS AND LEARNING

Lesson Learned - Categories
Project Management Capacity
Others - Dimensions Related to Public Processes/ Actors
Project Monitoring & Evaluation
