


PMR Public Report

Operation Number	BR-L1117	Chief of Operations Validation Date	10/18/22
Year- PMR Cycle	First period Jan-Jun 2022	Division Chief Validation Date	
Last Update	09/28/22	Country Representative Validation Date	
PMR Validation Stage	Validated by Chief of Operations		
Basic Data			
Operation Profile			
Operation Name	HISTORIC CENTER REVITALIZATION PROGRAM FOR THE MUNICÍPIO OF SÃO LUÍS	Loan Number	2715/OC-BR
Executing Agency	PREFEITURA MUNICIPAL DE SAO LUIS	Sector/Subsector	URBAN DEVELOPMENT AND HOUSING-NEIGHBORHOOD UPGRADING
Team Leader	TRIBOILLARD, CLEMENTINE CLAIRE DOMINIQUE	Overall Stage	Disbursing (From eligibility until all the Operations are closed)
Operation Type	Loan Operation	Country	Brazil
Lending Instrument	Investment Loan	Convergence related Operation(s)	
Borrower	PREFEITURA MUNICIPAL DE SAO LUIS		
Environmental and Social Safeguards			
Impacts Category	B	Was/Were the objective(s) of this operation reformulated?	NO
Safeguard Performance Rating	Partially Satisfactory	Date of approval	
Safeguard Performance Rating - Rationale	Desde a missão passada, a Agência Executora tem demonstrado avanço no cumprimento de requisitos de salvaguardas ambientais e sociais e engajamento com partes afetadas. No entanto, as obras de pavimentação do Terminal Fonte do Bispo, que seguem paralisadas, ainda não tiveram solução definida, trazendo riscos à segurança comunitária. Além disso, o Programa ainda não concluiu a aplicação de todas as medidas compensatórias previstas, pois aguarda a finalização de obras para a entrega de 58 quiosques e 75 triciclos a permissionários locais. O atraso na implementação da solução tem impactado a relação com os permissionários e traz alerta relativo à conclusão das compensações dentro do prazo contratual. . Para monitorar o avanço nas trataivas visando à resolução dos entraves, oPrograma tem sido monitorado com reuniões mensais de ponto de controle para acompanhamento das soluções e finalização das medidas compensatórias.		

Financial Data									
	Total Cost and Source					Available Funds (US\$)			
Operations	Original IDB	Current IDB	Local Counterpart	Co-Financing / Country	Total Original Cost	Current IDB	Disb. Amount to Date	% Disbursed	Undisbursed Amount
BR-L1117	13,590,000	13,590,000	13,590,000	0	27,180,000	13,590,000	12,533,346.06	92.22%	1,056,653.94
Aggregated	13,590,000	13,590,000	13,590,000	0	27,180,000	13,590,000	12,533,346.06	92.22%	1,056,653.94
Expense Categories by Loan Contract (cumulative values)									

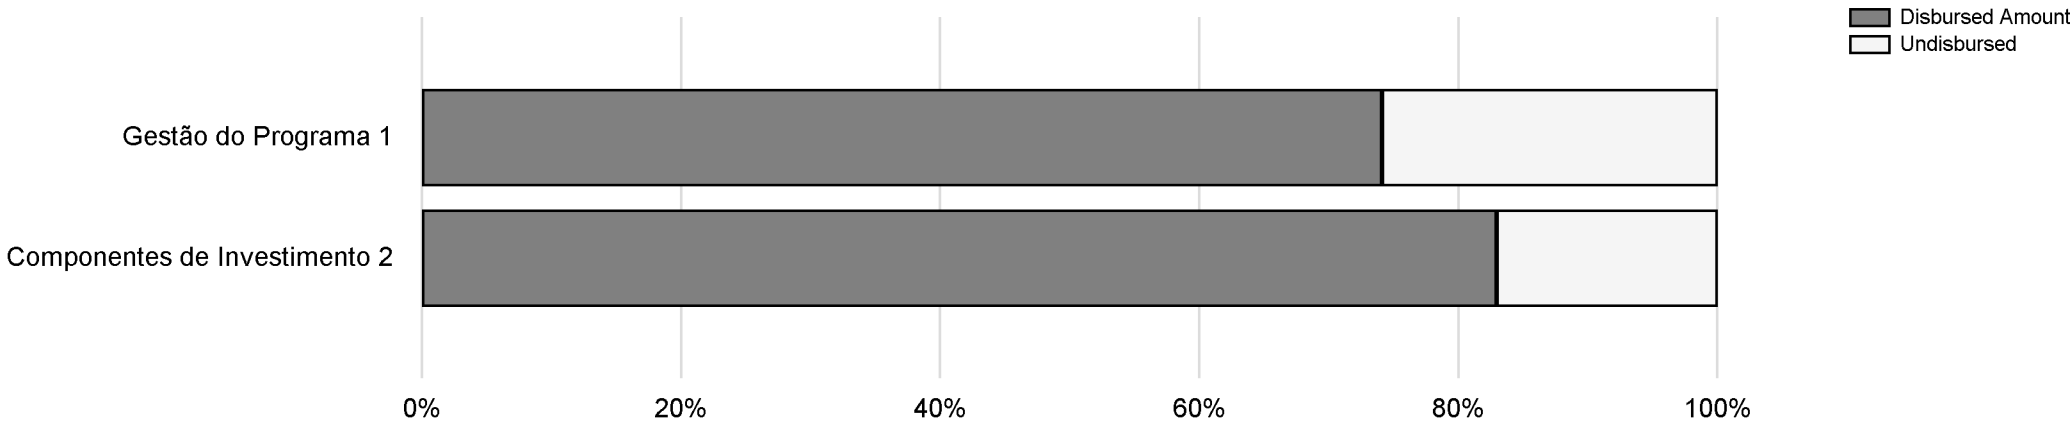

Please note that inactive indicators and outputs are not displayed; totals in the actual cost table may not match the sum of the cost of the outputs displayed, due to the cost of inactive outputs.

RESULTS MATRIX

General Development Objectives

General Development Objectives Nbr. 1: Valorización de la propiedad inmobiliaria

Observation:

Indicator		Unit of Measure	Baseline	Baseline Year	Expected Year of Achievement	EOP 2022	
1.1	Valorização imobiliária no Centro Histórico de São Luís - CHSL	R\$/m2	848	2012	2022	P	779
						A	-

Details

Means of Verification: Encuesta realizada por la UGP con las firmas inmobiliarias sobre inmuebles en venta.

Observations: Fuente: Encuesta realizada por la UGP con las firmas inmobiliarias sobre inmuebles en venta.

The General Development Objective indicator target is expected to be observed by the operation's "Fully Justified" date in Convergence (CO): No

Pro-Gender	No	Pro-Ethnicity	No	CRF indicator	

RESULTS MATRIX

Specific Development Objectives

Specific Development Objectives Nbr. 0: Aumento do número de empresas registradas no CHSL

Observation:

	Indicator	Unit of Measure	Baseline	Baseline Year		2013	2014	2015	2016	2020	2021	2022	EOP 2022
0.1	Número de empresas registradas (alvará emitido) pela PMSL no CHSL.	Empresas	4790	2012	P	-	-	75	-	-	-	-	75
					A	-	-	-	-	-	-	-	75

Details

Means of Verification: Datos informados por la SEMFAZ y SEPLAN obre la base de encuesta anual específica y datos administrativos

Observations: Fuente: Datos informados por la SEMFAZ y SEPLAN obre la base de encuesta anual específica y datos administrativos

Evaluation Methodology: -

Pro-Gender	No	Pro-Ethnicity	No	CRF indicator	

Specific Development Objectives Nbr. 1: Aumento do número de visitantes aos centros culturais do CHSL

Observation:

	Indicator	Unit of Measure	Baseline	Baseline Year		2013	2014	2015	2016	2020	2021	2022	EOP 2022
1.1	Número de visitantes anuais nos centros culturais estabelecidos no CHSL	Visitantes	44000	2012	P	-	-	50,000	-	-	-	-	50,000
					A	-	-	-	-	-	-	-	-

Details

Means of Verification: Informaciones suministradas por la SETUR y FUMPH sobre la base de datos informados por los establecimientos turísticos en la ciudad y otras fuentes secundarias

Observations: Fuente: Informaciones suministradas por la SETUR y FUMPH sobre la base de datos informados por los establecimientos turísticos en la ciudad y otras fuentes secundarias

Evaluation Methodology: -

Pro-Gender	No	Pro-Ethnicity	No	CRF indicator	

Specific Development Objectives Nbr. 2: Redução do número de moradores cadastrados em habitações precárias no CHSL

Observation:

	Indicator	Unit of Measure	Baseline	Baseline Year		2013	2014	2015	2016	2020	2021	2022	EOP 2022
2.0	Famílias vulneráveis reassentadas no CHSL	Famílias	0	2019	P	-	-	-	-	-	-	-	-
					A	-	-	-	-	-	-	-	-

Details

Means of Verification: Relatório produzido pelo Executor

Observations:

Evaluation Methodology: -

Pro-Gender	No	Pro-Ethnicity	No	CRF indicator	

Specific Development Objectives Nbr. 3: Fortalecimento Institucional do Município de São Luís

Observation:

	Indicator	Unit of Measure	Baseline	Baseline Year		2013	2014	2015	2016	2020	2021	2022	EOP 2022
3.0	Agências Governamentais Capacitadas	Agências	0	2017	P	-	-	-	-	-	-	-	-
					A	-	-	-	-	-	-	-	-

Details

Means of Verification: Relatório Semestral de Progresso

Observations:

Evaluation Methodology: -

Pro-Gender	No	Pro-Ethnicity	No	CRF indicator	

RESULTS MATRIX

OUTPUTS: ANNUAL PHYSICAL AND FINANCIAL PROGRESS

Component Nbr. 1 Proyectos estratégicos

				PHYSICAL PROGRESS		FINANCIAL PROGRESS	
	Output	Unit of Measure		2022	EOP 2022	2022	EOP 2022
1.01	Parque do Bom Menino e entorno requalificado	Obra	P	-	1	-	937,500
			P (a)	-	1	260,327.38	4,125,519.32
			A	-	1	-	3,865,191.94
1.02	Drenagem do Canal do Portinho concluída	Metros	P	-	3,500	-	1,978,125
			P (a)	-	3,500	-	1,703,840.42
			A	-	2,967	-	1,703,840.42
1.03	Edifício para funcionamento do Cine Teatro Municipal Roxy reabilitado	Obra	P	-	1	-	468,750
			P (a)	-	1	-	369,408.09
			A	-	1	-	369,408.09
1.04	Gerenciamento completo e continuado do parque de iluminação pública do Centro Histórico	Unidade	P	-	1	-	468,750
			P (a)	-	1	1,007,039.19	1,007,039.19
			A	-	1	-	-
1.05	Edifícios da Rua Portugal, 285 e 251 reabilitados	Obras	P	-	1	-	1,250,000
			P (a)	1	2	493,957.24	1,171,351.46
			A	-	1	126,162.83	803,557.05
1.06	Projetos Executivos e Estudos Ambientais	Unidade	P	-	8	-	650,000
			P (a)	1	6	82,105.06	764,105.5
			A	-	5	-	682,000.44
1.07	Obras de Contrapartida - UFMA	Obra	P	-	6	-	8,235,687.86
			P (a)	-	5	-	4,621,214.55
			A	-	4	-	4,621,214.55
1.08	Obras de requalificação da Praça da Saudade, Praça da Misericórdia e Entorno	Obras	P	-	-	-	-
			P (a)	-	3	-	1,837,409.21
			A	-	3	-	1,837,409.21
1.09	Obra de Requalificação da área do Terminal da Fonte do Bispo	Obra	P	-	-	-	-
			P (a)	1	2	1,848,640.4	5,346,678.6
			A	-	1	-	3,498,038.2
1.10	Urbanização do acoradouro das ruas Vila Gorete e Veleiros	Obras	P	-	-	-	-
			P (a)	-	1	-	4,746,302.2
			A	-	1	-	4,746,302.2
1.11	Obras de acessibilidade para áreas de tombamento federal	Obra	P	-	-	-	-
			P (a)	-	1	93,911.94	315,271.78
			A	-	1	51,685.5	273,045.34

Component Nbr. 2 Melhoras habitacionales

				PHYSICAL PROGRESS		FINANCIAL PROGRESS	
	Output	Unit of Measure		2022	EOP 2022	2022	EOP 2022
2.01	Diagnóstico e Estratégia de Intervenção para Adensamento do Centro Histórico Publicado	Plano	P	-	-	-	-
			P (a)	-	1	-	154,039.21
			A	-	1	-	154,039.21
2.02	Edifício da Rua da Palma 415 reabilitado para Casa do Bairro	Obra	P	-	1	-	206,250
			P (a)	-	1	-	155,067.9
			A	-	1	-	155,067.9
2.03	Edifício da Rua da Palma 195/205 reabilitado para Habitação de interesse social	Obra	P	-	1	-	484,375
			P (a)	-	1	412,062.99	541,710.22
			A	-	1	-	129,647.23
2.04	Edifício da Rua do Giz 445 reabilitado para Habitação de interesse social	Obra	P	-	1	-	334,375
			P (a)	-	1	122,396.79	284,606.07
			A	-	1	-	162,209.28
2.05	Plano de Trabalho Técnico Social para habitação de interesse social para as obras de Restauração e Requalificação dos Imóveis Situados na Rua da Pal nº 195/205 e Rua do Giz nº 445.	Plano	P	-	-	-	-
			P (a)	-	1	39,556.96	39,556.96
			A	-	-	4,823.1	4,823.1

Component Nbr. 3 Fortalecimiento institucional

				PHYSICAL PROGRESS		FINANCIAL PROGRESS	
	Output	Unit of Measure		2022	EOP 2022	2022	EOP 2022
3.01	Capacitação	Sessões de Capacitação	P	-	8	-	31,250
			P (a)	-	11	-	50,430.85
			A	-	11	-	50,430.85
3.02	Aquisição de Mobiliário	Unidade	P	-	1	-	62,500
			P (a)	-	1	217,563.29	217,563.29
			A	-	-	-	-
3.03	Aquisição de Equipamentos	Unidade	P	-	1	-	62,500
			P (a)	-	1	197,784.81	197,784.81
			A	-	-	-	-

Component Nbr. 4 Gerenciamiento del programa

				FINANCIAL PROGRESS
	Output	Unit of Measure		EOP
4.00			P	-
			P (a)	-
			A	-

Other Cost				
	Gerenciamento do Programa	P		1,793,312.51
		P (a)	514,080.05	1,841,446.27
		A	297,081.5	1,624,447.72
Total Cost				
	Total Cost	P	0	25,897,125.37
		P (a)	5,289,426.1	29,490,345.9
		A	479,752.93	24,680,672.73

CHANGES TO THE MATRIX					
Section	Name	Type of Change	Sub type	Modified By	Entered in System
Output	Obras do Perimetro 03 (Av. Sen. Vitorino Freire - da ponte do Canal do Portinho até a Casa do Maranhão) - Produto retirado do programa (retirado do programa)	Modify Milestone	Modify Milestone name	WESNEYB	9/20/2022

RISKS AND PLANNED RESPONSES

Risk ID	Risk Status		Risk Taxonomy		
3	Inactive		Goods, and Services		
	Response Actions				
	3.1	Management Strategy		Status	
		MITIGATE		INACTIVE	
	3.2	Management Strategy		Status	
		MITIGATE		INACTIVE	
	3.3	Management Strategy		Status	
		MITIGATE		INACTIVE	

Risk ID	Risk Status		Risk Taxonomy
6	Inactive		Organizational Structure
	Response Actions		
	6.0	Management Strategy	Status
		-	

Risk ID	Risk Status		Risk Taxonomy		
9	Inactive		Integrity		
	Response Actions				
	9.0	Management Strategy		Status	
		-			

Risk ID	Risk Status		Risk Taxonomy		
12	Inactive		Organizational Structure		
	Response Actions				
	12.0	Management Strategy		Status	
		-			

Risk ID	Risk Status		Risk Taxonomy		
15	Materialized		Goods, and Services		
	Response Actions				
	15.1	Management Strategy		Status	
		MITIGATE		ACTIVE	
	15.2	Management Strategy		Status	
		AVOID		COMPLETE	

Risk ID	Risk Status		Risk Taxonomy		
18	Inactive		Institutional Environment		
	Response Actions				
	18.0	Management Strategy		Status	
		-			

Risk ID	Risk Status		Risk Taxonomy
21	Inactive		Internal Processes
	Response Actions		
	21.1	Management Strategy	Status
		MITIGATE	ACTIVE

Risk ID	Risk Status		Risk Taxonomy
24	Active		Institutional Environment
	Response Actions		
	24.1	Management Strategy	Status
		MITIGATE	ACTIVE

Risk ID	Risk Status		Risk Taxonomy
27	Active		Institutional Environment
	Response Actions		
	27.1	Management Strategy	Status
		MITIGATE	ACTIVE

Risk ID	Risk Status		Risk Taxonomy
30	Inactive		Political Environment
	Response Actions		
	30.0	Management Strategy	Status
		-	

Risk ID	Risk Status		Risk Taxonomy
33	Materialized		Goods, and Services
	Response Actions		
	33.1	Management Strategy	Status
		MITIGATE	ACTIVE

Risk ID	Risk Status		Risk Taxonomy		
36	Inactive		Institutional Environment		
	Response Actions				
	36.1	Management Strategy		Status	
		MITIGATE		INACTIVE	
	36.2	Management Strategy		Status	
		MITIGATE		INACTIVE	

Risk ID	Risk Status		Risk Taxonomy
39	Materialized		Institutional Environment
	Response Actions		
	39.1	Management Strategy	Status
		ACCEPT	COMPLETE

IMPLEMENTATION STATUS AND LEARNING

Lesson Learned - Categories
Others - Fiduciary Dimensions
