

Rapport Résumé

Données Générales

Agence d' Exécution (EA): MINISTRY OF EDUCATION AND CULTURE
Secteur: EDUCATION-PRIMARY EDUCATION
Numéro(s) de Prêt(s): 2100/OC-JA
Étape: Approved
Type d' Opération: INV - Investissement
Opération(s) Connexe(s):
Sous-Type de l'Opération: SUP - Supplementary Financing

Fonds Disponibles (US\$)

Montant Courant Approuvé: 14.000.000,00
Montant Décaissé à ce Jour: 12.409.680,87
% Décaissé: 88,64
Solde: 1.590.319,13

Coût Total et Source de Financement

Initial BID: 14.000.000,00
Courant BID: 14.000.000,00
Pari Passu: 100,00
Cofinancement/Pays:
Estimation Initiale: 14.000.000,00
Période d'Amortissement (mois): 270

Catégorie d'Impact Environnemental et Social du Projet




Catégorie d'Impact Environnemental et Social du Projet: Aucun

Reformulation

() Les objectifs du projet ont-ils été reformulés?


Validation

Validé par le Chef de Division: 23-abr-2012
Validé par le Représentant: 26-abr-2012

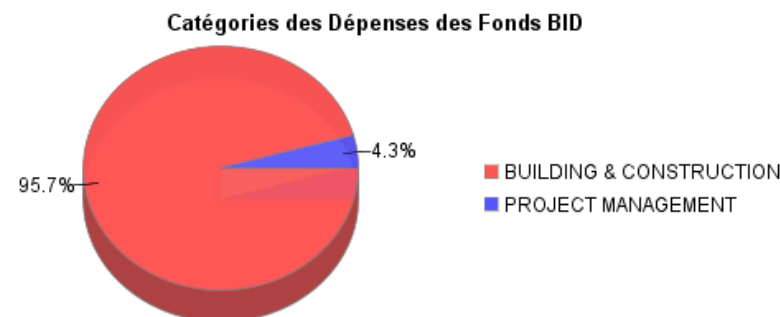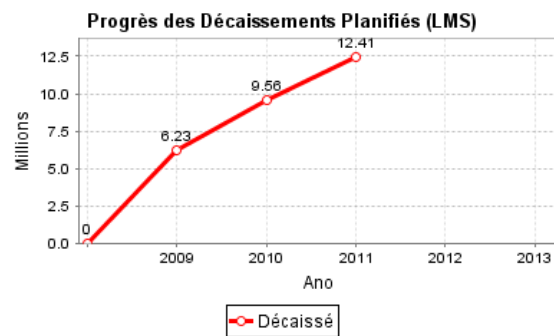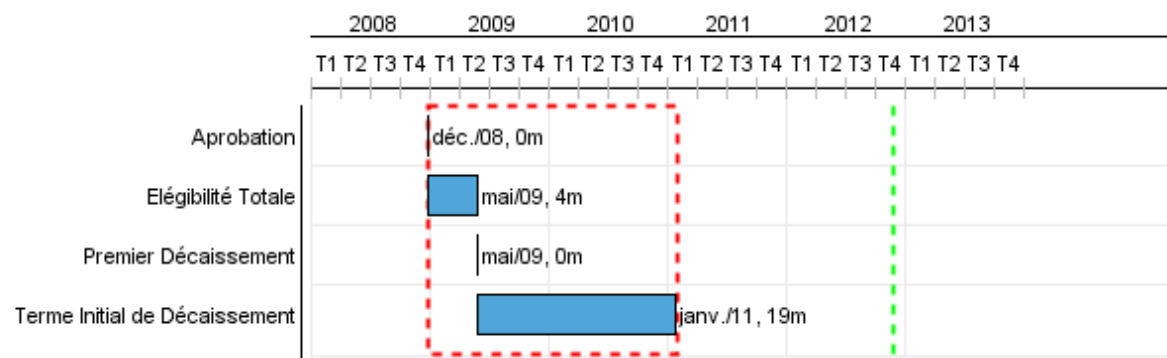

Progrès Cumulé à 2011

Progrès Cumulé

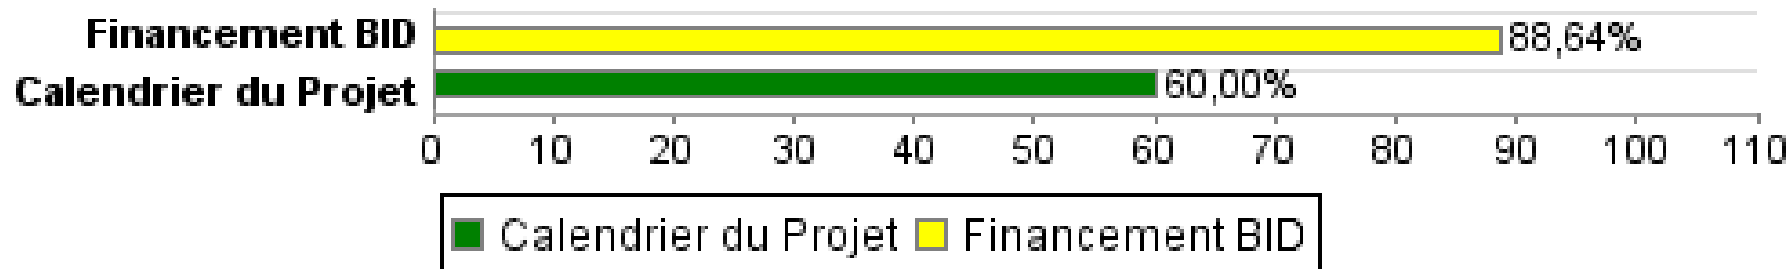

Résultats

Résultat: Occupancy rate reduced in benefited schools

Indicateur	Unité de Mesure	Ligne de Base	Année Ligne de Base		2009	2010	2011	2012	Fin du Projet
Occupancy rate in benefited schools	Ratio	186.00	2003	P		130.00		100.00	100,00
				A		106.00			
Students benefited by education projects	Students		2008	P	1,260.00	1,155.00		1,155.00	3.570,00
				A	1,260.00	1,155.00	1,785.00		

Résultat: Benefited schools maintained in good condition

Indicateur	Unité de Mesure	Ligne de Base	Année Ligne de Base		2009	2010	2011	2012	Fin du Projet
Maintenance plans delivered	Maintainance plans		2008	P	4.00	4.00	5.00	5.00	6,00
				A	4.00	4.00	5.00		

Résultat: Schools de-shifted in 3 miles radius from new PESP schools

Indicateur	Unité de Mesure	Ligne de Base	Année Ligne de Base		2009	2010	2011	2012	Fin du Projet
de-shifted schools	Schools		2008	P	1.00	4.00		4.00	4,00
				A					

Produites: Progrès Physique et Financier Annuel 2011

Description	Unité de Mesure	Physique			
		Planifié	Réel	Unités Cumulées	Unités FDP
Civil works					
New schools built (Hellshire; Mansfield)	Schools				2,00
Schools partially replaced (Red Hills)	Schools				1,00
Existing schools expanded (Chester castle; Lucea Primary)	Schools				2,00
Schools fully replaced (Fruitfull Vale; Sheffield)	Schools				2,00
Unallocated					
