
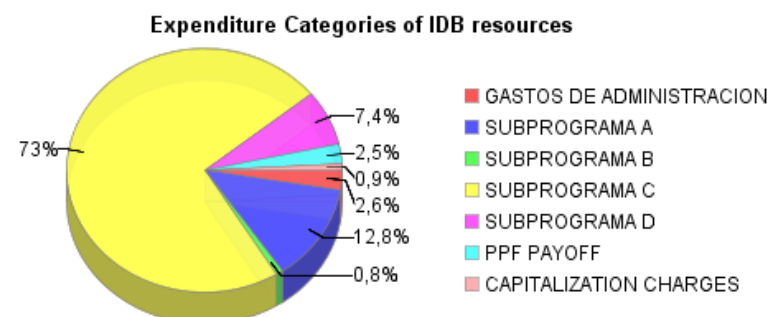




Summary Report

Basic Data		Available Funds (US\$)		Total Cost and Source	
Executing Agency (EA):	MINISTERIO DE VIVIENDA Y SERVICIOS BASICOS				
Sector:	URBAN DEVELOPMENT AND HOUSING-URBAN DEVELOPMENT CREDIT				
Loan Number(s):	1006/SF-BO	Current Approved Amount:	42.067.706,19	Original IDB:	45.800.000,00
Stage:	Approved	Disbursed Amount to Date:	42.067.706,19	Current IDB:	42.067.706,19
Operation Type:	INV - Investment	% Disbursed:	100,00	Pari-passu:	100,00
Related Operation(s):	BO0026, BO0183	Balance:		Co-Financing/Country:	11.000.000,00
Operation Subtype:	ESP - Specific Investment Operation			Original Estimate:	56.800.000,00
				Amortization Period (months):	354

Project Environmental and Social Impact Category	Reformulation	Validation
Project Environmental and Social Impact Category: B(R)	() Was the objective(s) of this project reformulated?	Validated by Division Chief: 09-abr-2013 Validated by Country Representative: 10-abr-2013

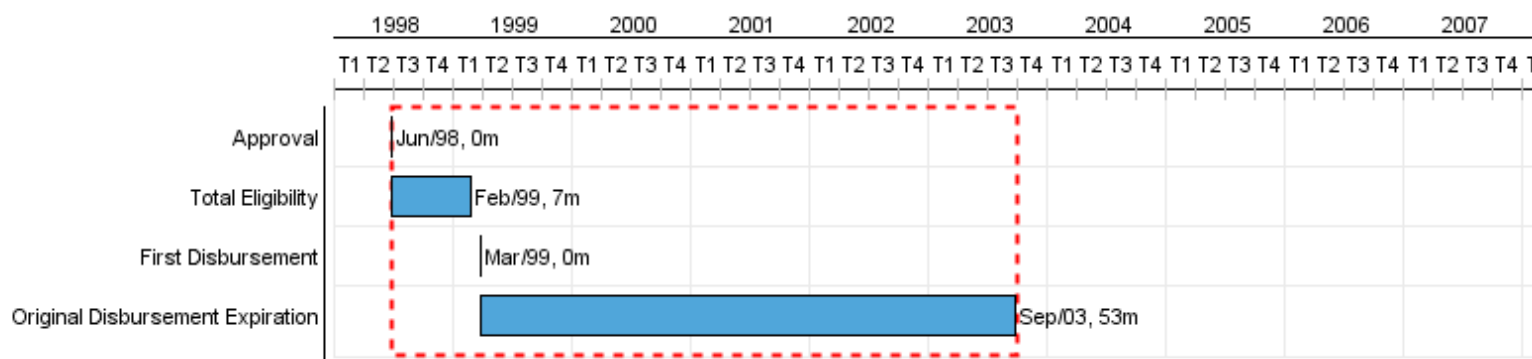

Accumulated Progress as of 2012

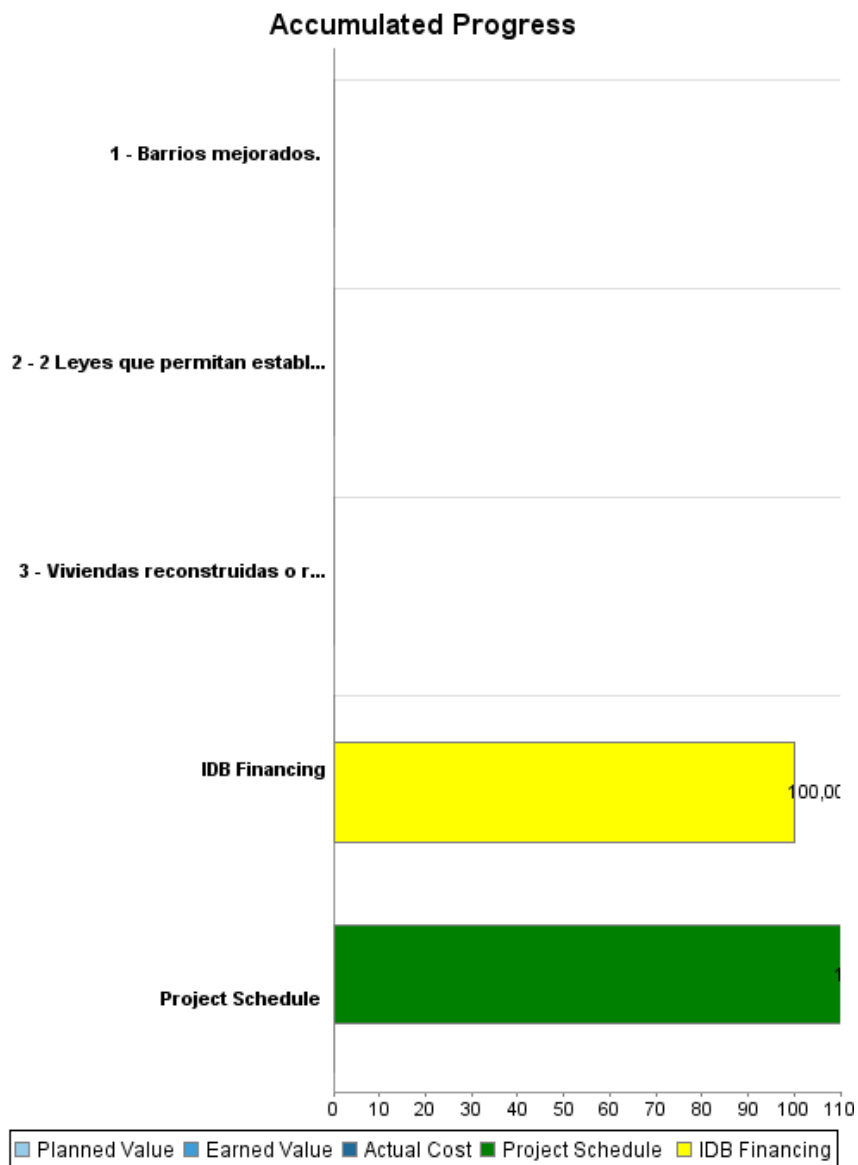

Outcomes

Outcome:	Contribuir a elevar la situación habitacional de la población, particularmente de aquella de más bajos ingresos.
-----------------	--

Indicator	Unit of Measure	Baseline	Baseline Year		2007	End of project
Acceso a servicios de saneamiento básico por parte de las familias beneficiarias del Programa.	Familias			P	23.000,00	
				A	56.000,00	

Outputs: Annual Physical and Financial Progress 2012

Description	Unit of Measure	Physical				Financial			
		Planned	Actual	Accumulated units	EOP units	Planned	Actual	Accumulated costs	EOP costs
Sub-Programa A. Implementación de la Política de Reforma del Sector Habitacional									
2 Leyes que permitan establecer una reforma legal e institucional que reduzca los costos de producción, transacción y financiamiento de la vivienda en Bolivia (en %).	Leyes				100,00				
Sub-Programa C. Proyectos Integrales de Mejoramiento de Barrios.									
Barrios mejorados.	Barrios				81,00				
Sub-Programa D. Reconstrucción de Viviendas en zonas urbanas de Aiquile, Mizque y Totora.									
Viviendas reconstruidas o refaccionadas en las zonas afectadas.	Viviendas				1.400,00				
Sub-Programa B. Desarrollo del Mercado Secundario (se canceló)									
TOTAL									
