
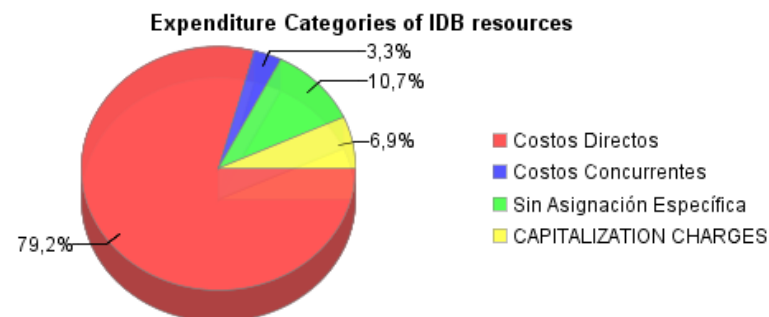




## Summary Report

Basic Data		Available Funds (US\$)		Total Cost and Source	
Executing Agency (EA):	INTENDENCIA MUNICIPAL DE MONTEVIDEO				
Sector:	WATER AND SANITATION				
Loan Number(s):	2647/OC-UR	Current Approved Amount:	20.500.000,00	Original IDB:	20.500.000,00
Stage:	Approved	Disbursed Amount to Date:		Current IDB:	20.500.000,00
Operation Type:	INV - Investment	% Disbursed:		Pari-passu:	67,00
Related Operation(s):	UR-T1074	Balance:	20.500.000,00	Co-Financing/Country:	10.000.000,00
Operation Subtype:	ESP - Specific Investment Operation			Original Estimate:	30.500.000,00
				Amortization Period (months):	246

Project Environmental and Social Impact Category	Reformulation	Validation
Project Environmental and Social Impact Category: B	( ) Was the objective(s) of this project reformulated?	Validated by Division Chief: 26-mar-2013 Validated by Country Representative: 12-abr-2013

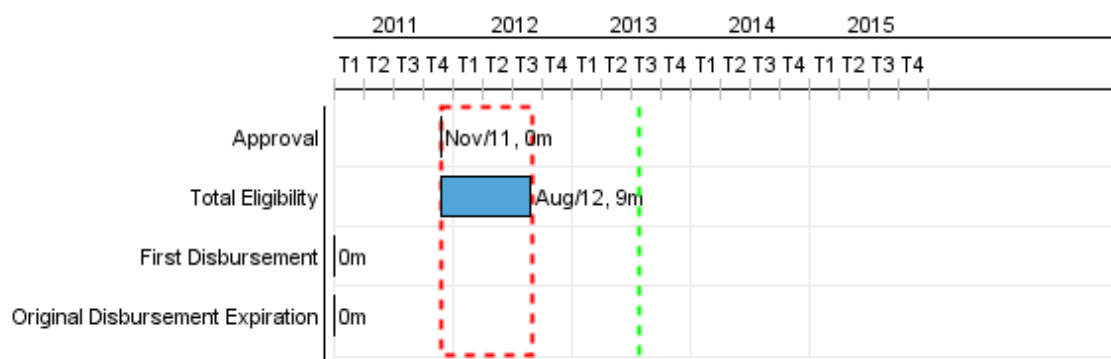

## Accumulated Progress as of 2012

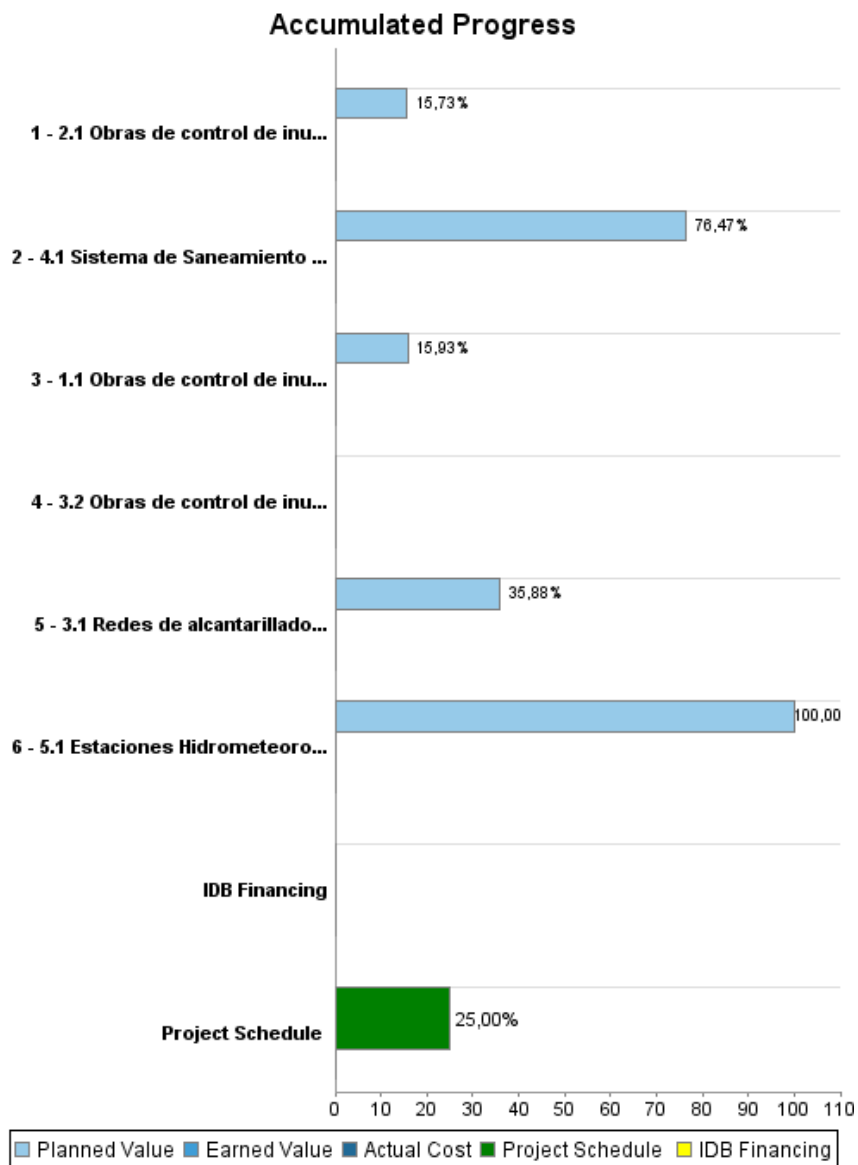

## Outcomes

<b>Outcome:</b>	Sistema de drenaje y saneamiento ambiental mejorado
-----------------	---

Indicator	Unit of Measure	Baseline	Baseline Year		End of project
Áreas inundables en Montevideo con un período de retorno de 10 años.	Áreas	11,00	2011	P	8,00
				A	
Carga orgánica vertida al Arroyo Pantanoso proveniente del PTIC	Kg DBO5/día	94,00	2012	P	
				A	

## Outputs: Annual Physical and Financial Progress 2012

Description	Unit of Measure	Physical				Financial			
		Planned	Actual	Accumulated units	EOP units	Planned	Actual	Accumulated costs	EOP costs
<b>Componente I. Obras de drenaje pluvial en la cuenca de Arroyo Seco</b>									
1.1 Obras de control de inundaciones	Tanques				2,00				6.844.000,00
<b>Componente II. Obras de drenaje pluvial en la cuenca del Arroyo Quitacalzones</b>									
2.1 Obras de control de inundaciones	Tanques				3,00				10.129.000,00
<b>Componente III. Obras de drenaje pluvial en la cuenca de la Cañada Peabody</b>									
3.1 Redes de alcantarillado pluvial construidas o ampliadas	km				4,60				4.746.000,00
3.2 Obras de control de inundaciones	Tanques				1,00				340.000,00
<b>Componente IV. Saneamiento ambiental para el PTI</b>									
4.1 Sistema de Saneamiento Ambiental y microdrenaje construido	Sistemas				1,00				1.275.000,00
<b>Componente V. Estaciones hidrometereológicas</b>									
5.1 Estaciones Hidrometeorológicas	Estaciones				12,00				50.000,00
<b>Compra Terrenos</b>									
Adquisición de Terrenos	N/A								671.000,00
<b>Costos administrativos y financieros</b>									
Costos Administrativos y Financieros	N/A					1.091.000,00	1.335.000,00		6.445.000,00
<b>TOTAL</b>						<b>1.091.000,00</b>	<b>1.335.000,00</b>		<b>30.500.000,00</b>
