



Operation Number: **UR-L1005**  
Year- PMR Cycle: **Second period Jan-Dec 2013**  
Last Update: **6/6/2014**  
PMR Validation Stage: **Validated by Representative**

Chief of Operations validation date: **06/06/2014**  
Division Chief validation date: **06/12/2014**  
Country Representative validation date: **06/12/2014**

Inter-American Development Bank - IDB  
Office of Strategic Planning and Development Effectiveness

## Operation Profile

### Basic Data

Operation name:	Montevideo Sanitation Program (PSU IV)	Loan Number:	1819/OC-UR
Executing Agency (EA):	INTENDENCIA MUNICIPAL DE MONTEVIDEO		
Team Leader:	Paez Rubio, Tania	Sector/Subsector:	AS
Operation Type:	Loan Operation	Overall Stage:	Disbursing (From eligibility until all the loans are closed).
Lending Instrument:	Investment Loan	Country:	URUGUAY
Borrower:	REPUBLICA ORIENTAL DE URUGUAY	Convergence related Operation(s):	UR-L1063

### Total Cost and Source

	Original IDB	Current Active IDB	Local Counterpart	Co-Financing/Country	Total operation cost - Original Estimate
Aggregated	\$161,400,000.00	\$161,400,000.00	\$28,450,000.00	\$0.00	\$189,850,000.00
UR-L1005	\$118,600,000.00	\$118,600,000.00	\$20,900,000.00	\$0.00	\$139,500,000.00
UR-L1063	\$42,800,000.00	\$42,800,000.00	\$7,550,000.00	\$0.00	\$50,350,000.00

### Available Funds (US\$)

	Current IDB	Disb. Amount to Date	% Disbursed	Undisbursed Balance
Aggregated	\$161400000.00	82001053.63	50.81%	\$79398946.37
UR-L1005	\$118,600,000.00	\$68,622,932.52	57.86%	\$49,977,067.48
UR-L1063	\$42,800,000.00	\$13,378,121.11	\$0.31	\$29,421,878.89


### Environmental and Social Safeguards

Main Operation	
Impacts Category:	B(R)
Safeguard Performance Rating:	Partially Satisfactory
Safeguard Performance Rating - Rationale:	En general, correcta gestión ambiental y social por parte del Ejecutor. Debe incluirse un anexo ambiental y social en informes semestrales al Banco.

### Reformulation Information

	Main Operation	Oper. UR-L1063
Was/Were the objective(s) of this operation reformulated?	NO	NO
Date of approval:		

Expense Categories by Loan Contract (cumulative values)

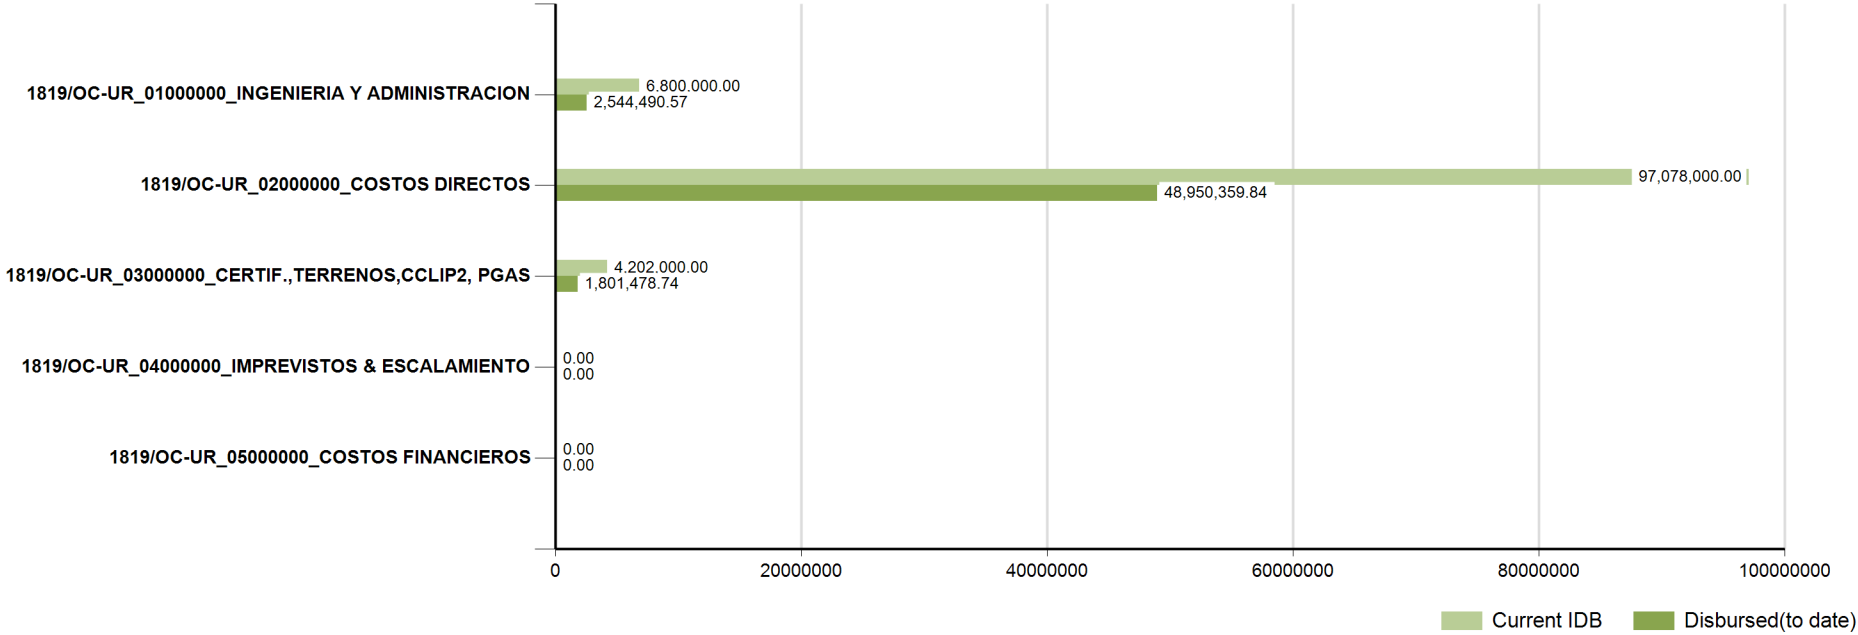

## Results Matrix

## Impacts

Impact:	1 Mejorar las condiciones de vida de la población del departamento de Montevideo, disminuyendo la contaminación en la bahía de Montevideo y playas aledañas							
Observation:								
Indicators	Flags*	Unit of Measure	Baseline	Baseline Year	Means of verification	Observations	EOP	
1.1 Carga orgánica vertida en tiempo seco a la bahía por descargas del Sistema de Saneamiento		Ton DBO/día	47.00	2010	Laboratorio de Calidad Ambiental y Unidad de Efluentes Industriales, Departamento de Desarrollo Ambiental. IM		P	16.00
							P(a)	16.00
							A	

RF - RF Indicator   SI - Sector Indicator   CI - Country Indicator   PG - Pro-Gender   PE - Pro-Ethnicity

## Outcomes

Outcome:	2 Cobertura de servicio de saneamiento incrementada															
Observation:																
							2010	2011	2012	2013	2014	2015	2016	EOP		
2.1 Caudal medio de aguas servidas con disposicion final adecuada		m3/s	2.30	2006	Registros de la planta		P								3.90	
	P(a)													3.90		
	A															
2.2 Hogares con conexiones sanitarias nuevas	RF	Hogares	378,000.00	2010	numero de unidades facturadas	Las unidades facturadas se refieren al nuemro de conexiones registradas por la IM	P	1,046.00	3,735.00	10,516.00	11,703.00	11,700.00	11,300.00		428,000.00	
							P(a)	1,046.00	3,735.00	10,516.00	11,703.00	11,700.00	11,300.00	10,546.00	428,000.00	
	A						1,046.00	3,735.00	10,516.00	1,157.00						
2.2 Hogares con aguas residuales tratadas		Hogares	265,000.00	2014	sistema de disposicion final oeste en funcionamiento		P									
	P(a)														122,000.00	387,000.00
	A															
Outcome:	3 Sostenibilidad del servicio de saneamiento y drenaje pluvial incrementada															
Observation:																

Indicators	Flags*	Unit of Measure	Baseline	Baseline Year	Means of verification	Observations								
							2010	2011	2012	2013	2014	2015	2016	EOP
3.1 Índice de cobertura de costos con ingresos propios.		%	65.00	2007	Informe de cumplimiento de compromiso de gestión (presentado por la División saneamiento)		P	85.00	90.00	95.00	95.00	95.00		95.00
							P(a)	85.00	90.00	95.00	95.00	125.00	110.00	95.00
							A	96.10	116.18					

 RF - RF Indicator

 SI - Sector Indicator

 CI - Country Indicator

 PG - Pro-Gender

 PE - Pro-Ethnicity

Outputs: Annual Physical and Financial Progress

Obras de Alcantarillado Sanitario y Drenaje Pluvial		Physical Progress			Financial Progress		
Outputs	Unit of Measure	2013		EOP	2013		EOP
Sistema de redes de alcantarillado sanitario y drenaje pluvial construído	sistemas	P		1.00	P	651,000.00	36,220,000.00
		P(a)		1.00	P(a)	651,000.00	35,761,000.00
		A		1.00	A	192,000.00	35,761,000.00
Sistema de disposición final de líquidos cloacales Oeste		Physical Progress			Financial Progress		
Outputs	Unit of Measure	2013		EOP	2013		EOP
Planta de Pretratamiento Oeste y estaciones de bombeo construídas	sistema	P		1.00	P	10,550,000.00	29,213,000.00
		P(a)		1.00	P(a)	10,550,000.00	29,213,000.00
		A			A	8,235,000.00	8,235,000.00
Emisario subfluvial a Punta Yeguas construído	emisarios	P		1.00	P	8,000,000.00	34,821,000.00
		P(a)		1.00	P(a)	8,000,000.00	48,003,000.00
		A			A	0.00	0.00
Tuberías de impulsión construídas	Km	P	6.00	16.00	P	11,400,000.00	27,121,000.00
		P(a)	6.00	15.50	P(a)	11,400,000.00	27,121,000.00
		A	5.50	5.50	A	17,419,000.00	17,419,000.00
Reasentamiento de familias		Physical Progress			Financial Progress		
Outputs	Unit of Measure	2013		EOP	2013		EOP
Familias reasentadas.	familias	P	0.00	341.00	P	924,000.00	12,916,000.00
		P(a)	0.00	341.00	P(a)	924,000.00	13,035,000.00
		A		341.00	A	1,043,000.00	13,035,000.00
Mejora de la Gestión de la División Saneamiento de la Intendencia de Montevideo		Physical Progress			Financial Progress		
Outputs	Unit of Measure	2013		EOP	2013		EOP
Fondo de conexiones intra-domiciliarias implementado	fondos	P		1.00	P	523,000.00	1,730,000.00
		P(a)		1.00	P(a)	523,000.00	1,709,000.00
		A		0.00	A	208,000.00	571,000.00
Plan Director de Saneamiento actualizado y consensuado	planes	P	0.00	1.00	P	954,000.00	3,815,000.00
		P(a)	0.00	1.00	P(a)	954,000.00	3,815,000.00
		A		0.00	A	0.00	0.00
Proyectos ejecutivos para las obras del segundo tramo del CLIPP elaborados	proyectos	P		1.00	P	0.00	3,000,000.00
		P(a)		1.00	P(a)	0.00	4,800,000.00
		A		0.00	A		0.00
Proyectos de Mejora de la Gestión comercial de la División Saneamiento implementados	proyectos	P	7.00	7.00	P	1,664,000.00	2,692,000.00
		P(a)	7.00	7.00	P(a)	1,664,000.00	3,519,000.00
		A	0.00	0.00	A	1,049,000.00	2,077,000.00
Gastos Financieros y Administrativos							

Other Cost		2013	Cost
Gastos Financieros y Administrativos	P	\$7,000,000.00	\$37,972,000.00
	P(a)	\$7,000,000.00	\$40,576,000.00
	A	\$4,292,000.00	\$24,871,000.00
Total Cost		2013	Total Cost
	P	\$41,666,000.00	\$189,500,000.00
	P(a)	\$41,666,000.00	\$141,593,000.00
	A	\$32,438,000.00	\$101,969,000.00

Changes to the Matrix

Section	Name	Type of Change	Reasons	Entered in the System	Agreed with Executing Agency
Outcome	Hogares en area saneada con disposicion final adecuada en zona oeste	Delete Outcome Indicator		6/4/2014	6/4/2014

Please note that the Overall Stage represents the stage of the operation at the time of this report’s publication, which might not necessarily match the stage of the operation during the PMR Cycle to which the report pertains.
