

PMR Operational Report

Operation Number	HA-X1002	Chief of Operations Validation Date	11/02/20
Year- PMR Cycle	First period Jan-Jun 2020	Division Chief Validation Date	
Last Update	10/09/20	Country Representative Validation Date	
PMR Validation Stage	Validated by Chief of Operations		

Basic Data

Operation Profile

Operation Name	Sustainable Land Management of the Upper Watersheds of South Western Haiti	Loan Number	GRT/FM-11803-HA
Executing Agency	Ministère de l'Agriculture, des Ressources Naturelles et du Développement Rural, Ministère de l'Environnement	Sector/Subsector	ENVIRONMENT AND NATURAL DISASTERS-ENVIRONMENTAL MANAGEMENT AND GOVERNANCE
Team Leader	ALBARET, GERAUD	Overall Stage	Fully Disbursed
Operation Type	Investment Grants	Country	Haiti
Lending Instrument		Convergence related Operation(s)	HA-G1023
Borrower			


Environmental and Social Safeguards

Impacts Category	C	Was/Were the objective(s) of this operation reformulated?	NO
Safeguard Performance Rating		Date of approval	
Safeguard Performance Rating - Rationale			

Financial Data

Item	Total Cost and Source					Available Funds (US\$)			
	Original IDB	Current IDB	Local Counterpart	Co-Financing / Country	Total Original Cost	Current IDB	Disb. Amount to Date	% Disb	Undisbursed Amount
HA-G1023	9,000,000	9,000,000	0	0	9,000,000	9,000,000	9,000,000	100.00%	0
HA-X1002	3,436,364	3,243,535.87	400,000	0	3,836,364	3,243,535.87	3,243,535.87	100.00%	0
Aggregated	12,436,364	12,243,535.87	400,000	0	12,836,364	12,243,535.87	12,243,535.87	100.00%	0

Expense Categories by Loan Contract (cumulative values)

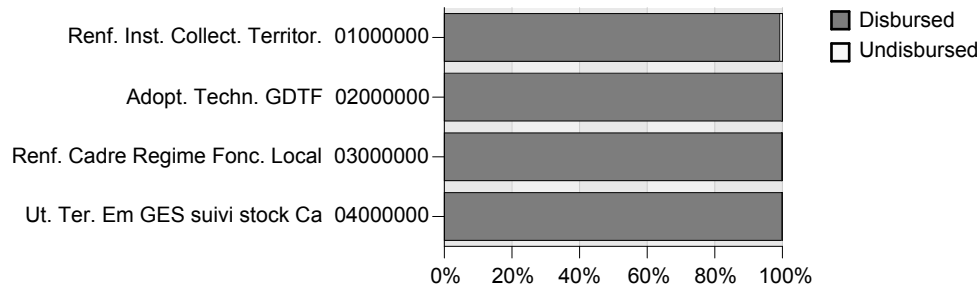

Please note that inactive indicators and outputs are not displayed; totals in the actual cost table may not match the sum of the cost of the outputs displayed, due to the cost of inactive outputs.

PMR Operational Report

RESULTS MATRIX

IMPACTS

Impact Nbr. 0: Increase farmers' median agricultural net income

Observation:

Indicator		Unit of Measure	Baseline	Baseline Year		2015	2016	2017	2018	2019	2020	EOP 2019
0.0	Income = (crop value+livestock value)-input costs	%	0.00	2013	P							
					P(a)	0.00	0.00	10.00	0.00	0.00	20.00	20.00
					A		0.00	0.00	0.00	0.00		0.00
Details												
Means of verification: Socio-economic surveys												
Pro-Gender		No		Pro-Ethnicity		No						

Impact Nbr. 1: Increase carbon stock

Observation:

Indicator		Unit of Measure	Baseline	Baseline Year		2015	2016	2017	2018	2019	2020	EOP 2019
1.1	Carbon stock assessment in the buffer zone of the Park	%	0.00	2014	P	5.00						5.00
					P(a)			5.00	0.00	0.00	0.00	5.00
					A			1.00	0.00	0.00		1.00
Details												
Means of verification: Monitoring system implemented by the project (component 4).												
Observations: The baseline will be the first milestone of the component 4.												
Pro-Gender		No		Pro-Ethnicity		No						

Indicator		Unit of Measure	Baseline	Baseline Year		2015	2016	2017	2018	2019	2020	EOP 2019
1.1	Carbon stock assessment inside the Park	%	0.00	2014	P							
					P(a)			2.00	0.00	0.00	0.00	2.00
					A			2.00	0.00	0.00		2.00
Details												
Means of verification: Monitoring system implemented by the project (component 4).												
Observations: The baseline will be the first milestone of the component 4												
Pro-Gender		No		Pro-Ethnicity		No						

PMR Operational Report

RESULTS MATRIX

OUTCOMES

Outcome Nbr. 0: Open the Park to public and regulate

Observation: Component 1

Indicator	Unit of Measure	Baseline	Baseline Year		2014	2015	2016	2017	2018	2019	EOP 2019
0.0	Number of visitor's autorizations given	Autorization	2014	P							
				P(a)	2.00	5.00	5.00	10.00	10.00	0.00	18.00
				A	2.00	3.00	3.00	0.00	6.00	0.00	8.00

Details

Means of verification: Filled forms of park authorities

Pro-Gender	No	Pro-Ethnicity	No
-------------------	----	----------------------	----

Indicator	Unit of Measure	Baseline	Baseline Year		2014	2015	2016	2017	2018	2019	EOP 2019
0.1	Number of autorization of research missions given	Autorization	2014	P							
				P(a)	1.00	2.00	3.00	3.00	3.00	0.00	10.00
				A	1.00	2.00	3.00	1.00	3.00	0.00	7.00

Details

Means of verification: Filled forms of park authorities

Pro-Gender	No	Pro-Ethnicity	No
-------------------	----	----------------------	----

Outcome Nbr. 1: Acquire for the country technological capacity and equipment to conduct carbon stock and Green House Gases emissions monitoring

Observation: Component 4

Indicator	Unit of Measure	Baseline	Baseline Year		2014	2015	2016	2017	2018	2019	EOP 2019
1.1	Carbon stock and Green House Gases emissions monitoring system established and operational	Monitoring System	2013	P		1.00					1.00
				P(a)			0.00	1.00	0.00	0.00	1.00
				A			0.00	1.00	0.00	0.00	1.00

Details

Means of verification: Final assessment report.

Observations: The assessment of the monitoring system will be included in the final evaluation, by an expert in this issue.

Pro-Gender	No	Pro-Ethnicity	No
-------------------	----	----------------------	----

Outcome Nbr. 2: Increase the area with permanent vegetal cover in the buffer zone thanks to better land tenure security

Observation: Component 3

Indicator	Unit of	Baseline	Baseline		2014	2015	2016	2017	2018	2019	EOP 2019
-----------	---------	----------	----------	--	------	------	------	------	------	------	----------

PMR Operational Report

RESULTS MATRIX

OUTCOMES

		Measure		Year								
2.1	Area with additional permanent vegetable cover in the buffer zone	ha	3,448.00	2012	P	30.00	50.00					80.00
					P(a)			0.00	4,948.00	3,148.00	0.00	4,948.00
					A			0.00	1,800.00	585.00	0.00	1,800.00

Details

Means of verification: Ext ante and ex post analysis of Geo-referenced photographs. At the beginning, at the end and 5 years after the end of the project.

Observations: Baseline : 2,536ha of dense forest, 912 ha of heterogenous forest (Background studies to design HA-X1002 operation, data from CNIGS (National Center for Geospatial information).)

Pro-Gender No **Pro-Ethnicity** No

Outcome Nbr. 3: Improve water and sediment containment in selected gullies of the upper watersheds of the Southern part of Haiti

Observation: Component 2

	Indicator	Unit of Measure	Baseline	Baseline Year		2014	2015	2016	2017	2018	2019	EOP 2019
3.1	Total volume of sediment contained by check-dams	m3	0.00	2013	P							
					P(a)			0.00	5,250.00	0.00	5,250.00	5,250.00
					A			0.00	0.00	0.00	0.00	0.00

Details

Means of verification: Annual surveys conducted by student interns

Observations: 75 microdam planned (20 on rural road and 55 on gullies). Each microdam will stock an average of 70m3 of sediment.

Pro-Gender No **Pro-Ethnicity** No

	Indicator	Unit of Measure	Baseline	Baseline Year		2014	2015	2016	2017	2018	2019	EOP 2019
3.2	Total annual volume of water stored by water retention tanks	m3	0.00	2013	P							
					P(a)			0.00	4,500.00	0.00	4,500.00	4,500.00
					A			0.00	0.00	0.00	0.00	0.00

Details

Means of verification: Annual surveys conducted by student interns

Observations: 75 microdam planned (20 on rural road and 55 on gullies). Each retention tank will stock annually an average of 60m3 : 10 rainfall event x 6m3 tank.

Pro-Gender No **Pro-Ethnicity** No

	Indicator	Unit of Measure	Baseline	Baseline Year		2014	2015	2016	2017	2018	2019	EOP 2019
3.3	Market gardens created in gullies	Hectare	0.00	2013	P							
					P(a)			0.00	75.00	0.00	75.00	75.00

PMR Operational Report

RESULTS MATRIX

OUTCOMES

3.3	Market gardens created in gullies	Hectare	0.00	2013	A			0.00	0.00	0.00	0.00	0.00
Details												
Means of verification: Annual surveys conducted by student interns												
Observations: 75 microdam planned (20 on rural road and 55 on gullies). Each microdam create a 1ha average garden (new area and better use of land just around)												
Pro-Gender		No			Pro-Ethnicity		No					

RESULTS MATRIX

OUTPUTS: ANNUAL PHYSICAL AND FINANCIAL PROGRESS

Component Nbr. 1 Strengthening local governance

	Output	Unit of Measure		PHYSICAL PROGRESS		FINANCIAL PROGRESS	
				2020	EOP 2019	2020	EOP 2019
1.1	Environmental Control and Surveillance Division (CSE) established and operational	CSE system	P		1		918,200
			P(a)	0	1	3,266	994,965
			A	0	1	3,266	994,965
1.2	Communal infrastructure projects executed	Projects	P		12		730,132
			P(a)	0	12	6,903	349,811
			A	0	12	6,903	349,811
1.3	Macaya infrastructures functional (Administrative Center, Hosting Center, Checkpoints)	Infrastructures	P		4		1,341,984
			P(a)	0	7	30,242	1,349,903
			A	0	7	30,242	1,349,903
1.4	Intercommunal agreement in the buffer zone elaborated and implemented	Medium	P		1		253,000
			P(a)	0	1	0	135,741
			A	0	1	0	135,741
1.5	Environmental Education Program implemented in Parks's buffer zone schools	School	P		23		128,082
			P(a)	0	38	647	202,453
			A	0	38	647	202,453
1.6	Priority activities of the management plan implemented	Activities	P		3		255,001
			P(a)	0	4	0	21,471
			A	0	4	0	21,471

Component Nbr. 2 Land and forest management

	Output	Unit of Measure		PHYSICAL PROGRESS		FINANCIAL PROGRESS	
				2020	EOP 2019	2020	EOP 2019
2.1	Farmers supported by the project	# of farmers	P		450		400,000
			P(a)	0	1,805	72,415	4,586,496
			A	0	1,805	72,415	4,586,496
2.2	Socio-Environmental impact assessed	Assessment	P		1		36,500
			P(a)	0	1	0	29,200
			A	0	1	0	29,200
2.3	Rural roads equipped with water harvesting structures	Km	P		20		1,931,640
			P(a)	0	13	53,906	1,912,120
			A	0	13	53,906	1,912,120
2.4	Private sector supported to develop strategic value chain	Project	P		3		310,000
			P(a)	0	0	0	0
			A	0	0	0	0

RESULTS MATRIX

OUTPUTS: ANNUAL PHYSICAL AND FINANCIAL PROGRESS

Component Nbr. 3 Local regulatory framework for land tenure

	Output	Unit of Measure		PHYSICAL PROGRESS		FINANCIAL PROGRESS	
				2020	EOP 2019	2020	EOP 2019
3.1	Park limits physically established	km	P		0		164,000
			P(a)	0	132	0	323,800
			A	0	132	0	323,800
3.2	Macaya National Park zoning plan legally established	Area (Hectares)	P		0		0
			P(a)	0	1	0	0
			A	0	1	0	0
3.3	Scientific research missions inside the park facilitated	Mission	P		0		492,368
			P(a)	0	9	0	280,292
			A	0	9	0	280,292
3.4	Macaya management plan established and published	Plan	P		0		161,000
			P(a)	0	1	36,043	368,373
			A	0	1	0	332,330

Component Nbr. 4 Monitoring emissions Green House Gases

	Output	Unit of Measure		PHYSICAL PROGRESS		FINANCIAL PROGRESS	
				2020	EOP 2019	2020	EOP 2019
4.1	Green House Gases emissions and carbon stock monitored inside Macaya Park	system	P		1		208,150
			P(a)	0	1	0	173,132
			A	0	1	0	173,132

Other Cost

	Evaluation	P					250,000
		P(a)				0	169,259
		A				0	169,259
	Audit	P					81,810
		P(a)				0	118,341
		A				0	118,341
	Project management	P					1,259,191
		P(a)				12,209.87	1,262,280.87
		A				54,796	1,304,867

Total Cost

	Total Cost	P					13,835,844
		P(a)				215,631.87	12,643,535.87
		A				222,175	12,650,079

CHANGES TO THE MATRIX

No information available for this section

IMPLEMENTATION STATUS AND LEARNING

Lesson Learned - Categories
Acquisitions and Procurement - Bidding Stage
Environmental and Social Factors
Others - Dimensions Related to Public Processes/ Actors
Others - Fiduciary Dimensions
Others - Technical-Sectorial Dimensions
Project Design
Project Management Capacity
Project Monitoring & Evaluation
