

PMR Operational Report

Operation Number	UR-L1149	Chief of Operations Validation Date	10/22/20
Year- PMR Cycle	First period Jan-Jun 2020	Division Chief Validation Date	
Last Update	10/09/20	Country Representative Validation Date	
PMR Validation Stage	Validated by Chief of Operations		

Basic Data

Operation Profile

Operation Name	Ciudad del Plata Sanitation Program, Stage I	Loan Number	4642/OC-UR
Executing Agency	OFICINA DE PLANEAMIENTO Y PRESUPUESTO DE LA PRESIDENCIA DE LA REPUBLICA	Sector/Subsector	WATER AND SANITATION-SANITATION URBAN
Team Leader	BASANI, MARCELLO	Overall Stage	Disbursing (From eligibility until all the Operations are closed)
Operation Type	Loan Operation	Country	Uruguay
Lending Instrument	Investment Loan	Convergence related Operation(s)	
Borrower	REPUBLICA ORIENTAL DE URUGUAY		


Environmental and Social Safeguards

Impacts Category	B	Was/Were the objective(s) of this operation reformulated?	NO
Safeguard Performance Rating	Partially Satisfactory	Date of approval	
Safeguard Performance Rating - Rationale	La operación no presenta una capacidad adecuada de gestión para los asuntos socioambientales, lo cual además se vislumbra en deficientes reportes de gestión de estos aspectos. Además, el Programa no cuenta con un programa de involucramiento de partes interesadas que contemple la gestión de quejas y reclamos. Esto a su vez se ve dificultado por un inminente cambio de ejecutor que supondrá dificultades para una adecuada implementación de las políticas socioambientales del Banco.		

Financial Data

Item	Total Cost and Source					Available Funds (US\$)			
	Original IDB	Current IDB	Local Counterpart	Co-Financing / Country	Total Original Cost	Current IDB	Disb. Amount to Date	% Disb	Undisbursed Amount
UR-L1149	20,000,000	20,000,000	0	0	20,000,000	20,000,000	1,000,000	5.00%	19,000,000
Aggregated	20,000,000	20,000,000	0	0	20,000,000	20,000,000	1,000,000	5.00%	19,000,000

Expense Categories by Loan Contract (cumulative values)

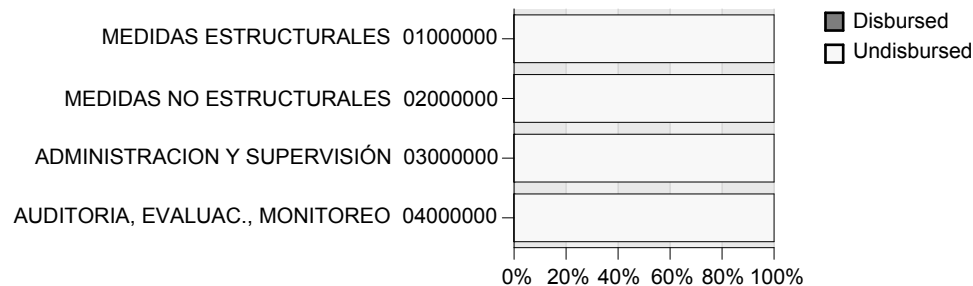

Please note that inactive indicators and outputs are not displayed; totals in the actual cost table may not match the sum of the cost of the outputs displayed, due to the cost of inactive outputs.

PMR Operational Report

RESULTS MATRIX

IMPACTS

No information available for this section

PMR Operational Report

RESULTS MATRIX

OUTCOMES

Outcome Nbr. 1: Hogares con aguas residuales tratadas en el área de influencia del proyecto

Observation:

Indicator		Unit of Measure	Baseline	Baseline Year		2019	2020	2021	2022	2023	2024	EOP 2024
1.1	Nuevos hogares cuyas aguas residuales son tratadas en la Planta de ciudad del Plata en el área de intervención del proyecto	Número de hogares	0.00	2018	P			348.00	697.00	738.00		1,783.00
					P(a)			348.00	697.00	738.00		1,783.00
					A							
Details												
Pro-Gender		No			Pro-Ethnicity		No					

Outcome Nbr. 2: Hogares con conexión habilitada a redes de saneamiento en el área de influencia del proyecto

Observation:

Indicator		Unit of Measure	Baseline	Baseline Year		2019	2020	2021	2022	2023	2024	EOP 2024
2.1	Porcentaje de hogares con conexión habilitada a redes de saneamiento en el área de intervención del proyecto	% de hogares	0.00	2018	P			29.00	33.00	38.00		60.00
					P(a)			0.00	0.00	60.00		60.00
					A							
Details												
Pro-Gender		No			Pro-Ethnicity		No					

Outcome Nbr. 3: Hogares con acceso a redes de saneamiento en el área de influencia del proyecto

Observation:

Indicator		Unit of Measure	Baseline	Baseline Year		2019	2020	2021	2022	2023	2024	EOP 2024
3.1	Nuevos hogares con acceso a la red de saneamiento en el área de intervención del proyecto	# of households	0.00	2018	P		600.00	390.00	1,500.00	500.00		2,990.00
					P(a)		600.00	990.00	1,500.00	500.00		2,990.00
					A							
Details												
Pro-Gender		No	Pro-Ethnicity		No							

Outcome Nbr. 4: Mejora en la capacidad de tratamiento de la planta de aguas residuales de Ciudad del Plata

Observation:

Indicator		Unit of Measure	Baseline	Baseline Year		2019	2020	2021	2022	2023	2024	EOP 2024
4.1	DBO5 removido en la planta de tratamiento de Ciudad del Plata	KgDBO /día	82.00	2018	P					337.00		337.00

PMR Operational Report

RESULTS MATRIX

OUTCOMES

4.1	DBO5 removido en la planta de tratamiento de Ciudad del Plata	KgDBO /día	82.00	2018	P(a)					337.00		337.00
					A							
Details												
Pro-Gender		No		Pro-Ethnicity		No						

Outcome Nbr. 5: Mejora de las familias con jefas de hogar al acceso a los servicios de saneamiento

Observation:

Indicator		Unit of Measure	Baseline	Baseline Year		2019	2020	2021	2022	2023	2024	EOP 2024
5.1	Porcentaje de subsidios entregados a jefas de hogar	%	0.00	2018	P			15.00	15.00	20.00		50.00
					P(a)			0.00	0.00	50.00		50.00
					A							
Details												
Pro-Gender		No			Pro-Ethnicity			No				

RESULTS MATRIX

OUTPUTS: ANNUAL PHYSICAL AND FINANCIAL PROGRESS

Component Nbr. 1 Componente I. Medidas estructurales

	Output	Unit of Measure		PHYSICAL PROGRESS		FINANCIAL PROGRESS	
				2020	EOP 2024	2020	EOP 2024
1.1	Proyectos ejecutivos finalizados	Proyectos ejecutivos	P	1	2	250,000	500,000
			P(a)	0	1	300,000	500,000
			A	0	0	0	0
1.2	Sistema de saneamiento construido y operando	Sistema	P	0	1	5,115,938	16,200,000
			P(a)	0	1	2,000,000	16,200,000
			A	0	0	344,127	747,803

Component Nbr. 2 Componente II. Medidas no estructurales

	Output	Unit of Measure		PHYSICAL PROGRESS		FINANCIAL PROGRESS	
				2020	EOP 2024	2020	EOP 2024
2.1	Plan de conexiones ejecutado	Plan	P	0	1	161,839	2,000,000
			P(a)	0	1	50,000	2,000,000
			A	0	0	0	0

Other Cost

	Administración del Programa	P			239,613	724,840
		P(a)			329,519	724,840
		A			0	0
	Supervisión de obras	P			35,032	175,160
		P(a)			70,064	175,160
		A			0	0
	Auditoría externa	P			5,000	25,000
		P(a)			5,000	25,000
		A			0	0
	Evaluación y monitoreo	P				375,000
		P(a)				375,000
		A			0	0

Total Cost

	Total Cost	P			5,807,422	20,000,000
		P(a)			2,754,583	20,000,000
		A			344,127	747,803

PMR Operational Report

CHANGES TO THE MATRIX

Section	Name	Reasons	Type of Change	Subtype	Modified By	Entered in the System
Output	Proyectos ejecutivos finalizados	All changes made to the matrix were proposed by the executing agency as part of a planning adjustment that modifies annual goals, but not the EOP goals.	Modify Output	Modify Physical EOP P(a) value - caused by a change in the Physical P(a).	PAULAG	10/06/2020

PMR Operational Report

IMPLEMENTATION STATUS AND LEARNING

Lesson Learned - Categories
