

PMR Public Report

Operation Number	BR-L1497	Chief of Operations Validation Date	04/06/21
Year- PMR Cycle	Second period Jan-Dec 2020	Division Chief Validation Date	04/21/21
Last Update	03/29/21	Country Representative Validation Date	04/21/21
PMR Validation Stage	Validated by Representative		

Basic Data

Operation Profile

Operation Name	Vitória Urban Improvement and Citizen Security Program (First Stage of the Sustainable Vitória Action Plan)	Loan Number	4617/OC-BR
Executing Agency	SECRETARIA ESPECIAL DE ESTADO DE GESTAO-SEGES	Sector/Subsector	URBAN DEVELOPMENT AND HOUSING-URBAN LAND PLANNING AND MANAGEMENT
Team Leader	ALVES, DALVE ALEXANDRE SORIA	Overall Stage	Disbursing (From eligibility until all the Operations are closed)
Operation Type	Loan Operation	Country	Brazil
Lending Instrument	Investment Loan	Convergence related Operation(s)	
Borrower	MUNICIPIO DE VITÓRIA - ES		


Environmental and Social Safeguards

Impacts Category	B	Was/Were the objective(s) of this operation reformulated?	NO
Safeguard Performance Rating	Satisfactory	Date of approval	
Safeguard Performance Rating - Rationale	As obras previstas para o programa ainda não iniciaram e a AE está na fase de elaboração de documentos conceituais, como Termos de Referências dos projetos executivos, estudos ambientais, e possui boa capacidade de gestão dos temas sociais e ambientais, com equipe ampla e qualificada e adequada articulação institucional.		

Financial Data

Item	Total Cost and Source					Available Funds (US\$)			
	Original IDB	Current IDB	Local Counterpart	Co-Financing / Country	Total Original Cost	Current IDB	Disb. Amount to Date	% Disb	Undisbursed Amount
BR-L1497	100,000,000	100,000,000	25,000,000	0	125,000,000	100,000,000	300,000	0.30%	99,700,000
Aggregated	100,000,000	100,000,000	25,000,000	0	125,000,000	100,000,000	300,000	0.30%	99,700,000

Expense Categories by Loan Contract (cumulative values)

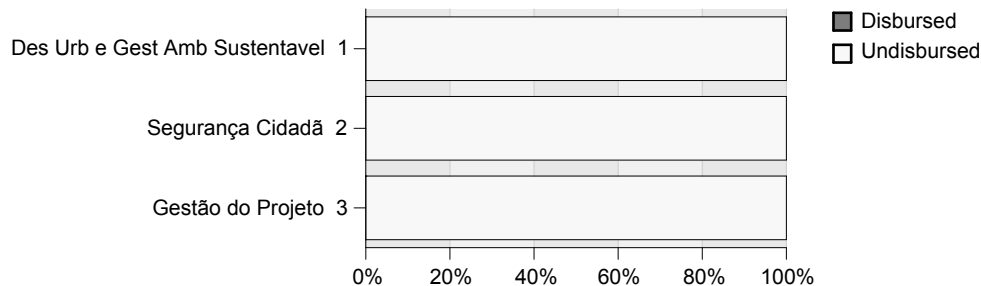

PMR Public Report

RESULTS MATRIX

General Development Objectives

No information available for this section

PMR Public Report

RESULTS MATRIX

Specific Development Objectives

Specific Development Objectives Nbr. 1: Resultado 1. Aumento do valor das propriedades imobiliárias na ON

Observation:

Indicator		Unit of Measure	Baseline	Baseline Year		2024	EOP 2024
1.0	Valor médio dos imóveis em na ON	R\$/m2	2,020.00	2018	P	2,890.00	2,890.00
					A		
Details							
Means of verification: Informes de progreso							
Pro-Gender		No	Pro-Ethnicity		No		

Specific Development Objectives Nbr. 2: Resultado 2. Ampliação da cobertura vegetal no MV

Observation:

Indicator		Unit of Measure	Baseline	Baseline Year		2024	EOP 2024
2.0	Área verde por habitante no Município de Vitória (MV)	R\$/m2	83.50	2017	P	84.80	84.80
					A		
Details							
Means of verification: Informes de progreso							
Observations: Informes de progreso							
Pro-Gender		No		Pro-Ethnicity		No	

Specific Development Objectives Nbr. 3: Resultado 3. Agências governamentais fortalecidas

Observation:

Indicator		Unit of Measure	Baseline	Baseline Year		2024	EOP 2024
3.0	Órgãos governamentais que se beneficiam de projetos que fortalecem instrumentos tecnológicos e de gestão para melhorar a prestação de serviços públicos	unid	0.00	2017	P	5.00	5.00
					A		
Details							
Means of verification: Informes de progreso							
Observations: Informes de progreso							
Pro-Gender		No		Pro-Ethnicity		No	

Specific Development Objectives Nbr. 4: Resultado 5. Redução de homicídios de jovens de 15 a 24 anos nas 5 regiões prioritárias da MV.

Observation:

Indicator		Unit of	Baseline	Baseline		2024	EOP 2024
-----------	--	---------	----------	----------	--	------	----------

PMR Public Report

RESULTS MATRIX

Specific Development Objectives

		Measure		Year			
4.0	Redução de homicídios de jovens (homens e mulheres) de 15 a 24 anos nas 5 regiões prioritárias da MV.	tx homicio	134.50	2017	P	121.50	121.50
					A		
Details							
Means of verification: Informes de progreso							
Observations: Informes de progreso							
Pro-Gender		No		Pro-Ethnicity		No	
Indicator		Unit of Measure	Baseline	Baseline Year		2024	EOP 2024
4.2	Homicídios de mulheres nas 5 regiões prioritárias da MV	tx de roubo	12.30	2017	P	11.00	11.00
					A		
Details							
Means of verification: Informes de progreso							
Observations: Informes de progreso							
Pro-Gender		No		Pro-Ethnicity		No	
Indicator		Unit of Measure	Baseline	Baseline Year		2024	EOP 2024
4.3	Homicídios de jovens de 15 a 24 anos (homens e mulheres afrodescendentes) nas 5 regiões do MV	tx de roubo	120.40	2017	P	108.00	108.00
					A		
Details							
Means of verification: Informes de progreso							
Observations: Informes de progreso							
Pro-Gender		No		Pro-Ethnicity		No	

RESULTS MATRIX

OUTPUTS: ANNUAL PHYSICAL AND FINANCIAL PROGRESS

Component Nbr. 1 Componente I. Desenvolvimento Urbano e Gestão Ambiental Sustentável

	Output	Unit of Measure		PHYSICAL PROGRESS		FINANCIAL PROGRESS	
				2020	EOP 2024	2020	EOP 2024
1.1	Orla Noroeste Requalificada- 1A	hectares	P	0	31,800	0	14,735,000
			P(a)	0	31,800	0	14,735,000
			A	0	0	0	0
1.2	Orla Noroeste Requalificada- 1B	hectares	P	0	72,600	0	15,400,000
			P(a)	0	72,600	0	15,400,000
			A	0	0	0	0
1.3	Ciclovía Tancredão – Praça dos Namorados Implantada	Km	P	0	13	0	4,000,000
			P(a)	0	13	0	4,000,000
			A	0	0	0	0
1.4	Ligações Intradomiciliares de Esgoto Realizadas	Unidade	P	0	3,249	0	1,481,000
			P(a)	0	3,249	0	1,481,000
			A	0	0	0	0
1.5	Plantas de Parcelamento Aprovadas	Unidade	P	0	3	0	700,000
			P(a)	0	3	0	700,000
			A	0	0	0	0
1.6	Plano de Manejo da Área de Proteção Ambiental do Maciço Central Elaborado	Plano	P	0	1	0	200,000
			P(a)	0	1	0	200,000
			A	0	0	0	0
1.7	Áreas verdes restauradas	hectares	P	0	88	0	2,280,000
			P(a)	0	88	0	2,280,000
			A	0	0	0	0
1.8	Fontes de Água Implantadas	Unidade	P	0	15	0	430,000
			P(a)	0	15	0	430,000
			A	0	0	0	0
1.9	Obras de contenção realizadas	Obra	P	0	60	0	4,705,000
			P(a)	0	60	0	4,705,000
			A	0	0	0	0
1.10	Plano Diretor de Mudanças Climáticas Elaborado	Plano	P	0	1	0	1,300,000
			P(a)	0	1	0	1,300,000
			A	0	0	0	0
1.11	Inventário Arborização Urbano atualizado	Inventário	P	0	1	0	500,000
			P(a)	0	1	0	500,000
			A	0	0	0	0
1.12	Servidores Capacitados	servidores	P	0	250	0	500,000
			P(a)	0	250	0	500,000
			A	50	50	0	0
1.13	Palácio Municipal reformado	Unidade	P	0	1	0	9,500,000
			P(a)	0	1	0	9,500,000
			A	0	0	0	0
1.14	Centro de Inteligência Municipal - CIM implantado	centro	P	0	1	0	14,320,000
			P(a)	0	1	0	14,320,000
			A	0	0	0	0
1.15	Sistema de Alerta da Defesa Civil implantado	Unidade	P	0	1	0	1,600,000
			P(a)	0	1	0	1,600,000

RESULTS MATRIX

OUTPUTS: ANNUAL PHYSICAL AND FINANCIAL PROGRESS

	Output	Unit of Measure		PHYSICAL PROGRESS		FINANCIAL PROGRESS	
				2020	EOP 2024	2020	EOP 2024
1.15	Sistema de Alerta da Defesa Civil implantado	Unidade	A	0	0	0	0
1.16	Plano Estratégico do Centro Histórico elaborado	Plano	P	0	1	0	700,000
			P(a)	0	1	0	700,000
			A	0	0	0	0
1.17	Plano Diretor de Mobilidade Urbana elaborado	Plano	P	0	1	0	1,300,000
			P(a)	0	1	0	1,300,000
			A	0	0	0	0
1.18	Estudos e Projetos realizados	Projeto	P	3	7	0	2,277,000
			P(a)	0	4	0	2,777,000
			A	0	1	0	0
1.19	Plano Urbanístico da Orla Noroeste	Plano	P	0	1	0	300,000
			P(a)	0	1	0	300,000
			A	0	0	0	0

RESULTS MATRIX

OUTPUTS: ANNUAL PHYSICAL AND FINANCIAL PROGRESS

Component Nbr. 2 Componente II. Segurança Cidadã

	Output	Unit of Measure		PHYSICAL PROGRESS		FINANCIAL PROGRESS	
				2020	EOP 2024	2020	EOP 2024
2.1	Equipamentos de Saúde implantados (construção ou reforma)	unidade	P	0	4	0	7,780,000
			P(a)	0	4	0	7,780,000
			A	0	0	0	0
2.2	Escolas de Ensino Fundamental implantadas (construção ou reforma)	escola	P	0	4	0	12,050,000
			P(a)	0	4	0	12,050,000
			A	0	0	0	0
2.3	Equipamentos Públicos de Assistência Social implantados	unidade	P	0	7	0	5,264,000
			P(a)	0	7	0	5,264,000
			A	0	0	0	0
2.4	Centros de Informática implantados para o Vix Lab	centro	P	0	8	0	2,000,000
			P(a)	0	8	0	2,000,000
			A	0	0	0	0
2.5	Capacitações para Guarda Municipal realizada	cursos	P	0	9	17,200	172,000
			P(a)	0	10	0	189,200
			A	0	0	17,200	17,200
2.6	Base da Guarda Municipal Construída	unidade	P	0	1	0	2,365,000
			P(a)	0	1	0	2,365,000
			A	0	0	0	0
2.7	Rede Integrada de Prevenção Social da Violência implantada	unidade	P	0	1	0	500,000
			P(a)	0	1	0	500,000
			A	0	0	0	0
2.8	Atividades Culturais e Artísticas realizadas	Atividade	P	0	105	0	1,050,000
			P(a)	0	115	0	1,050,000
			A	0	0	0	0
2.9	Escolas atendidas por Educação em Direitos Humanos	Escolas	P	0	14	0	1,000,000
			P(a)	0	14	0	1,000,000
			A	0	0	0	0
2.10	Pessoas atendidas pelo Programa Qualifica VIX	pessoas	P	0	15,000	0	1,000,000
			P(a)	0	15,000	0	1,000,000
			A	0	0	0	0
2.11	Escolinha de Educação Esportiva implantadas na região 1, 2, 3, 4 e 7	Escolinha	P	0	5	0	1,000,000
			P(a)	0	5	0	1,000,000
			A	0	0	0	0

Other Cost

	Gestão do Projeto	P			310,000	14,091,000
		P(a)			310,000	14,073,800
		A			608,289.57	608,289.57

Total Cost

	Total Cost	P			327,200	124,500,000
		P(a)			310,000	125,000,000
		A			625,489.57	625,489.57

CHANGES TO THE MATRIX

Section	Name	Type of Change	Subtype	Modified By	Entered in the System
Output	Capacitações para Guarda Municipal realizada	Modify Output	Modify Financial EOP P(a) value - caused by a change in the Financial P(a).	DANIELADO	03/26/2021
	Ciclovía Tancredão – Praça dos Namorados Implantada	Modify contribution to CRF Indicator	Flag contribution to CRF indicator	DANIELADO	03/29/2021
	Estudos e Projetos realizados	Modify Output	Modify Physical Historical Actual	DANIELADO	03/26/2021
	Orla Noroeste Requalificada- 1A	Modify contribution to CRF Indicator	Flag contribution to CRF indicator	DANIELADO	03/29/2021
	Orla Noroeste Requalificada- 1B	Modify contribution to CRF Indicator	Flag contribution to CRF indicator	DANIELADO	03/29/2021
	Áreas verdes restauradas	Modify contribution to CRF Indicator	Flag contribution to CRF indicator	DANIELADO	03/29/2021

PMR Public Report

IMPLEMENTATION STATUS AND LEARNING

Lesson Learned - Categories

Project Monitoring & Evaluation
