

PMR Public Report

Operation Number	HA-L1087	Chief of Operations Validation Date	04/15/21
Year- PMR Cycle	Second period Jan-Dec 2020	Division Chief Validation Date	04/29/21
Last Update	03/29/21	Country Representative Validation Date	05/16/21
PMR Validation Stage	Validated by Representative		

Basic Data

Operation Profile

Operation Name	Water Management Program in the Artibonite Basin	Loan Number	3089/GR-HA
Executing Agency	MINISTERE DE L'AGRICULTURE DES RESSOURCES NATURELLES ET DU DEVELOPPEMENT RURAL	Sector/Subsector	AGRICULTURE AND RURAL DEVELOPMENT-SUSTAINABLE AGRICULTURAL DEVELOPMENT
Team Leader	DE SALVO, CARMINE PAOLO	Overall Stage	Disbursing (From eligibility until all the Operations are closed)
Operation Type	Grant Financing Product	Country	Haiti
Lending Instrument	Investment Loan	Convergence related Operation(s)	
Borrower	REPUBLIQUE D'HAITI		


Environmental and Social Safeguards

Impacts Category	B	Was/Were the objective(s) of this operation reformulated?	NO
Safeguard Performance Rating		Date of approval	
Safeguard Performance Rating - Rationale			

Financial Data

Item	Total Cost and Source					Available Funds (US\$)			
	Original IDB	Current IDB	Local Counterpart	Co-Financing / Country	Total Original Cost	Current IDB	Disb. Amount to Date	% Disb	Undisbursed Amount
HA-L1087	0	25,000,000	2,500,000	0	27,500,000	25,000,000	23,559,590.39	94.24%	1,440,409.61
Aggregated	0	25,000,000	2,500,000	0	27,500,000	25,000,000	23,559,590.39	94.24%	1,440,409.61

Expense Categories by Loan Contract (cumulative values)

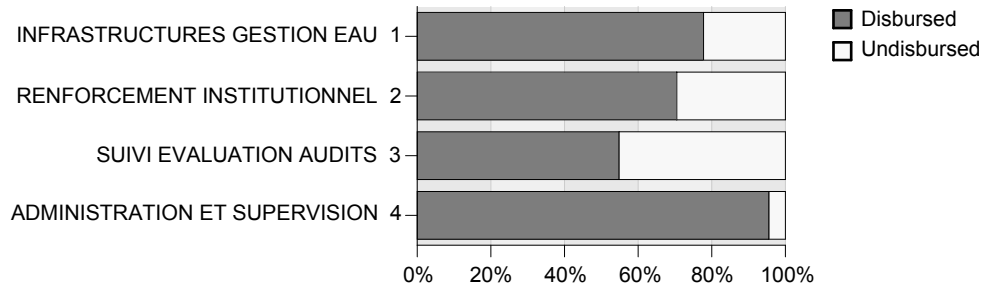

Please note that inactive indicators and outputs are not displayed; totals in the actual cost table may not match the sum of the cost of the outputs displayed, due to the cost of inactive outputs.

PMR Public Report

RESULTS MATRIX

General Development Objectives

General Development Objectives Nbr. 1: Decrease crop, livestock and infrastructure losses caused by flooding in the Artibonite watershed.

Observation:

	Indicator	Unit of Measure	Baseline	Baseline Year	Expected Year of Achievement		Target
1.1	Value of annual agricultural damages caused by flooding in the Artibonite watershed	USD thousands	8,700.00	2013	2021	P	1,738.00
						A	

Details

Means of verification: Means of Verification: Specific evaluation by the Ministry of Agriculture, using the same sample as Artelia.

Observations: Source of baseline: Artelia surveys

Pro-Gender	No	Pro-Ethnicity	No
The General Development objective indicator target is expected to be observed by the operation's "Fully Justified" date in Convergence (CO)			
	No		

PMR Public Report

RESULTS MATRIX

General Development Objectives

General Development Objectives Nbr. 2: Increase agricultural productivity in the Artibonite watershed.

Observation:

	Indicator	Unit of Measure	Baseline	Baseline Year	Expected Year of Achievement		Target
2.1	In the irrigation district: average annual gross margins of rice for beneficiary farmers	US\$/Ha	1,176.00	2013	2021	P	1,515.00
						A	

Details

Means of verification: Household surveys during the final evaluation (ex-post economic analysis), using the same sample as Artelia.

Observations: Source and year of baseline: Artelia and AECOM.

Pro-Gender No **Pro-Ethnicity** No

The General Development objective indicator target is expected to be observed by the operation's "Fully Justified" date in Convergence (CO) No

	Indicator	Unit of Measure	Baseline	Baseline Year	Expected Year of Achievement		Target
2.2	In the upper watershed: difference in average annual gross margins in selected gullies between the group of beneficiaries and control	US\$/Ha	0.00	2013	2021	P	1,556.00
						A	

Details

Means of verification: Household surveys conducted by the firm contracted for impact evaluation.

Observations: (1) According to a study (Bayard, 2013), the typical crop association in gullies change from a low-profit grain-based cropping pattern ?without? infrastructure to a high-profit banana-grain-based pattern ?with? infrastructure.(2) The randomized phase-in o

Pro-Gender No **Pro-Ethnicity** No

The General Development objective indicator target is expected to be observed by the operation's "Fully Justified" date in Convergence (CO) No

PMR Public Report

RESULTS MATRIX

Specific Development Objectives

Specific Development Objectives Nbr. 1: OUTCOME 1: Improve water and sediment containment in selected gullies of the upper Artibonite watershed.

Observation:

Indicator		Unit of Measure	Baseline	Baseline Year		2014	2015	2016	2017	2018	2019	2020	EOP 2021
1.1	Indicator 1.1: Total volume of sediment contained by check-dams	m3	0.00	2013	P								66,500.00
					A								

Details

Means of verification: Day-to-day observations and measurements performed by field-based students affiliated to MARNDR's Studies and Programming Unit (UEP)

Observations: The volume of sediments contained is a good indicator of the program's environmental benefit because in the absence of check-dams, these sediments would have flown downstream and contributed to the silting of infrastructures, including the Péligre reservoir

Pro-Gender No **Pro-Ethnicity** No

Indicator		Unit of Measure	Baseline	Baseline Year		2014	2015	2016	2017	2018	2019	2020	EOP 2021
1.2	Indicator 1.2: Market gardens created in the gullies	Ha	0.00	2013	P								620.00
					A								

Details

Means of verification: Day-to-day observations and measurements performed by field-based students affiliated to MARNDR's Studies and Programming Unit (UEP)

Observations: The total area of market gardens created on the upstream side of check-dams is a good indicator of the program's local economic benefit (agricultural intensification systematically observed on those areas).

Pro-Gender No **Pro-Ethnicity** No

Indicator		Unit of Measure	Baseline	Baseline Year		2014	2015	2016	2017	2018	2019	2020	EOP 2021
1.3	Indicator 1.3: Total annual volume of water stored by water retention tanks	m3	0.00	2013	P								52,000.00
					A								

Details

Means of verification: Day-to-day observations and measurements performed by field-based students affiliated to MARNDR's Studies and Programming Unit (UEP)

Observations: Water retention tanks built on the downstream side of check-dams will store rainwater and will thus facilitate access to water usable for agricultural as well as domestic purposes by local populations. Field observation (Saintil, 2013) suggests that a wat

Pro-Gender No **Pro-Ethnicity** No

Indicator		Unit of Measure	Baseline	Baseline Year		2014	2015	2016	2017	2018	2019	2020	EOP 2021
1.4	Indicator 1.4: Farmers who benefit from new cultivable area and better access to water.	# of farmers	0.00	2013	P								2,350.00
					A								

PMR Public Report

RESULTS MATRIX

Specific Development Objectives

Details												
Means of verification: Household surveys performed by field-based students affiliated to MARNDR's Studies and Programming Unit (UEP)												
Observations: Each check-dam will benefit one farmer (and his family). Each water tank will benefit at least 10 additional farmers (and their family).												
Pro-Gender		No			Pro-Ethnicity		No					

Specific Development Objectives Nbr. 2: OUTCOME 2: Improve water distribution in the Artibonite irrigation district

Observation:

Indicator		Unit of Measure	Baseline	Baseline Year		2014	2015	2016	2017	2018	2019	2020	EOP 2021
2.1	Indicator 2.1: Surface of the irrigation district that benefit optimal waterflows in the pilot area	Ha	0.00	2013	P								3,300.00
					A								

Details												
Means of verification: Water flows will be measured at gates (100 measuring devices installed, including a tele-monitoring unit at ODVA = output 6).												
Observations: ?Optimal flows? means that actual waterflows measured are consistent with theoretical waterflows (for which the canals were designed) and that there is no excess, scarcity or waste of water in the irrigation system.												
Pro-Gender		No			Pro-Ethnicity		No					

Indicator		Unit of Measure	Baseline	Baseline Year		2014	2015	2016	2017	2018	2019	2020	EOP 2021
2.2	Indicator 2.2: Number of farmers that benefit a better water distribution in the pilot area of the irrigation district	# of farmers	0.00	2013	P								6,400.00
					A								

Details												
Means of verification: Water Users Associations' registry of members.												
Pro-Gender		No			Pro-Ethnicity		No					

Specific Development Objectives Nbr. 3: OUTCOME 3: Decrease waterlogging in the Artibonite irrigation district

Observation:

Indicator		Unit of Measure	Baseline	Baseline Year		2014	2015	2016	2017	2018	2019	2020	EOP 2021
3.1	Indicator 3.1: Surface cultivated in formerly uncultivated and hydromorphic area	Ha	0.00	2013	P								3,000.00
					A								

Details												
Means of verification: Measures of areas with GPS.												
Pro-Gender		No			Pro-Ethnicity		No					

Indicator		Unit of Measure	Baseline	Baseline Year		2014	2015	2016	2017	2018	2019	2020	EOP 2021
-----------	--	-----------------	----------	---------------	--	------	------	------	------	------	------	------	----------

PMR Public Report

RESULTS MATRIX

Specific Development Objectives

3.2	Indicator 3.2: Number of farmers cultivating in formerly uncultivated and hydromorphic area	# of farmers	0.00	2013	P								7,500.00
					A								
Details													
Means of verification: WUA's registry of members.													
Pro-Gender		No			Pro-Ethnicity		No						

Specific Development Objectives Nbr. 4: OUTCOME 4: Improve flood management at Peligre dam

Observation:

Indicator		Unit of Measure	Baseline	Baseline Year		2014	2015	2016	2017	2018	2019	2020	EOP 2021
4.1	Indicator 4.1: Days with water level at Péligre dam above the maximum limit for flood management	Days	75.00	2011	P	75.00	0.00	0.00	0.00	0.00			0.00
					A	0.00	0.00	0.00					
Details													
Means of verification: EDH operation reports at Peligre dam and flood management software (see output 8)													
Observations: According to the dam?s operations manual, if the water level is above 166 Meters Above Sea Level (MASL) between May 1st and June 15th or above 168 MASL between September 15th and October 15th, the Péligre dam cannot act as a buffer in case of heavy rains													
Pro-Gender		No			Pro-Ethnicity			No					

Indicator		Unit of Measure	Baseline	Baseline Year		2014	2015	2016	2017	2018	2019	2020	EOP 2021
4.2	Indicator 4.2: Days with water flows released by Péligre dam above 400 m3/sec	Days	18.00	2011	P	18.00	0.00	0.00	0.00	0.00			0.00
					A	0.00	0.00	0.00					
Details													
Means of verification: EDH operation reports at Peligre dam and flood management software (see output 8)													
Observations: Flooding in the Valley is inevitable if Canneau dam receives water flows above 500 m3/sec, then if Peligre dam releases more than 400 M3/sec (flow at Canneau = flows from Peligre + flows for others tributaries).													
Pro-Gender		No			Pro-Ethnicity			No					

Specific Development Objectives Nbr. 5: OUTCOME 5: Improve ODVA's internal management

Observation:

Indicator		Unit of Measure	Baseline	Baseline Year		2014	2015	2016	2017	2018	2019	2020	EOP 2021
5.1	Indicator 5.1: Financial statements prepared by external auditors issued with a positive opinion	Audit	0.00	2013	P	0.00	0.00	0.00	1.00	1.00			1.00
					A	0.00	0.00	0.00					
Details													
Means of verification: Annual audits prepared by external auditors..													

PMR Public Report

RESULTS MATRIX

Specific Development Objectives

Observations: The correct fiduciary and internal control management of ODVA is a key part of the general capacity of ODVA to properly operate and maintain the main infrastructures of the irrigation district. Targets don't cumulate.

Pro-Gender No **Pro-Ethnicity** No

Specific Development Objectives Nbr. 6: OUTCOME 6: Improve operations and maintenance of hydraulic infrastructures and equipment in the irrigation district

Observation:

Indicator		Unit of Measure	Baseline	Baseline Year		2014	2015	2016	2017	2018	2019	2020	EOP 2021
6.1	Indicator 6.1: Secondary and tertiary canals and drains dredged (manually) by the 3 WUAs in the pilot area	Meters	86.00	2012	P	86.00	86.00	108.00	136.40	136.40			1,364.00
					A	0.00	0.00	40.60					

Details

Means of verification: WUAs annual reports on operations, maintenance and collection of water tariffs (reports controlled by Technical Assistance firm)

Observations: Measures the level of maintenance provided by WUAs. The existing network counts with 86Km of canals and drains; the project will built 50.4 additional Km. The dredging of the existing 86Km by WUAs in 2012 was financed by ODVA. Targets don't cumulate.

Pro-Gender No **Pro-Ethnicity** No

Indicator		Unit of Measure	Baseline	Baseline Year		2014	2015	2016	2017	2018	2019	2020	EOP 2021
6.2	Indicator 6.2: Rate of cost recovery in the 3 WUAs of the pilot area	%	0.00	2013	P	0.00	50.00	75.00	75.00	75.00			75.00
					A	0.00	0.00	0.00					

Details

Means of verification: WUAs annual reports on operations, maintenance and collection of water tariffs (reports controlled by Technical Assistance firm)

Observations: Measures the WUAs' financial viability (the capacity of WUAs to operate without subsidies). Water tariffs will be at least \$US10/Ha/year. Targets don't cumulate.

Pro-Gender No **Pro-Ethnicity** No

RESULTS MATRIX

OUTPUTS: ANNUAL PHYSICAL AND FINANCIAL PROGRESS

Component Nbr. 1 Component 1. Water and sediment management infrastructures

	Output	Unit of Measure		PHYSICAL PROGRESS		FINANCIAL PROGRESS	
				2020	EOP 2021	2020	EOP 2021
1.1	Output 1: Water and sediment containment infrastructures built in gullies in the pilot area of the upper watershed	Infrastructures	P		950		5,262,500
			P(a)	50	397	400,000	3,622,111.27
			A	50	397	666,485	3,562,111.27
1.2	Output 2: Electromechanical system (gates and automatic control) at Canneau dam rehabilitated	System	P		1		621,143
			P(a)		1	233,250	1,234,624.57
			A	0	1	882,986	1,164,624.57
1.3	Output 3: Protection walls preventing the Left and Right Banks Master Canals from collapsing downstream Canneau dam: built	Wall	P		2		2,690,986
			P(a)		2		1,881,593.95
			A	0	2	26,836	1,881,593.95
1.4	Output 4: Secondary and tertiary irrigation and drainage canals built or rehabilitated, and equipped, in the pilot area of the irrigation district	Kilometers	P		50.4		4,441,708
			P(a)		41.7	88,685.42	3,485,935.64
			A	0	41.7	0	3,485,935.64
1.5	Output 5: Primary irrigation and drainage canals dredged in the irrigation district	Meters	P		120,000		3,451,500
			P(a)		115,168	1,000,000	1,742,556.04
			A	0	115,168	0	1,522,556.04
1.6	Output 6: Equipment to regulate and measure water flow built/installed on the main canals of the irrigation district	Device	P		100		1,435,320
			P(a)		1		198,998.51
			A	0	1	0	198,998.51

RESULTS MATRIX

OUTPUTS: ANNUAL PHYSICAL AND FINANCIAL PROGRESS

Component Nbr. 2 Component 2. Institutional strengthening

	Output	Unit of Measure		PHYSICAL PROGRESS		FINANCIAL PROGRESS	
				2020	EOP 2021	2020	EOP 2021
2.1	Output 7: Meetings of the Péligre Commission taking place	Meetings	P		27		345,000
			P(a)	1	14	20,000	187,041.13
			A	2	14	37,225	187,041.13
2.2	Output 8: Flood management system (composed of water level gauges, flood management software and one computer per dam) operating at the Péligre and Canneau dams	System	P		1		338,725
			P(a)	0	0	200,000	30,000
			A	0	0	0	0
2.3	Output 10: ODVA's procedures manual for operation and maintenance of infrastructure and equipment prepared	Manual	P		1		128,011
			P(a)		1	5,000	173,535.22
			A	0	1	0	173,535.22
2.4	Output 11: CIA-ODVA's staff trained	Staff	P		20		256,024
			P(a)		20	10,000	347,069.44
			A	0		0	347,069.44
2.5	Output 12: Annual technical and financial plan and annual technical and financial report of operation and maintenance of primary infrastructures under ODVA's responsibility prepared	Reports/plans	P		9		256,023
			P(a)	0	4	10,000	347,069.34
			A	0	4	0	347,069.34
2.6	Output 13: CIA-ODVA equipped with a package of operating equipment	Package of equipment	P		1		90,000
			P(a)	1	2	1,300,000	2,052,914
			A	1	2	2,020,790	2,052,914
2.7	Output 14: ODVA's administrative and financial staff trained	Staff	P		10		150,000
			P(a)		10		21,110.39
			A	0		0	21,110.39
2.8	Output 15: Accounting software installed at the ODVA's administrative and financial service	Accounting software	P		1		15,000
			P(a)		1		19,474.65
			A	0	1	0	19,474.65
2.9	Output 16: ODVA's administrative and financial service equipped with a package of operating equipment	Package of equipment	P		1		60,000
			P(a)		1		65,759.42
			A	0	1	0	65,759.42
2.10	Output 17: DGSE-ODVA equipped with a package of operating equipment	Package of equipment	P		1		140,000
			P(a)		1	44,000	191,370.94
			A	0	1	0	191,370.94
2.11	Output 18: Water Users Associations (WUAs) equipped with office, IT equipment and motorcycles	WUAs	P		16		695,000
			P(a)	1	4	254,000	596,923
			A	1	4	219,394	581,923
2.12	Output 19: DGSE and WUA staff trained	Staff	P		170		1,487,054.5
			P(a)	0	170	130,000	1,794,563.1
			A	65		173,823	1,744,563.1
2.13	Output 20: Annual technical and financial plan and annual technical and financial report of operation and maintenance of infrastructures under WUAs' responsibility: prepared	Reports/plans	P		24		1,487,055.5
			P(a)	0	3	130,000	1,794,564.09
			A	0	3	173,824	1,744,564.09
2.14	Output 21: Farmers in Artibonite and Centre receiving agricultural inputs in support of agricultural operations in the context of the Covid19 pandemic	# of farmers	P		0		0
			P(a)	13,000	26,000	1,000,000	464,898.73
			A	25,300	25,300	376,036	376,036

RESULTS MATRIX**OUTPUTS: ANNUAL PHYSICAL AND FINANCIAL PROGRESS**

Component Nbr. 3 Administration, Monitoring and Evaluation, Audits, Contingencies

				PHYSICAL PROGRESS	FINANCIAL PROGRESS
	Output	Unit of Measure		EOP	EOP
3.			P		
			P(a)		
			A		

Other Cost

	Administration, Monitoring and Evaluation, Audits, Contingencies	P				3,898,950
		P(a)			400,000	4,641,558.57
		A			651,869.12	4,241,558.57

Total Cost

	Total Cost	P				27,500,000
		P(a)			5,224,935.42	24,893,672
		A			5,229,268.12	23,909,809.27

CHANGES TO THE MATRIX

Section	Name	Type of Change	Subtype	Modified By	Entered in the System
Output	Output 13: CIA-ODVA equipped with a package of operating equipment	Modify Output	Modify Financial EOP P(a) value - caused by a change in the Financial P(a).	DESALVO	03/29/2021
	Output 18: Water Users Associations (WUAs) equipped with office, IT equipment and motorcycles	Modify Output	Modify Financial EOP P(a) value - caused by a change in the Financial P(a).	DESALVO	03/29/2021
	Output 19: DGSE and WUA staff trained	Modify Output	Modify Financial EOP P(a) value - caused by a change in the Financial P(a).	DESALVO	03/29/2021
	Output 1: Water and sediment containment infrastructures built in gullies in the pilot area of the upper watershed	Modify Output	Modify Financial EOP P(a) value - caused by a change in the Financial P(a).	DESALVO	03/29/2021
	Output 20: Annual technical and financial plan and annual technical and financial report of operation and maintenance of infrastructures under WUAs? responsibility: prepared	Modify Output	Modify Financial EOP P(a) value - caused by a change in the Financial P(a).	DESALVO	03/29/2021
	Output 21: Farmers in Artibonite and Centre receiving agricultural inputs in support of agricultural operations in the context of the Covid19 pandemic	Modify Output	Modify Financial EOP P(a) value - caused by a change in the Financial P(a).	DESALVO	03/29/2021
		Modify contribution to CRF Indicator	Flag contribution to CRF indicator	DESALVO	03/27/2021
	Output 2: Electromechanical system (gates and automatic control) at Canneau dam rehabilitated	Modify Output	Modify Financial EOP P(a) value - caused by a change in the Financial P(a).	DESALVO	03/29/2021
	Output 3: Protection walls preventing the Left and Right Banks Master Canals from collapsing downstream Canneau dam: built	Modify Output	Modify Financial EOP P(a) value - caused by a change in the Financial P(a).	DESALVO	03/29/2021
	Output 5: Primary irrigation and drainage canals dredged in the irrigation district	Modify Output	Modify Financial EOP P(a) value - caused by a change in the Financial P(a).	DESALVO	03/29/2021
	Output 7: Meetings of the Péligre Commission taking place	Modify Output	Modify Financial EOP P(a) value - caused by a change in the Financial P(a).	DESALVO	03/29/2021
			Modify Physical EOP P(a) value - caused by a change in the Physical P(a).	CEDRICKJ	03/23/2021
	Output 8: Flood management system (composed of water level gauges, flood management software and one computer per dam) operating at the Péligre and Canneau dams	Modify Output	Modify Financial EOP P(a) value - caused by a change in the Financial P(a).	DESALVO	03/29/2021

PMR Public Report

IMPLEMENTATION STATUS AND LEARNING

Lesson Learned - Categories

Project Design
