

PMR Public Report

Operation Number	BO-L1067	Chief of Operations Validation Date	10/18/21
Year- PMR Cycle	First period Jan-Jun 2021	Division Chief Validation Date	
Last Update	10/04/21	Country Representative Validation Date	
PMR Validation Stage	Validated by Chief of Operations		

Basic Data

Operation Profile

Operation Name	Strengthening of Integrated Health Networks in the Department of Potosi	Loan Number	2614/BL-BO, 2614/BL-BO-1, 2614/BL-BO-2
Executing Agency	MINISTERIO DE PREVISION SOCIAL Y SALUD PUBLICA	Sector/Subsector	HEALTH-HEALTH SERVICES
Team Leader	BUSCARONS CUESTA, LUIS	Overall Stage	Fully Disbursed
Operation Type	Loan Operation	Country	Bolivia
Lending Instrument	Investment Loan	Convergence related Operation(s)	
Borrower	REPUBLICA DE BOLIVIA		


Environmental and Social Safeguards

Impacts Category	B	Was/Were the objective(s) of this operation reformulated?	NO
Safeguard Performance Rating	Partially Unsatisfactory	Date of approval	
Safeguard Performance Rating - Rationale	Debido a incumplimientos en acuerdos previos para el área de construcción del hospital, licencias ambientales (LASP). Se construyó el hospital de Llallagua en territorio indígena se establecieron acuerdos con el ayllu Chullpa y se acordaron medidas de compensación específicas que no se han cumplido, se desarrolló un plan de acción correctiva por primera vez en 2016, el cual no fue cumplido. La misión de supervisión del año 2021 mostró avances en estas áreas identificadas, pero que todavía no son suficientes para dar por cumplidos los compromisos. El equipo BID ha realizado un esfuerzo conjunto con la agencia ejecutora y se han contratado consultores externos para que puedan colaborar con el cumplimiento de los pendientes. Al haberse evidenciado que existe acciones concretas con responsables y tiempos definidos para la verificación de los compromisos, además de evidencia inicial de cumplimiento, el desempeño de esta última misión es de Parcialmente Insatisfactorio.		

Financial Data

Item	Total Cost and Source					Available Funds (US\$)			
	Original IDB	Current IDB	Local Counterpart	Co-Financing / Country	Total Original Cost	Current IDB	Disb. Amount to Date	% Disb	Undisbursed Amount
BO-L1067	35,000,000	35,000,000	7,270,000	0	42,270,000	35,000,000	35,000,000	100.00%	0
Aggregated	35,000,000	35,000,000	7,270,000	0	42,270,000	35,000,000	35,000,000	100.00%	0

Expense Categories by Loan Contract (cumulative values)

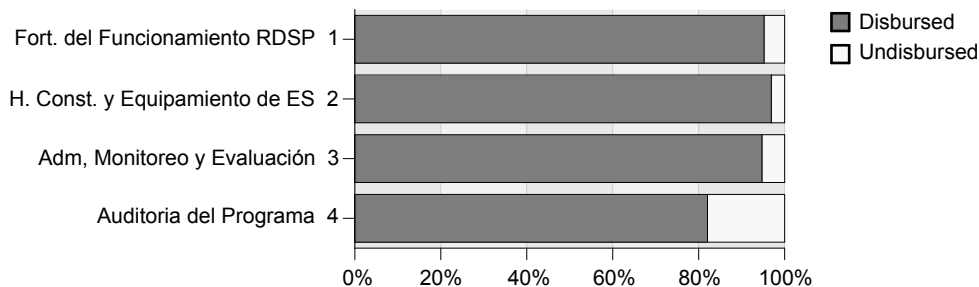

Please note that inactive indicators and outputs are not displayed; totals in the actual cost table may not match the sum of the cost of the outputs displayed, due to the cost of inactive outputs.

PMR Public Report

RESULTS MATRIX

General Development Objectives

General Development Objectives Nbr. 1: Mortalidad materno infantil en el Departamento de Potosi reducida

Observation:

	Indicator	Unit of Measure	Baseline	Baseline Year	Expected Year of Achievement		Target
1.1	Tasa de mortalidad infantil por 1000 NV	por 1000 NV	50.00	2003	2017	P	30.00
						A	

Details

Means of verification: Encuesta Nacional de Demografia y Salud

Pro-Gender No **Pro-Ethnicity** No

The General Development
bjective indicator target is
expected to be observed by
the operation's "Fully
Justified" date
in Convergence (CO)

	Indicator	Unit of Measure	Baseline	Baseline Year	Expected Year of Achievement		Target
1.2	Razon de Mortalidad materna en el Departamento de Potosi	Razon	310.00	2008	2017	P	100.00
						A	

Details

Means of verification: Encuesta Nacional de Demografia y Salud

Observations: Existe discrepancias entre las cifras de fuentes nacionales (Ministerio de Salud) e internacionales (OMS/OPS) para este indicador, siendo los internacionales en el rango de 350 - 400 para Potosí. Adicionalmente, es probable que en los primeros años de ejecución, se registrarán más muertes por mejoras en el registro. (2015, esta por publicarse un estudio específico sobre mortalidad materna a partir del levantamiento de información en puestos "Centinela")

Pro-Gender Yes **Pro-Ethnicity** No

The General Development
bjective indicator target is
expected to be observed by
the operation's "Fully
Justified" date
in Convergence (CO)

	Indicator	Unit of Measure	Baseline	Baseline Year	Expected Year of Achievement		Target
1.3	Tasa de Mortalidad neonatal	por 1000 NV	27.00	2003	2017	P	0.00
						A	

PMR Public Report

RESULTS MATRIX

General Development Objectives

Details			
Means of verification: Encuesta Nacional de Demografia y Salud			
Pro-Gender	No	Pro-Ethnicity	No
<p>The General Development objective indicator target is expected to be observed by the operation's "Fully Justified" date in Convergence (CO)</p>			

PMR Public Report

RESULTS MATRIX

Specific Development Objectives

Specific Development Objectives Nbr. 1: Acceso a servicios de salud de calidad en el Departamento de Potosi mejorado

Observation:

Indicator		Unit of Measure	Baseline	Baseline Year		2013	2014	2015	2016	2017	2018	2020	2021	EOP 2022
1.1	Cobertura de Parto Institucional	porcentaje	36.00	2010	P									55.00
					A				0.00	50.00	64.40			

Details

Means of verification: SNIS Departamental (Potosí)

Pro-Gender	Yes	Pro-Ethnicity	No
-------------------	-----	----------------------	----

Indicator		Unit of Measure	Baseline	Baseline Year		2013	2014	2015	2016	2017	2018	2020	2021	EOP 2022
1.2	Mujeres con complicación obstétrica atendidas en Hospital	Porcentaje	56.00	2010	P									80.00
					A				0.00		20.10			

Details

Means of verification: Registros hospitalarios

Observations: El proyecto deberá establecer un sistema de monitoreo específico para este indicador.

Pro-Gender	Yes	Pro-Ethnicity	No
-------------------	-----	----------------------	----

Indicator		Unit of Measure	Baseline	Baseline Year		2013	2014	2015	2016	2017	2018	2020	2021	EOP 2022
1.3	Disponibilidad de mantenimiento de equipos médicos y no médicos por nivel de establecimientos de salud	Porcentaje	10.00	2011	P									50.00
					A				0.00		0.00			

Details

Means of verification: Informes específicos del proyecto.

Pro-Gender	No	Pro-Ethnicity	No
-------------------	----	----------------------	----

Indicator		Unit of Measure	Baseline	Baseline Year		2013	2014	2015	2016	2017	2018	2020	2021	EOP 2022
1.4	Establecimientos de Salud que cumplan con las normas de caracterización del Ministerio de Salud y Deportes en cuanto a infraestructura, equipo y Recursos Humanos	Número	0.00	2011	P									200.00
					A				0.00		13.00			

Details

Means of verification: Informes de Servicio Departamental de Salud, al final del proyecto se puede verificar con el Estudio de Brechas

Pro-Gender	No	Pro-Ethnicity	No
-------------------	----	----------------------	----

PMR Public Report

RESULTS MATRIX

Specific Development Objectives

Indicator		Unit of Measure	Baseline	Baseline Year		2013	2014	2015	2016	2017	2018	2020	2021	EOP 2022
1.5	Recursos Humanos con capacitación CONE por tipo de establecimiento de salud	Personas	50.00	2011	P									200.00
					A				0.00		0.00			

Details

Means of verification: Informe específico del proyecto.

Pro-Gender

No

Pro-Ethnicity

No

Indicator		Unit of Measure	Baseline	Baseline Year		2013	2014	2015	2016	2017	2018	2020	2021	EOP 2022
1.6	Personas Atendidas por un paquete básico de servicios de salud, que incluye parto institucional (madre y niño)	# of beneficiaries	1,902.00	2013	P	0.00	500.00	1,000.00	1,500.00	2,000.00				5,000.00
					A		0.00	0.00	0.00		20,271.00			

Details

Means of verification: Registro del Bono Juana Azurduy

Observations: Se considerará al binomio Madre - Hijo que ha recibido atención al parto y atención post-parto

Pro-Gender

No

Pro-Ethnicity

No

	Indigenous				P									
					A						20,271.00			

RESULTS MATRIX

OUTPUTS: ANNUAL PHYSICAL AND FINANCIAL PROGRESS

Component Nbr. 1 Fortalecimiento de la Red Departamental de Potosi

	Output	Unit of Measure		PHYSICAL PROGRESS		FINANCIAL PROGRESS	
				2021	EOP 2022	2021	EOP 2022
1.1	Diagnosticos del sector salud realizados.	Estudio	P		3		100,000
			P(a)		3		128,305.14
			A		3		128,305.14
1.2	Plan de promoción de salud implementado	Plan	P		1		1,018,000
			P(a)		1		337,326.79
			A		1		349,178.79
1.3	Obstetricas incorporadas al sistema de salud	Personas	P		30		210,000
			P(a)		30		535,612
			A		30		535,612
1.4	Personal de los centros de primer nivel capacitado	Personas	P		200		200,000
			P(a)		306		177,071.15
			A		306		177,071.15
1.5	Sistema de Comunicación de referencias y urgencias implementado	Sistema	P		1		500,000
			P(a)		1		1,460,170.77
			A		1		1,460,202.77
1.6	Protocolo de referencia y retorno elaborado y/o adecuado	Documento	P		1		75,000
			P(a)		1		5,002.48
			A		1		5,002.48
1.7	Unidad de transporte para referencias y urgencias incorporada	Unidad	P		1		450,000
			P(a)		1		311,867
			A		1		311,867
1.8	Estrategia de Gestión Institucional de la Red Departamental implementada	Estrategia	P		1		1,314,000
			P(a)		1	4,507	1,495,500.3
			A		1	0	1,490,993.3
1.9	Personas capacitadas en mantenimiento de equipo médico-industrial, gestión financiera-administrativa y/o gestión de infraestructura y personal	Personas	P		90		280,000
			P(a)		90		322,696.02
			A		125		327,504.02
1.10	Sistema de Gestión de Medicamentos implementado	Sistema	P		1		68,000
			P(a)		1	7,289	44,783.76
			A		1	0	37,494.76

RESULTS MATRIX

OUTPUTS: ANNUAL PHYSICAL AND FINANCIAL PROGRESS

Component Nbr. 2 Inversiones en infraestructura y equipamiento

	Output	Unit of Measure		PHYSICAL PROGRESS		FINANCIAL PROGRESS	
				2021	EOP 2022	2021	EOP 2022
2.1	Hospital "Madre Obrera" de Llalagua diseñado	Hospital	P		1		310,000
			P(a)		1		452,429.71
			A		1		452,429.71
2.2	Hospital "Madre Obrera" de Llalagua construido	Hospital	P		1		6,730,000
			P(a)		1	53,211.45	12,488,833.38
			A		1	53,211.45	12,488,833.38
2.3	Capacidad del Hospital "Madre Obrera" de Llalagua ampliada	Hospital	P		0		0
			P(a)		0	665,678.56	665,678.56
			A		1	496,950.86	496,950.86
2.4	Hospital "Madre Obrera" de Llalagua equipado	Hospital	P		1		2,106,000
			P(a)		1		1,224,358.27
			A		1		1,224,358.26
2.5	Hospital Ocuri construido	Hospital	P		1		4,200,000
			P(a)		1	880,936.16	6,918,906.17
			A		1	0	6,037,970.01
2.6	Capacidad del Hospital de Ocuri ampliada	Hospital	P		0		0
			P(a)		0	6,143.89	6,143.89
			A		1	0	0
2.7	Hospital de Ocuri equipado	Hospital	P		1		1,180,000
			P(a)		1		516,210.22
			A		1		516,210.22
2.8	Hospitales de Ocuri y Llalagua operando	Hospital	P		2		4,220,000
			P(a)	0	2		4,220,000
			A	0	0	0	56,338
2.9	Centro de coordinación de urgencias construido	Centro	P		1		450,000
			P(a)		1		1,049,893.47
			A		1		1,049,893.47
2.10	Establecimientos de salud ampliados y/o remodelados	Establecimiento	P		1		2,800,000
			P(a)		7		2,732,912.87
			A		7		2,732,912.87
2.11	Establecimientos de salud construidos	Establecimiento	P		2		1,800,000
			P(a)		2		1,942,152.62
			A		2		1,942,152.62
2.12	Establecimientos de salud equipados	Establecimiento	P		8		8,549,185
			P(a)		11		2,030,175.9
			A		11		2,030,175.9

Other Cost

	Administración y/o fortalecimiento institucional MSD y SEDES	P				740,000
		P(a)			13,358	1,522,528
		A			0	1,509,170
	Auditorías	P				200,000
		P(a)			46,647	251,564.03
		A			20,475	225,392.03
	Imprevistos	P				995,000

RESULTS MATRIX

OUTPUTS: ANNUAL PHYSICAL AND FINANCIAL PROGRESS

	Imprevistos	P(a)				0
		A				0
	Monitoreo y evaluación	P				1,100,000
		P(a)			20,000	137,316.06
		A			0	117,316.06
	Administración y/o fortalecimiento institucional FPS	P				2,674,815
		P(a)				1,865,140.18
		A				1,865,140.19

Total Cost

	Total Cost	P				42,270,000
		P(a)			1,697,771.06	42,842,578.74
		A			570,637.31	37,568,474.99

CHANGES TO THE MATRIX

No information available for this section

RISKS AND PLANNED RESPONSES

Risk ID	Risk Status		Risk Taxonomy
1	Active		N/A
	Response actions		
	1.1	Management Strategy	Status
		-	
	1.2	Management Strategy	Status
		-	
	1.3	Management Strategy	Status
		-	

Risk ID	Risk Status		Risk Taxonomy
2	Inactive		N/A
	Response actions		
	2.1	Management Strategy	Status
		-	
	2.2	Management Strategy	Status
		-	
	2.3	Management Strategy	Status
		-	

Risk ID	Risk Status		Risk Taxonomy
3	Mitigated		N/A
	Response actions		
	3.1	Management Strategy	Status
		-	
	3.2	Management Strategy	Status
		-	
	3.3	Management Strategy	Status
		-	

RISKS AND PLANNED RESPONSES

Risk ID	Risk Status		Risk Taxonomy
	3.4	Management Strategy	Status
		-	

Risk ID	Risk Status		Risk Taxonomy
4	Mitigated		N/A
	Response actions		
	4.1	Management Strategy	Status
		-	
	4.2	Management Strategy	Status
		-	
	4.3	Management Strategy	Status
		-	
	4.4	Management Strategy	Status
		-	

Risk ID	Risk Status		Risk Taxonomy
5	Mitigated		N/A
	Response actions		
	5.1	Management Strategy	Status
		-	
	5.2	Management Strategy	Status
		-	
	5.3	Management Strategy	Status
		-	
	5.4	Management Strategy	Status
		-	

RISKS AND PLANNED RESPONSES

Risk ID	Risk Status		Risk Taxonomy
6	Active		N/A
	Response actions		
	6.1	Management Strategy	Status
		-	
	6.2	Management Strategy	Status
		-	
	6.3	Management Strategy	Status
		-	
	6.4	Management Strategy	Status
		-	
	6.5	Management Strategy	Status
		-	
	6.6	Management Strategy	Status
		-	

Risk ID	Risk Status		Risk Taxonomy
7	Mitigated		N/A
	Response actions		
	7.1	Management Strategy	Status
		-	
	7.2	Management Strategy	Status
		-	

Risk ID	Risk Status		Risk Taxonomy
8	Mitigated		N/A
	Response actions		
	8.0	Management Strategy	Status
		-	

RISKS AND PLANNED RESPONSES

Risk ID	Risk Status		Risk Taxonomy

Risk ID	Risk Status		Risk Taxonomy
9	Active		N/A
	Response actions		
	9.1	Management Strategy	Status
		-	

PMR Public Report

IMPLEMENTATION STATUS AND LEARNING

Lesson Learned - Categories
Intra/Inter Coordination
Others - Organizational and Managerial Dimensions
Project Management Capacity
