

# PMR Public Report

<b>Operation Number</b>	AR-L1258	<b>Chief of Operations Validation Date</b>	10/21/21
<b>Year- PMR Cycle</b>	First period Jan-Jun 2021	<b>Division Chief Validation Date</b>	
<b>Last Update</b>	10/01/21	<b>Country Representative Validation Date</b>	
<b>PMR Validation Stage</b>	Validated by Chief of Operations		

## Basic Data

### Operation Profile

<b>Operation Name</b>	Water and Sanitation Services Development Program – Belgrano Plan	<b>Loan Number</b>	4312/OC-AR
<b>Executing Agency</b>	MINISTERIO DE OBRAS PUBLICAS , MINISTERIO DEL INTERIOR	<b>Sector/Subsector</b>	WATER AND SANITATION-WATER SUPPLY URBAN
<b>Team Leader</b>	MORENO MORENO, HENRY ALBERTO	<b>Overall Stage</b>	Disbursing (From eligibility until all the Operations are closed)
<b>Operation Type</b>	Loan Operation	<b>Country</b>	Argentina
<b>Lending Instrument</b>	Investment Loan	<b>Convergence related Operation(s)</b>	
<b>Borrower</b>	NACION ARGENTINA		


## Environmental and Social Safeguards

<b>Impacts Category</b>	B	<b>Was/Were the objective(s) of this operation reformulated?</b>	NO
<b>Safeguard Performance Rating</b>	Partially Unsatisfactory	<b>Date of approval</b>	
<b>Safeguard Performance Rating - Rationale</b>	Las obras en ejecución no cuentan con un Programa de información y consulta acordado ni que tenga la NO del Banco. Tampoco cuentan con un Programa de similares características para la gestión de quejas y reclamos.		

## Financial Data

Item	Total Cost and Source					Available Funds (US\$)			
	Original IDB	Current IDB	Local Counterpart	Co-Financing / Country	Total Original Cost	Current IDB	Disb. Amount to Date	% Disb	Undisbursed Amount
AR-L1258	200,000,000	200,000,000	70,000,000	0	270,000,000	200,000,000	6,631,384	3.32%	193,368,616
Aggregated	200,000,000	200,000,000	70,000,000	0	270,000,000	200,000,000	6,631,384	3.32%	193,368,616

## Expense Categories by Loan Contract (cumulative values)

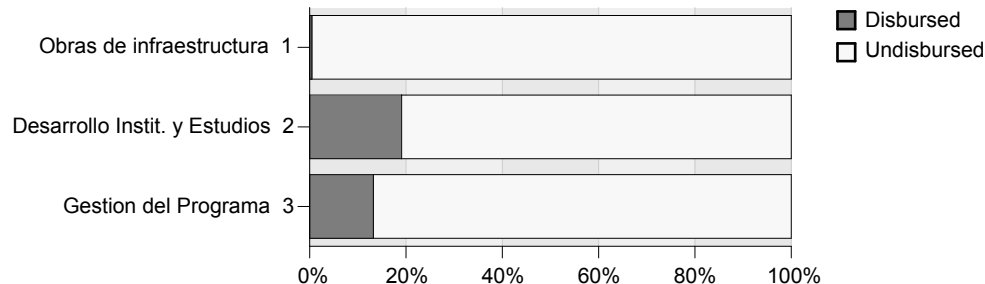

Please note that inactive indicators and outputs are not displayed; totals in the actual cost table may not match the sum of the cost of the outputs displayed, due to the cost of inactive outputs.

## PMR Public Report

### RESULTS MATRIX

#### General Development Objectives

**General Development Objectives Nbr. 0:** Mejora de la Salud y el Bienestar de la Población

**Observation:**

	Indicator	Unit of Measure	Baseline	Baseline Year	Expected Year of Achievement		Target
0.0	Incidencia de diarreas agudas en provincias del Plan Belgrano.	Incidencia de diarreas agudas en provincias del Plan Belgrano.	3,415.00	2017	2023	P	2,732.00
						A	3,415.00

#### Details

**Means of verification:** Boletín integrado de vigilancia de la Dirección Nacional de Epidemiología y Análisis de la Situación de Salud, Ministerio de Salud de la Nación.

**Observations:** Ninguna

<b>Pro-Gender</b>	No	<b>Pro-Ethnicity</b>	No
<b>The General Development objective indicator target is expected to be observed by the operation's "Fully Justified" date in Convergence (CO)</b>			
	No		

## PMR Public Report

### RESULTS MATRIX

#### Specific Development Objectives

**Specific Development Objectives Nbr. 0:** Resultado 1: Cobertura del servicio de agua potable ampliada

**Observation:**

Indicator		Unit of Measure	Baseline	Baseline Year		2017	2018	2019	2020	2021	2023	EOP 2023
0.0	Hogares con nuevo acceso a sistemas de agua potable por red en la región del Plan Belgrano.	# of households	0.00	2017	P	0.00	0.00	0.00	0.00	0.00	1,500.00	1,500.00
					A	0.00	0.00	0.00	0.00			

#### Details

**Means of verification:** Informe Semestral de Progreso del Programa e informe de Evaluación final del proyecto

**Observations:** Se considerarán los hogares beneficiarios de cada proyecto. Se medirá por proyecto/obra, se reportará globalmente

**Pro-Gender** No **Pro-Ethnicity** No

Indicator		Unit of Measure	Baseline	Baseline Year		2017	2018	2019	2020	2021	2023	EOP 2023
0.1	Cobertura de agua potable en la región del Plan Belgrano.	%	92.40	2010	P	0.00	0.00	0.00	0.00	0.00	92.47	92.47
					A	0.00	0.00	0.00	0.00			

#### Details

**Means of verification:** Informe de Evaluación final del proyecto en base a datos de Censo de Población y Vivienda y Encuestas Permanentes de Hogares del INDEC

**Pro-Gender** No **Pro-Ethnicity** No

**Specific Development Objectives Nbr. 1:** Resultado 2: Cobertura del servicio de saneamiento ampliada

**Observation:**

Indicator		Unit of Measure	Baseline	Baseline Year		2017	2018	2019	2020	2021	2023	EOP 2023
1.0	Hogares con acceso a nuevas redes cloacales en la región del Plan Belgrano	# of households	0.00	2016	P	0.00	0.00	0.00	8,750.00	14,500.00	29,000.00	29,000.00
					A	0.00	0.00	0.00	0.00			

#### Details

**Means of verification:** Informe Semestral de Progreso del Programa e informe de Evaluación final del proyecto;

**Observations:** se considerarán los hogares beneficiarios de cada proyecto. Se medirá por proyecto/obra y se reportará globalmente

**Pro-Gender** No **Pro-Ethnicity** No

Indicator		Unit of Measure	Baseline	Baseline Year		2017	2018	2019	2020	2021	2023	EOP 2023
1.1	Hogares cuyas aguas residuales son tratadas en la región del Plan Belgrano	Households (#)	100,000.00	2017	P	0.00	0.00	0.00	200,000.00	219,000.00	219,000.00	219,000.00
					A	0.00	0.00	0.00	0.00			0.00

#### Details

## PMR Public Report

### RESULTS MATRIX

#### Specific Development Objectives

**Means of verification:** Informe Semestral de Progreso del Programa e informe de Evaluación final del proyecto

**Observations:** Se considerarán los hogares beneficiarios de cada proyecto. Se medirá por proyecto/obra, se reportará globalmente.

**Pro-Gender** No **Pro-Ethnicity** No

Indicator		Unit of Measure	Baseline	Baseline Year		2017	2018	2019	2020	2021	2023	EOP 2023
1.2	Cobertura de saneamiento en la región del Plan Belgrano.	%	46.70	2010	P	0.00	0.00	0.00	0.00	48.14	0.00	48.14
					A	0.00	0.00	0.00	0.00			

#### Details

**Means of verification:** Informe de Evaluación final del proyecto en base a datos de Censo de Población y Vivienda y Encuestas Permanentes de Hogares del INDEC

**Pro-Gender** No **Pro-Ethnicity** No

**Specific Development Objectives Nbr. 2:** Resultado 3: Desempeño operativo y financiero de los prestadores de servicios mejorados

**Observation:**

Indicator		Unit of Measure	Baseline	Baseline Year		2017	2018	2019	2020	2021	2023	EOP 2023
2.0	Autosuficiencia financiera (ingresos operativos/costos de operación, mantenimiento y administración). Aguas de Formosa	%	87.00	2016	P	0.00	0.00	0.00	0.00	0.00	110.00	110.00
					A	0.00	0.00	0.00	0.00			0.00

#### Details

**Means of verification:** Informe Semestral de Progreso del Programa e informe de evaluación final.

**Pro-Gender** No **Pro-Ethnicity** No

Indicator		Unit of Measure	Baseline	Baseline Year		2017	2018	2019	2020	2021	2023	EOP 2023
2.1	Autosuficiencia financiera (ingresos operativos/costos de operación, mantenimiento y administración). Agua Potable de Jujuy	%	92.70	2017	P	0.00	0.00	0.00	0.00	0.00	99.80	99.80
					A	0.00	0.00	0.00	0.00			

#### Details

**Means of verification:** Informe Semestral de Progreso del Programa e informe de evaluación final.

**Pro-Gender** No **Pro-Ethnicity** No

Indicator		Unit of Measure	Baseline	Baseline Year		2017	2018	2019	2020	2021	2023	EOP 2023
2.2	Cobertura de micromedición en la región del Plan Belgrano (Hogares con micromedidores de agua instalados y en funcionamiento / Total de hogares con servicio de agua potable por red)	%	41.00	2016	P	0.00	0.00	0.00	0.00	41.30	0.00	41.30
					A	0.00	0.00	0.00	0.00			

#### Details

## PMR Public Report

### RESULTS MATRIX

#### Specific Development Objectives

**Means of verification:** Informe Semestral de Progreso del Programa e informe de evaluación final.

Pro-Gender	No	Pro-Ethnicity	No
------------	----	---------------	----

## RESULTS MATRIX

## OUTPUTS: ANNUAL PHYSICAL AND FINANCIAL PROGRESS

## Component Nbr. 1 Componente 1: Obras de infraestructura

	Output	Unit of Measure		PHYSICAL PROGRESS		FINANCIAL PROGRESS	
				2021	EOP 2023	2021	EOP 2023
1.1	Sistemas de Agua Potable construidos	sistema	P	0	1	8,021,538	15,000,000
			P(a)	0	1	8,021,538	15,317,490
			A	0	0	0	0
1.2	Sistemas de Saneamiento construidos	sistema	P	5	5	86,785,683	232,000,000
			P(a)	0	5	714,278	230,235,771.86
			A	1	1	1,263,538	1,755,905.21

## Component Nbr. 2 Componente 2: Desarrollo institucional y estudios

	Output	Unit of Measure		PHYSICAL PROGRESS		FINANCIAL PROGRESS	
				2021	EOP 2023	2021	EOP 2023
2.1	Actividades realizadas por los prestadores priorizadas en los Planes de Gestión por Resultados	No. de Planes	P	2	4		5,325,000
			P(a)	1	3	1,171,246.5	6,827,146.43
			A	0	2	0	5,655,899.93
2.2	Micromedidores instalados en la región del Plan Belgrano.	No. de micromedidores	P	11,250	25,000	4,500,000	9,675,000
			P(a)	5,625	25,000	1,537,500	9,675,000
			A	0	0	0	0
2.3	Macromedidores instalados instalados en la región del Plan Belgrano.	No. de macromedidores	P	72	160	2,250,000	5,000,000
			P(a)	36	160	431,250	5,000,003
			A	0	0	0	0

## Other Cost

	Administración del Programa	P			300,000	1,500,000
		P(a)			300,000	1,444,588.71
		A			505,277	854,166.71
	Monitoreo, Evaluación y Auditorías	P			400,000	1,500,000
		P(a)			400,000	1,500,000
		A			38,873	38,873

## Total Cost

	Total Cost	P			102,257,221	270,000,000
		P(a)			12,575,812.5	270,000,000
		A			1,807,688	8,304,844.85

**CHANGES TO THE MATRIX**

No information available for this section

## RISKS AND PLANNED RESPONSES

Risk ID	Risk Status		Risk Taxonomy
1	Active		Planning
	Response actions		
	1.1	Management Strategy	Status
		MITIGATE	ACTIVE
Risk ID	Risk Status		Risk Taxonomy
2	Active		Sustainability
	Response actions		
	2.0	Management Strategy	Status
		-	
Risk ID	Risk Status		Risk Taxonomy
3	Inactive		Sustainability
	Response actions		
	3.0	Management Strategy	Status
		-	
Risk ID	Risk Status		Risk Taxonomy
4	Inactive		Social Environment
	Response actions		
	4.0	Management Strategy	Status
		-	
Risk ID	Risk Status		Risk Taxonomy
5	Inactive		Organizational Structure
	Response actions		
	5.0	Management Strategy	Status
		-	



RISKS AND PLANNED RESPONSES

Risk ID	Risk Status		Risk Taxonomy
6	Active		Economic and Financial Environment
	Response actions		
	6.0	Management Strategy	Status
		-	

# PMR Public Report

## IMPLEMENTATION STATUS AND LEARNING

Lesson Learned - Categories
