

PMR Public Report

Operation Number	PE-L1226	Chief of Operations Validation Date	10/20/21
Year- PMR Cycle	First period Jan-Jun 2021	Division Chief Validation Date	
Last Update	10/07/21	Country Representative Validation Date	
PMR Validation Stage	Validated by Chief of Operations		

Basic Data

Operation Profile

Operation Name	Comprehensive Rural Water and Sanitation Program (PIASAR)	Loan Number	4442/OC-PE
Executing Agency	MINISTERIO DE VIVIENDA CONSTRUCCION Y SANEAMIENTO	Sector/Subsector	WATER AND SANITATION
Team Leader	PAEZ RUBIO, TANIA	Overall Stage	Disbursing (From eligibility until all the Operations are closed)
Operation Type	Loan Operation	Country	Peru
Lending Instrument	Investment Loan	Convergence related Operation(s)	
Borrower	REPUBLICA DEL PERU		


Environmental and Social Safeguards

Impacts Category	B	Was/Were the objective(s) of this operation reformulated?	NO
Safeguard Performance Rating	Partially Satisfactory	Date of approval	
Safeguard Performance Rating - Rationale	La Agencia Ejecutora ha implementado adecuadamente los Planes de Manejo Ambiental. Se coloca una clasificación de Parcialmente Satisfactorio ya que si bien se encuentran implementando los planes y programas de gestión, se detectaron algunas brechas en la implementación del Mecanismo de Atención y Resolución de Quejas y Reclamos, en el manejo de Calidad de Aguas y Plan de Monitoreo Ambiental, y en la implementación de medidas para prevenir la transmisión de COVID en la comunidad.		

Financial Data

Item	Total Cost and Source					Available Funds (US\$)			
	Original IDB	Current IDB	Local Counterpart	Co-Financing / Country	Total Original Cost	Current IDB	Disb. Amount to Date	% Disb	Undisbursed Amount
PE-L1226	100,000,000	100,000,000	26,000,000	0	126,000,000	100,000,000	50,967,685.3	50.97%	49,032,314.7
Aggregated	100,000,000	100,000,000	26,000,000	0	126,000,000	100,000,000	50,967,685.3	50.97%	49,032,314.7

Expense Categories by Loan Contract (cumulative values)

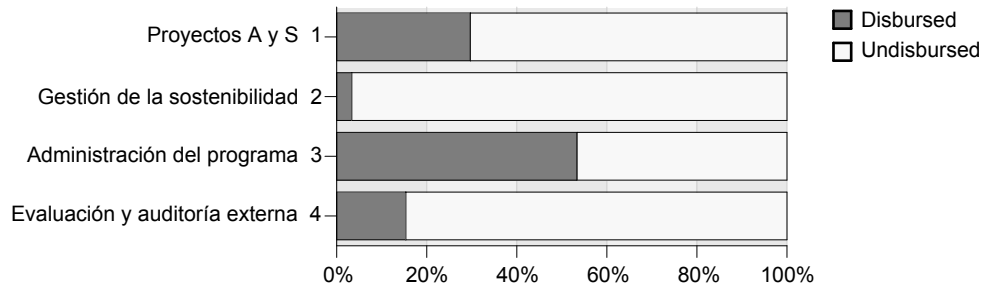

PMR Public Report

RESULTS MATRIX

General Development Objectives

No information available for this section

PMR Public Report

RESULTS MATRIX

Specific Development Objectives

Specific Development Objectives Nbr. 0: Resultado 1. Mayor acceso a agua segura en centros poblados rurales

Observation:

Indicator		Unit of Measure	Baseline	Baseline Year		2018	2019	2020	2021	2022	EOP 2022
0.0	Hogares en centros poblados rurales con acceso a agua segura	# of households	0.00	2017	P	0.00	0.00	0.00	5,000.00	10,000.00	15,000.00
					A	0.00	0.00		4,320.00		4,320.00
Details											
Means of verification: Informe de firma consultora para el fortalecimiento de la sostenibilidad a partir de encuestas a las JASS											
Observations: Se incluyen sólo los hogares de los centros poblados del programa											
Pro-Gender		No			Pro-Ethnicity			No			
	Resiliency measures included in design (# households)				P						
					A						

Specific Development Objectives Nbr. 1: Resultado 2. Mayor acceso a saneamiento seguro en centros poblados rurales

Observation:

Indicator		Unit of Measure	Baseline	Baseline Year		2018	2019	2020	2021	2022	EOP 2022
1.0	Hogares en centros poblados rurales con acceso a saneamiento seguro	# of households	0.00	2017	P	0.00	0.00	0.00	5,000.00	10,000.00	15,000.00
					A	0.00	0.00		4,523.00		4,523.00
Details											
Means of verification: Informe de firma consultora para el fortalecimiento de la sostenibilidad a partir de encuestas a las JASS											
Observations: Se incluyen sólo los hogares de los centros poblados del programa											
Pro-Gender		No			Pro-Ethnicity			No			
	Resiliency measures included in design (# households)				P						
					A						

Indicator		Unit of Measure	Baseline	Baseline Year		2018	2019	2020	2021	2022	EOP 2022
1.1	Hogares en centros poblados rurales que utilizan las UBS construidas por el programa	%	0.00	2017	P	0.00	0.00	0.00	60.00	80.00	80.00
					A	0.00	0.00		200.00		
Details											
Means of verification: Informe de firma consultora para el fortalecimiento de la sostenibilidad a partir de encuestas a una muestra de población beneficiaria											
Observations: Se incluyen sólo los hogares de los centros poblados del programa											
Pro-Gender		No			Pro-Ethnicity			No			

PMR Public Report

RESULTS MATRIX

Specific Development Objectives

Specific Development Objectives Nbr. 2: Resultado 3. Prestadores e Instituciones del sector AyS fortalecidas para la gestión sostenible de los sistemas de AyS

Observation:

Indicator		Unit of Measure	Baseline	Baseline Year		2018	2019	2020	2021	2022	EOP 2022
2.0	Sistemas de agua funcionando según especificaciones técnicas de diseño	%	0.00	2017	P	0.00	0.00	0.00	90.00	90.00	90.00
					A	0.00	0.00		32.00		

Details

Means of verification: Informe de firma consultora para el fortalecimiento de la sostenibilidad a partir del reporte de operación de las JASS

Observations: Se incluyen sólo los sistemas del Programa

Pro-Gender No **Pro-Ethnicity** No

Indicator		Unit of Measure	Baseline	Baseline Year		2018	2019	2020	2021	2022	EOP 2022
2.1	JASS cuyos ingresos operativos cubren los costos de AOM	%	0.00	2017	P	0.00	0.00	0.00	70.00	90.00	90.00
					A	0.00	0.00		0.00		

Details

Means of verification: Informes financieros de las JASS

Observations: Sobre el total de JASS del Programa.

Pro-Gender No **Pro-Ethnicity** No

Indicator		Unit of Measure	Baseline	Baseline Year		2018	2019	2020	2021	2022	EOP 2022
2.2	Sistemas rurales construidos por el programa con seguimiento anual de indicadores de prestación por parte del MVCS	%	0.00	2017	P	0.00	0.00	0.00	80.00	80.00	80.00
					A	0.00	0.00		0.00		

Details

Means of verification: Cuestionario sobre abastecimiento de AyS en el ámbito rural e Informe final del MVCS

Pro-Gender No **Pro-Ethnicity** No

Indicator		Unit of Measure	Baseline	Baseline Year		2018	2019	2020	2021	2022	EOP 2022
2.3	JASS con al menos dos mujeres en su Consejo Directivo	%	0.00	2017	P	0.00	0.00	0.00	0.00	50.00	50.00
					A	0.00	28.00		28.00		

Details

Means of verification: Actas de conformación de las JASS

Observations: Sobre el total de las JASS que se conformen durante la ejecución del Programa.

PMR Public Report

RESULTS MATRIX

Specific Development Objectives

Pro-Gender		No	Pro-Ethnicity				No				
Indicator		Unit of Measure	Baseline	Baseline Year		2018	2019	2020	2021	2022	EOP 2022
2.4	Núcleos Ejecutores con al menos una mujer en su estructura organizativa	%	0.00	2017	P	0.00	25.00	60.00			60.00
					A	0.00	18.00		80.00		
Details											
Means of verification: Actas de conformación de los Núcleos Ejecutores											
Observations: Sobre el total de los Núcleos Ejecutores del Programa.											
Pro-Gender		No	Pro-Ethnicity				No				

RESULTS MATRIX

OUTPUTS: ANNUAL PHYSICAL AND FINANCIAL PROGRESS

Component Nbr. 1 Componente I: Proyectos de Agua Potable y Saneamiento

	Output	Unit of Measure		PHYSICAL PROGRESS		FINANCIAL PROGRESS	
				2021	EOP 2022	2021	EOP 2022
1.1	Estudios definitivos de proyectos de AyS actualizados	Estudios	P	0	100	119,582.4	1,596,808
			P(a)	16	100	12,683	1,617,740
			A	10	88	0	37,678
1.2	Sistemas de agua potable en entros poblados rurales construidos o mejorados	Sistemas	P	20	100	17,112,020.4	43,204,617
			P(a)	20	100	10,875,474	42,299,997.19
			A	8	50	5,171,604	21,196,107.19
1.3	Unidades Básicas Sanitarias (UBS) en centros poblados rurales construidas	UBS	P	3,175	10,000	26,214,409.2	61,924,291.8
			P(a)	2,000	10,000	18,672,666.7	61,924,291.8
			A	1,152	4,523	7,691,103	31,484,438.98
1.4	JASS capacitadas para administrar, operar y mantener los servicios de AyS durante la operación asistida en la gestión del servicio	JAAS	P	20	100	792,028	1,510,386
			P(a)	30	100	242,382.25	1,510,385.78
			A	21	68	159,126	393,505.53
1.5	ATM capacitadas para brindar asistencia técnica a las JASS durante la operación asistida en la gestión del servicio	ATM	P	20	62	530,992	1,006,924
			P(a)	20	62	201,985.21	1,006,923.63
			A	10	45	145,866	321,106.42
1.6	Personas capacitadas en educación sanitaria y ambiental y uso de los servicios de AyS	Personas	P	9,000	15,000	2,224,754	4,776,757
			P(a)	9,000	15,000	331,255.75	4,776,757.09
			A	6,345	10,407	79,563	540,413.34
1.7	Núcleos Ejecutores capacitados en gestión y administración de proyectos	Núcleos Ejecutores	P	5	30	278,561.4	455,801
			P(a)	5	32	60,595.56	455,800.57
			A	11	38	13,261	101,307.01

RESULTS MATRIX

OUTPUTS: ANNUAL PHYSICAL AND FINANCIAL PROGRESS

Component Nbr. 2 Componente II: Gestión de la Sostenibilidad de los Servicios y Fortalecimiento de las Entidades del Sector

	Output	Unit of Measure		PHYSICAL PROGRESS		FINANCIAL PROGRESS	
				2021	EOP 2022	2021	EOP 2022
2.1	JASS equipadas para la adecuada AOM	JASS	P	50	100	289,646.4	492,691
			P(a)	53	100	403,600.37	492,691.44
			A	22	36	40,450	90,061.07
2.2	ATMs fortalecidas para brindar asistencia técnica a las JASS	ATM	P	42	62	619,972.4	1,454,300
			P(a)	35	62	972,702.29	1,454,299.63
			A	17	29	114,156	159,027.34
2.3	DRVCS fortalecidas para brindar asistencia técnica a las ATMs	Institución	P	5	9	114,803	350,858.2
			P(a)	4	9	197,347.2	350,858.2
			A	0	0	10,644	10,644
2.4	PNSR fortalecido para brindar asistencia técnica a las DRVCS y ATMs	Institución	P	0	1	149,844	303,660
			P(a)	0	1	220,006	303,660
			A	0	0	0	0
2.5	Personal del PNSR capacitado para brindar asistencia técnica a las ATMs y las DRVCS	Personas	P	25	85	158,776	539,839
			P(a)	25	600	67,073.17	539,838.56
			A	0	540	5,721	57,245.39
2.6	Sistemas de agua potable con operación técnica asistida concluida	Sistemas	P	59	100	497,686	788,319
			P(a)	42	100	146,646.34	788,319.34
			A	8	8	0	0
2.7	Sistemas de agua potable con reforzamiento de la AOM post construcción	Sistemas	P	40	80	1,014,334	2,000,000
			P(a)	12	80	105,971.34	1,999,999.68
			A	0	0	42,576	45,472.34
2.8	Diseño e implementación del plan de comunicación del programa	Plan	P	1	1	218,108.4	345,076
			P(a)	0	2	210,721.8	345,076.19
			A	1	3	55,775	123,008.39

Other Cost

	Seguimiento, Evaluación, Auditoria	P			193,343.5	627,797
		P(a)			193,343.5	627,797
		A			502,271	622,415.15
	Administración del Programa	P			1,098,232	4,621,875
		P(a)			1,447,182.87	4,621,875
		A			558,127	3,360,306

Total Cost

	Total Cost	P			51,627,093.1	126,000,000
		P(a)			34,361,637.35	125,116,311.1
		A			14,590,243	58,542,736.15

CHANGES TO THE MATRIX

No information available for this section

RISKS AND PLANNED RESPONSES

Risk ID	Risk Status		Risk Taxonomy
1	Active		Planning
	Response actions		
	1.1	Management Strategy	Status
		MITIGATE	ACTIVE
	1.2	Management Strategy	Status
		MITIGATE	ACTIVE
Risk ID	Risk Status		Risk Taxonomy
2	Active		Natural Environment
	Response actions		
	2.1	Management Strategy	Status
		MITIGATE	ACTIVE
Risk ID	Risk Status		Risk Taxonomy
3	Active		Social Environment
	Response actions		
	3.1	Management Strategy	Status
		MITIGATE	ACTIVE
	3.2	Management Strategy	Status
		MITIGATE	ACTIVE
Risk ID	Risk Status		Risk Taxonomy
4	Active		Natural Environment
	Response actions		
	4.1	Management Strategy	Status
		MITIGATE	ACTIVE
Risk ID	Risk Status		Risk Taxonomy
5	Active		Planning

RISKS AND PLANNED RESPONSES

Risk ID	Risk Status		Risk Taxonomy
	Response actions		
	5.1	Management Strategy	Status
		MITIGATE	ACTIVE
Risk ID	Risk Status		Risk Taxonomy
6	Active		Goods, and Services
	Response actions		
	6.1	Management Strategy	Status
		MITIGATE	ACTIVE
Risk ID	Risk Status		Risk Taxonomy
7	Active		Planning
	Response actions		
	7.1	Management Strategy	Status
		MITIGATE	ACTIVE
	7.2	Management Strategy	Status
		MITIGATE	ACTIVE
Risk ID	Risk Status		Risk Taxonomy
8	Active		Human Resources
	Response actions		
	8.1	Management Strategy	Status
		MITIGATE	ACTIVE
Risk ID	Risk Status		Risk Taxonomy
9	Active		Natural Environment
	Response actions		
	9.1	Management Strategy	Status
		MITIGATE	ACTIVE

RISKS AND PLANNED RESPONSES

Risk ID	Risk Status		Risk Taxonomy
10	Active		Legal Environment
	Response actions		
	10.0	Management Strategy	Status
		-	

PMR Public Report

IMPLEMENTATION STATUS AND LEARNING

Lesson Learned - Categories
Acquisitions and Procurement - Bidding Stage
Intra/Inter Coordination
Project Management Capacity
