


# PMR Public Report

Operation Number	BR-L1497	Chief of Operations Validation Date	04/17/22
Year- PMR Cycle	Second period Jan-Dec 2021	Division Chief Validation Date	05/04/22
Last Update	04/08/22	Country Representative Validation Date	05/05/22
PMR Validation Stage	Validated by Representative		
Basic Data			
Operation Profile			
Operation Name	Vitória Urban Improvement and Citizen Security Program (First Stage of the Sustainable Vitória Action Plan)	Loan Number	4617/OC-BR
Executing Agency	SECRETARIA ESPECIAL DE ESTADO DE GESTAO-SEGES	Sector/Subsector	URBAN DEVELOPMENT AND HOUSING-URBAN LAND PLANNING AND MANAGEMENT
Team Leader	ALVES, DALVE ALEXANDRE SORIA	Overall Stage	Disbursing (From eligibility until all the Operations are closed)
Operation Type	Loan Operation	Country	Brazil
Lending Instrument	Investment Loan	Convergence related Operation(s)	
Borrower	MUNICIPIO DE VITÓRIA - ES		
Environmental and Social Safeguards			
Impacts Category	B	Was/Were the objective(s) of this operation reformulated?	NO
Safeguard Performance Rating	Satisfactory	Date of approval	
Safeguard Performance Rating - Rationale	A missão foi considerada satisfatória, a Agência Executora demonstrou que se reestruturou de forma adequada, possui os profissionais técnicos requeridos; o TDR do PGAS para o Programa está em fase de licitação e possui previsão de contratação para o início do primeiro trimestre de 2022; os estudos ambientais estão sendo desenvolvidos por equipe própria; as obras da Orla Noroeste possuem previsão de contratação para o segundo trimestre de 2022. O terreno indicado para a construção do Centro de Inteligência Municipal, que apresentava um passivo ambiental foi descartado e o Centro será implantado em prédio já existente.		

Financial Data									
	Total Cost and Source					Available Funds (US\$)			
Operations	Original IDB	Current IDB	Local Counterpart	Co-Financing / Country	Total Original Cost	Current IDB	Disb. Amount to Date	% Disbursed	Undisbursed Amount
BR-L1497	100,000,000	100,000,000	25,000,000	0	125,000,000	100,000,000	300,000	0.30%	99,700,000
Aggregated	100,000,000	100,000,000	25,000,000	0	125,000,000	100,000,000	300,000	0.30%	99,700,000

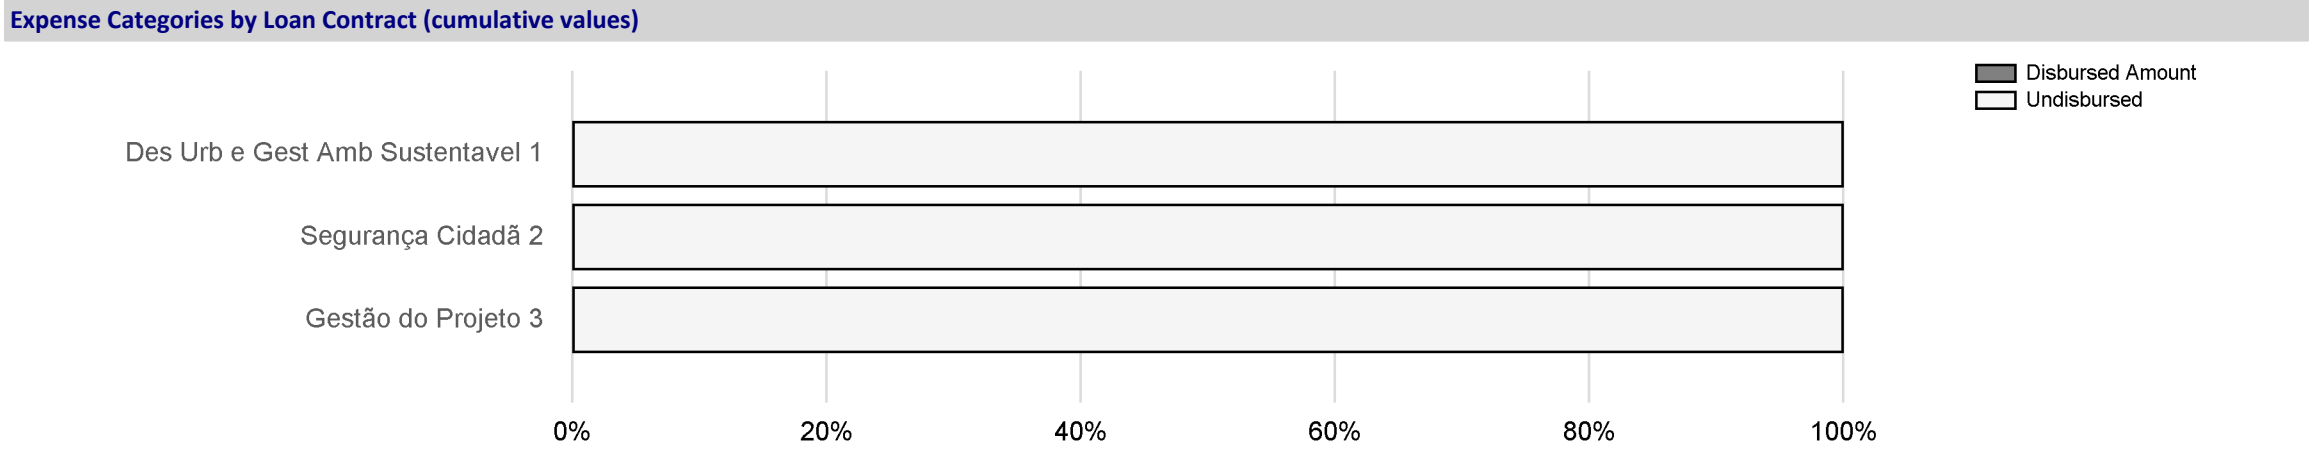

Please note that inactive indicators and outputs are not displayed; totals in the actual cost table may not match the sum of the cost of the outputs displayed, due to the cost of inactive outputs.

RESULTS MATRIX
General Development Objectives

RESULTS MATRIX

Specific Development Objectives

Specific Development Objectives Nbr. 1: Resultado 1. Aumento do valor das propriedades imobiliárias na ON

Observation:

Indicator		Unit of Measure	Baseline	Baseline Year		2024	EOP 2024
1.0	Valor médio dos imóveis em na ON	R\$/m2	2020	2018	P	2,890	2,890
					A	-	-

Details

Means of Verification: Informes de Progreso

Observations:

Evaluation Methodology: -

Pro-Gender	No	Pro-Ethnicity	No	CRF indicator			

Specific Development Objectives Nbr. 2: Resultado 2. Ampliação da cobertura vegetal no MV

Observation:

Indicator		Unit of Measure	Baseline	Baseline Year		2024	EOP 2024
2.0	Área verde por habitante no Município de Vitória (MV)	R\$/m2	83.5	2017	P	84.8	84.8
					A	-	-

Details

Means of Verification: Informes de Progreso

Observations: Informes de progreso

Evaluation Methodology: -

Pro-Gender	No	Pro-Ethnicity	No	CRF indicator			

Specific Development Objectives Nbr. 3: Resultado 3. Agências governamentais fortalecidas

Observation:

Indicator		Unit of Measure	Baseline	Baseline Year		2024	EOP 2024
3.0	Órgãos governamentais que se beneficiam de projetos que fortalecem instrumentos tecnológicos e de gestão para melhorar a prestação de serviços públicos	unid	0	2017	P	5	5
					A	-	-

Details

Means of Verification: Informes de Progreso

Observations: Informes de progreso

Evaluation Methodology: -

Pro-Gender	No	Pro-Ethnicity	No	CRF indicator			

Specific Development Objectives Nbr. 4: Resultado 5. Redução de homicídios de jovens de 15 a 24 anos nas 5 regiões prioritárias da MV.

Observation:

Indicator		Unit of Measure	Baseline	Baseline Year		2024	EOP 2024
4.0	Redução de homicídios de jovens (homens e mulheres) de 15 a 24 anos nas 5 regiões prioritárias da MV.	tx homicio	134.5	2017	P	121.5	121.5
					A	-	-

Details

Means of Verification: Informes de Progreso

Observations: Informes de progreso

Evaluation Methodology: -

Pro-Gender	No	Pro-Ethnicity	No	CRF indicator	

	Indicator	Unit of Measure	Baseline	Baseline Year		2024	EOP 2024
4.2	Homicídios de mulheres nas 5 regiões prioritárias da MV	tx de roubo	12.3	2017	P	11	11
					A	-	-

Details

Means of Verification: Informes de Progreso

Observations: Informes de progreso

Evaluation Methodology: -

Pro-Gender	No	Pro-Ethnicity	No	CRF indicator	

	Indicator	Unit of Measure	Baseline	Baseline Year		2024	EOP 2024
4.3	Homicídios de jovens de 15 a 24 anos (homens e mulheres afrodescendentes) nas 5 regiões do MV	tx de roubo	120.4	2017	P	108	108
					A	-	-

Details

Means of Verification: Informes de Progreso

Observations: Informes de progreso

Evaluation Methodology: -

Pro-Gender	No	Pro-Ethnicity	No	CRF indicator	

RESULTS MATRIX

OUTPUTS: ANNUAL PHYSICAL AND FINANCIAL PROGRESS

Component Nbr. 1 Componente I. Desenvolvimento Urbano e Gestão Ambiental Sustentável

				PHYSICAL PROGRESS		FINANCIAL PROGRESS	
	Output	Unit of Measure		2021	EOP 2024	2021	EOP 2024
1.01	Orla Noroeste Requalificada- 1A	Hectares	P	-	31,800	3,700,000	14,735,000
			P (a)	-	31,800	-	16,100,000
			A	-	-	-	-
1.02	Orla Noroeste Requalificada- 1B	Hectares	P	-	72,600	-	15,400,000
			P (a)	-	72,600	-	14,035,000
			A	-	-	-	-
1.03	Ciclovía Tancredão – Praça dos Namorados Implantada	km	P	-	13	-	4,000,000
			P (a)	-	13	-	3,855,000
			A	-	-	-	-
1.04	Ligações Intradomiciliares de Esgoto Realizadas	Unidade	P	-	3,249	300,000	1,481,000
			P (a)	-	3,249	-	1,481,000
			A	-	-	-	-
1.05	Plantas de Parcelamento Aprovadas	Unidade	P	-	3	-	700,000
			P (a)	-	3	-	845,000
			A	-	-	-	-
1.06	Plano de Manejo da Área de Proteção Ambiental do Maciço Central Elaborado	Plano	P	1	1	200,000	200,000
			P (a)	-	1	-	200,000
			A	-	-	-	-

1.07	Áreas verdes restauradas	Hectares	P	-	88	456,000	2,280,000
			P (a)	-	88	-	2,280,000
			A	-	-	-	-
1.08	Fontes de Água Implantadas	Unidade	P	-	15	100,000	430,000
			P (a)	-	15	-	430,000
			A	-	-	-	-
1.09	Obras de contenção realizadas	Obra	P	-	60	950,000	4,705,000
			P (a)	-	60	-	4,705,000
			A	-	-	-	-
1.10	Plano Diretor de Mudanças Climáticas Elaborado	Plano	P	-	1	260,000	1,300,000
			P (a)	-	1	-	1,300,000
			A	-	-	-	-
1.11	Inventário Arborização Urbano atualizado	Inventário	P	-	1	-	500,000
			P (a)	-	1	-	500,000
			A	-	-	-	-
1.12	Servidores Capacitados	servidores	P	125	250	250,000	500,000
			P (a)	-	250	100,000	500,000
			A	-	50	-	-
1.13	Palácio Municipal reformado	Unidade	P	-	1	-	9,500,000
			P (a)	-	1	-	9,460,000
			A	-	-	-	-
1.14	Centro de Inteligência Municipal - CIM implantado	Centro	P	-	1	-	14,320,000
			P (a)	-	1	-	14,120,000
			A	-	-	-	-
1.15	Sistema de Alerta da Defesa Civil implantado	Unidade	P	-	1	-	1,600,000
			P (a)	-	1	-	1,600,000
			A	-	-	-	-
1.16	Plano Estratégico do Centro Histórico elaborado	Plano	P	-	1	-	700,000
			P (a)	-	1	-	700,000
			A	-	-	-	-
1.17	Plano Diretor de Mobilidade Urbana elaborado	Plano	P	-	1	325,000	1,300,000
			P (a)	-	1	-	1,300,000
			A	-	-	-	-
1.18	Estudos e Projetos realizados	Projeto	P	3	7	450,000	2,277,000
			P (a)	2	7	450,000	3,017,000
			A	-	1	-	-
1.19	Plano Urbanístico da Orla Noroeste	Plano	P	-	1	-	300,000
			P (a)	-	1	-	300,000
			A	-	-	-	-

Component Nbr. 2    Componente II. Segurança Cidadã

				PHYSICAL PROGRESS		FINANCIAL PROGRESS	
	Output	Unit of Measure		2021	EOP 2024	2021	EOP 2024
2.01	Equipamentos de Saúde implantados (construção ou reforma)	Unidade	P	-	4	1,460,000	7,780,000
			P (a)	-	4	460,000	8,076,000
			A	-	-	-	-
2.02	Escolas de Ensino Fundamental implantadas (construção ou reforma)	escola	P	-	4	2,600,000	12,050,000
			P (a)	-	4	-	12,050,000
			A	-	-	-	-
2.03	Equipamentos Públicos de Assistência Social implantados	Unidade	P	-	7	973,000	5,264,000
			P (a)	-	7	-	5,580,000
			A	-	-	-	-
2.04	Centros de Informática implantados para o Vix Lab	Centro	P	8	8	250,000	2,000,000
			P (a)	8	8	250,000	1,676,000
			A	-	-	-	-
2.05	Capacitações para Guarda Municipal realizada	cursos	P	3	9	51,600	172,000
			P (a)	4	9	51,600	172,000
			A	1	1	4,208.07	21,408.07
2.06	Base da Guarda Municipal Construída	Unidade	P	-	1	480,000	2,365,000
			P (a)	-	1	480,000	2,365,000
			A	-	-	-	-
2.07	Rede Integrada de Prevenção Social da Violência implantada	Unidade	P	1	1	500,000	500,000
			P (a)	1	1	500,000	500,000
			A	-	-	-	-
2.08	Atividades Culturais e Artísticas realizadas	Atividade	P	35	105	315,000	1,050,000
			P (a)	35	105	315,000	1,050,000
			A	33	33	183,037.61	183,037.61
2.09	Escolas atendidas por Educação em Direitos Humanos	Escolas	P	2	14	125,000	1,000,000
			P (a)	2	17	125,000	1,000,000
			A	17	17	14,364	14,364
2.10	Pessoas atendidas pelo Programa Qualifica VIX	Pessoas	P	2,500	15,000	250,000	1,000,000
			P (a)	2,500	15,000	250,000	1,000,000
			A	3,430	3,430	128,434.15	128,434.15
2.11	Escolinha de Educação Esportiva implantadas na regioao 1, 2, 3, 4 e 7	Escolinha	P	2	5	-	1,000,000
			P (a)	2	5	-	712,000
			A	-	-	-	-

Other Cost				
	Gestão do Projeto	P	3,430,500	14,091,000
		P (a)	1,430,500	14,091,000
		A	727,251.12	1,335,540.69
Total Cost				
	Total Cost	P	17,426,100	124,500,000
		P (a)	4,412,100	125,000,000
		A	1,057,294.95	1,682,784.52

CHANGES TO THE MATRIX

Section	Name	Type of Change	Sub type	Modified By	Entered in System
Output	Atividades Culturais e Artísticas realizadas	Modify Output	Modify Physical EOP P(a) value - caused by a change in the Physical P(a).	BCAMARANO	3/24/2022
	Capacitações para Guarda Municipal realizada	Modify Output	Modify Financial EOP P(a) value - caused by a change in the Financial P(a).	BCAMARANO	3/18/2022
			Modify Physical EOP P(a) value - caused by a change in the Physical P(a).	BCAMARANO	3/18/2022
	Centro de Inteligência Municipal - CIM implantado	Modify Output	Modify Financial EOP P(a) value - caused by a change in the Financial P(a).	BCAMARANO	3/18/2022
	Centros de Informática implantados para o Vix Lab	Modify Output	Modify Financial EOP P(a) value - caused by a change in the Financial P(a).	BCAMARANO	3/18/2022
	Ciclovía Tancredão – Praça dos Namorados Implantada	Modify Output	Modify Financial EOP P(a) value - caused by a change in the Financial P(a).	BCAMARANO	3/18/2022
	Equipamentos de Saúde implantados (construção ou reforma)	Modify Output	Modify Financial EOP P(a) value - caused by a change in the Financial P(a).	BCAMARANO	3/18/2022
	Equipamentos Públicos de Assistência Social implantados	Modify Output	Modify Financial EOP P(a) value - caused by a change in the Financial P(a).	BCAMARANO	3/18/2022
	Escolas atendidas por Educação em Direitos Humanos	Modify Output	Modify Physical EOP P(a) value - caused by a change in the Physical P(a).	BCAMARANO	3/18/2022
	Escolinha de Educação Esportiva implantadas na regioao 1, 2, 3, 4 e 7	Modify Output	Modify Financial EOP P(a) value - caused by a change in the Financial P(a).	BCAMARANO	3/18/2022
	Estudos e Projetos realizados	Modify Output	Modify Financial EOP P(a) value - caused by a change in the Financial P(a).	BCAMARANO	3/18/2022
			Modify Physical EOP P(a) value - caused by a change in the Physical P(a).	BCAMARANO	3/18/2022
	Orla Noroeste Requalificada- 1A	Modify Output	Modify Financial EOP P(a) value - caused by a change in the Financial P(a).	BCAMARANO	3/18/2022
	Orla Noroeste Requalificada- 1B	Modify Output	Modify Financial EOP P(a) value - caused by a change in the Financial P(a).	BCAMARANO	3/18/2022
	Palácio Municipal reformado	Modify Output	Modify Financial EOP P(a) value - caused by a change in the Financial P(a).	BCAMARANO	3/18/2022
	Plantas de Parcelamento Aprovadas	Modify Output	Modify Financial EOP P(a) value - caused by a change in the Financial P(a).	BCAMARANO	3/18/2022

RISKS AND PLANNED RESPONSES

Risk ID	Risk Status		Risk Taxonomy
2	Active		Institutional Environment
	Response Actions		
	2.1	Management Strategy	Status
		AVOID	ACTIVE

Risk ID	Risk Status		Risk Taxonomy
4	Inactive		Social Environment
	Response Actions		
	4.0	Management Strategy	Status
		-	

Risk ID	Risk Status		Risk Taxonomy
6	Materialized		Economic and Financial Environment
	Response Actions		
	6.0	Management Strategy	Status
		-	

Risk ID	Risk Status		Risk Taxonomy
8	Active		Economic and Financial Environment
	Response Actions		
	8.1	Management Strategy	Status
		AVOID	ACTIVE

Risk ID	Risk Status		Risk Taxonomy
10	Active		Economic and Financial Environment
	Response Actions		
	10.0	Management Strategy	Status
		-	



Risk ID	Risk Status		Risk Taxonomy
12	Active		Natural Environment
	Response Actions		
	12.1	Management Strategy	Status
		AVOID	ACTIVE

Risk ID	Risk Status		Risk Taxonomy
13	Active		Social Environment
	Response Actions		
	13.0	Management Strategy	Status
		-	

Risk ID	Risk Status		Risk Taxonomy
15	Active		Institutional Environment
	Response Actions		
	15.0	Management Strategy	Status
		-	

IMPLEMENTATION STATUS AND LEARNING

Lesson Learned - Categories
Project Management Capacity
Acquisitions and Procurement - Bidding Stage
