


PMR Public Report

Operation Number	GU-X1005	Chief of Operations Validation Date	04/05/22
Year- PMR Cycle	Second period Jan-Dec 2021	Division Chief Validation Date	04/07/22
Last Update	04/05/22	Country Representative Validation Date	05/05/22
PMR Validation Stage	Validated by Representative		
Basic Data			
Operation Profile			
Operation Name	Water and Sanitation Program for Human Development	Loan Number	GRT/WS-11905-GU
Executing Agency	SECRETARIA GENERAL DE LA PRESIDENCIA, INSTITUTO DE FOMENTO MUNICIPAL	Sector/Subsector	WATER AND SANITATION
Team Leader	GOBITZ, HUMBERTO A.	Overall Stage	Disbursing (From eligibility until all the Operations are closed)
Operation Type	Investment Grants	Country	Guatemala
Lending Instrument		Convergence related Operation(s)	GU-L1039
Borrower			
Environmental and Social Safeguards			
Impacts Category	B13	Was/Were the objective(s) of this operation reformulated?	NO
Safeguard Performance Rating	Partially Satisfactory	Date of approval	
Safeguard Performance Rating - Rationale	Se ha mejorado la gestión socioambiental, sin embargo, se mantiene el desempeño en PS debido a que no se ha completado la Gestión de derechos de paso, asunto que se mantiene desde la misión anterior y que por contrato debía estar finiquitado antes de iniciar las obras. Además, existen conflictos con la comunidad de San Pedro Sacatepéquez debido a quejas por la pavimentación de las calles después de finalizadas las obras. Está pendiente igualmente la entrega un informe de corta de árboles y compensación forestal, en especial clarificando el tipo de ecosistema natural que se está interviniendo en San Pedro Sacatepequez.		

Financial Data									
	Total Cost and Source					Available Funds (US\$)			
Operations	Original IDB	Current IDB	Local Counterpart	Co-Financing / Country	Total Original Cost	Current IDB	Disb. Amount to Date	% Disbursed	Undisbursed Amount
GU-L1039	50,000,000	50,000,000	0	0	50,000,000	50,000,000	43,800,000	87.60%	6,200,000
GU-X1005	50,000,000	50,000,000	0	0	50,000,000	50,000,000	39,200,000	78.40%	10,800,000
Aggregated	100,000,000	100,000,000	0	0	100,000,000	100,000,000	83,000,000	83.00%	17,000,000
Expense Categories by Loan Contract (cumulative values)									

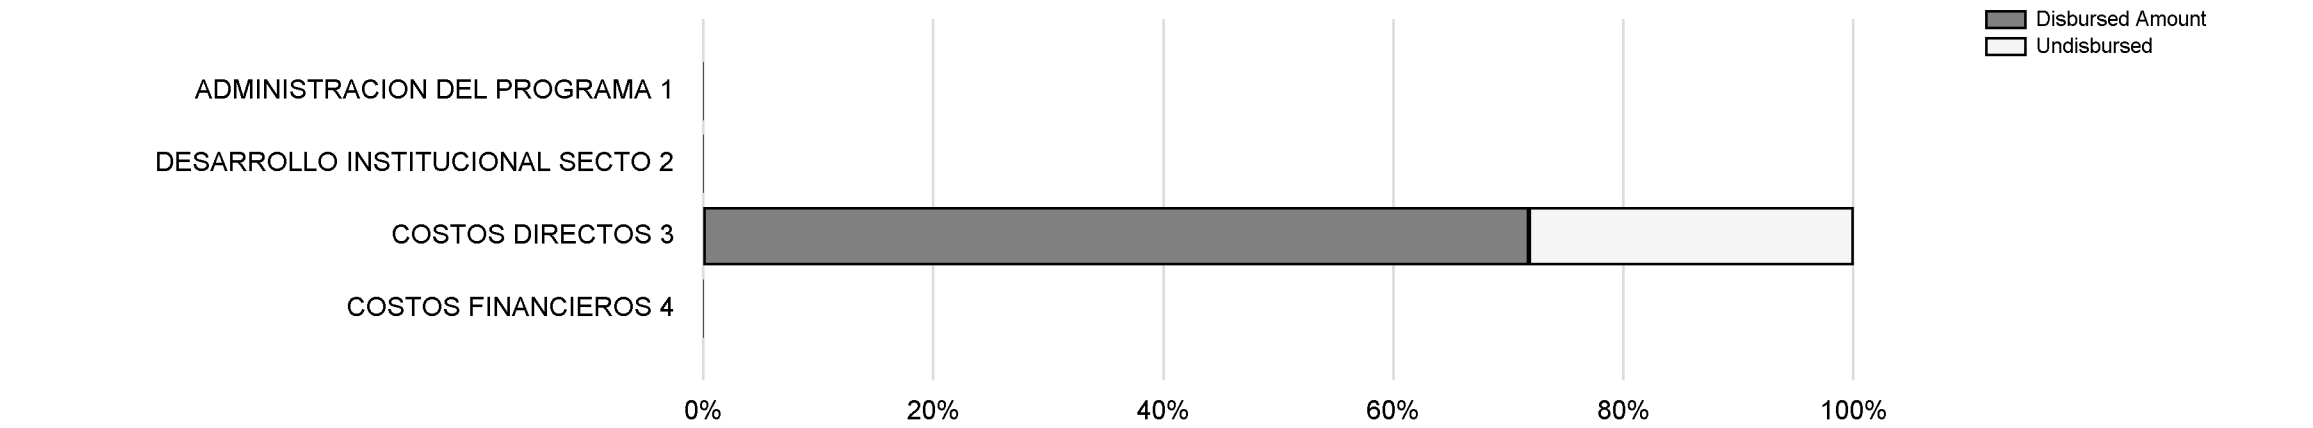

Please note that inactive indicators and outputs are not displayed; totals in the actual cost table may not match the sum of the cost of the outputs displayed, due to the cost of inactive outputs.

RESULTS MATRIX
General Development Objectives

RESULTS MATRIX

Specific Development Objectives

Specific Development Objectives Nbr. 1: Plan de Consolidación Institucional del Ministerio de Salud Publica y asistencia Social -MSPAS-, en temas de rectoría, regulación y planificación de prestación de servicios de agua potable y saneamiento implementada

Observation:

	Indicator	Unit of Measure	Baseline	Baseline Year		2013	2014	2015	2016	2017	2018	2019	2020	2021	2022	EOP 2023
1.1	Rectoria sectorial fortalecida y funcionando	Entidades	0	2012	P	-	-	-	-	1	-	-	-	-	-	1
					A	-	-	-	-	-	-	-	-	-	-	-

Details

Means of Verification: Documentos Legales del Ministerio de Salud creando la direccion de Direccion de agua potable y saneamiento, para ejercer la rectoria del sector.

Observations:

Evaluation Methodology: -

Pro-Gender	No	Pro-Ethnicity	No	CRF indicator	

Specific Development Objectives Nbr. 2: Unidad especializada en el desarrollo de Programas de agua potable y saneamiento instituida en el Gobierno Central

Observation:

	Indicator	Unit of Measure	Baseline	Baseline Year		2013	2014	2015	2016	2017	2018	2019	2020	2021	2022	EOP 2023
2.1	Entidad ejecutora de Programas sectoriales autonoma funcionando	Entidad	0	2012	P	-	-	-	-	1	-	-	-	-	-	1
					A	-	-	-	-	-	-	-	-	-	-	-

Details

Means of Verification: Informe de desempeño del Programa a los 5 años de la firma del contrato del contrato de préstamo o cuando se hayan alcanzado el 75 % de avance.

Observations:

Evaluation Methodology: -

Pro-Gender	No	Pro-Ethnicity	No	CRF indicator	

Specific Development Objectives Nbr. 3: Cobertura servicios de agua potable y saneamiento autosostenibles ,incrementada la República de Guatemala

Observation:

	Indicator	Unit of Measure	Baseline	Baseline Year		2013	2014	2015	2016	2017	2018	2019	2020	2021	2022	EOP 2023
3.1	Hogares rurales con sistema de agua potable contruidos o rehabilitados	# of households	0	2012	P	200	4,600	4,600	4,700	4,160	-	-	-	-	-	18,260
					A	42	745	789	-	1,311	3,206	1,595	-	4,092	-	7,688

Details

Means of Verification: Informes de SEGEPLAN, y de los entes rector y ejecutor del sector

Observations: En la matriz de resultado original, se habían expresado los resultados en forma de porcentaje y número de beneficiarios, por lo que se ha utilizado la ponderación de hogares en función de la tasa promedio definida por la Encuesta Nacional de Vivienda 2011

Evaluation Methodology: -

Pro-Gender	No	Pro-Ethnicity	No	CRF indicator	2.4.a Households with improved access to water (#) (C)

	Indicator	Unit of Measure	Baseline	Baseline Year		2013	2014	2015	2016	2017	2018	2019	2020	2021	2022	EOP 2023
3.1	Hogares periurbanos y urbanos con solución de agua potable contruidos o rehabilitados	# of households	0	2012	P	-	-	6,000	15,000	5,000	-	-	-	-	-	26,000
					A	-	-	-	-	-	-	982	-	815	-	982

Details

Means of Verification: Informes de SEGEPLAN, y de los entes rector y ejecutor del sector

Observations:

Evaluation Methodology: -

Pro-Gender	No	Pro-Ethnicity	No	CRF indicator	2.4.a Households with improved access to water (#) (C)
------------	----	---------------	----	---------------	--

RESULTS MATRIX

OUTPUTS: ANNUAL PHYSICAL AND FINANCIAL PROGRESS

Component Nbr. 1 Componente 1. Desarrollo Institucional del Sector

				PHYSICAL PROGRESS		FINANCIAL PROGRESS	
	Output	Unit of Measure		2021	EOP 2023	2021	EOP 2023
1.01	Entidad Rectora Sectorial de agua y saneamiento funcionando	Entidad	P	-	1	-	1,500,000
			P (a)	-	-	43,688	1,500,000
			A	-	-	-	-
1.02	Entidad ejecutora especializada del sector de agua y saneamiento funcionando	Entidad	P	-	1	-	1,500,000
			P (a)	-	-	-	1,127,664
			A	-	-	-	1,127,664
1.03	Entidad rectora de la calidad de agua para consumo humano fortalecida	Entidad	P	-	1	-	700,000
			P (a)	-	1	-	700,000
			A	-	-	-	-

Component Nbr. 2 Componente 2. Inversiones en Infraestructura

				PHYSICAL PROGRESS		FINANCIAL PROGRESS	
	Output	Unit of Measure		2021	EOP 2023	2021	EOP 2023
2.01	Sistemas de agua potable y/o saneamiento rurales diseñados	Sistemas	P	-	335	-	3,400,000
			P (a)	-	46	-	9,604
			A	-	46	-	9,604
2.02	Sistemas de agua potable y/o saneamiento diseñados en comunidades urbanos	Sistemas	P	-	32	-	3,000,000
			P (a)	-	17	-	886,085.03
			A	-	17	-	886,085.03
2.03	Sistemas rurales de agua potable contruidos o rehabilitados	Sistemas	P	-	220	-	34,908,000
			P (a)	3	59	1,445,326	21,437,717.92
			A	3	56	634,194	21,023,476.92
2.04	Sistemas rurales con solución de saneamiento básico construidos o rehabilitados	Sistemas	P	-	280	-	23,272,000
			P (a)	2	78	99,532	9,237,816.24
			A	2	76	84,944	8,961,656.24
2.05	Sistemas periurbanos y urbanos con solución de agua potable construídos o rehabilitados	Sistemas	P	-	32	-	13,272,000
			P (a)	3	9	8,967,018	22,242,657.16
			A	2	4	4,726,163	15,937,901.16
2.06	Sistemas periurbanos y urbanos con solución de alcantarillado construídos o rehabilitados	Sistemas	P	-	32	-	8,848,000
			P (a)	3	10	14,210,890	35,967,044.85
			A	2	5	9,817,919	26,319,132.85

Component Nbr. 3 Componente 3. Desarrollo Comunitario y fortalecimiento Municipal para la prestación de servicios de agua y saneamiento

				PHYSICAL PROGRESS		FINANCIAL PROGRESS	
	Output	Unit of Measure		2021	EOP 2023	2021	EOP 2023
3.01	Organizaciones comunitarias rurales sosteniendo los sistema de agua y saneamiento	Organización	P	-	280	-	4,000,000
			P (a)	2	116	55,851	1,134,946.55
			A	2	113	49,744	1,112,892.55
3.02	Personas de Comunidades Rurales capacitadas en educación sanitaria y ambiental	Personas	P	-	84,000	-	1,000,000
			P (a)	405	60,558	55,850	982,306.72
			A	405	60,508	50,702	961,261.72
3.03	Gobiernos municipales fortalecidos en prestación de servicios de agua potable y saneamiento	Government agencies (#)	P	-	32	-	1,500,000
			P (a)	3	9	64,115	287,369.65
			A	1	4	62,965	247,114.65
3.04	Personas de la municipalidad capacitadas	Personas	P	-	320	-	500,000
			P (a)	30	90	64,115	281,497.69
			A	10	40	62,680	240,957.69

Component Nbr. 4 Administración del programa

				FINANCIAL PROGRESS
	Output	Unit of Measure		EOP
4.00			P	-
			P (a)	-
			A	-

Other Cost				
	Administración del Programa	P		2,600,000
		P (a)	424,605	4,205,290.19
		A	449,956	3,887,389.49
Total Cost				
	Total Cost	P		100,000,000
		P (a)	25,430,990	100,000,000
		A	15,939,267	80,715,136.3

CHANGES TO THE MATRIX					
Section	Name	Type of Change	Sub type	Modified By	Entered in System
Output	Organizaciones comunitarias rurales sosteniendo los sistema de agua y saneamiento	Modify Output	Modify Physical EOP P(a) value - caused by a change in the Physical P(a).	ADELAA	3/19/2022
	Personas de Comunidades Rurales capacitadas en educación sanitaria y ambiental	Modify Output	Modify Financial EOP P(a) value - caused by a change in the Financial P(a).	ADELAA	3/19/2022
			Modify Physical EOP P(a) value - caused by a change in the Physical P(a).	ADELAA	3/19/2022
	Sistemas periurbanos y urbanos con solución de agua potable construídos o rehabilitados	Modify Output	Modify Financial EOP P(a) value - caused by a change in the Financial P(a).	ADELAA	3/19/2022
			Modify Physical EOP P(a) value - caused by a change in the Physical P(a).	ADELAA	3/21/2022
	Sistemas periurbanos y urbanos con solución de alcantarillado construídos o rehabilitados	Modify Output	Modify Financial EOP P(a) value - caused by a change in the Financial P(a).	ADELAA	3/19/2022
			Modify Physical EOP P(a) value - caused by a change in the Physical P(a).	ADELAA	3/21/2022
	Sistemas rurales con solución de saneamiento básico construidos o rehabilitados	Modify Output	Modify Financial EOP P(a) value - caused by a change in the Financial P(a).	ADELAA	3/19/2022
			Modify Physical EOP P(a) value - caused by a change in the Physical P(a).	ADELAA	3/15/2022
	Sistemas rurales de agua potable contruídos o rehabilitados	Modify Output	Modify Financial EOP P(a) value - caused by a change in the Financial P(a).	ADELAA	3/19/2022
			Modify Physical EOP P(a) value - caused by a change in the Physical P(a).	ADELAA	3/15/2022

RISKS AND PLANNED RESPONSES

Risk ID	Risk Status		Risk Taxonomy
1	Active		Planning
	Response Actions		
	1.1	Management Strategy	Status
		MITIGATE	COMPLETE

Risk ID	Risk Status		Risk Taxonomy		
4	Active		Natural Environment		
	Response Actions				
	4.1	Management Strategy		Status	
		TRANSFER		ACTIVE	

Risk ID	Risk Status		Risk Taxonomy
6	Active		Institutional Environment
	Response Actions		
	6.1	Management Strategy	Status
		TRANSFER	ACTIVE

Risk ID	Risk Status		Risk Taxonomy		
8	Active		Institutional Environment		
	Response Actions				
	8.1	Management Strategy		Status	
		TRANSFER		ACTIVE	

IMPLEMENTATION STATUS AND LEARNING

Lesson Learned - Categories
Project Design
