


PMR Public Report

Operation Number	BO-L1067	Chief of Operations Validation Date	10/14/22
Year- PMR Cycle	First period Jan-Jun 2022	Division Chief Validation Date	
Last Update	09/30/22	Country Representative Validation Date	
PMR Validation Stage	Validated by Chief of Operations		
Basic Data			
Operation Profile			
Operation Name	Strengthening of Integrated Health Networks in the Department of Potosi	Loan Number	2614/BL-BO, 2614/BL-BO-1, 2614/BL-BO-2
Executing Agency	MINISTERIO DE PREVISION SOCIAL Y SALUD PUBLICA	Sector/Subsector	HEALTH-HEALTH SERVICES
Team Leader	BUSCARONS CUESTA, LUIS	Overall Stage	Fully Disbursed
Operation Type	Loan Operation	Country	Bolivia
Lending Instrument	Investment Loan	Convergence related Operation(s)	
Borrower	REPUBLICA DE BOLIVIA		
Environmental and Social Safeguards			
Impacts Category	B	Was/Were the objective(s) of this operation reformulated?	NO
Safeguard Performance Rating	Partially Unsatisfactory	Date of approval	
Safeguard Performance Rating - Rationale	Debido a incumplimientos en acuerdos previos para el área de construcción del hospital, licencias ambientales (LASP). Se construyó el hospital de Llallagua en territorio indígena se establecieron acuerdos con el ayllu Chullpa y se acordaron medidas de compensación específicas que no se han cumplido, se desarrolló un plan de acción correctiva por primera vez en 2016, el cual no fue cumplido. La misión de supervisión del año 2021 mostró avances en estas áreas identificadas, pero que todavía no son suficientes para dar por cumplidos los compromisos. El equipo BID ha realizado un esfuerzo conjunto con la agencia ejecutora y se han contratado consultores externos para que puedan colaborar con el cumplimiento de los pendientes. Al haberse evidenciado que existe acciones concretas con responsables y tiempos definidos para la verificación de los compromisos, además de evidencia inicial de cumplimiento, el desempeño de esta última misión es de Parcialmente Insatisfactorio.		

Financial Data									
	Total Cost and Source					Available Funds (US\$)			
Operations	Original IDB	Current IDB	Local Counterpart	Co-Financing / Country	Total Original Cost	Current IDB	Disb. Amount to Date	% Disbursed	Undisbursed Amount
BO-L1067	35,000,000	35,000,000	7,270,000	0	42,270,000	35,000,000	35,000,000	100.00%	-
Aggregated	35,000,000	35,000,000	7,270,000	0	42,270,000	35,000,000	35,000,000	0.00%	-
Expense Categories by Loan Contract (cumulative values)									

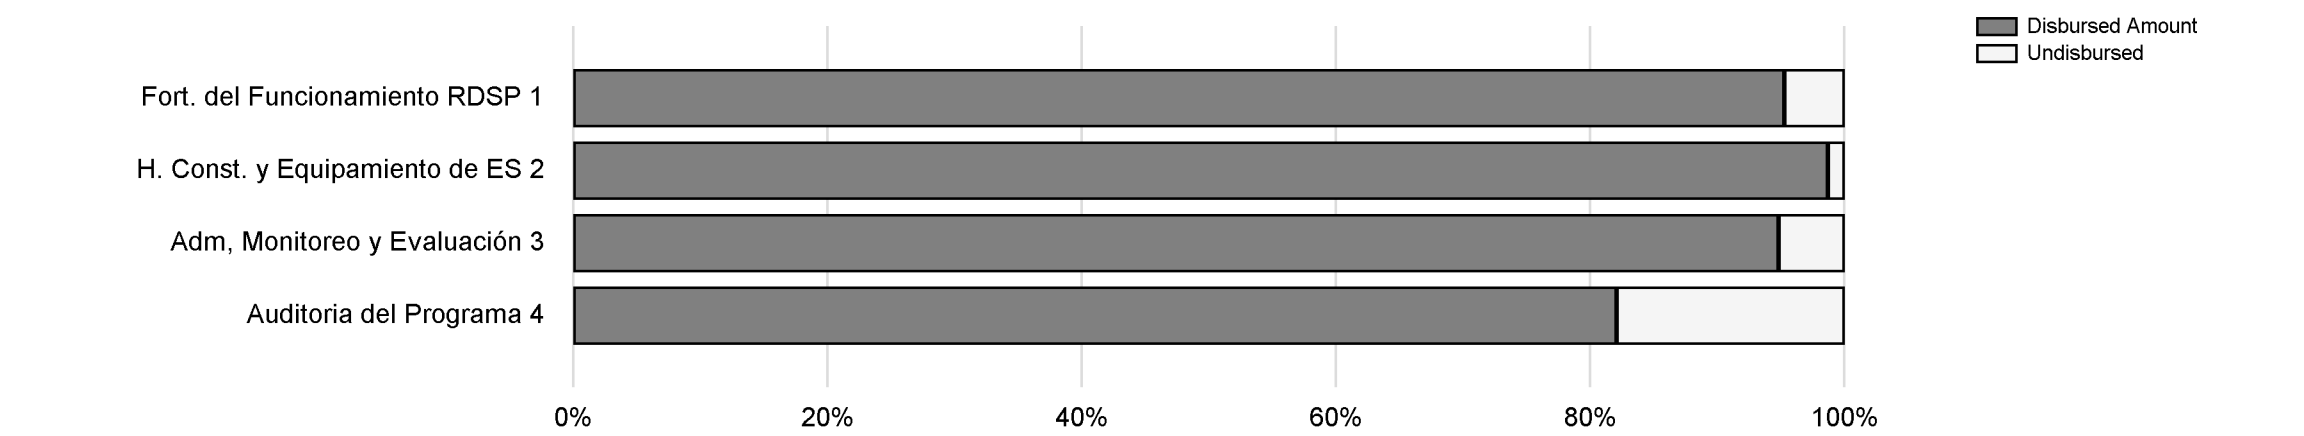

Please note that inactive indicators and outputs are not displayed; totals in the actual cost table may not match the sum of the cost of the outputs displayed, due to the cost of inactive outputs.

RESULTS MATRIX

General Development Objectives

General Development Objectives Nbr. 1: Mortalidad materno infantil en el Departamento de Potosi reducida

Observation:

Indicator		Unit of Measure	Baseline	Baseline Year	Expected Year of Achievement	EOP 2023	
1.1	Tasa de mortalidad infantil por 1000 NV	por 1000 NV	50	2003	2017	P	30
						A	-

Details

Means of Verification: Encuesta Nacional de Demografia y Salud

Observations:

The General Development Objective indicator target is expected to be observed by the operation's "Fully Justified" date in Convergence (CO): No

Pro-Gender	No	Pro-Ethnicity	No	CRF indicator					
Indicator				Unit of Measure	Baseline	Baseline Year	Expected Year of Achievement	EOP 2023	
1.2	Razon de Mortalidad materna en el Departamento de Potosi			Razon	310	2008	2017	P	100
								A	-
Details									

Means of Verification: Encuesta Nacional de Demografia y Salud

Observations: Existe discrepancias entre las cifras de fuentes nacionales (Ministerio de Salud) e internacionales (OMS/OPS) para este indicador, siendo los internacionales en el rango de 350 - 400 para Potosí. Adicionalmente, es probable que en los primeros años de ejecución, se registrarán más muertes por mejoras en el registro.(2015, esta por publicarse un estudio específico sobre mortalidad materna a partir del levantamiento de información en puestos "Centinela")

The General Development Objective indicator target is expected to be observed by the operation's "Fully Justified" date in Convergence (CO): No

Pro-Gender	Yes	Pro-Ethnicity	No	CRF indicator	Maternal mortality ratio (number of maternal deaths per 100,000 live births) ()				
Indicator				Unit of Measure	Baseline	Baseline Year	Expected Year of Achievement	EOP 2023	
1.3	Tasa de Mortalidad neonatal			por 1000 NV	27	2003	2017	P	-
								A	-
Details									

Means of Verification: Encuesta Nacional de Demografia y Salud

Observations:

The General Development Objective indicator target is expected to be observed by the operation's "Fully Justified" date in Convergence (CO): No

Pro-Gender	No	Pro-Ethnicity	No	CRF indicator			

RESULTS MATRIX															
Specific Development Objectives															
Specific Development Objectives Nbr. 1: Acceso a servicios de salud de calidad en el Departamento de Potosi mejorado															
Observation:															
	Indicator	Unit of Measure	Baseline	Baseline Year		2013	2014	2015	2016	2017	2018	2020	2021	2022	EOP 2023
1.1	Cobertura de Parto Institucional	Porcentaje	36	2010	P	-	-	-	-	-	-	-	-	-	55
					A	-	-	-	-	50	64.4	-	-	-	-
Details															
Means of Verification: SNIS Departamental (Potosi)															
Observations:															
Evaluation Methodology: -															
Pro-Gender	Yes	Pro-Ethnicity	No	CRF indicator											
	Indicator	Unit of Measure	Baseline	Baseline Year		2013	2014	2015	2016	2017	2018	2020	2021	2022	EOP 2023
1.2	Mujeres con complicación obstétrica atendidas en Hospital	Porcentaje	56	2010	P	-	-	-	-	-	-	-	-	-	80
					A	-	-	-	-	-	20.1	-	-	-	-
Details															
Means of Verification: Registros hospitalarios															
Observations: El proyecto deberá establecer un sistema de monitoreo específico para este indicador.															
Evaluation Methodology: -															
Pro-Gender	Yes	Pro-Ethnicity	No	CRF indicator											
	Indicator	Unit of Measure	Baseline	Baseline Year		2013	2014	2015	2016	2017	2018	2020	2021	2022	EOP 2023
1.3	Disponibilidad de mantenimiento de equipos médicos y no médicos por nivel de establecimientos de salud	Porcentaje	10	2011	P	-	-	-	-	-	-	-	-	-	50
					A	-	-	-	-	-	-	-	-	-	-
Details															
Means of Verification: Informes específicos del proyecto.															
Observations:															
Evaluation Methodology: -															
Pro-Gender	No	Pro-Ethnicity	No	CRF indicator											
	Indicator	Unit of Measure	Baseline	Baseline Year		2013	2014	2015	2016	2017	2018	2020	2021	2022	EOP 2023
1.4	Establecimientos de Salud que cumplan con las normas de caracterización del Ministerio de Salud y Deportes en cuanto a infraestructura, equipo y Recursos Humanos	Número	0	2011	P	-	-	-	-	-	-	-	-	-	200
					A	-	-	-	-	-	13	-	-	-	-
Details															
Means of Verification: Informes de Servicio Departamental de Salud, al final del proyecto se puede verificar con el Estudio de Brechas															
Observations:															
Evaluation Methodology: -															
Pro-Gender	No	Pro-Ethnicity	No	CRF indicator											

1.5	Recursos Humanos con capacitación CONE por tipo de establecimiento de salud	Personas	50	2011	P	-	-	-	-	-	-	-	-	-	200
					A	-	-	-	-	-	-	-	-	-	
Details															
Means of Verification: Informe específico del proyecto.															
Observations:															
Evaluation Methodology: -															
Pro-Gender	No	Pro-Ethnicity	No	CRF indicator											
IndicatorUnit of MeasureBaselineBaseline Year201320142015201620172018202020212022EOP 2023															
1.6	Personas Atendidas por un paquete básico de servicios de salud, que incluye parto institucional (madre y niño)	# of beneficiaries	1902	2013	P	-	500	1,000	1,500	2,000	-	-	-	-	5,000
					A	-	-	-	-	-	20,271	-	-	-	-
Details															
Means of Verification: Registro del Bono Juana Azurduy															
Observations: Se considerará al binomio Madre - Hijo que ha recibido atención al parto y atención post-parto															
Evaluation Methodology: -															
Pro-Gender	No	Pro-Ethnicity	No	CRF indicator	2.2 Beneficiaries receiving health services (#) (C)										
Disaggregation			Indigenous				P	-	-	-	-	-	-	-	-
							A	-	-	-	-	-	20,271	-	-

RESULTS MATRIX

OUTPUTS: ANNUAL PHYSICAL AND FINANCIAL PROGRESS

Component Nbr. 1 Fortalecimiento de la Red Departamental de Potosi

				PHYSICAL PROGRESS		FINANCIAL PROGRESS	
	Output	Unit of Measure		2022	EOP 2023	2022	EOP 2023
1.01	Diagnosticos del sector salud realizados.	estudio	P	-	3	-	100,000
			P (a)	-	3	-	128,305.14
			A	-	3	-	128,305.14
1.02	Plan de promoción de salud implementado	Plan	P	-	1	-	1,018,000
			P (a)	-	10	-	349,178.79
			A	-	10	-	349,178.79
1.03	Obstetricas incorporadas al sistema de salud	Personas	P	-	30	-	210,000
			P (a)	-	30	-	535,612
			A	-	30	-	535,612
1.04	Personal de los centros de primer nivel capacitado	Personas	P	-	200	-	200,000
			P (a)	-	306	-	177,071.15
			A	-	306	-	177,071.15
1.05	Sistema de Comunicación de referencias y urgencias implementado	Sistema	P	-	1	-	500,000
			P (a)	-	1	-	1,460,202.77
			A	-	1	-	1,460,202.77
1.06	Protocolo de referencia y retorno elaborado y/o adecuado	Documento	P	-	1	-	75,000
			P (a)	-	1	-	5,002.48
			A	-	1	-	5,002.48
1.07	Unidad de transporte para referencias y urgencias incorporada	Unidad	P	-	1	-	450,000
			P (a)	-	1	-	311,867
			A	-	1	-	311,867
1.08	Estrategia de Gestión Institucional de la Red Departamental implementada	Estrategia	P	-	1	-	1,314,000
			P (a)	-	1	-	1,492,807.36
			A	-	1	-	1,492,807.36
1.09	Personas capacitadas en mantenimiento de equipo médico-industrial, gestión financiera-administrativa y/o gestión de infraestructura y personal	Personas	P	-	90	-	280,000
			P (a)	-	125	-	327,504.02
			A	-	125	-	327,504.02
1.10	Sistema de Gestión de Medicamentos implementado	Sistema	P	-	1	-	68,000
			P (a)	-	1	-	37,494.76
			A	-	1	-	37,494.76

Component Nbr. 2 Inversiones en infraestructura y equipamiento

				PHYSICAL PROGRESS		FINANCIAL PROGRESS	
	Output	Unit of Measure		2022	EOP 2023	2022	EOP 2023
2.01	Hospital "Madre Obrera" de Llalagua diseñado	Hospital	P	-	1	-	310,000
			P (a)	-	1	-	452,429.71
			A	-	1	-	452,429.71
2.02	Hospital "Madre Obrera" de Llalagua construido	Hospital	P	-	1	-	6,730,000
			P (a)	-	1	18,317.79	13,005,021.27
			A	-	1	571.97	12,987,275.45
2.03	Capacidad del Hospital "Madre Obrera" de Llalagua ampliada	Hospital	P	-	-	-	-
			P (a)	-	1	149,488.08	149,488.08
			A	-	1	-	-
2.04	Hospital "Madre Obrera" de Llalagua equipado	Hospital	P	-	1	-	2,106,000
			P (a)	-	1	-	1,224,358.26
			A	-	1	-	1,224,358.26
2.05	Hospital Ocuri construido	Hospital	P	-	1	-	4,200,000
			P (a)	-	1	284,745.5	6,402,715.52
			A	-	1	176,392.71	6,294,362.73
2.06	Capacidad del Hospital de Ocurí ampliada	Hospital	P	-	-	-	-
			P (a)	-	1	522,334.55	522,334.55
			A	-	1	-	-
2.07	Hospital de Ocurí equipado	Hospital	P	-	1	-	1,180,000
			P (a)	-	1	-	516,210.22
			A	-	1	-	516,210.22
2.08	Hospitales de Ocurí y Llalagua operando	Hospital	P	-	2	-	4,220,000
			P (a)	-	2	482,103.19	4,220,000.01
			A	-	-	2,652.41	58,990.41
2.09	Centro de coordinación de urgencias construido	Centro	P	-	1	-	450,000
			P (a)	-	1	-	1,049,893.47
			A	-	1	-	1,049,893.47
2.10	Establecimientos de salud ampliados y/o remodelados	Establecimiento	P	-	1	-	2,800,000
			P (a)	-	7	-	2,732,912.87
			A	-	7	-	2,732,912.87
2.11	Establecimientos de salud construidos	Establecimiento	P	-	2	-	1,800,000
			P (a)	-	2	-	1,942,152.62
			A	-	2	-	1,942,152.62
2.12	Establecimientos de salud equipados	Establecimiento	P	-	8	-	8,549,185
			P (a)	-	11	-	2,030,175.9
			A	-	11	-	2,030,175.9

Other Cost				
	Administración y/o fortalecimiento institucional MSD y SEDES	P		740,000
		P (a)	23,076.25	1,532,246.25
		A	0	1,509,170
	Auditorías	P		200,000
		P (a)	10,213.97	265,392.22

	Auditorías	A	10,213.97	235,606.19
	Imprevistos	P		995,000
		P (a)	0	0
		A	0	0
	Monitoreo y evaluación	P		1,100,000
		P (a)	20,000	137,316.06
		A	0	117,316.06
	Administración y/o fortalecimiento institucional FPS	P		2,674,815
		P (a)	0	1,865,140.19
		A	0	1,865,140.19
Total Cost				
	Total Cost	P	0	42,270,000
		P (a)	1,510,279.33	42,872,832.67
		A	189,831.06	37,841,039.55

CHANGES TO THE MATRIX					
Section	Name	Type of Change	Sub type	Modified By	Entered in System
Output	Capacidad del Hospital "Madre Obrera" de Llalagua ampliada	Modify Output	Modify Physical EOP P(a) value - caused by a change in the Physical P(a).	ACONDE	9/29/2022
	Capacidad del Hospital de Ocurí ampliada	Modify Output	Modify Physical EOP P(a) value - caused by a change in the Physical P(a).	ACONDE	9/29/2022
	Personas capacitadas en mantenimiento de equipo médico-industrial, gestión financiera-administrativa y/o gestión de infraestructura y personal	Modify Output	Modify Physical EOP P(a) value - caused by a change in the Physical P(a).	ACONDE	9/29/2022
	Plan de promoción de salud implementado	Modify Output	Modify Physical EOP P(a) value - caused by a change in the Physical P(a).	ACONDE	9/29/2022

RISKS AND PLANNED RESPONSES

Risk ID	Risk Status		Risk Taxonomy	
3	Inactive		Planning	
	Response Actions			
	3.1	Management Strategy	Status	
		-		
	3.2	Management Strategy	Status	
		-		
	3.3	Management Strategy	Status	
		-		

Risk ID	Risk Status		Risk Taxonomy		
6	Inactive		Fiduciary		
	Response Actions				
	6.1	Management Strategy		Status	
		-			
	6.2	Management Strategy		Status	
		-			
	6.3	Management Strategy		Status	
		-			

Risk ID	Risk Status		Risk Taxonomy
9	Mitigated		Planning
	Response Actions		
	9.1	Management Strategy	Status
		-	
	9.2	Management Strategy	Status
		-	
	9.3	Management Strategy	Status
		-	
	9.4	Management Strategy	Status
		-	

Risk ID	Risk Status		Risk Taxonomy
12	Mitigated		Sustainability
	Response Actions		
	12.1	Management Strategy	Status
		-	
	12.2	Management Strategy	Status
		-	
	12.3	Management Strategy	Status
		-	
	12.4	Management Strategy	Status
		-	

Risk ID	Risk Status		Risk Taxonomy
15	Mitigated		Economic and Financial Environment
	Response Actions		
	15.1	Management Strategy	Status
		-	
	15.2	Management Strategy	Status
		-	
	15.3	Management Strategy	Status
		-	
	15.4	Management Strategy	Status
		-	

Risk ID	Risk Status		Risk Taxonomy
18	Inactive		Sustainability
	Response Actions		
	18.1	Management Strategy	Status
		-	
	18.2	Management Strategy	Status
		-	
	18.3	Management Strategy	Status
		-	
	18.4	Management Strategy	Status
		-	
	18.5	Management Strategy	Status
		-	
	18.6	Management Strategy	Status
		-	

Risk ID	Risk Status		Risk Taxonomy		
21	Mitigated		Environmental and Social Sustainability		
	Response Actions				
	21.1	Management Strategy		Status	
		-			
	21.2	Management Strategy		Status	
		-			

Risk ID	Risk Status		Risk Taxonomy
24	Mitigated		Natural Environment
	Response Actions		
	24.0	Management Strategy	Status
		-	

Risk ID	Risk Status		Risk Taxonomy
27	Inactive		Human Resources
	Response Actions		
	27.1	Management Strategy	Status
		-	

Risk ID	Risk Status		Risk Taxonomy
29	Inactive		Economic and Financial Environment
	Response Actions		
	29.0	Management Strategy	Status
		-	

IMPLEMENTATION STATUS AND LEARNING

Lesson Learned - Categories
Intra/Inter Coordination
