


PMR Public Report

Operation Number	BR-L1497	Chief of Operations Validation Date	10/18/22
Year- PMR Cycle	First period Jan-Jun 2022	Division Chief Validation Date	
Last Update	09/30/22	Country Representative Validation Date	
PMR Validation Stage	Validated by Chief of Operations		

Basic Data			
Operation Profile			
Operation Name	Vitória Urban Improvement and Citizen Security Program (First Stage of the Sustainable Vitória Action Plan)	Loan Number	4617/OC-BR
Executing Agency	SECRETARIA ESPECIAL DE ESTADO DE GESTAO-SEGES	Sector/Subsector	URBAN DEVELOPMENT AND HOUSING-URBAN LAND PLANNING AND MANAGEMENT
Team Leader	SILVA HERREROS, JORGE ALEJANDRO	Overall Stage	Disbursing (From eligibility until all the Operations are closed)
Operation Type	Loan Operation	Country	Brazil
Lending Instrument	Investment Loan	Convergence related Operation(s)	
Borrower	MUNICIPIO DE VITÓRIA - ES		
Environmental and Social Safeguards			
Impacts Category	B	Was/Were the objective(s) of this operation reformulated?	NO
Safeguard Performance Rating	Satisfactory	Date of approval	
Safeguard Performance Rating - Rationale	A missão foi considerada satisfatória, a Agência Executora demonstrou que se reestruturou de forma adequada, possui os profissionais técnicos requeridos; o TDR do PGAS para o Programa está em fase de licitação e possui previsão de contratação para o início do primeiro trimestre de 2022; os estudos ambientais estão sendo desenvolvidos por equipe própria; as obras da Orla Noroeste possuem previsão de contratação para o segundo trimestre de 2022. O terreno indicado para a construção do Centro de Inteligência Municipal, que apresentava um passivo ambiental foi descartado e o Centro será implantado em prédio já existente.		

Financial Data									
	Total Cost and Source					Available Funds (US\$)			
Operations	Original IDB	Current IDB	Local Counterpart	Co-Financing / Country	Total Original Cost	Current IDB	Disb. Amount to Date	% Disbursed	Undisbursed Amount
BR-L1497	100,000,000	100,000,000	25,000,000	0	125,000,000	100,000,000	3,300,000	3.30%	96,700,000
Aggregated	100,000,000	100,000,000	25,000,000	0	125,000,000	100,000,000	3,300,000	3.30%	96,700,000

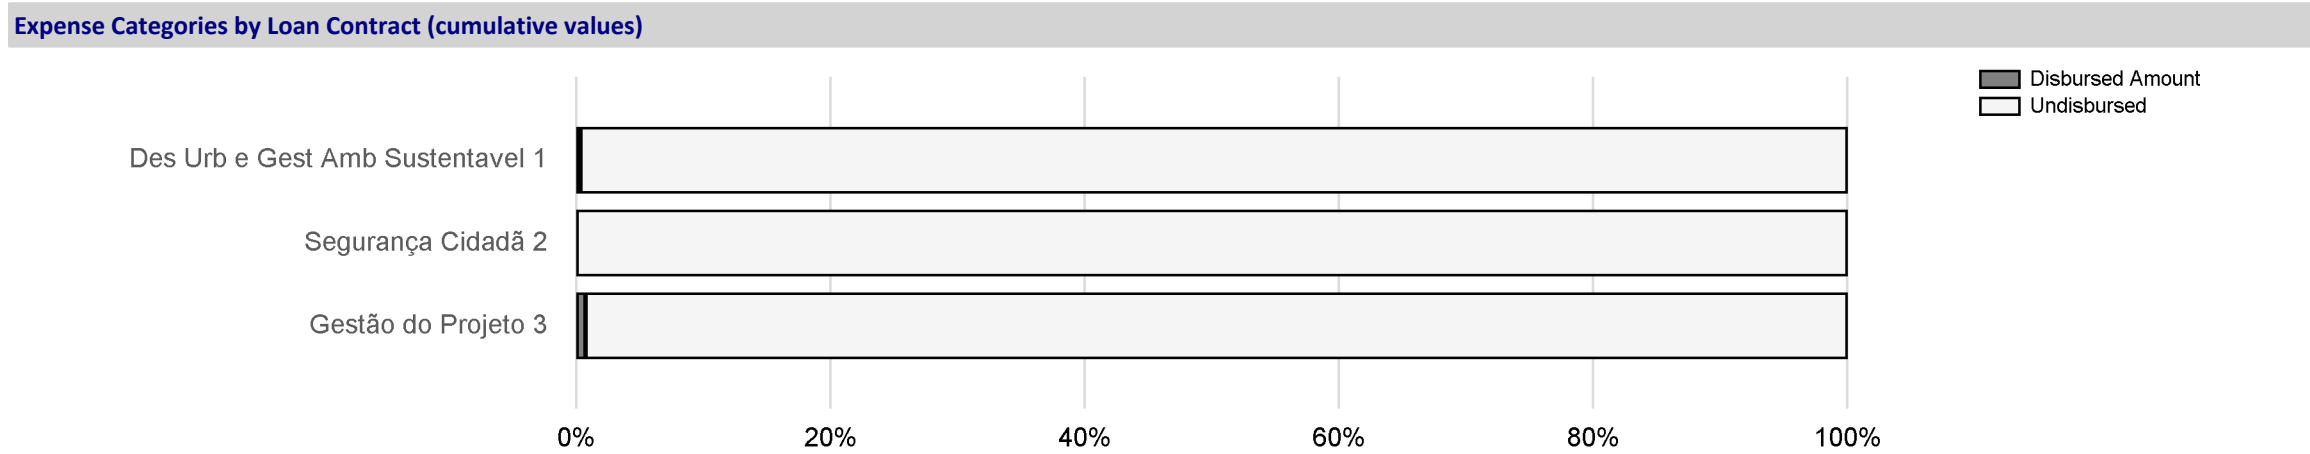

Please note that inactive indicators and outputs are not displayed; totals in the actual cost table may not match the sum of the cost of the outputs displayed, due to the cost of inactive outputs.

RESULTS MATRIX
General Development Objectives

RESULTS MATRIX

Specific Development Objectives

Specific Development Objectives Nbr. 1: Resultado 1. Aumento do valor das propriedades imobiliárias na ON

Observation:

	Indicator	Unit of Measure	Baseline	Baseline Year		2024	EOP 2024
1.0	Valor médio dos imóveis em na ON	R\$/m2	2020	2018	P	2,890	2,890
					A	-	-

Details

Means of Verification: Informes de Progreso

Observations:

Evaluation Methodology: -

Pro-Gender	No	Pro-Ethnicity	No	CRF indicator	

Specific Development Objectives Nbr. 2: Resultado 2. Ampliação da cobertura vegetal no MV

Observation:

	Indicator	Unit of Measure	Baseline	Baseline Year		2024	EOP 2024
2.0	Área verde por habitante no Município de Vitória (MV)	R\$/m2	83.5	2017	P	84.8	84.8
					A	-	-

Details

Means of Verification: Informes de Progreso

Observations: Informes de progreso

Evaluation Methodology: -

Pro-Gender	No	Pro-Ethnicity	No	CRF indicator	

Specific Development Objectives Nbr. 3: Resultado 3. Agências governamentais fortalecidas

Observation:

	Indicator	Unit of Measure	Baseline	Baseline Year		2024	EOP 2024
3.0	Órgãos governamentais que se beneficiam de projetos que fortalecem instrumentos tecnológicos e de gestão para melhorar a prestação de serviços públicos	unid	0	2017	P	5	5
					A	-	-

Details

Means of Verification: Informes de Progreso

Observations: Informes de progreso

Evaluation Methodology: -

Pro-Gender	No	Pro-Ethnicity	No	CRF indicator	

Specific Development Objectives Nbr. 4: Resultado 5. Redução de homicídios de jovens de 15 a 24 anos nas 5 regiões prioritárias da MV.

Observation:

	Indicator	Unit of Measure	Baseline	Baseline Year		2024	EOP 2024
4.0	Redução de homicídios de jovens (homens e mulheres) de 15 a 24 anos nas 5 regiões prioritárias da MV.	tx homicio	134.5	2017	P	121.5	121.5
					A	-	-

Details

Evaluation Methodology: -

Pro-Gender	No	Pro-Ethnicity	No	CRF indicator					
Indicator		Unit of Measure		Baseline	Baseline Year		2024	EOP 2024	
4.2	Homicídios de mulheres nas 5 regiões prioritárias da MV			tx de roubo	12.3	2017	P	11	11
							A	-	-
Details									

Means of Verification: Informes de Progreso

Observations: Informes de progreso

Evaluation Methodology: -

Pro-Gender	No	Pro-Ethnicity	No	CRF indicator				

Means of Verification: Informes de Progreso

Observations: Informes de progreso

Evaluation Methodology: -

Pro-Gender	No	Pro-Ethnicity	No	CRF indicator			

RESULTS MATRIX

OUTPUTS: ANNUAL PHYSICAL AND FINANCIAL PROGRESS

Component Nbr. 1 Componente I. Desenvolvimento Urbano e Gestão Ambiental Sustentável

				PHYSICAL PROGRESS		FINANCIAL PROGRESS	
	Output	Unit of Measure		2022	EOP 2024	2022	EOP 2024
1.01	Orla Noroeste Requalificada- 1A	Hectares	P	-	31,800	7,335,000	14,735,000
			P (a)	-	31,800	2,500,000	16,100,000
			A	-	-	-	-
1.02	Orla Noroeste Requalificada- 1B	Hectares	P	-	72,600	3,850,000	15,400,000
			P (a)	-	72,600	-	14,035,000
			A	-	-	-	-
1.03	Ciclovía Tancredão – Praça dos Namorados Implantada	km	P	-	13	2,000,000	4,000,000
			P (a)	-	13	-	3,855,000
			A	-	-	-	-
1.04	Ligações Intradomiciliares de Esgoto Realizadas	Unidade	P	-	3,249	440,000	1,481,000
			P (a)	-	3,249	-	1,481,000
			A	-	-	-	-
1.05	Plantas de Parcelamento Aprovadas	Unidade	P	1	3	175,000	700,000
			P (a)	-	3	80,000	845,000
			A	-	-	-	-
1.06	Plano de Manejo da Área de Proteção Ambiental do Maciço Central Elaborado	Plano	P	-	1	-	200,000
			P (a)	-	1	-	200,000
			A	-	-	-	-

1.07	Áreas verdes restauradas	Hectares	P	-	88	680,000	2,280,000
			P (a)	-	88	-	2,280,000
			A	-	-	-	-
1.08	Fontes de Água Implantadas	Unidade	P	-	15	230,000	430,000
			P (a)	-	15	50,000	430,000
			A	-	-	-	-
1.09	Obras de contenção realizadas	Obra	P	20	60	1,400,000	4,705,000
			P (a)	15	60	1,292,000	4,705,000
			A	4	4	405,554.84	405,554.84
1.10	Plano Diretor de Mudanças Climáticas Elaborado	Plano	P	-	1	390,000	1,300,000
			P (a)	-	1	-	1,300,000
			A	-	-	-	-
1.11	Inventário Arborização Urbano atualizado	Inventário	P	1	1	500,000	500,000
			P (a)	-	1	470,000	500,000
			A	-	-	43,667.68	43,667.68
1.12	Servidores Capacitados	servidores	P	-	250	-	500,000
			P (a)	20	250	50,000	500,000
			A	-	50	-	-
1.13	Palácio Municipal reformado	Unidade	P	-	1	2,375,000	9,500,000
			P (a)	-	1	-	9,460,000
			A	-	-	-	-
1.14	Centro de Inteligência Municipal - CIM implantado	Centro	P	-	1	2,800,000	14,320,000
			P (a)	-	1	-	14,120,000
			A	-	-	-	-
1.15	Sistema de Alerta da Defesa Civil implantado	Unidade	P	-	1	800,000	1,600,000
			P (a)	-	1	-	1,600,000
			A	-	-	-	-
1.16	Plano Estratégico do Centro Histórico elaborado	Plano	P	-	1	175,000	700,000
			P (a)	-	1	140,000	700,000
			A	-	-	-	-
1.17	Plano Diretor de Mobilidade Urbana elaborado	Plano	P	-	1	650,000	1,300,000
			P (a)	-	1	200,000	1,300,000
			A	-	-	-	-
1.18	Estudos e Projetos realizados	Projeto	P	-	7	680,000	2,277,000
			P (a)	3	7	1,100,000	3,017,000
			A	2	3	83,031.69	83,031.69
1.19	Plano Urbanístico da Orla Noroeste	Plano	P	1	1	300,000	300,000
			P (a)	-	1	-	300,000
			A	-	-	-	-

				PHYSICAL PROGRESS		FINANCIAL PROGRESS	
	Output	Unit of Measure		2022	EOP 2024	2022	EOP 2024
2.01	Equipamentos de Saúde implantados (construção ou reforma)	Unidade	P	-	4	2,190,000	7,780,000
			P (a)	-	4	-	8,076,000
			A	-	-	-	-
2.02	Escolas de Ensino Fundamental implantadas (construção ou reforma)	escola	P	-	4	3,050,000	12,050,000
			P (a)	-	4	500,000	12,050,000
			A	-	-	-	-
2.03	Equipamentos Públicos de Assistência Social implantados	Unidade	P	-	7	2,432,000	5,264,000
			P (a)	-	7	-	5,580,000
			A	-	-	-	-
2.04	Centros de Informática implantados para o Vix Lab	Centro	P	-	8	750,000	2,000,000
			P (a)	-	8	234,640	1,676,000
			A	-	-	-	-
2.05	Capacitações para Guarda Municipal realizada	cursos	P	4	9	68,800	172,000
			P (a)	-	9	-	172,000
			A	-	1	-	21,408.07
2.06	Base da Guarda Municipal Construída	Unidade	P	-	1	1,405,000	2,365,000
			P (a)	-	1	-	2,365,000
			A	-	-	-	-
2.07	Rede Integrada de Prevenção Social da Violência implantada	Unidade	P	-	1	-	500,000
			P (a)	-	1	-	500,000
			A	-	-	-	-
2.08	Atividades Culturais e Artísticas realizadas	Atividade	P	30	105	315,000	1,050,000
			P (a)	-	105	100,000	1,050,000
			A	-	33	8,077.49	191,115.1
2.09	Escolas atendidas por Educação em Direitos Humanos	Escolas	P	4	14	200,700	1,000,000
			P (a)	-	17	85,636	1,000,000
			A	-	17	-	14,364
2.10	Pessoas atendidas pelo Programa Qualifica VIX	Pessoas	P	5,000	15,000	250,000	1,000,000
			P (a)	1,700	15,000	100,000	1,000,000
			A	-	3,430	-	128,434.15
2.11	Escolinha de Educação Esportiva implantadas na regioao 1, 2, 3, 4 e 7	Escolinha	P	3	5	333,000	1,000,000
			P (a)	-	5	-	712,000
			A	-	-	-	-

Other Cost				
	Gestão do Projeto	P	3,430,500	14,091,000
		P (a)	1,500,000	14,091,000
		A	214,514.99	1,550,055.68
Total Cost				
	Total Cost	P	39,205,000	124,500,000
		P (a)	8,402,276	125,000,000
		A	754,846.69	2,437,631.21

CHANGES TO THE MATRIX					
Section	Name	Type of Change	Sub type	Modified By	Entered in System
Output	Base da Guarda Municipal Construída	Modify contribution to CRF Indicator	Flag contribution to CRF indicator	BCAMARANO	9/29/2022
	Equipamentos de Saúde implantados (construção ou reforma)	Modify contribution to CRF Indicator	Flag contribution to CRF indicator	BCAMARANO	9/29/2022
	Equipamentos Públicos de Assistência Social implantados	Modify contribution to CRF Indicator	Flag contribution to CRF indicator	BCAMARANO	9/29/2022
	Escolas de Ensino Fundamental implantadas (construção ou reforma)	Modify contribution to CRF Indicator	Flag contribution to CRF indicator	BCAMARANO	9/29/2022
	Fontes de Água Implantadas	Modify contribution to CRF Indicator	Flag contribution to CRF indicator	BCAMARANO	9/29/2022
	Ligações Intradomiciliares de Esgoto Realizadas	Modify contribution to CRF Indicator	Flag contribution to CRF indicator	BCAMARANO	9/29/2022
	Obras de contenção realizadas	Modify contribution to CRF Indicator	Flag contribution to CRF indicator	BCAMARANO	9/29/2022
	Plantas de Parcelamento Aprovadas	Modify contribution to CRF Indicator	Flag contribution to CRF indicator	BCAMARANO	9/29/2022

RISKS AND PLANNED RESPONSES

Risk ID	Risk Status		Risk Taxonomy
3	Active		Institutional Environment
	Response Actions		
	3.1	Management Strategy	Status
		AVOID	ACTIVE

Risk ID	Risk Status		Risk Taxonomy
6	Inactive		Social Environment
	Response Actions		
	6.0	Management Strategy	Status
		-	

Risk ID	Risk Status		Risk Taxonomy
9	Materialized		Economic and Financial Environment
	Response Actions		
	9.0	Management Strategy	Status
		-	

Risk ID	Risk Status		Risk Taxonomy
12	Active		Economic and Financial Environment
	Response Actions		
	12.1	Management Strategy	Status
		AVOID	ACTIVE

Risk ID	Risk Status		Risk Taxonomy
15	Active		Economic and Financial Environment
	Response Actions		
	15.0	Management Strategy	Status
		-	

Risk ID	Risk Status		Risk Taxonomy
18	Inactive		Natural Environment
	Response Actions		
	18.1	Management Strategy	Status
		AVOID	COMPLETE

Risk ID	Risk Status		Risk Taxonomy
21	Active		Social Environment
	Response Actions		
	21.0	Management Strategy	Status
		-	

Risk ID	Risk Status		Risk Taxonomy
24	Active		Institutional Environment
	Response Actions		
	24.0	Management Strategy	Status
		-	

IMPLEMENTATION STATUS AND LEARNING

Lesson Learned - Categories
Project Management Capacity
Intra/Inter Coordination
Project Design
