	Task Name	Duration	Start	Finish	Predece	Cost	2017	2018	2019	2020
0	[redacted]									
1	**Componente 2 Mejoramiento de la infraestructura de transporte urbano**	**797 days**	**Wed 5/10**	**Thu 5/28/20**		**$56,556,500.00**	**$0.00**	**$0.00**	**$0.00**	**$0.00**
2	**Otras Condiciones Componente 2**	**181 days**	**Wed 5/10**	**Wed 1/17/1**		**$0.00**	**$0.00**	**$0.00**	**$0.00**	**$0.00**
3	Aprobación reformulación	70 days	Wed 5/10	Tue 8/15/17		$0.00	$0.00	$0.00	$0.00	$0.00
4	Firma contrato modificatorio	45 days	Wed 8/16	Tue 10/17/1	3	$0.00	$0.00	$0.00	$0.00	$0.00
5	Firma convenio subsidiario	22 days	Wed 8/16	Thu 9/14/17	3	$0.00	$0.00	$0.00	$0.00	$0.00
6	Firma del Contrato Ejecución	22 days	Thu 6/15/	Fri 7/14/17	3SS+16	$0.00	$0.00	$0.00	$0.00	$0.00
7	Cumplimiento de condiciones previas	66 days	Wed 10/1	Wed 1/17/1	4	$0.00	$0.00	$0.00	$0.00	$0.00
8	2.1 Producto 4: Obras civiles, incluida infraestructura de estaciones a lo largo de la línea plateada concluidas	749 days	Mon 7/17	Thu 5/28/20		$25,658,551.62	$0.00	$0.00	$0.00	$0.00
9	**2.1.1 Entregable: Diseño de Línea completado**	**321 days**	**Mon 7/17**	**Mon 10/8/1**		**$5,608,247.14**	**$0.00**	**$0.00**	**$0.00**	**$0.00**
10	**Estudios Estación Faro Murillo completados**	44 days	Mon 7/17	Thu 9/14/17	6	$0.00	$0.00	$0.00	$0.00	$0.00
11	**ESTUDIOS BÁSICOS DE LÍNEA PLATEADA**	**66 days**	**Thu 1/18/**	**Thu 4/19/18**		**$434,782.61**	**$0.00**	**$0.00**	**$0.00**	**$0.00**
12	GEOTECNIA, HIDROLOGÍA Y RESISTIVIDAD LÍNEA PLATEADA	44 days	Thu 1/18/	Tue 3/20/18	6,7	$260,869.57	$0.00	$0.00	$0.00	$0.00
13	TOPOGRAFÍA LÍNEA PLATEADA	44 days	Thu 1/18/	Tue 3/20/18	12SS	$86,956.52	$0.00	$0.00	$0.00	$0.00
14	EDL I, EDL II LÍNEA PLATEADA	44 days	Thu 1/18/	Tue 3/20/18	13SS	$43,478.26	$0.00	$0.00	$0.00	$0.00
15	EDL III LÍNEA PLATEADA	22 days	Wed 3/21	Thu 4/19/18	14	$43,478.26	$0.00	$0.00	$0.00	$0.00
16	**RESTO DE ESTUDIOS BÁSICOS**	**110 days**	**Thu 1/18/**	**Wed 6/20/1**		**$1,413,043.48**	**$0.00**	**$0.00**	**$0.00**	**$0.00**
17	ESTUDIO DE EVALUACIÓN DE IMPACTO AMBIENTAL	22 days	Wed 3/21	Thu 4/19/18	15SS	$50,051.63	$0.00	$0.00	$0.00	$0.00
18	ESTUDIO DE MERCADO / DEMANDA	22 days	Wed 3/21	Thu 4/19/18	15SS	$50,051.63	$0.00	$0.00	$0.00	$0.00
19	ESTUDIO TÉCNICO DEL SISTEMA INTERMODAL	22 days	Fri 4/20/1	Mon 5/21/1	18	$47,107.41	$0.00	$0.00	$0.00	$0.00
20	ORGANIZACIÓN PARA LA IMPLEMENTACIÓN DEL PROYECTO	22 days	Mon 2/19	Tue 3/20/18	12SS+2	$47,107.41	$0.00	$0.00	$0.00	$0.00
21	EVALUACIÓN SOCIOECONÓMICA, FINANCIERA Y ANÁLISIS DE SENSIBILIDAD	22 days	Fri 4/20/1	Mon 5/21/1	19SS	$50,051.63	$0.00	$0.00	$0.00	$0.00
22	ESTUDIO DE IMPACTO VIAL	44 days	Thu 1/18/	Tue 3/20/18	12SS	$50,051.63	$0.00	$0.00	$0.00	$0.00
23	ENTREGA TESA ENTREGA N° 1	22 days	Wed 3/21	Thu 4/19/18	13	$559,311.07	$0.00	$0.00	$0.00	$0.00
24	ENTREGA TESA ENTREGA N° 2 (Revisión TESA)	22 days	Tue 5/22/	Wed 6/20/1	23FS+2	$559,311.07	$0.00	$0.00	$0.00	$0.00
25	**ESTUDIOS COMPLEMENTARIOS DE LÍNEA PLATEADA**	**100 days**	**Tue 5/22/**	**Mon 10/8/1**		**$108,695.65**	**$0.00**	**$0.00**	**$0.00**	**$0.00**
26	ESTUDIO DE AFECTACIONES LÍNEA PLATEADA	66 days	Tue 5/22/	Tue 8/21/18	17,18,1	$43,478.26	$0.00	$0.00	$0.00	$0.00
27	AVALÚOS LÍNEA PLATEADA	44 days	Wed 8/8/	Mon 10/8/1	26FS-10	$65,217.39	$0.00	$0.00	$0.00	$0.00
28	**PROYECTOS DE ARQUITECTURA L. Plateada**	**154 days**	**Thu 1/18/**	**Tue 8/21/18**		**$3,651,725.40**	**$0.00**	**$0.00**	**$0.00**	**$0.00**
29	Esqu. Funcionales Arquitectura Estacs. L. Plateada	**154 days**	**Thu 1/18/**	**Tue 8/21/18**		**$3,651,725.40**	**$0.00**	**$0.00**	**$0.00**	**$0.00**
30	Desarrollo Esqs. Funcionales Estaciones L. Plateada	22 days	Thu 1/18/	Fri 2/16/18	12SS	$93,612.16	$0.00	$0.00	$0.00	$0.00
31	Final Aprobaciones Esqs. Funcionales Ests. L. Plateada	22 days	Mon 2/19	Tue 3/20/18	30	$93,612.16	$0.00	$0.00	$0.00	$0.00
32	Proyectos de Estructura de Mástiles L. Plateada	22 days	Wed 3/21	Thu 4/19/18	31	$93,612.16	$0.00	$0.00	$0.00	$0.00
33	Desarrollo Proys. de Estructura de Mástiles Estacs. L. Plateada	22 days	Wed 3/21	Thu 4/19/18	32SS	$93,612.16	$0.00	$0.00	$0.00	$0.00
34	Final Aprobaciones Proys. de Estructura de Mástiles Estacs. L. Plateada	22 days	Wed 3/21	Thu 4/19/18	32SS	$97,867.26	$0.00	$0.00	$0.00	$0.00
35	Proyectos Básicos de Arquitectura Estacs. L. Plateada	22 days	Wed 3/21	Thu 4/19/18	32SS	$97,867.26	$0.00	$0.00	$0.00	$0.00
36	Desarrollo Proys. Básicos Arquitectura Estacs. L. Plateada	22 days	Wed 3/21	Thu 4/19/18	32SS	$102,122.36	$0.00	$0.00	$0.00	$0.00
37	Final Aprobaciones Proys. Básicos Arquitectura Estacs. L. Plateada	22 days	Wed 3/21	Thu 4/19/18	32SS	$108,505.01	$0.00	$0.00	$0.00	$0.00
38	Proyectos Básicos Trazado de Instalaciones Estacs. L. Plateada	22 days	Fri 4/20/1	Mon 5/21/1	37	$117,866.22	$0.00	$0.00	$0.00	$0.00
39	Desarrollo Proys. Básicos Trazado de Instalacs. Estacs. L. Plateada	22 days	Fri 4/20/1	Mon 5/21/1	38SS	$120,844.79	$0.00	$0.00	$0.00	$0.00
40	Final Aprobaciones Proys. Básicos Trazado de Instalacs. Estacs. L. Plateada	22 days	Fri 4/20/1	Mon 5/21/1	39SS	$89,782.58	$0.00	$0.00	$0.00	$0.00
41	Proyectos de Estructuras Estacs. L. Plateada	22 days	Fri 4/20/1	Mon 5/21/1	40SS	$113,185.62	$0.00	$0.00	$0.00	$0.00
42	Desarrollo Proys. de Estructuras Estacs. L. Plateada	22 days	Fri 4/20/1	Mon 5/21/1	41SS	$160,417.21	$0.00	$0.00	$0.00	$0.00
43	Final Aprobaciones Proys. de Estructuras Estacs. L. Plateada	22 days	Fri 4/20/1	Mon 5/21/1	42SS	$92,761.14	$0.00	$0.00	$0.00	$0.00
44	Proyectos de Ingeniería Detalle de Arquitectura Estacs. L. Plateada	22 days	Tue 5/22/	Wed 6/20/1	43	$97,867.26	$0.00	$0.00	$0.00	$0.00
45	Desarrollo Proyectos Ing. Detalle Arquitectura Estacs. L. Plateada	22 days	Tue 5/22/	Wed 6/20/1	44SS	$89,357.07	$0.00	$0.00	$0.00	$0.00
46	Final Aprobaciones Proys. Ing. Detalle Arqu. Estacs. L. Plateada	22 days	Tue 5/22/	Wed 6/20/1	45SS	$97,867.26	$0.00	$0.00	$0.00	$0.00
47	Proyectos Ingeniería Detalle Instalaciones Básicas Estacs. L. Plateada	22 days	Tue 5/22/	Wed 6/20/1	46SS	$97,867.26	$0.00	$0.00	$0.00	$0.00
48	Desarrollo Proys. Ing. Detalle Insts. Básicas Estacs. L. Plateada	22 days	Tue 5/22/	Wed 6/20/1	47SS	$99,143.79	$0.00	$0.00	$0.00	$0.00
49	Final Aprobaciones Proys. Ing. Detalle Insts. Básicas Estacs. L. Plateada	22 days	Tue 5/22/	Wed 6/20/1	48SS	$217,435.53	$0.00	$0.00	$0.00	$0.00
50	Proyectos Ingeniería Detalle Instalaciones Complementarias Estacs. L. Plateada	22 days	Thu 6/21/	Fri 7/20/18	49	$285,091.59	$0.00	$0.00	$0.00	$0.00
51	Desarrollo Proys. Ing. Detalle Insts. Compl. Estacs. L. Plateada	22 days	Thu 6/21/	Fri 7/20/18	50SS	$268,071.20	$0.00	$0.00	$0.00	$0.00
52	Final Aprobaciones Proys. Ing. Detalle Insts. Compl. Estacs. L. Plateada	22 days	Thu 6/21/	Fri 7/20/18	51SS	$184,671.27	$0.00	$0.00	$0.00	$0.00
53	Proyectos de Ingeniería de Detalle Exteriores Estacs. L. Plateada	22 days	Thu 6/21/	Fri 7/20/18	52SS	$184,671.27	$0.00	$0.00	$0.00	$0.00
54	Desarrollo Proyectos Ingeniería Detalle Ext. Estacs. L. Plateada	22 days	Thu 6/21/	Fri 7/20/18	53SS	$184,671.27	$0.00	$0.00	$0.00	$0.00
55	Final Aprobaciones Proys. Ing. Detalle Ext. Estacs. L. Plateada	22 days	Thu 6/21/	Fri 7/20/18	54SS	$184,671.27	$0.00	$0.00	$0.00	$0.00
56	PROYECTOS DE OBRAS COMPLEMENTARIAS L. Plateada	44 days	Thu 6/21/	Tue 8/21/18	55SS	$184,671.27	$0.00	$0.00	$0.00	$0.00
57	**2.1.2 Entregable: Obras Civiles Construcción Edificios LP concluidas**	**572 days**	**Wed 3/21**	**Thu 5/28/20**		**$17,623,766.32**	**$0.00**	**$0.00**	**$0.00**	**$0.00**
58	**Obras civiles Faro Murillo concluida**	**198 days**	**Wed 8/22**	**Fri 5/24/19**		**$1,055,005.41**	**$0.00**	**$0.00**	**$0.00**	**$0.00**
59	Obra Gruesa E-P2 (Faro Murillo)	88 days	Wed 8/22	Fri 12/21/18	56	$481,251.65	$0.00	$0.00	$0.00	$0.00
60	Final Obras Civiles e Instalaciones. Complementarias E-P2	22 days	Tue 3/26/	Wed 4/24/1	65SS-22	$92,502.14	$0.00	$0.00	$0.00	$0.00
61	Áreas Exteriores Edificio E-P2 (Faro Murillo)	22 days	Thu 4/25/	Fri 5/24/19	60	$481,251.62	$0.00	$0.00	$0.00	$0.00
62	**Obras civiles de edificios concluidas**	**572 days**	**Wed 3/21**	**Thu 5/28/20**		**$16,568,760.91**	**$0.00**	**$0.00**	**$0.00**	**$0.00**
63	Obra Gruesa E-P1 (16 de Julio)	22 days	Tue 10/23	Wed 11/21/	56FS+4	$481,251.62	$0.00	$0.00	$0.00	$0.00
64	Obra Gruesa E-P3 (Mirador)	22 days	Tue 10/23	Wed 11/21/	56FS+4	$481,251.62	$0.00	$0.00	$0.00	$0.00
65	Resto Obras Civiles L. Plateada	22 days	Thu 4/25/	Fri 5/24/19	64FS+1	$481,251.62	$0.00	$0.00	$0.00	$0.00
66	Final Obras Civiles e Instalacs. Complementarias E-P1	22 days	Mon 5/27	Tue 6/25/19	65	$92,502.14	$0.00	$0.00	$0.00	$0.00
67	Final Obras Civiles e Instalacs. Complementarias E-P3	22 days	Fri 7/26/1	Mon 8/26/1	66FS+2	$92,502.14	$0.00	$0.00	$0.00	$0.00
68	Áreas Exteriores E-P1 (16 de Julio)	22 days	Mon 5/27	Tue 6/25/19	66SS	$481,251.62	$0.00	$0.00	$0.00	$0.00
69	Áreas Exteriores Edificio E-P3 (Mirador)	22 days	Fri 7/26/1	Mon 8/26/1	68FS+2	$481,251.62	$0.00	$0.00	$0.00	$0.00
70	EJECUCIÓN DE OBRAS COMPLEMENTARIAS L. Plateada	176 days	Thu 9/26/	Thu 5/28/20	69FS+2	$92,502.14	$0.00	$0.00	$0.00	$0.00
71	**CONSTRUCCIÓN OBRA CIVIL FUNCIONAL L. Plateada**	**286 days**	**Wed 3/21**	**Wed 4/24/1**		**$13,884,996.39**	**$0.00**	**$0.00**	**$0.00**	**$0.00**
72	CONSTRUCCIÓN OBRA CIVIL FUNCIONAL L. Plateada	0 days	Wed 11/2	Wed 11/21/	63	$462,510.69	$0.00	$0.00	$0.00	$0.00
73	Fundamentos torres	22 days	Tue 3/26/	Wed 4/24/1	63FS+8	$2,406,258.11	$0.00	$0.00	$0.00	$0.00
74	Trabajos Previos Fundamentos E-P1	22 days	Fri 9/21/1	Mon 10/22/	56FS+2	$2,406,258.11	$0.00	$0.00	$0.00	$0.00
75	Fundamentos E-P1 retorno	22 days	Tue 10/23	Wed 11/21/	74	$2,406,258.11	$0.00	$0.00	$0.00	$0.00
76	Trabajos Previos Fundamentos E-P2	22 days	Wed 3/21	Thu 4/19/18	14	$2,406,258.11	$0.00	$0.00	$0.00	$0.00
77	Fundamentos E-P2 motriz intermedia	44 days	Mon 7/23	Thu 9/20/18	76FS+6	$2,406,258.11	$0.00	$0.00	$0.00	$0.00
78	Trabajos Previos Fundamentos E-P3	22 days	Tue 10/23	Wed 11/21/	77FS+2	$928,675.21	$0.00	$0.00	$0.00	$0.00
79	Fundamentos E-P3 retorno	44 days	Tue 10/23	Fri 12/21/18	78SS	$462,519.94	$0.00	$0.00	$0.00	$0.00
80	**2.1.3 Entregable: Supervisión y Fiscalización realizadas**	**528 days**	**Fri 4/20/1**	**Tue 4/28/20**		**$1,894,548.16**	**$0.00**	**$0.00**	**$0.00**	**$0.00**
81	Supervision	528 days	Fri 4/20/1	Tue 4/28/20	11	$1,082,599.16	$0.00	$0.00	$0.00	$0.00
82	Fiscalizacion	528 days	Fri 4/20/1	Tue 4/28/20	81SS	$811,949.00	$0.00	$0.00	$0.00	$0.00
83	**2.1.4 Entregable: Plan de Reasentamiento**	308 days	Thu 11/16	Mon 1/21/1	5FS+44	$531,990.00	$0.00	$0.00	$0.00	$0.00
84	2.2 Producto 5: Sistema electromecánico y equipamiento instalado y en funcionamiento	641 days	Tue 10/17	Tue 3/31/20		$30,897,948.38	$0.00	$0.00	$0.00	$0.00
85	**2.2.1 Entregable: Sistema Electromecánico Implementado**	**485 days**	**Tue 10/17**	**Mon 8/26/1**		**$22,876,388.21**	**$0.00**	**$0.00**	**$0.00**	**$0.00**
86	**FABRICACIÓN L. Plateada**	88 days	Tue 10/17	Thu 2/15/18	5FS+22	$0.00	$0.00	$0.00	$0.00	$0.00
87	**CONSTRUCCIÓN, EQUIPAMIENTO Y MONTAJE L. Plateada**	**353 days**	**Thu 4/19/**	**Mon 8/26/1**		**$22,876,388.21**	**$0.00**	**$0.00**	**$0.00**	**$0.00**
88	**TRANSPORTE E IMPORTACIÓN EQUIPOS L. Plateada**	44 days	Thu 4/19/	Tue 6/19/18	86FS+4	$0.00	$0.00	$0.00	$0.00	$0.00
89	**MONTAJE L. Plateada**	**242 days**	**Fri 9/21/1**	**Mon 8/26/1**		**$22,876,388.21**	**$0.00**	**$0.00**	**$0.00**	**$0.00**
90	CONSTRUCCIÓN, EQUIPAMIENTO Y MONTAJE L. Plateada	22 days	Fri 9/21/1	Mon 10/22/	74SS	$4,813,164.38	$0.00	$0.00	$0.00	$0.00
91	Montaje de Torres	22 days	Fri 9/21/1	Mon 10/22/	74SS	$4,813,164.38	$0.00	$0.00	$0.00	$0.00
92	Montaje de Estaciones y Garaje	22 days	Tue 10/23	Wed 11/21/	91	$4,813,164.38	$0.00	$0.00	$0.00	$0.00
93	Montaje E-P1	22 days	Thu 11/22	Fri 12/21/18	92	$1,201,003.47	$0.00	$0.00	$0.00	$0.00
94	Montaje E-P2	22 days	Thu 11/22	Fri 12/21/18	93SS	$1,201,003.47	$0.00	$0.00	$0.00	$0.00
95	Tendido, tensado y empalme cable 1	22 days	Mon 12/2	Tue 1/22/19	94	$1,201,003.47	$0.00	$0.00	$0.00	$0.00
96	Montaje E-P3	22 days	Thu 11/22	Fri 12/21/18	94SS	$1,207,866.35	$0.00	$0.00	$0.00	$0.00
97	Tendido, tensado y empalme cable 2	44 days	Thu 4/25/	Tue 6/25/19	96FS+8	$1,207,866.35	$0.00	$0.00	$0.00	$0.00
98	Garaje E-P1	44 days	Thu 4/25/	Tue 6/25/19	97SS	$1,207,866.35	$0.00	$0.00	$0.00	$0.00
99	Montaje cabinas	22 days	Fri 7/26/1	Mon 8/26/1	98FS+2	$1,210,285.61	$0.00	$0.00	$0.00	$0.00
100	**2.2.2 Entregable: Diseño y construcción de sistemas complementarios LP concluidos**	**308 days**	**Thu 6/21/**	**Mon 8/26/1**		**$2,608,695.66**	**$0.00**	**$0.00**	**$0.00**	**$0.00**
101	Proyectos Ingeniería Detalle Instalaciones Complementarias Estacs. L. Plateada	22 days	Thu 6/21/	Fri 7/20/18	49	$778,715.12	$0.00	$0.00	$0.00	$0.00
102	Desarrollo Proys. Ing. Detalle Insts. Compl. Estacs. L. Plateada	22 days	Mon 5/27	Tue 6/25/19	101FS+	$778,715.12	$0.00	$0.00	$0.00	$0.00
103	Final Aprobaciones Proys. Ing. Detalle Insts. Compl. Estacs. L. Plateada	22 days	Fri 7/26/1	Mon 8/26/1	102FS+	$1,051,265.42	$0.00	$0.00	$0.00	$0.00
104	**2.2.3 Entregable: Puesta en marcha y recepcion finalizada**	**200 days**	**Wed 6/26**	**Tue 3/31/20**		**$5,412,864.51**	**$0.00**	**$0.00**	**$0.00**	**$0.00**
105	**PUESTA EN MARCHA**	**44 days**	**Wed 6/26**	**Mon 8/26/1**		**$2,941,204.50**	**$0.00**	**$0.00**	**$0.00**	**$0.00**
106	PUESTA EN FUNCIONAMIENTO Y AJUSTES L. Plateada S1	22 days	Wed 6/26	Thu 7/25/19	102	$469,696.28	$0.00	$0.00	$0.00	$0.00
107	PUESTA EN FUNCIONAMIENTO Y AJUSTES L. Plateada S2	22 days	Wed 6/26	Thu 7/25/19	106SS	$790,686.96	$0.00	$0.00	$0.00	$0.00
108	PRUEBAS L. Plateada	22 days	Wed 6/26	Thu 7/25/19	106SS	$518,954.55	$0.00	$0.00	$0.00	$0.00
109	CAPACITACIÓN PREVIA L. Plateada	22 days	Fri 7/26/1	Mon 8/26/1	108	$692,170.43	$0.00	$0.00	$0.00	$0.00
110	FUNCIONAMIENTO EN PRÁCTICAS L. Plateada	22 days	Fri 7/26/1	Mon 8/26/1	109SS	$469,696.28	$0.00	$0.00	$0.00	$0.00
111	**ENTREGA PARA FUNCIONAMIENTO COMERCIAL CONCLUIDA**	**178 days**	**Fri 7/26/1**	**Tue 3/31/20**		**$2,471,660.01**	**$0.00**	**$0.00**	**$0.00**	**$0.00**
112	ENTREGA FINAL DE OBRAS L. Plateada	0 days	Fri 7/26/1	Fri 7/26/19	113SS	$790,686.96	$0.00	$0.00	$0.00	$0.00

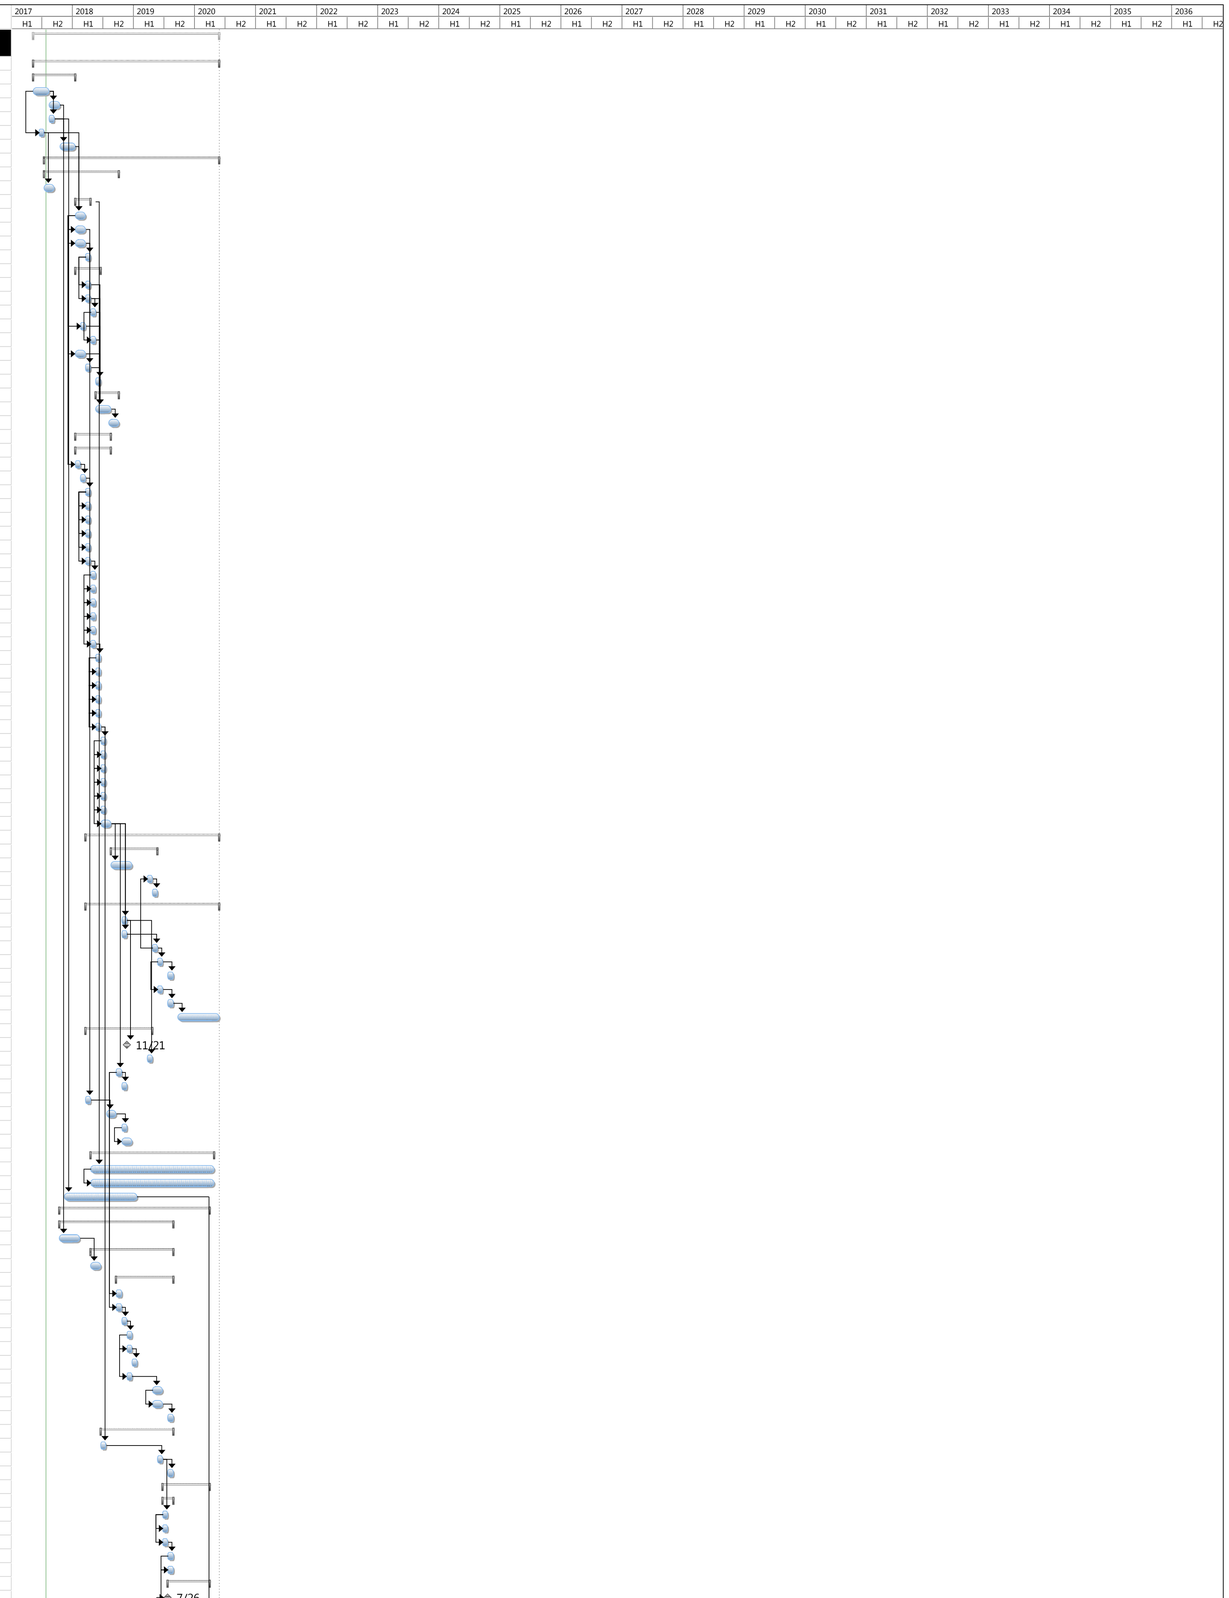

Project: BO-L1079 PEP POA
Date: Wed 7/26/17

Task | Split | Milestone | Summary | Project Summary | Inactive Task | Inactive Milestone | Inactive Summary | Manual Task | Duration-only | Manual Summary Rollup | Manual Summary | Start-only | Finish-only | External Tasks | External Milestone | Deadline | Progress | Manual Progress

	Task Name	Duration	Start	Finish	Predece	Cost	2017	2018	2019	2020
113	Tareas previas a la EFC L. Plateada	22 days	Fri 7/26/1	Mon 8/26/1	110SS	$518,954.55	$0.00	$0.00	$0.00	$0.00
114	Entrega para FC L. Plateada	30 days	Tue 8/27/	Mon 10/7/1	113	$692,170.43	$0.00	$0.00	$0.00	$0.00
115	Recepción provisional	30 days	Tue 10/8/	Mon 11/18/	114	$0.00	$0.00	$0.00	$0.00	$0.00
116	Recepción definitiva	30 days	Mon 1/20/	Fri 2/28/20	115FS+	$0.00	$0.00	$0.00	$0.00	$0.00
117	Fin de obras L. Plateada	22 days	Mon 3/2/2	Tue 3/31/20	116	$469,848.07	$0.00	$0.00	$0.00	$0.00
118	Obras finalizadas	0 days	Tue 3/31/	Tue 3/31/20	117	$0.00	$0.00	$0.00	$0.00	$0.00
119	H: Mejoramiento Infraestructura urbano completado	0 days	Tue 3/31/	Tue 3/31/20	117,83	$0.00	$0.00	$0.00	$0.00	$0.00



Project: BO-L1079 PEP POA
Date: Wed 7/26/17

Task · Split · Milestone · Summary · Project Summary · Inactive Task · Inactive Milestone · Inactive Summary · Manual Task · Duration-only · Manual Summary Rollup · Manual Summary · Start-only · Finish-only · External Tasks · External Milestone · Deadline · Progress · Manual Progress
