








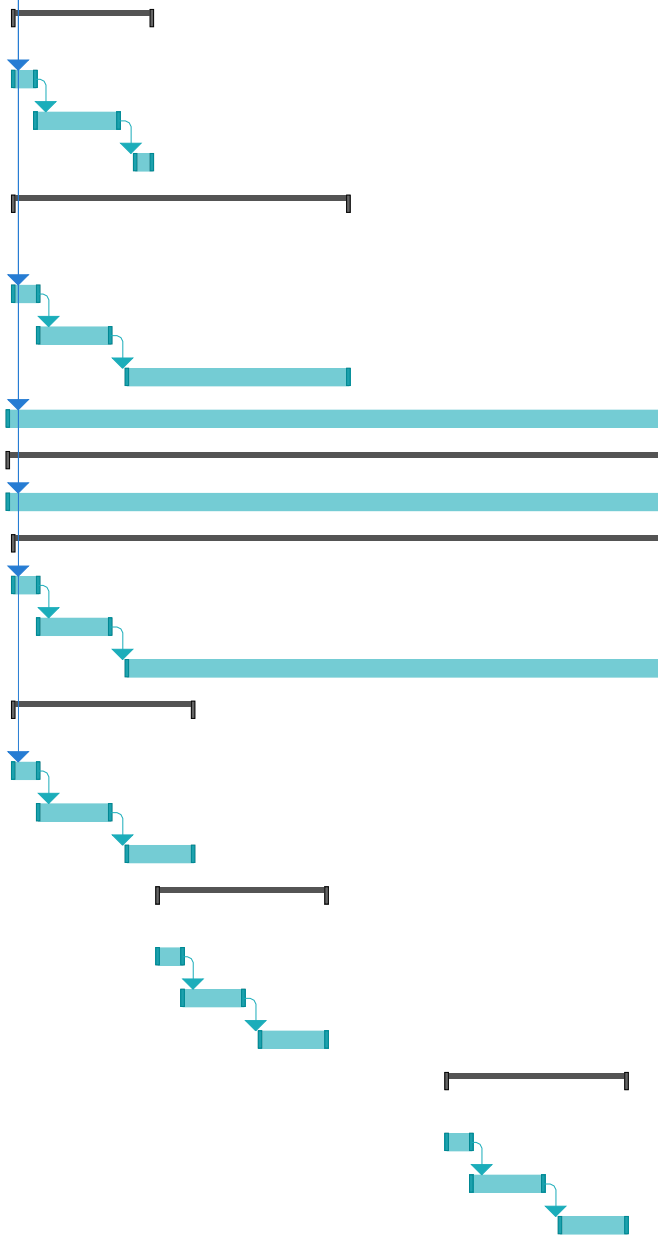

Id	Nombre de tarea	Comienzo	Fin	2017	2018	2019	2020	2021	Total	2016		2017		2018		2019		2020		2021		2022
										S2	S1	S2	S1	S2	S1	S2	S1	S2	S1	S2		
177	Adquisicion de servidor, equipamiento auxiliares, software para la UCP	mar 04/07/17	lun 18/06/18	\$0	\$200.000	\$0	\$0	\$0	\$200.000													
178	Preparacion de datos tecnicos	mar 04/07/17	lun 28/08/17	\$0	\$0	\$0	\$0	\$0	\$0													
179	Proceso de contratacion	mar 29/08/17	lun 26/03/18	\$0	\$0	\$0	\$0	\$0	\$0													
180	Entrega de bienes	mar 08/05/18	lun 18/06/18	\$0	\$200.000	\$0	\$0	\$0	\$200.000													
181	Contrato de Firma Consultora para el diseño, desarrollo e implementaacion de un tablero control para la gestion de programas UCP	mar 04/07/17	lun 28/10/19	\$60.000	\$140.000	\$0	\$0	\$0	\$200.000													
182	Proceso de Lista Corta	mar 04/07/17	lun 04/09/17	\$0	\$0	\$0	\$0	\$0	\$0													
183	Proceso de contratacion	mar 05/09/17	lun 05/03/18	\$0	\$0	\$0	\$0	\$0	\$0													
184	Ejecucion del servicio	mar 17/04/18	lun 28/10/19	\$60.000	\$140.000	\$0	\$0	\$0	\$200.000													
185	Fortalecimiento Institucional SENASBA	mar 20/06/17	lun 27/12/21	\$50.000	\$50.000	\$50.000	\$50.000	\$0	\$200.000													
186	Auditoria, Monitoreo y Evaluacion	mar 20/06/17	lun 27/12/21	\$150.000	\$190.000	\$170.000	\$70.000	\$370.000	\$950.000													
187	Asesoría Externa en temas legales y adquisiciones	mar 20/06/17	lun 27/12/21	\$20.000	\$20.000	\$20.000	\$20.000	\$20.000	\$100.000													
188	Contrato de Firma para Auditoria Externa	mar 04/07/17	lun 27/12/21	\$50.000	\$50.000	\$50.000	\$50.000	\$50.000	\$250.000													
189	Proceso de Lista Corta	mar 04/07/17	lun 04/09/17	\$0	\$0	\$0	\$0	\$0	\$0													
190	Proceso de contratacion	mar 05/09/17	lun 05/03/18	\$0	\$0	\$0	\$0	\$0	\$0													
191	Ejecucion del servicio	mar 17/04/18	lun 27/12/21	\$50.000	\$50.000	\$50.000	\$50.000	\$50.000	\$250.000													
192	Contrato de Firma Consultora para el levantamiento de linea de base	mar 04/07/17	lun 01/10/18	\$80.000	\$120.000	\$0	\$0	\$0	\$200.000													
193	Proceso de Lista Corta	mar 04/07/17	lun 04/09/17	\$0	\$0	\$0	\$0	\$0	\$0													
194	Proceso de contratacion	mar 05/09/17	lun 05/03/18	\$0	\$0	\$0	\$0	\$0	\$0													
195	Ejecucion del servicio	mar 17/04/18	lun 01/10/18	\$80.000	\$120.000	\$0	\$0	\$0	\$200.000													
196	Contrato de Firma Consultora para la evaluaciòn medio termino	mié 04/07/18	mar 03/09/19	\$0	\$0	\$100.000	\$0	\$0	\$100.000													
197	Proceso de Lista Corta	mié 04/07/18	mar 04/09/18	\$0	\$0	\$0	\$0	\$0	\$0													
198	Proceso de contratacion	mié 05/09/18	mar 05/02/19	\$0	\$0	\$0	\$0	\$0	\$0													
199	Ejecucion del servicio	mié 20/03/19	mar 03/09/19	\$0	\$0	\$100.000	\$0	\$0	\$100.000													
200	Contrato Firma Consultora para Evaluacion Final y economica expost	vie 03/07/20	jue 30/09/21	\$0	\$0	\$0	\$0	\$300.000	\$300.000													
201	Proceso de Lista Corta	vie 03/07/20	jue 03/09/20	\$0	\$0	\$0	\$0	\$0	\$0													
202	Proceso de contratacion	vie 04/09/20	jue 04/03/21	\$0	\$0	\$0	\$0	\$0	\$0													
203	Ejecucion del servicio	vie 16/04/21	jue 30/09/21	\$0	\$0	\$0	\$0	\$300.000	\$300.000													
