

PMR Public Report

Operation Number	BR-L1535	Chief of Operations Validation Date	04/22/23
Year- PMR Cycle	Second period Jan-Dec 2022	Division Chief Validation Date	04/24/23
Last Update	03/27/23	Country Representative Validation Date	04/25/23
PMR Validation Stage	Validated by Representative		

Basic Data

Operation Profile

Operation Name	Fiscal Management Modernization Project for the State of Paraíba - PROFISCO II PB	Loan Number	5188/OC-BR
Executing Agency	SECRETARIA DE ESTADO DA RECEITA DA PARAIBA	Sector/Subsector	REFORM / MODERNIZATION OF THE STATE-FISCAL POLICY FOR SUSTAINABILITY AND GROWTH
Team Leader	MARTINEZ FRITSCHER, ANDRE CARLOS	Overall Stage	Disbursing (From eligibility until all the Operations are closed)
Operation Type	Loan Operation	Country	Brazil
Lending Instrument	Investment Loan	Convergence related Operation(s)	
Borrower	GOVERNO DO ESTADO DA PARAIBA		


Environmental and Social Safeguards

Impacts Category	C	Was/Were the objective(s) of this operation reformulated?	NO
Safeguard Performance Rating		Date of approval	
Safeguard Performance Rating - Rationale			

Financial Data

	Total Cost and Source					Available Funds (US\$)			
Operations	Original IDB	Current IDB	Local Counterpart	Co-Financing / Country	Total Original Cost	Current IDB	Disb. Amount to Date	% Disbursed	Undisbursed Amount
BR-L1535	38,412,000	38,412,000	4,268,000	0	42,680,000	38,412,000	1,450,403.1	3.78%	36,961,596.9
Aggregated	38,412,000	38,412,000	4,268,000	0	42,680,000	38,412,000	1,450,403.1	3.78%	36,961,596.9

Expense Categories by Loan Contract (cumulative values)

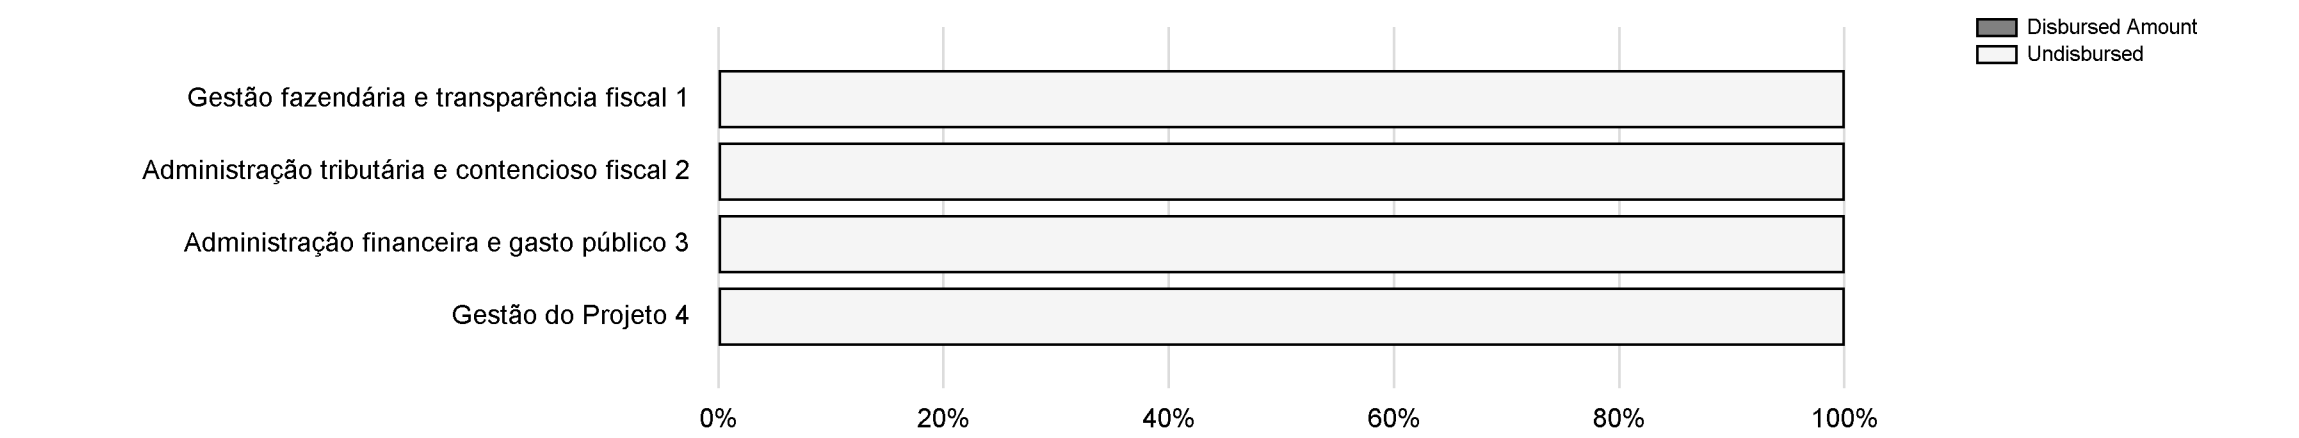

Please note that inactive indicators and outputs are not displayed; totals in the actual cost table may not match the sum of the cost of the outputs displayed, due to the cost of inactive outputs.

RESULTS MATRIX

General Development Objectives

General Development Objectives Nbr. 1: Diminuição da relação do déficit fiscal primário e o PIB estadual

Observation: Diminuição da relação do déficit fiscal primário e o PIB estadual. O ano de referência foi alterado para evitar a influência de choques exógenos transitórios (crise gerada pelo Covid).

Indicator		Unit of Measure	Baseline	Baseline Year	Expected Year of Achievement	EOP 2026	
1.0	Resultado Primário / PIB-PB	%	0.37	2019	2026	P	1.39
						A	-

Details

Means of Verification: Informe de Datos del balance del estado

Observations: Ver PME

The General Development Objective indicator target is expected to be observed by the operation's "Fully Justified" date in Convergence (CO): No

Pro-Gender	No	Pro-Ethnicity	No	CRF indicator			

General Development Objectives Nbr. 2: Aumento da relação entre a arrecadação tributária e o PIB estadual

Observation: Aumento da relação entre a arrecadação tributária e o PIB estadual. O ano de referência foi alterado para evitar a influência de choques exógenos transitórios (crise gerada pelo Covid).

Indicator		Unit of Measure	Baseline	Baseline Year	Expected Year of Achievement	EOP 2026	
2.0	Arrecadação tributária / PIB-PB	%	7.88	2021	2026	P	8.34
						A	-
Details							

Pro-Gender	No	Pro-Ethnicity	No	CRF indicator			

General Development Objectives Nbr. 3: Diminuição da relação da dívida corrente líquida e o PIB estadual

Pro-Gender	No	Pro-Ethnicity	No	CRF indicator			

<b>General Development Objectives Nbr. 3:</b> Diminuição da relação da dívida corrente líquida e o PIB estadual							
<b>Observation:</b> Diminuição da relação da dívida corrente líquida e o PIB estadual. O ano de referência foi alterado para evitar a influência de choques exógenos transitórios (crise gerada pelo Covid).							

Pro-Gender	No	Pro-Ethnicity	No	CRF indicator			

Details							
Means of Verification: Informe de Datos del balance del estado							
Observations: Ver PME							
The General Development Objective indicator target is expected to be observed by the operation's "Fully Justified" date in Convergence (CO): No							
Pro-Gender	No	Pro-Ethnicity	No	CRF indicator			

RESULTS MATRIX											
Specific Development Objectives											
Specific Development Objectives Nbr. 1: Aumento da relação entre as metas estratégicas de planejamento que foram cumpridas e o total de metas planejadas											
Observation:											
	Indicator	Unit of Measure	Baseline	Baseline Year		2022	2023	2024	2025	2026	EOP 2026
1.0	Quantidade de metas cumpridas / total de metas planejadas	%	0	2021	P	-	-	40	60	80	80
					A	-	-	-	-	-	-
Details											

Means of Verification: Informe de Datos del balance del estado

Observations: Ver PME

Evaluation Methodology: -

Pro-Gender	No	Pro-Ethnicity	No	CRF indicator	

Specific Development Objectives Nbr. 2: Diminuição da relação entre o custo para arrecadar e a arrecadação tributária

Observation:											
	Indicator	Unit of Measure	Baseline	Baseline Year		2022	2023	2024	2025	2026	EOP 2026
2.0	Orçamento de funcionamento da SEFAZ/ Arrecadação tributária	%	5.66	2021	P	5.66	5.66	4.43	4.3	4	4
					A	3.93	-	-	-	-	-
Details											

Means of Verification: Informe de la Gerencia Operacional de Recaudación – GOA/SEFAZPB

Observations: Ver PME

Evaluation Methodology: -

Pro-Gender	No	Pro-Ethnicity	No	CRF indicator	

Specific Development Objectives Nbr. 3: Redução da discrepância entre o orçamento planejado e o orçamento executado

Observation:											
	Indicator	Unit of Measure	Baseline	Baseline Year		2022	2023	2024	2025	2026	EOP 2026
3.0	Orçamento planejado / Orçamento executado	%	4.34	2021	P	4.4	4.3	4.2	4.1	4	4
					A	15.42	-	-	-	-	-
Details											

Means of Verification: Informe de Datos del balance del estado

Observations: Ver PME

Evaluation Methodology: -

Pro-Gender	No	Pro-Ethnicity	No	CRF indicator	

RESULTS MATRIX

OUTPUTS: ANNUAL PHYSICAL AND FINANCIAL PROGRESS

Component Nbr. 1 Gestão Fazendária e Transparência Fiscal

				PHYSICAL PROGRESS		FINANCIAL PROGRESS	
	Output	Unit of Measure		2022	EOP 2026	2022	EOP 2026
1.01	1.1 Modelo de Gestão Estratégica do Estado por Resultado	Módulo	P	-	7	-	2,210,372.9
			P (a)	-	7	-	2,210,372.9
			A	-	-	-	-
1.02	1.2 Modelo de Gestão de Pessoas	Módulo	P	-	7	-	918,908
			P (a)	-	7	-	918,908
			A	-	-	-	-
1.03	1.3 Modelo de Tecnologia da Informação	Módulo	P	-	14	-	12,174,450
			P (a)	-	14	-	12,174,450
			A	-	-	1,102,941.8	1,102,941.8
1.04	1.4 Modelo de Gestão de Compras	Módulo	P	-	2	-	4,191,349.99
			P (a)	-	2	-	4,191,349.99
			A	-	-	-	-
1.05	1.5 Modelo de Transparência e Cidadania Fiscal	Módulo	P	-	2	-	1,746,919.11
			P (a)	-	2	-	1,746,919.11
			A	-	-	-	-

Component Nbr. 2 Administração Tributária e Contencioso Fiscal

				PHYSICAL PROGRESS		FINANCIAL PROGRESS	
	Output	Unit of Measure		2022	EOP 2026	2022	EOP 2026
2.01	2.1 Modelo de Gestão de Políticas Tributárias	Módulo	P	-	4	-	385,000
			P (a)	-	4	-	385,000
			A	-	-	-	-
2.02	2.2 Modelo de Gestão de Informações Econômico-fiscais	Módulo	P	-	4	-	924,000
			P (a)	-	4	-	924,000
			A	-	-	-	-
2.03	2.3 Modelo de Fiscalização e Inteligência Fiscal	Módulo	P	-	4	-	5,718,000
			P (a)	-	4	-	5,718,000
			A	-	-	-	-
2.04	2.4 Modelo de Gestão do Contencioso Fiscal	Módulo	P	-	3	-	1,630,000
			P (a)	-	3	-	1,630,000
			A	-	-	-	-
2.05	2.5 Modelo de Prestação de Serviços aos Contribuintes	Módulo	P	-	3	-	1,064,000
			P (a)	-	3	-	1,064,000
			A	-	-	-	-
2.06	2.6 Modelo de Gestão de Arrecadação e Cobrança	Modelo	P	-	1	-	386,000
			P (a)	-	1	-	386,000
			A	-	-	-	-

				PHYSICAL PROGRESS		FINANCIAL PROGRESS	
	Output	Unit of Measure		2022	EOP 2026	2022	EOP 2026
3.01	3.1 Modelo de Gestão de Políticas Públicas do Governo	Módulo	P	-	4	-	592,000.11
			P (a)	-	4	-	592,000.11
			A	-	-	-	-
3.02	3.2 Modelo de Gestão da Execução Financeira	Módulo	P	-	2	-	550,000
			P (a)	-	2	-	550,000
			A	-	-	-	-
3.03	3.3 Modelo de Supervisão das Empresas Estatais	Modelo	P	-	1	-	153,649
			P (a)	-	1	-	153,649
			A	-	-	-	-
3.04	3.4 Modelo de Gestão Contábil e de Custos	Módulo	P	-	2,021	-	9,128,864.89
			P (a)	-	2,021	-	9,128,864.89
			A	-	-	-	-
3.05	3.5 Modelo de Gestão da Dívida Pública	Módulo	P	-	2	-	185,000
			P (a)	-	2	-	185,000
			A	-	-	-	-
3.06	3.6 Modelo de Gestão dos Investimentos Públicos do Estado	Módulo	P	-	5	-	321,486
			P (a)	-	5	-	321,486
			A	-	-	-	-

Other Cost				
	A1. Monitoramento e avaliação	P	0	377,777.78
		P (a)	0	377,777.78
		A	0	0
	A2. Auditoria	P	0	22,222.22
		P (a)	0	22,222.22
		A	0	0
Total Cost				
	Total Cost	P	0	42,680,000
		P (a)	0	42,680,000
		A	1,102,941.8	1,102,941.8

CHANGES TO THE MATRIX					
Section	Name	Type of Change	Sub type	Modified By	Entered in System
Output	1. Sistema administrativo de cobrança do crédito administrativo, com procedimentos de gestão de risco do contribuinte e novos procedimentos de financiamento de dívidas.	Create Milestone	N/A	HELIOO	3/17/2023
	3.4.1 - Processo de convergência contábil	Modify Milestone	Modify Milestone name	HELIOO	3/17/2023
			Modify Unit of Measure	HELIOO	3/17/2023
	3.4.2 - Patrimônio imobiliário do Estado identificado, inventariado e reavaliado	Modify Milestone	Modify Milestone name	HELIOO	3/17/2023
			Modify Unit of Measure	HELIOO	3/17/2023

RISKS AND PLANNED RESPONSES

Risk ID	Risk Status		Risk Taxonomy		
1	Inactive		Political Environment		
	Response Actions				
	1	Management Strategy		Status	

Risk ID	Risk Status		Risk Taxonomy
2	Active		Technical Design
	Response Actions		
	2	Management Strategy	Status

Risk ID	Risk Status		Risk Taxonomy		
3	Inactive		Political Environment		
	Response Actions				
	3	Management Strategy		Status	

Risk ID	Risk Status		Risk Taxonomy		
4	Inactive		Political Environment		
	Response Actions				
	4	Management Strategy		Status	

Risk ID	Risk Status		Risk Taxonomy		
5	Inactive		Political Environment		
	Response Actions				
	5	Management Strategy		Status	

Risk ID	Risk Status		Risk Taxonomy		
6	Inactive		Political Environment		
	Response Actions				
	6	Management Strategy		Status	

Risk ID	Risk Status		Risk Taxonomy
7	Inactive		Political Environment
	Response Actions		
	7	Management Strategy	Status

Risk ID	Risk Status		Risk Taxonomy
8	Active		Political Environment
	Response Actions		
	8.01	Management Strategy	Status
		MITIGATE	ACTIVE

Risk ID	Risk Status		Risk Taxonomy		
9	Inactive		Political Environment		
	Response Actions				
	9	Management Strategy		Status	

Risk ID	Risk Status		Risk Taxonomy		
10	Active		Political Environment		
	Response Actions				
	10	Management Strategy		Status	

Risk ID	Risk Status		Risk Taxonomy
11	Active		Internal Processes
	Response Actions		
	11.01	Management Strategy	Status
		MITIGATE	ACTIVE





IMPLEMENTATION STATUS AND LEARNING

Lesson Learned - Categories
Intra/Inter Coordination
Acquisitions and Procurement - Provider Performance and Supervision
