



Operation Number: **BR-L1372**
Year- PMR Cycle: **First period Jan-Jun 2015**
Last Update: **1/27/2016**
PMR Validation Stage: **Validated by Representative**

Chief of Operations validation date: **10/13/2015**
Division Chief validation date: **10/14/2015**
Country Representative validation date: **10/16/2015**

Inter-American Development Bank - IDB
Office of Strategic Planning and Development Effectiveness

Operation Profile

Basic Data

Operation name:	Integrated Prog for Social Inclusion and Urban Requalification: Fam Paranaense	Loan Number:	3129/OC-BR
Executing Agency (EA):	ESTADO DO PARANA		
Team Leader:	Ochoa,Francisco Jose	Sector/Subsector:	POVERTY ALLEVIATION
Operation Type:	Loan Operation	Overall Stage:	Disbursing (From eligibility until all the loans are closed).
Lending Instrument:	Investment Loan	Country:	BRAZIL
Borrower:	ESTADO DO PARANA		
		Convergence related Operation(s):	

Total Cost and Source

	Original IDB	Current Active IDB	Local Counterpart	Co-Financing/Country	Total operation cost - Original Estimate
BR-L1372	\$60,000,000.00	\$60,000,000.00	\$40,000,000.00	\$0.00	\$100,000,000.00

Available Funds (US\$)

	Current IDB	Disb. Amount to Date	% Disbursed	Undisbursed Balance
BR-L1372	\$60,000,000.00	\$1,638,497.81	2.73%	\$58,361,502.19


Environmental and Social Safeguards

Main Operation	
Impacts Category:	
Safeguard Performance Rating:	
Safeguard Performance Rating - Rationale:	

Reformulation Information

Main Operation	
Was/Were the objective(s) of this operation reformulated?	NO
Date of approval:	

Expense Categories by Loan Contract (cumulative values)

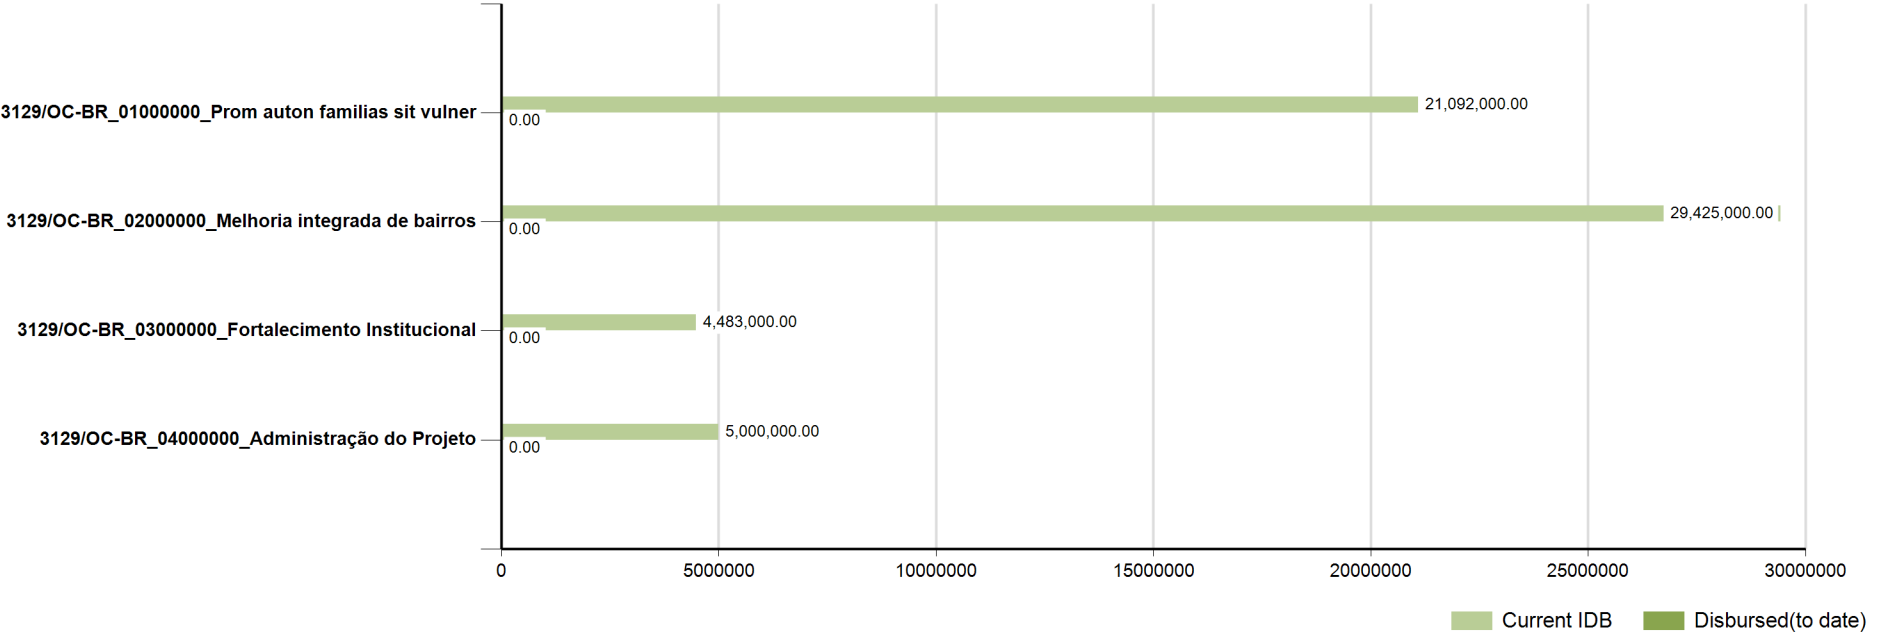

Results Matrix

Impacts

Impact:	0 Condiçao de vida das familias mediante acoes do Governo melhoradas							
Observation:								
Indicators	Flags*	Unit of Measure	Baseline	Baseline Year	Means of verification	Observations	EOP	
0.0 Familias com acesso e uso dos servicos em educacao, saude e desenvolvimento social produtivo melhorados		%		2014	Sistema de informacao do Programa		P	
							P(a)	
							A	
0.1 Familias com indice melhorado de habilitação psicosocial		%		2014			P	
							P(a)	
							A	
0.2 Familias abordadas pelo programa ao concluir 24 meses de acompanhamento, que deram continuidade a sua propria habilitacao social		%		2014			P	
							P(a)	
							A	

 RF - RF Indicator
 SI - Sector Indicator
 CI - Country Indicator
 PG - Pro-Gender
 PE - Pro-Ethnicity

Outcomes

Outcome:	0 Resultado Final 1: Autonomia das Famílias vulneráveis melhorado							
Observation:								
Indicators	Flags*	Unit of Measure	Baseline	Baseline Year	Means of verification	Observations	EOP	
0.0 Famílias que após dois anos de acompanhamento, possuem 60% das ações do plano de ação cumpridas		%		2014	Sistema de informação do Programa		P	60.00
	P(a)							
	A							
0.1 Mulheres e homens participantes dos empreendimentos financiados pelo programa que melhoram sua renda		%		2014	Sistema de informação do Programa		P	60.00
	P(a)							
	A							
0.2 Crianças entre 06 e 14 anos, que estavam fora da escola, foram incorporados e permaneceram na escola após dois anos de acompanhamento		%		2014	Sistema de informação do Programa		P	50.00
	P(a)							
	A							

Outcome:	0 Resultado Final 2: Bairros integralmente melhorados							
Observation:								
Indicators	Flags*	Unit of Measure	Baseline	Baseline Year	Means of verification	Observations	EOP	
0.0 Familias atendidas pelo subcomponent e 2.1 que habitam em casas de materiais e pisos permanentes		%	30.00	2014	Relatorio semestral do Programa		P	100.00
							P(a)	
							A	
0.1 Familias atendidas pelo subcomponent e 2.1 com acesso a agua potavel no domicilio		%	50.00	2014	Relatorio semestral do Programa		P	100.00
							P(a)	
							A	
Outcome:	0 Resultado Final 3: Capacidade institucional fortalecida							
Observation:								
Indicators	Flags*	Unit of Measure	Baseline	Baseline Year	Means of verification	Observations	EOP	
0.0 Participantes da capacitacao sobre a metodologia do programa e que obtiveram pelo menos 60% da prova de conhecimento		%	0.00	2014	Testes de conhecimento		P	90.00
							P(a)	
							A	

Componente I: Promoção a Autonomia das Famílias em Situação de Vulnerabilidade		Physical Progress			Financial Progress		
Outputs	Unit of Measure		2015	EOP		2015	EOP
Planos de Ação Familiar pactuados com a família beneficiária elaborados	Individuals	P	4,720.00	22,000.00	P	901,000.00	14,410,366.00
		P(a)	4,720.00	22,000.00	P(a)	901,000.00	14,410,366.00
		A	4,973.00	4,973.00	A	5,411,108.00	5,411,108.00
Incentivos fundo a fundo para ações da assistência social nos municípios	Municípios	P	130.00	130.00	P	1,324,000.00	8,774,200.00
		P(a)	130.00	130.00	P(a)	1,324,000.00	8,774,200.00
		A	82.00	0.00	A	716,010.00	716,010.00
Transferências do Piso Paranaense de Assistência Social	Transferências	P	53.00	53.00	P	1,500,000.00	10,781,000.00
		P(a)	53.00	53.00	P(a)	1,500,000.00	10,781,000.00
		A	53.00	0.00	A	324,857.00	324,857.00
Famílias beneficiadas pelo "Renda Família Paranaense"	Famílias	P	30,000.00	40,000.00	P	7,000,000.00	10,000,000.00
		P(a)	30,000.00	40,000.00	P(a)	7,000,000.00	10,000,000.00
		A	40,837.00	40,837.00	A	3,483,687.00	3,483,687.00
Pessoas perfil FP capacitadas e certificadas (SETS)	Capacitações	P	0.00	3,480.00	P	100,000.00	2,522,478.00
		P(a)	0.00	3,480.00	P(a)	100,000.00	2,522,478.00
		A		0.00	A		0.00
Projetos produtivos familiares rurais implementados (SEAB)	Projetos	P	700.00	5,600.00	P	660,000.00	7,256,760.00
		P(a)	700.00	5,600.00	P(a)	660,000.00	7,256,760.00
		A		0.00	A		0.00
Famílias participantes de novos projetos de inclusao socio produtiva em funcionamento (economia solidaria)	Famílias	P	0.00	560.00	P	100,000.00	2,522,154.00
		P(a)	0.00	560.00	P(a)	100,000.00	2,522,154.00
		A		0.00	A		0.00
Componente II: Melhoria Integrada de Bairros		Physical Progress			Financial Progress		
Outputs	Unit of Measure		2015	EOP		2015	EOP
Famílias com casas novas recebidas	Famílias	P	0.00	594.00	P	1,127,500.00	17,940,000.00
		P(a)	0.00	594.00	P(a)	1,127,500.00	17,940,000.00
		A		0.00	A		0.00
Lotes regularizados	Lotes	P	0.00	328.00	P	0.00	6,560,000.00
		P(a)	0.00	328.00	P(a)	0.00	6,560,000.00
		A		0.00	A		0.00
CRAS construídos e em funcionamento	CRAS	P	0.00	22.00	P	730,055.00	6,361,544.00
		P(a)	0.00	22.00	P(a)	730,055.00	6,361,544.00
		A		0.00	A		0.00
CREAS construídos e em funcionamento	CREAS	P	0.00	8.00	P	731,056.00	3,238,498.00
		P(a)	0.00	8.00	P(a)	731,056.00	3,238,498.00
		A		0.00	A		0.00
Componente III: Fortalecimento Institucional		Physical Progress			Financial Progress		
Outputs	Unit of Measure		2015	EOP		2015	EOP
Investigações e estudos realizados	Estudos	P	2.00	7.00	P	370,370.00	1,620,000.00
		P(a)	2.00	7.00	P(a)	370,370.00	1,620,000.00
		A		0.00	A		0.00
Participantes do Programa Capacitados	Participantes	P	2,460.00	12,300.00	P	100,000.00	2,113,000.00
		P(a)	2,460.00	12,300.00	P(a)	100,000.00	2,113,000.00
		A		0.00	A		0.00
Modulos do Sistema de informacoes Gerenciais desenhados e em funcionamento	Sistema	P	0.00	6.00	P	200,000.00	900,000.00
		P(a)	0.00	6.00	P(a)	200,000.00	900,000.00
		A		0.00	A		0.00
Componente IV: Administração do Projeto							

Other Cost		2015	Cost
Administração	P	\$500,000.00	\$4,000,000.00
	P(a)	\$500,000.00	\$4,000,000.00
	A		\$0.00
Contingencia	P	\$0.00	\$1,000,000.00
	P(a)	\$0.00	\$1,000,000.00
	A		\$0.00
Total Cost		2015	Total Cost
	P	\$15,343,981.00	\$100,000,000.00
	P(a)	\$15,343,981.00	\$94,591,681.00
	A	\$9,935,662.00	\$9,935,662.00

Changes to the Matrix

No information related to this operation.

Please note that the Overall Stage represents the stage of the operation at the time of this report’s publication, which might not necessarily match the stage of the operation during the PMR Cycle to which the report pertains.
