



Operation Number: **BR-L1252**
Year- PMR Cycle: **Segundo período enero-diciembre 2013**
Last Update: **5/30/2014**
PMR Validation Stage: **Validada por el Representante de País**

Chief of Operations validation date: **06/13/2014**
Division Chief validation date: **06/24/2014**
Country Representative validation date: **07/10/2014**

Inter-American Development Bank - IDB
Office of Strategic Planning and Development Effectiveness

Operation Profile

Basic Data

Operation name:	Prog. Nacional de Apoyo a la Gestión Adm. y Fiscal Municipios Brasileños-PNAFM	Loan Number:	2248/OC-BR
Executing Agency (EA):	SECRETARIA EXECUTIVA DO MINISTÉRIO DA FA ZENDA		
Team Leader:	Cartaxo,Maria de Fatima	Sector/Subsector:	FISCAL POLICY FOR SUSTAINABILITY AND GROWTH
Operation Type:	Loan Operation	Overall Stage:	Desembolso (De la elegibilidad hasta que todos los préstamos están cerrados).
Lending Instrument:	Investment Loan	Country:	BRAZIL
Borrower:	REPUBLICA FEDERATIVA DO BRASIL	Convergence related Operation(s):	

Total Cost and Source

	Original IDB	Current Active IDB	Local Counterpart	Co-Financing/Country	Total operation cost - Original Estimate
BR-L1252	\$150,000,000.00	\$150,000,000.00	\$16,600,000.00	\$0.00	\$166,600,000.00

Available Funds (US\$)

	Current IDB	Disb. Amount to Date	% Disbursed	Undisbursed Balance
BR-L1252	\$150,000,000.00	\$78,410,000.00	52.27%	\$71,590,000.00


Environmental and Social Safeguards

Main Operation	
Impacts Category:	C
Safeguard Performance Rating:	
Safeguard Performance Rating - Rationale:	

Reformulation Information

Main Operation	
Was/Were the objective(s) of this operation reformulated?	NO
Date of approval:	

Expense Categories by Loan Contract (cumulative values)

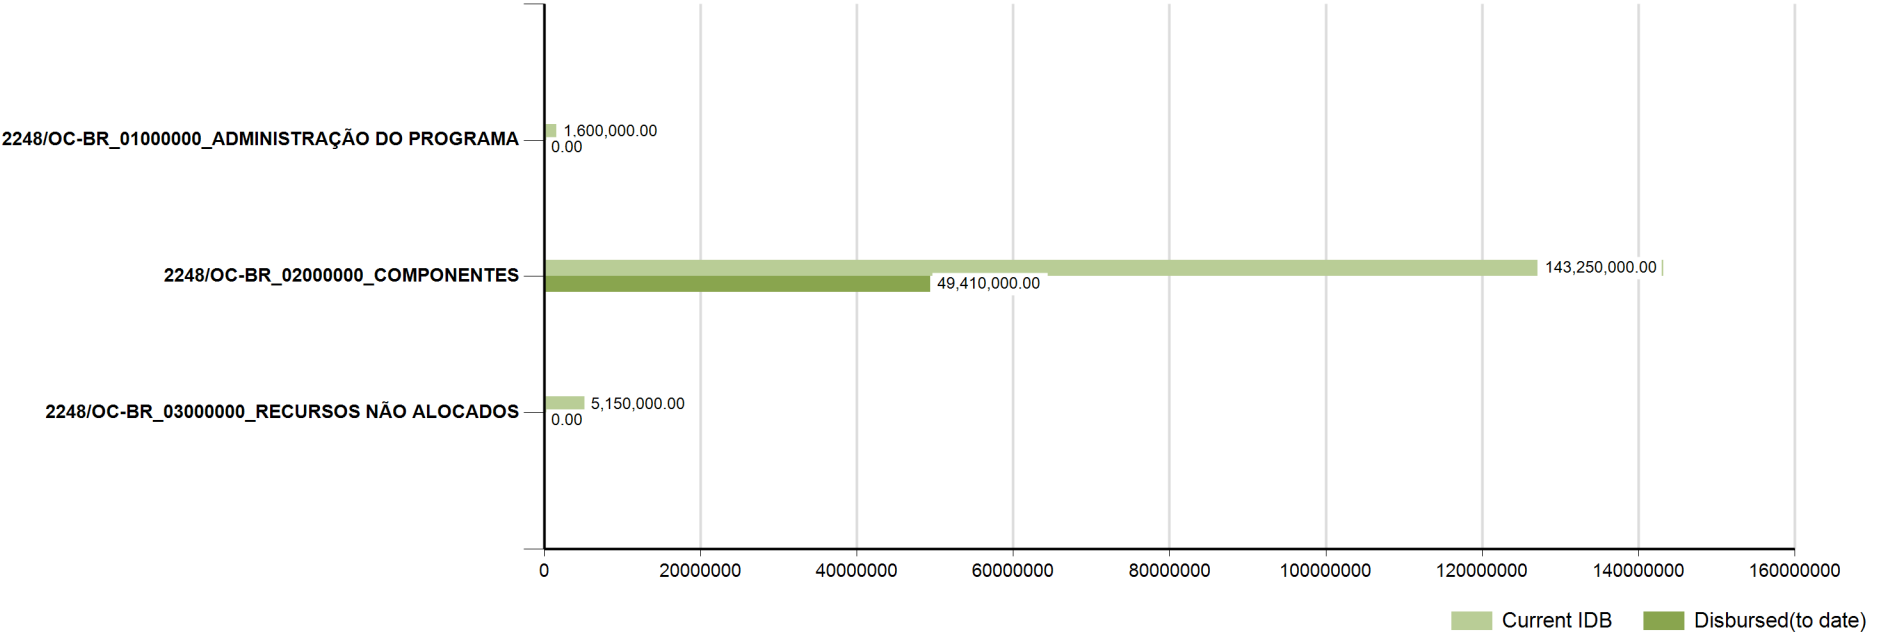

Observation:													
Indicators	Flags*	Unit of Measure	Baseline	Baseline Year	Means of verification	Observations	2010	2011	2012	2013	2014	2015	EOP
5.1 município com potencial de receita própria identificados.		município	0.00	2009	Relatório Semestral de Progresso		P						50.00
							P(a)						11.00
							A		5.00	18.00			
Outcome:	6 R6 - Linha de base para os 4 eixos estruturadores do Programa definida: atenção ao cidadão, administração tributária, gestão do cadastro de contribuintes e administração orçamentária e financeira es medida de manera independente por los municipios												
Observation:													
Indicators	Flags*	Unit of Measure	Baseline	Baseline Year	Means of verification	Observations	2010	2011	2012	2013	2014	2015	EOP
6.1 municípios participante do Programa com diagnóstico de linha de base dos eixos estruturadores realizado.		município	0.00	2009	Relatório Semestral de Progresso		P						50.00
							P(a)						11.00
							A	5.00	8.00	18.00			

Outputs: Annual Physical and Financial Progress

COMPONENTE I - COORDINACIÓN Y ASISTENCIA TÉCNICA NACIONAL		Physical Progress			Financial Progress		
Outputs	Unit of Measure		2013	EOP		2013	EOP
Projetos de fortalecimento institucional municipal apoiados em sua elaboração e revisão	projetos	P	10.00	78.00	P	6,111.97	276,559.86
		P(a)	7.00	149.00	P(a)	6,111.97	276,559.86
		A	22.00	135.00	A	6,111.97	55,223.94
Governo - Municípios apoiados para contratação de operações de crédito	Governments	P	1.00	12.00	P	2,424.63	195,123.17
		P(a)		49.00	P(a)		195,123.17
		A		49.00	A		33,424.63
Governo - Municípios apoiados na gestão dos respectivos projetos, envolvendo monitoramento e avaliação / Indicador: visitas técnicas de supervisão realizadas duranre a 2a fase do PNAFM	Governments	P		30.00	P	243,173.13	2,058,865.63
		P(a)	3.00	68.00	P(a)	143,173.13	2,058,896.50
		A	22.00	54.00	A	143,173.13	1,029,185.26
Banco de melhores práticas na área fiscal criado. / Indicador: eventos realizados para a difusão do Banco de Melhores práticas	eventos	P		1.00	P	189,780.00	1,138,930.00
		P(a)	1.00	18.00	P(a)	189,780.00	1,138,930.00
		A	4.00	9.00	A	189,780.00	508,128.00
Convênios e acordos de cooperação celebrados, tanto no âmbito nacional quanto no internacional	convênios	P		1.00	P	39,896.64	239,379.84
		P(a)		1.00	P(a)	39,896.64	279,276.56
		A			A	39,896.64	79,793.28
Conferência técnica e estudos, no âmbito nacional e internacional, realizados.	conferência	P		1.00	P	72,213.65	433,068.35
		P(a)		4.00	P(a)		433,068.00
		A	3.00	3.00	A		87,215.30
Plano de Comunicação interna e externa elaborado, incluindo mecanismos de transparência e comunicação com a sociedade.	plano	P		1.00	P	135,021.53	810,129.20
		P(a)		1.00	P(a)		810,129.89
		A			A		135,021.53
Piloto de Polo de modernização regional implantado.	Piloto	P		1.00	P	195,005.17	1,170,031.01
		P(a)		1.00	P(a)		1,170,031.51
		A			A		195,005.17
Curso de EAD implantados.	cursos	P		2.00	P	1,564,885.41	9,389,427.02
		P(a)	1.00	1.00	P(a)	1,564,880.41	9,389,307.64
		A	1.00	1.00	A	1,564,880.41	3,394,651.23
Reunião de avaliação das ações do Programa realizadas.	reuniões	P		1.00	P	125,219.64	888,677.84
		P(a)		16.00	P(a)		848,676.87
		A	3.00	7.00	A		200,439.28
COMPONENTE II - FORTALECIMIENTO INSTITUCIONAL MUNICIPAL		Physical Progress			Financial Progress		
Outputs	Unit of Measure		2013	EOP		2013	EOP
Projetos municipais implantados.	projetos	P	0.00	10.00	P	35,625,000.00	142,500,268.23
		P(a)	7.00	35.00	P(a)	2,625,000.00	142,500,000.00
		A	7.00	23.00	A	28,664,761.51	75,464,543.04
Outros							

Other Cost		2013	Cost
Administração do Programa.	P	\$266,670.00	\$1,333,330.00
	P(a)		\$1,600,000.00
	A		\$0.00
Imprevistos.	P		\$5,900,000.00
	P(a)		\$5,900,000.00
	A		\$0.00

Total Cost		2013	Total Cost
	P	\$38,465,401.77	\$166,333,790.15
	P(a)	\$4,568,842.15	\$131,097,824.99
	A	\$30,608,603.66	\$81,182,630.66

Changes to the Matrix

No information related to this operation.

Please note that the Overall Stage represents the stage of the operation at the time of this report’s publication, which might not necessarily match the stage of the operation during the PMR Cycle to which the report pertains.
