
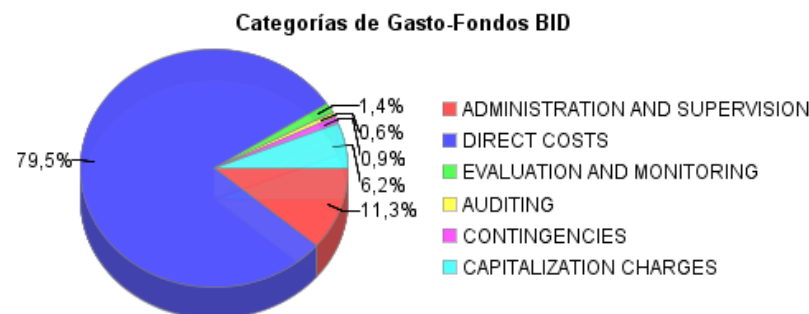
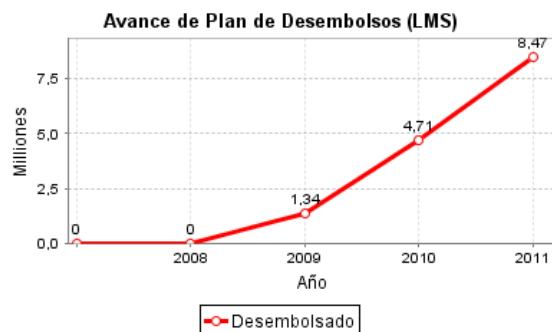



Informe Resumido

Datos Básicos del Proyecto		Fondos Disponibles (US\$)	Costo total y Fuente
Agencia Ejecutora (AE):	MINISTERIO DE AGRICULTURA		
Sector:	AGRICULTURE AND RURAL DEVELOPMENT-AGROBUSINESS		
Número(s) de Préstamo:	1929/BL-GY	Monto Aprobado Actual:	20.900.000,00
Etapas:	Approved	Monto Desembolsado a la fecha:	7.874.858,43
Tipo de Operación:	INV - Inversión	% Desembolsado:	37,68
Operación(es) Relacionada(s):		Saldo:	13.025.141,57
Subtipo de Operación:	ESP - Inversión Específica		
		BID Original:	20.900.000,00
		Actual BID:	20.900.000,00
		Pari-passu:	95,00
		Co-financiamiento/País:	1.019.000,00
		Estimado Original:	21.919.000,00
		Período de Amortización (meses):	288

Categoría de Impacto Ambiental y Social del Proyecto	Reformulación	Validación
Categoría de Impacto Ambiental y Social del Proyecto:	B () ¿El objetivo (s) del proyecto fue reformulado?	Validado por el Jefe de División: Sep 30, 2011 Validado por Representante de País: Oct 17, 2011

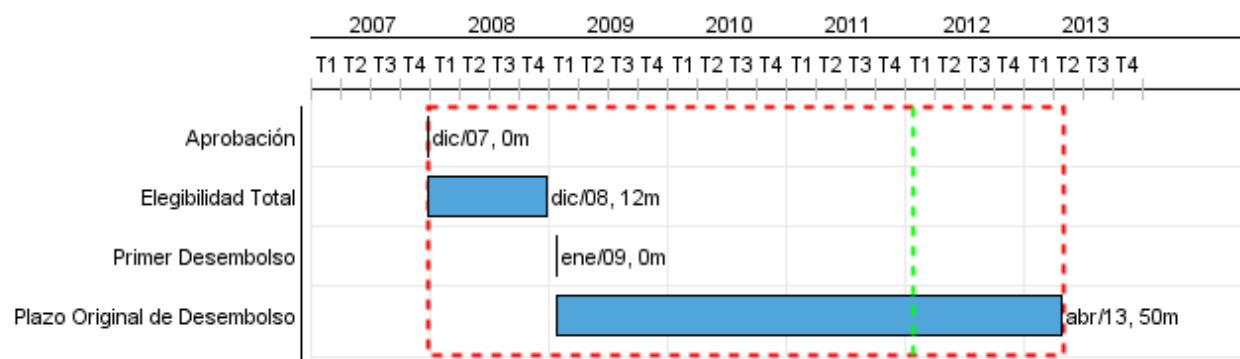

Progreso Acumulado al 2011

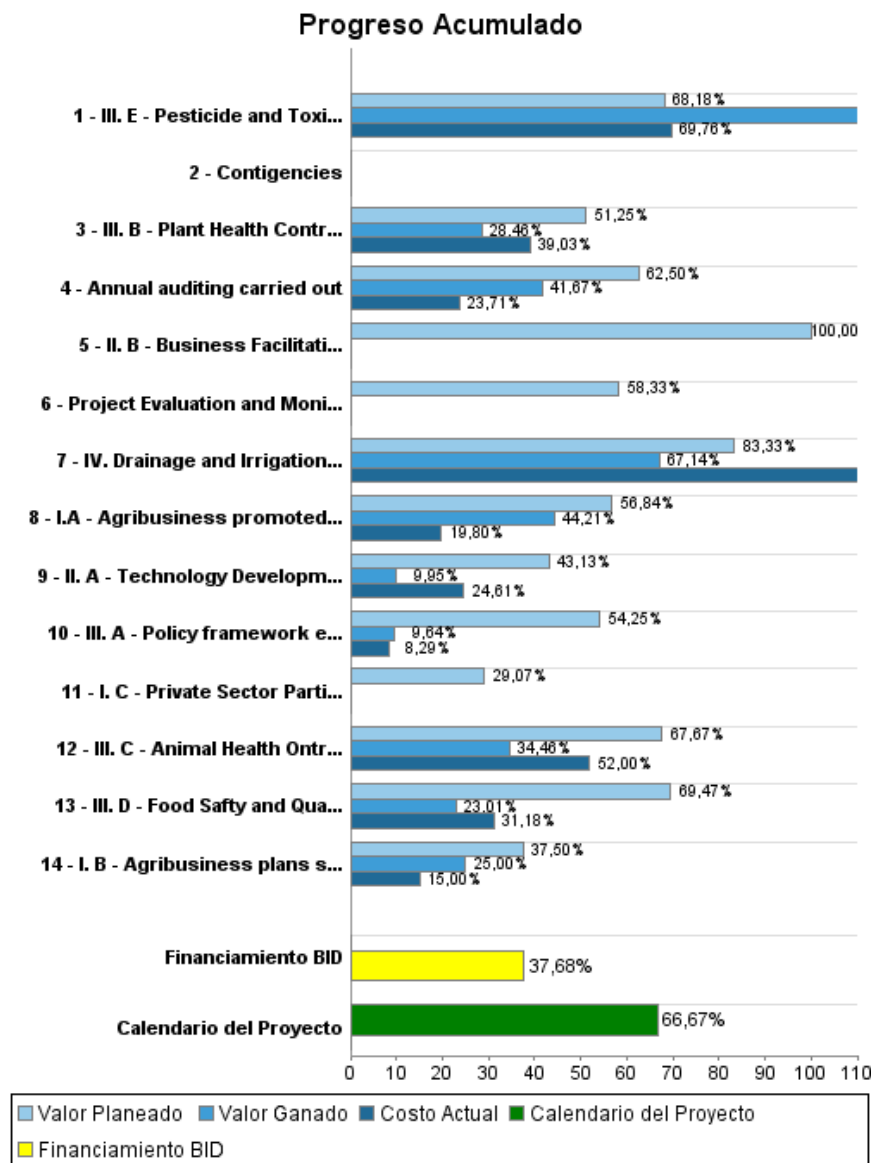

Resultados

Resultado:	Private Sector Entrepreneurship (PSE) into Agribusiness: Private initiative to increase exports of selected agro-chains fostered.
Supuestos:	1. Willingness to cooperate among cluster members; 2. Adequate overall business climate

Indicador	Unidad de Medida	Línea de base	Año Línea de base		2010	2011	Fin de Proyecto
Private Sector institutional arrangements for aquaculture, livestock, and fruit and vegetables clusters, consolidated.	unit		2007	P A			3,00

Resultado:	Agribusiness Export and Facilitation Services (AES): Public services needed to support the selected agrobusiness of productive chains strengthened.
Supuestos:	Infrastructure and logistic services are non-binding restrictions to increase exports.

Indicador	Unidad de Medida	Línea de base	Año Línea de base		2010	2011	Fin de Proyecto
National Agricultural Research Institut (NARI); National Dairy Development Programme (NDDP) and the Aquaculture Research Station at Mon Repos strenghtened.	services		2008	P A	2,00 1,00	1,00	3,00
Procedures and systems for facilitating access to land for agribusiness investores and stard incentive regime for the sub-sectors implemented	procedures for 3 subsectors		2008	P A	3,00 1,00		3,00
Shared-facilities related to non-traditional exports implemented and operated under private-sector participation schemes	abattoir		2008	P A			1,00
Samples for trial beef exports to higher-value markets ready	yes=1; no=0		2008	P A			1,00

Resultado:	Agricultural Health and Food Saefety Services (AHFSS): Effectiveness of animal health, plant health and food safety units of Ministry of Agriculture and Health improved.
Supuestos:	1. Willingness to reach agreements by third countries 2. No political issues on raising border control measures

Indicador	Unidad de Medida	Línea de base	Año Línea de base		2010	2011	Fin de Proyecto
Country kept free from fruit fly, pink mealy bugs and foot-and mouth disease - FMD	free=1; not free= 0	1,00	2008	P A	1,00 1,00		1,00
Autonomos agricultural health agencies established and providing health services for exporters (Agricultural Health and Food Services, AHFSS)	Agencies		2008	P A		1,00	2,00
Bovine Tuberculosis (BT) and Brucelosis eradicated (Region 1, 2 and 3)	free = 1; not free = 0		2008	P A			1,00
Public awareness on good sanitary practices (ratings increased from poor to fair)	fair=1; poor=0		2008	P A			1,00

Resultado:	D&I Sistem Canals Polder improved
-------------------	-----------------------------------

Indicador	Unidad de Medida	Línea de base	Año Línea de base		2010	2011	Fin de Proyecto
Drainage and Irrigation infrastructure of Canal Polder D&I area rehabilitated, including primarily & secondary drainage & irrigation channels and water contro structures rehabilitated.	sistem		2008	P A		1,00	1,00

Productos: Progreso Físico y Financiero Anual 2011

Descripción	Unidad de medida	Físico				Financiero			
		Planeado	Actual	Unidades Acumuladas	Unidades FDP	Planeado	Actual	Costos Acumulados	Costos FDP
I. Private Sector Entrepreneurship into Agribusiness (PSE)									
I.A - Agribusiness promoted and consolidated (PSE)	unit	7,00	3,00		20,00	725.000,00	314.000,00		2.947.000,00
I. B - Agribusiness plans supported / co-financed and implemented (PSE)	Empresas	4,00			28,00	250.000,00			2.000.000,00
I. C - Private Sector Participation in Agribusiness Facilities promoted (PSE)	heads / year	3.000,00			12.000,00	100.000,00			1.032.000,00
II. Agribusiness Export and Facilitation Services (AES)									
II. A - Technology Development and Transfer supported	unit	5,00	2,00		11,00	200.000,00	138.000,00		1.949.000,00
II. B - Business Facilitation System implemented and operating	Public Land Investment Opportunity Promotion System	1,00			1,00	242.000,00			592.000,00
III. Strengthening and consolidating of agricultural health and food safety services (AHFSS)									
III. A - Policy framework established and Coordination Mecanisms operating (AHFSS)	unit				9,00	60.000,00	16.000,00		212.000,00
III. B - Plant Health Control System established and operating (AHFSS)	unit	2,00	1,00		5,00	300.000,00	315.000,00		1.561.000,00
III. C - Animal Health Ontrol System established and operating (AHFSS)	unit	2,00	1,00		5,00	400.000,00	563.000,00		2.069.000,00
III. D - Food Safty and Quality Assurance System implemented (AHFSS)	unit	3,00	1,00		6,00	260.000,00	182.000,00		1.166.000,00
III. E - Pesticide and Toxic Chemincal Control Board implemented and operating (AHFSS)	unit	5,00	1,00		10,00	150.000,00	138.000,00		396.000,00
IV. Drainage and Irrigation Rehabilitation (DIR)									
IV. Drainage and Irrigation Sistem rehabilitated	Farmers	200,00	200,00		200,00	750.000,00	1.228.000,00		2.700.000,00
Evaluation and Monitoring									
Project Evaluation and Monitoring carried out	evaluation reports	1,00			2,00	75.000,00			300.000,00
Contingencies									
Contingencies	N/A								198.000,00
Financial Costs									
Auditing									
Annual auditing carried out	report	1,00			5,00	25.000,00	14.000,00		120.000,00
Project Administration and Supervision									

INFORME DE SEGUIMIENTO DE PROGRESO

GY-L1007 - Programa de Diversificación de las Exportaciones Agropecuarias
2011 1º período con cierre al (30-Set-2011)

Banco Interamericano de Desarrollo - BID

Oficina de Planificación Estratégica y Efectividad en el Desarrollo
Última Actualización del PMR: 29/09/2011

Descripción	Unidad de medida	Físico				Financiero			
		Planeado	Actual	Unidades Acumuladas	Unidades FDP	Planeado	Actual	Costos Acumulados	Costos FDP
TOTAL						3.537.000,00	2.908.000,00		17.242.000,00
