
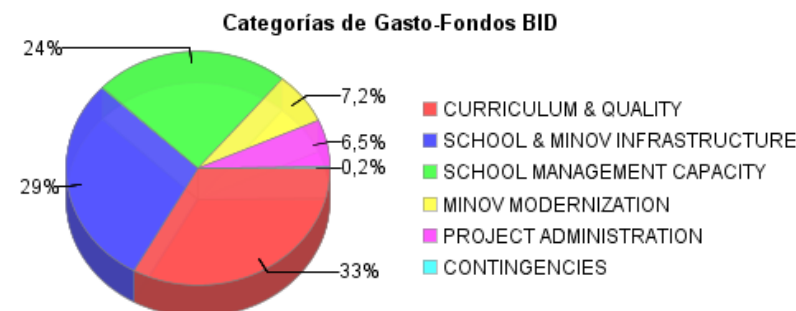
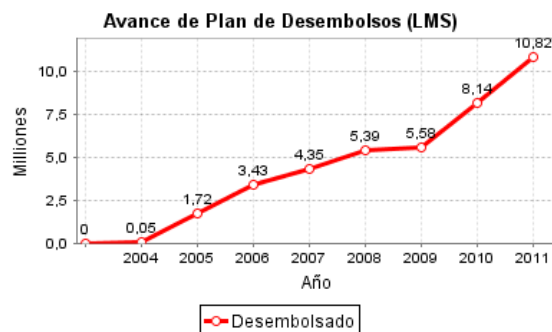



## Informe Resumido

Datos Básicos del Proyecto		Fondos Disponibles (US\$)	Costo total y Fuente
Agencia Ejecutora (AE):	MINISTRY OF EDUCATION SCIENCE AND CULTURE (MINOW)		
Sector:	EDUCATION-PRIMARY EDUCATION		
Número(s) de Préstamo:	1521/OC-SU	Monto Aprobado Actual:	12.500.000,00
Etapas:	Approved	Monto Desembolsado a la fecha:	10.362.329,07
Tipo de Operación:	INV - Inversión	% Desembolsado:	82,90
Operación(es) Relacionada(s):	TC9909010, SU-L1019	Saldo:	2.137.670,93
Subtipo de Operación:	ESP - Inversión Específica		
		BID Original:	12.500.000,00
		Actual BID:	12.500.000,00
		Pari-passu:	89,00
		Co-financiamiento/País:	1.000.000,00
		Estimado Original:	13.500.000,00
		Período de Amortización (meses):	234

Categoría de Impacto Ambiental y Social del Proyecto	Reformulación	Validación
Categoría de Impacto Ambiental y Social del Proyecto: B13(R)	( ) ¿El objetivo (s) del proyecto fue reformulado?	Validado por el Jefe de División: Sep 21, 2011 Validado por Representante de País: Sep 27, 2011

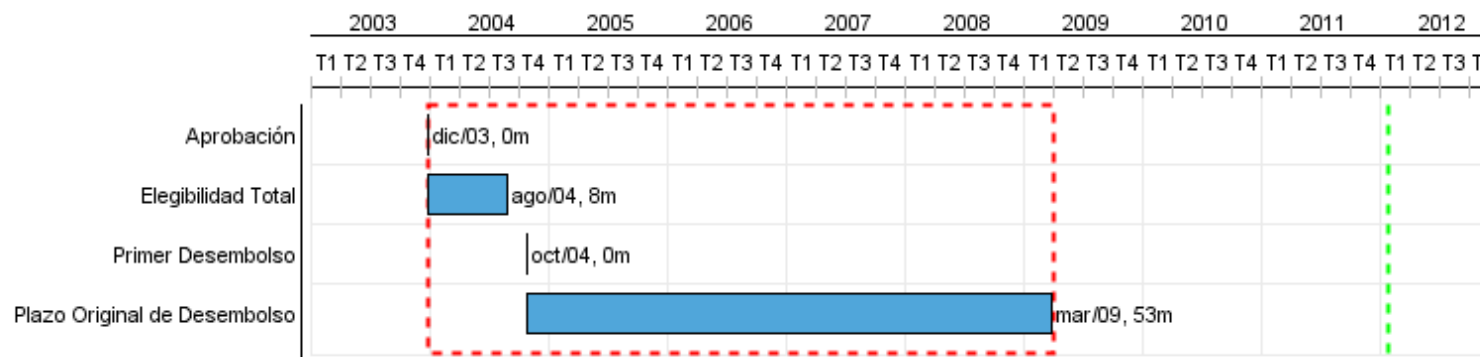

## Progreso Acumulado al 2011

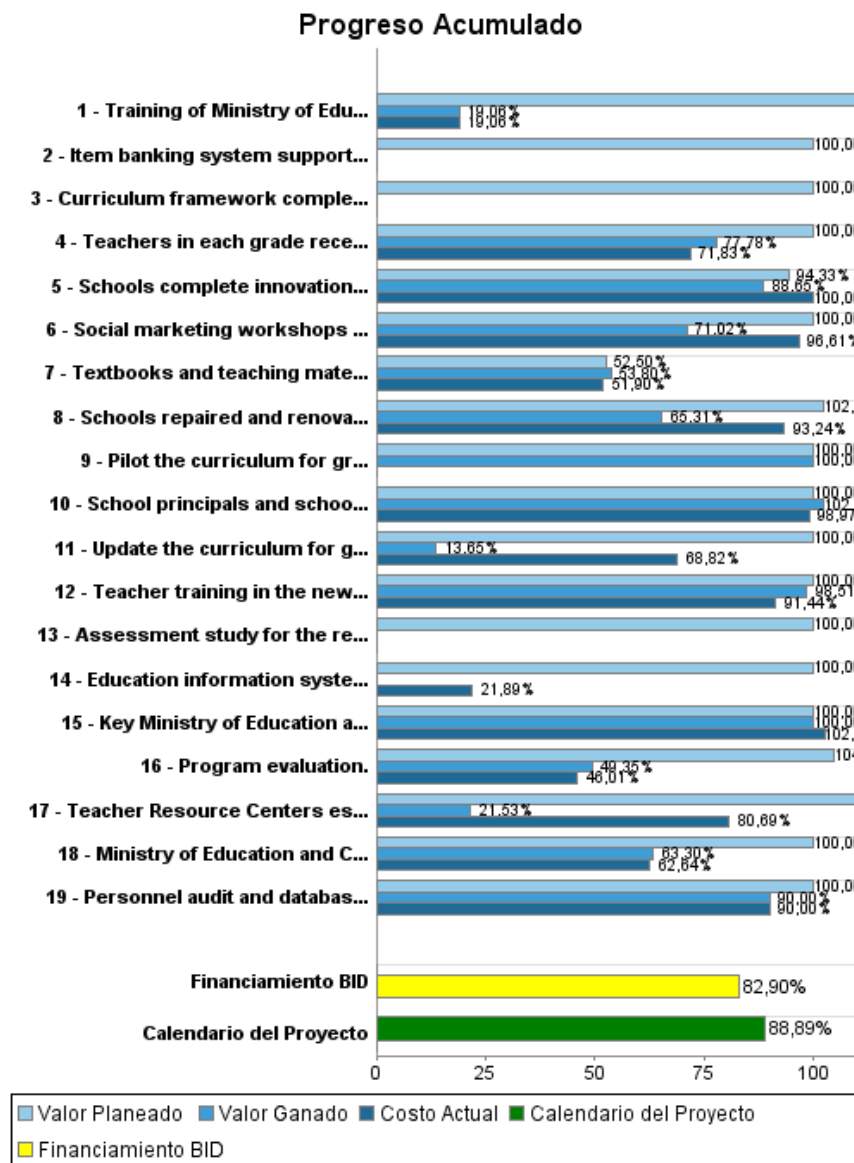

## Resultados

<b>Resultado:</b>	Contribute to the development of human capital in Suriname.
<b>Supuestos:</b>	Macroeconomic and fiscal stability.

Indicador	Unidad de Medida	Línea de base	Año Línea de base		2009	2010	2011	Fin de Proyecto
Coverage of basic education (grades 6-10)	percent	45,00	2003	P	50,00	50,00	50,00	50,00
				A	57,00	57,00		
School completion rate in 6th grade.	percent	50,00	2001	P	55,00	55,00	55,00	55,00
				A	53,00	53,00		
Students benefitted by education projects.	Students		2003	P			17.000,00	17.000,00
				A				

<b>Resultado:</b>	Improved quality and increased efficiency of the basic education system.
<b>Supuestos:</b>	Adequate financial resources allocated to the MOECD. Different donor agencies working on education in Suriname coordinate their activities.

Indicador	Unidad de Medida	Línea de base	Año Línea de base		2009	2010	2011	Fin de Proyecto
Coverage of basic education in grades 6 to 10.	percent	45,00	2003	P	50,00	50,00	50,00	50,00
				A	57,00	57,00		
Repetition rates in Grade 1.	percent	25,00	2003	P	17,50	17,50	17,50	18,00
				A		20,00		
Repetition rates in grade 2.	percent	20,00	2003	P	14,00	14,00	14,00	14,00
				A		16,00		
Repetition rates in grade 3.	percent	22,00	2003	P	15,40	15,40	15,40	15,00
				A		17,60		
Drop out rates in grade 1.	percent	7,00	2003	P	5,60	5,60	5,60	5,60
				A		3,22		
Drop out rates in grade 2.	percent	7,00	2003	P	5,60	5,60	5,60	5,60
				A		3,22		
Drop out rates in grade 3.	percent	8,00	2003	P	6,40	6,40	6,40	6,40
				A		3,68		

## Productos: Progreso Físico y Financiero Anual 2011

Descripción	Unidad de medida	Físico				Financiero			
		Planeado	Actual	Unidades Acumuladas	Unidades FDP	Planeado	Actual	Costos Acumulados	Costos FDP
<b>SUPPORT ESTABLISHMENT OF A REVISED BASIC EDUCATION CYCLE AND QUALITY IMPROVEMENT</b>									
Update the curriculum for grades 1 - 5.	grades	2,00			4,00	1.721.921,15	890.817,97		2.342.521,15
Teacher training in the new curriculum content and revised teaching materials completed.	Teachers	900,00	822,00		2.700,00				43.000,00
Assessment study for the revision of junior secondary completed.	study	1,00			1,00				15.000,00
Teachers in each grade receive teaching guides and learning materials consistent with the revised curriculum.	grades	2,00	2,00		2,00	525.000,00	484.832,64		675.000,00
Pilot the curriculum for grades 1 to 2.	grades				2,00				150.000,00
Curriculum framework completed.	framework	1,00	1,00		1,00				30.000,00
Textbooks and teaching materials delivered to schools.	teaching materials	80.000,00	106.000,00		90.000,00	58.000,00	58.000,00		1.320.000,00
Social marketing workshops completed.	workshops	2,00			35,00	25.000,00			152.700,00
Item banking system supporting assessment for the new curriculum developed.	System	1,00			1,00	150.000,00			150.000,00
<b>STRENGTHENING OF MANAGEMENT CAPACITIES AT SCHOOL LEVEL</b>									
Teacher Resource Centers established.	centers	10,00	4,00		10,00	740.000,00	407.826,77		1.375.000,00
Schools complete innovation fund projects.	projects	50,00	28,00		72,00	171.000,00	164.853,87		1.358.000,00
School principals and school leaders trained in school leadership and management.	principals/ school leaders				625,00				201.425,00
<b>RENOVATION AND UPGRADING OF SCHOOL AND MINOV INFRASTRUCTURE.</b>									
Schools repaired and renovated.	schools	8,00			55,00	240.000,00			3.557.000,00
Ministry of Education and Community Development departments renovated.	departments	1,00			4,00	40.000,00			117.500,00
<b>MODERNIZATION AND STRENGTHENING OF MOECD AND THE SCHOOL SYSTEM.</b>									
Personnel audit and database completed.	database								37.000,00
Key Ministry of Education and Community Development departments better equipped.	departments				4,00				115.000,00
Education information system network established.	network	1,00			1,00	200.000,00	43.772,35		200.000,00
Program evaluation.	evaluation	1,00			2,00	75.000,00			138.000,00
Training of Ministry of Education and Community Development personnel on the use of the information system completed.	Schools	30,00			30,00	75.000,00			105.000,00
<b>PROJECT FINANCE AND ADMINISTRATION</b>									

## INFORME DE SEGUIMIENTO DE PROGRESO

SU0023 - Mejoramiento de la Educación Básica.  
2011 1º período con cierre al (30-Set-2011)

Banco Interamericano de Desarrollo - BID

Oficina de Planificación Estratégica y Efectividad en el Desarrollo  
Última Actualización del PMR: 21/09/2011

Descripción	Unidad de medida	Físico				Financiero			
		Planeado	Actual	Unidades Acumuladas	Unidades FDP	Planeado	Actual	Costos Acumulados	Costos FDP
TOTAL						4.020.921,15	2.050.103,60		12.082.146,15
