

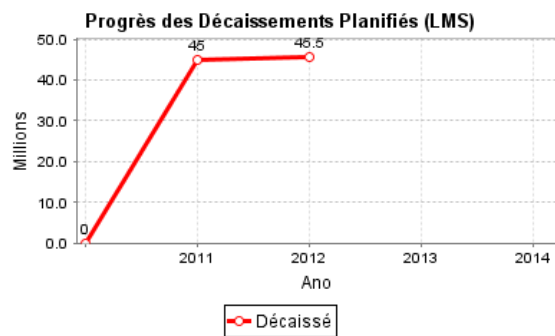



## Rapport Résumé

Données Générales		Fonds Disponibles (US\$)	Coût Total et Source de Financement
Agence d' Exécution (EA):	MINISTRY OF FINANCE AND THE ECONOMY		
Secteur:	SOCIAL INVESTMENT		
Numéro(s) de Prêt(s):	2599/OC-TT;2598/OC-TT	Montant Courant Approuvé:	50.000.000,00
Étape:	Approved	Montant Décaissé à ce Jour:	45.000.000,00
Type d' Opération:	HIB - Hybrid Operation	% Décaissé:	90,00
Opération(s) Connexe(s):	TT-T1010, RG-P1442	Solde:	5.000.000,00
Sous-Type de l'Opération:	HIB - Hybrid Operation		
		Initial BID:	50.000.000,00
		Courant BID:	50.000.000,00
		Pari Passu:	100,00
		Cofinancement/Pays:	
		Estimation Initiale:	50.000.000,00
		Période d'Amortissement (mois):	198

Catégorie d'Impact Environnemental et Social du Projet	Reformulation	Validation
Catégorie d'Impact Environnemental et Social du Projet: B13	( ) Les objectifs du projet ont-ils été reformulés?	Validé par le Chef de Division: 21-sep-2012 Validé par le Représentant: 28-sep-2012

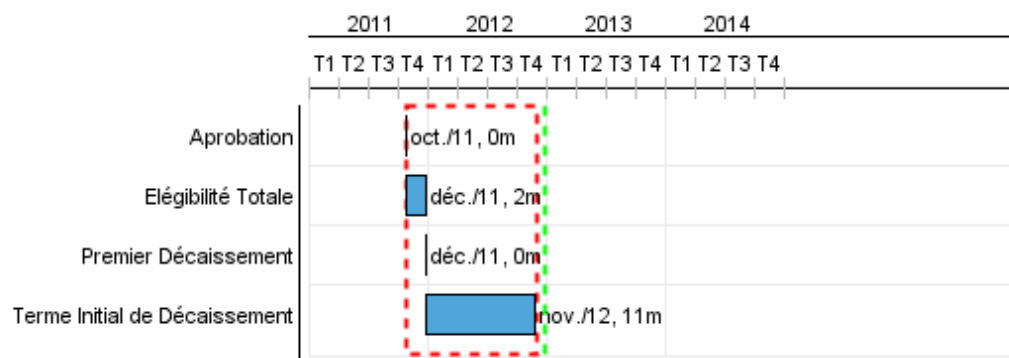

## Progrès Cumulé à 2012

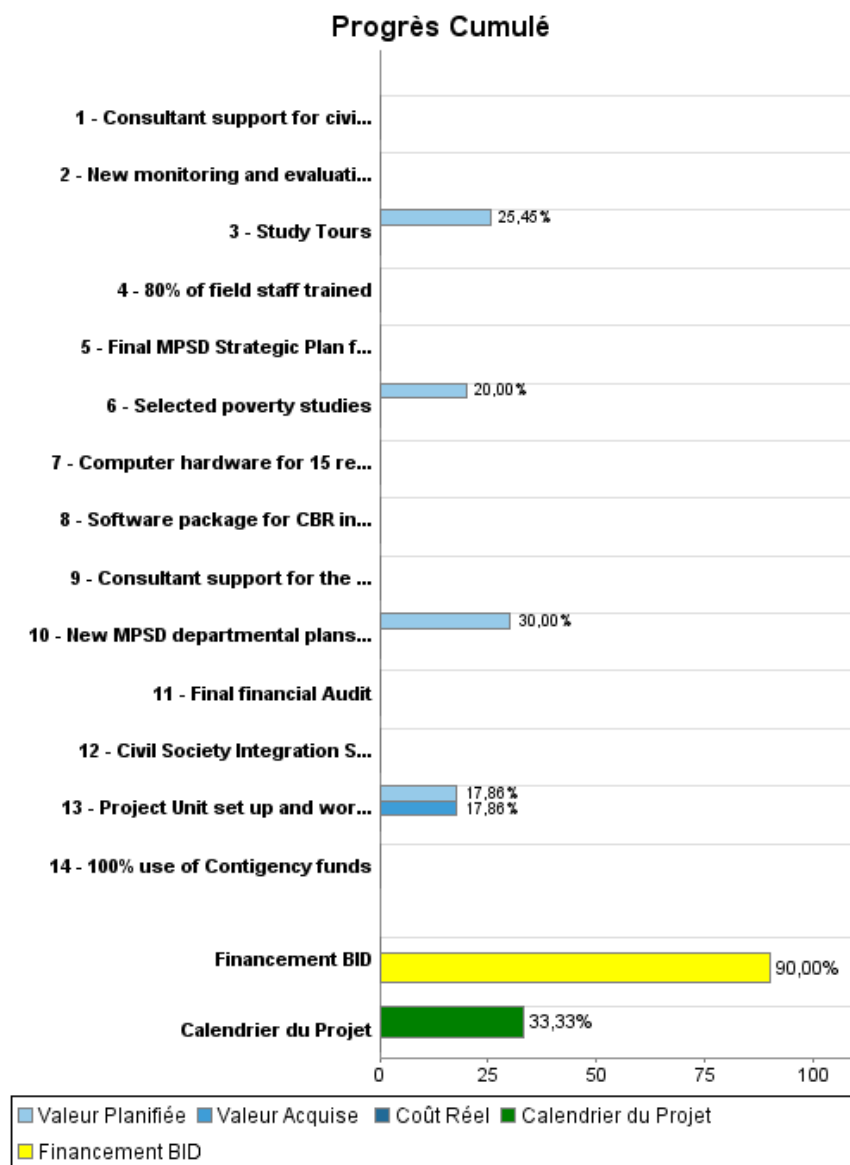

## Résultats

<b>Résultat:</b>	The MPSD strategic plan updated and detailed departmental operational plans developed and documented
<b>Suposições:</b>	The strategic plan and departmental operational plans would be guided by a change management consultant and be based on a common consensus achieved through a series of workshops.

Indicateur	Unité de Mesure	Ligne de Base	Année Ligne de Base		2012	2013	2014	Fin du Projet
A series of stakeholder workshops done to reach a common agreement on the strategic plan and departmental operational plans	number of workshops		2012	P A	2.00	2.00	1.00	5.00

<b>Résultat:</b>	Staff trained to support the consolidated cash transfer plan as outlined in the Policy Results Matrix of the PBL component
<b>Suposições:</b>	The consultant to undertake the training is hired in a timely manner and that all the required staff have been installed.

Indicateur	Unité de Mesure	Ligne de Base	Année Ligne de Base		2012	2013	2014	Fin du Projet
80% of the staff have been trained	%		2012	P A	10.00	20.00	50.00	80.00

<b>Résultat:</b>	Central beneficiary registry (CBR) implemented
<b>Suposições:</b>	The IT expansion plan and the conceptual design for the CBR are completed by the end of 2013

Indicateur	Unité de Mesure	Ligne de Base	Année Ligne de Base		2012	2013	2014	Fin du Projet
Central Beneficiary Registry contains 300 beneficiary names	number of beneficiaries		2012	P A		100.00	200.00	300.00

<b>Résultat:</b>	Monitoring and Evaluation Framework implemented
<b>Suposições:</b>	The M & E consultant is hired in a timely manner and that the M & E staff are in place at the MPSD

Indicateur	Unité de Mesure	Ligne de Base	Année Ligne de Base		2012	2013	2014	Fin du Projet
Stakeholder Workshops on the application of the new M & E Framework completed	number of workshops		2012	P A	1.00	1.00	1.00	3.00

<b>Résultat:</b>	Civil Society Integration Plan implemented
<b>Suposições:</b>	Consultant to develop integration plan hired by December 2012

Indicateur	Unité de Mesure	Ligne de Base	Année Ligne de Base		2012	2013	2014	Fin du Projet
Civil Society consultation workshops completed	number of		2012	P		5.00	5.00	10.00

## RAPPORT DE SUIVI

TT-L1014 - Social Safety Net Reform Program  
2012 1<sup>o</sup> período con cierre al (30-sept.-2012)

Banque Interaméricaine de Développement - BID

Bureau de la planification stratégique et de l'efficacité du développement  
Dernière Mise à Jour: 19/09/2012

	workshops			A				
--	-----------	--	--	---	--	--	--	--

**Produites: Progrès Physique et Financier Annuel 2012**

Description	Unité de Mesure	Physique				Financier			
		Planifié	Réel	Unités Cumulées	Unités FDP	Planifié	Réel	Coûts Cumulées	Coûts FDP
<b>Update and Finalization of MPSD Strategic Plan</b>									
Final MPSD Strategic Plan for the period 2011 to 2016	Number				1,00				300.000,00
New MPSD departmental plans in line with new strategic plan	Number				6,00	30.000,00			100.000,00
80% of field staff trained	%				80,00				1.000.000,00
<b>Set up of Central Beneficiary Registry</b>									
Computer hardware for 15 regional district offices and MPSD Head Office	Number of computers				20,00				1.000.000,00
Software package for CBR installed	Number of software packages				1,00				550.000,00
<b>New Monitoring and Evaluation Framework completed</b>									
New monitoring and evaluation framework implemented in 40% of SSN programs	%				40,00				300.000,00
<b>Civil Society Integration Strategy and Implementation Plan</b>									
Civil Society Integration Strategy and Implementation Plan implemented	Number of plans implemented				1,00				200.000,00
<b>Research Studies</b>									
Selected poverty studies	number of studies	2,00			6,00	100.000,00			500.000,00
Consultant support for civil society integration strategy	number of consultants				1,00				50.000,00
Consultant support for the Central Beneficiary Registry	number of consultants				1,00				50.000,00
Study Tours	number of study tours	2,00			6,00	140.000,00			550.000,00
<b>Project Administration</b>									
Project Unit set up and working	number of project unit	1,00	1,00		1,00	50.000,00			280.000,00
Final financial Audit	number of final audits				1,00				20.000,00
100% use of Contingency funds	%				100,00				100.000,00
<b>TOTAL</b>						<b>320.000,00</b>			<b>5.000.000,00</b>
