
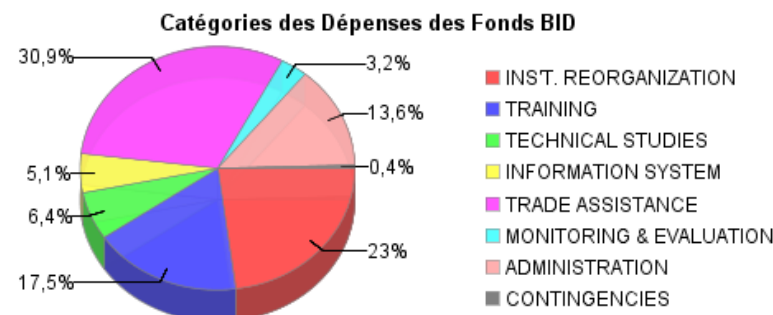
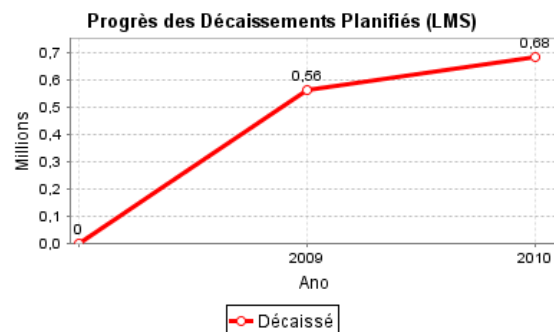



Rapport Résumé

Données Générales		Fonds Disponibles (US\$)		Coût Total et Source de Financement	
Agence d' Exécution (EA):	MINISTRY OF TRADE AND INDUSTRY				
Secteur:	REFORM / MODERNIZATION OF THE STATE-TRADE POLICIES				
Numéro(s) de Prêt(s):	1454/OC-TT	Montant Courant Approuvé:	5.000.000,00	Initial BID:	5.000.000,00
Étape:	Approved	Montant Décaissé à ce Jour:	2.755.501,10	Courant BID:	5.000.000,00
Type d' Opération:	INV - Investissement	% Décaissé:	55,11	Pari Passu:	63,16
Opération(s) Connexe(s):		Solde:	2.244.498,90	Cofinancement/Pays:	2.100.000,00
Sous-Type de l'Opération:	SEF - Sector Facility			Estimation Initiale:	7.100.000,00
				Période d'Amortissement (mois):	180

Catégorie d'Impact Environnemental et Social du Projet	Reformulation	Validation
Catégorie d'Impact Environnemental et Social du Projet:	B () Les objectifs du projet ont-ils été reformulés?	Validé par le Chef de Division: Apr 19, 2011 Validé par le Représentant: Apr 27, 2011

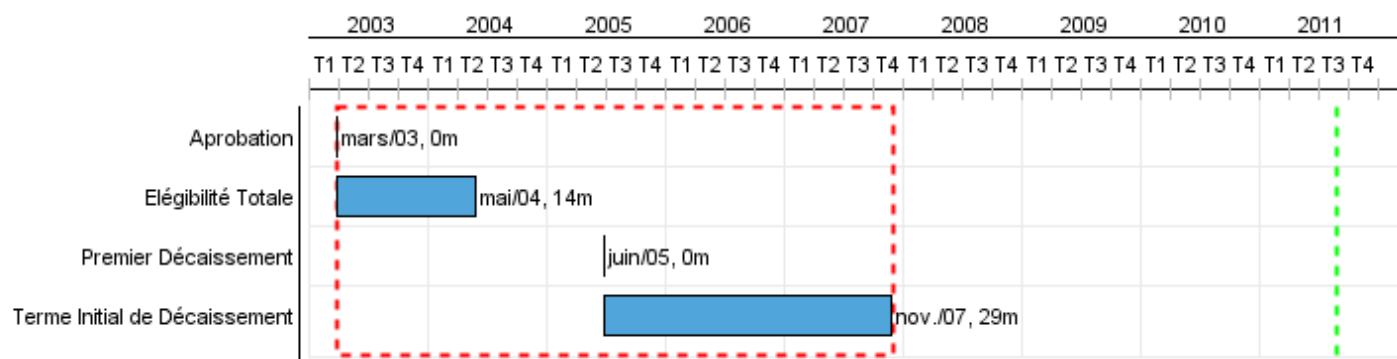

Progrès Cumulé à 2010

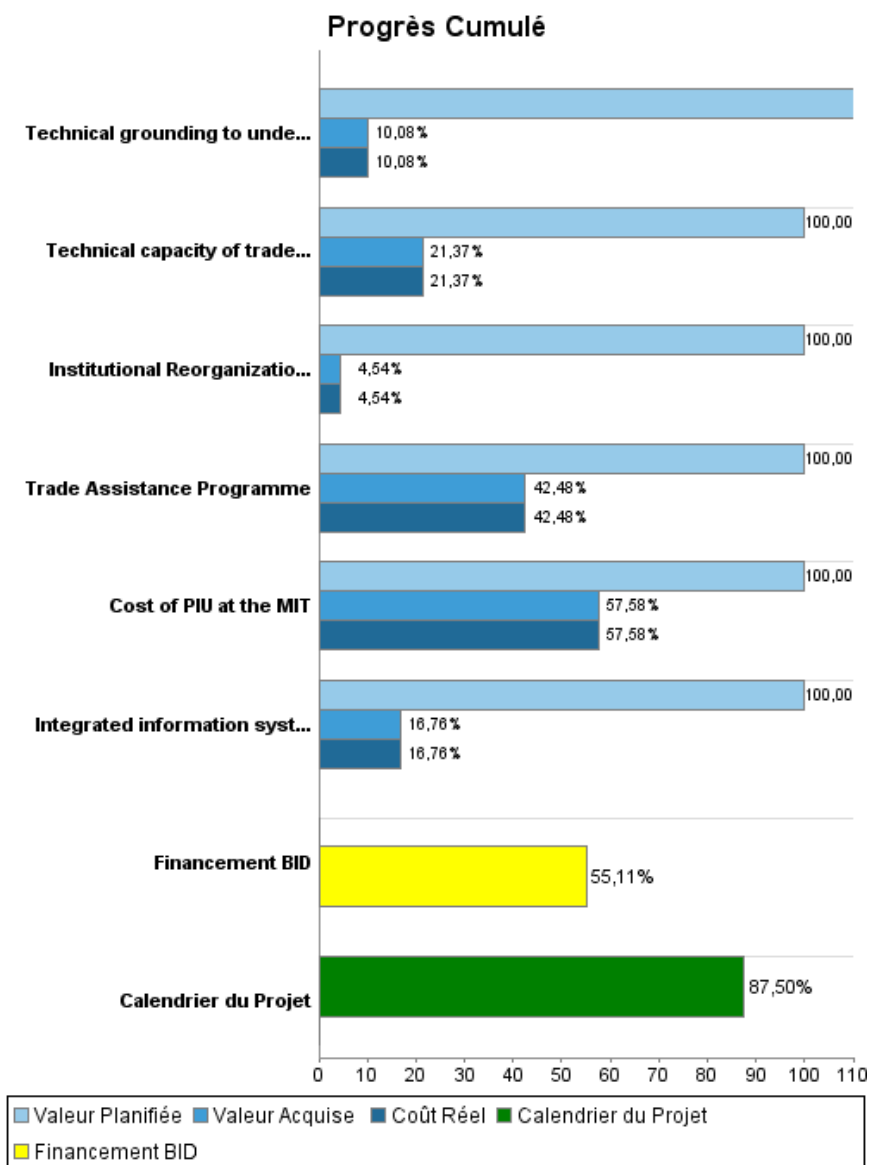

Résultats

Résultat: To strengthen the country's technical and institutional capacity to formulate trade policy and negotiate and implement trade agreements.

Indicateur	Unité de Mesure	Ligne de Base	Année Ligne de Base		2009	Fin du Projet
A reorganized Ministry that is adaptable, effective and productive	Re-structuring and Training Plan			P A	1,00	1,00
Trained personnel with competencies in trade disciplines to analyse and provide solution options for a range of policy issues	No of trained sr personnel in trade policy			P A	3,00 3,00	3,00
A Trinidad and Tobago trade policy document	Trade Policy Document			P A	1,00 1,00	1,00
Database of goods and services established	Database			P A	1,00	1,00
Updated Matrix of trade assistance activities for 2009/2010	Updated Matrix			P A	1,00 1,00	0,00
Mid Term Review completed	Final Mid Term Review Report			P A	1,00 1,00	0,00

Résultat: To strengthen the country's ability to attract Foreign Direct Investment

Indicateur	Unité de Mesure	Ligne de Base	Année Ligne de Base		2009	Fin du Projet
Consulting firm that will design and develop the new FDI system hired	1 Contract			P A		1,00

Produites: Progrès Physique et Financier Annuel 2010

Description	Unité de Mesure	Physique				Financier			
		Planifié	Réel	Unités Cumulées	Unités FDP	Planifié	Réel	Coûts Cumulées	Coûts FDP
Institutional Reorganization and Strengthening									
Institutional Reorganization and Strengthening						788.013,00			1.071.478,00
Technical capacity of trade related staff in public institutions is improved and strengthened									
Technical capacity of trade related staff in public institutions is improved and strengthened						436.050,00			554.160,00
Technical grounding to underpin trade policy on priority matters in place.									
Technical grounding to underpin trade policy on priority matters in place.						100.000,00			100.000,00
Integrated information system for the trade sector operational									
Integrated information system for the trade sector operational						545.000,00			738.071,00
Trade Assistance Programme									
Trade Assistance Programme						200.000,00			420.472,00
Administration									
Cost of PIU at the MIT	US\$					40.500,00			134.988,00
TOTAL						2.109.563,00			3.019.169,00
