



Operation Number: **PR0125**
Year- PMR Cycle: **First period Jan-Jun 2014**
Last Update: **10/27/2014**
PMR Validation Stage: **Validated by Representative**

Chief of Operations validation date: **11/02/2014**
Division Chief validation date: **11/02/2014**
Country Representative validation date: **11/03/2014**

Inter-American Development Bank - IDB
Office of Strategic Planning and Development Effectiveness

Operation Profile

Basic Data

Operation name:	Social Investment Program II	Loan Number:	1422/OC-PR,1422/OC-PR-CPS
Executing Agency (EA):	SECRETARIA DE ACCION SOCIAL ,SECRETARIA DE ACCION SOCIAL		
Team Leader:	Alvarado,Nohora Rocio	Sector/Subsector:	POVERTY ALLEVIATION
Operation Type:	Loan Operation	Overall Stage:	Closed (All the loans are closed).
Lending Instrument:	Investment Loan	Country:	PARAGUAY
Borrower:	REPUBLICA DE PARAGUAY ,REPUBLICA DE PARAGUAY		Convergence related Operation(s):

Total Cost and Source

	Original IDB	Current Active IDB	Local Counterpart	Co-Financing/Country	Total operation cost - Original Estimate
PR0125	\$28,400,000.00	\$22,326,456.37	\$4,600,000.00	\$0.00	\$33,000,000.00

Available Funds (US\$)

	Current IDB	Disb. Amount to Date	% Disbursed	Undisbursed Balance
PR0125	\$22,326,456.37	\$22,326,456.37	100.00%	\$0.00


Environmental and Social Safeguards

Main Operation	
Impacts Category:	B(R)
Safeguard Performance Rating:	
Safeguard Performance Rating - Rationale:	


Reformulation Information

Main Operation	
Was/Were the objective(s) of this operation reformulated?	NO
Date of approval:	

Expense Categories by Loan Contract (cumulative values)

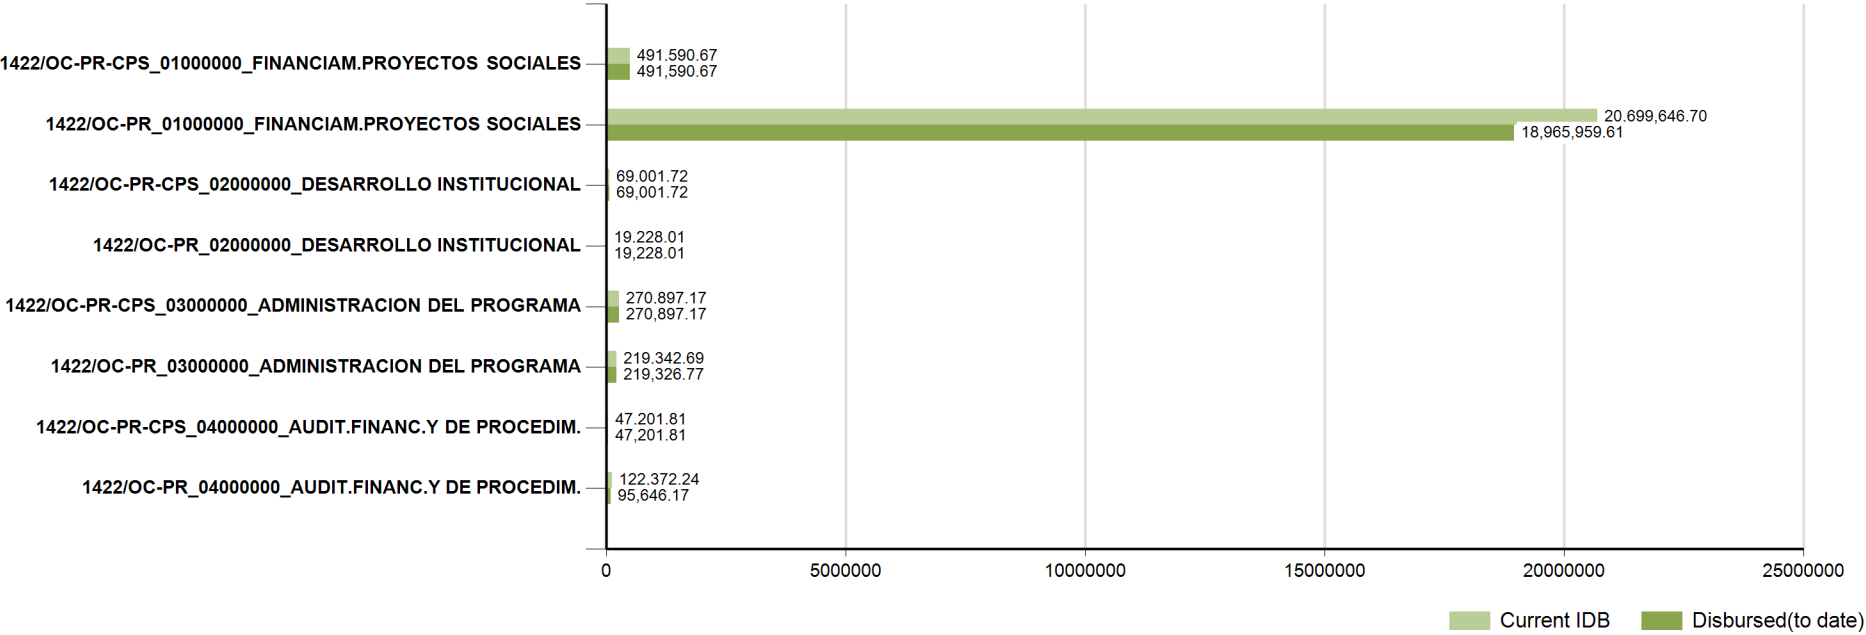

Expense Categories by Operation (cumulative values)

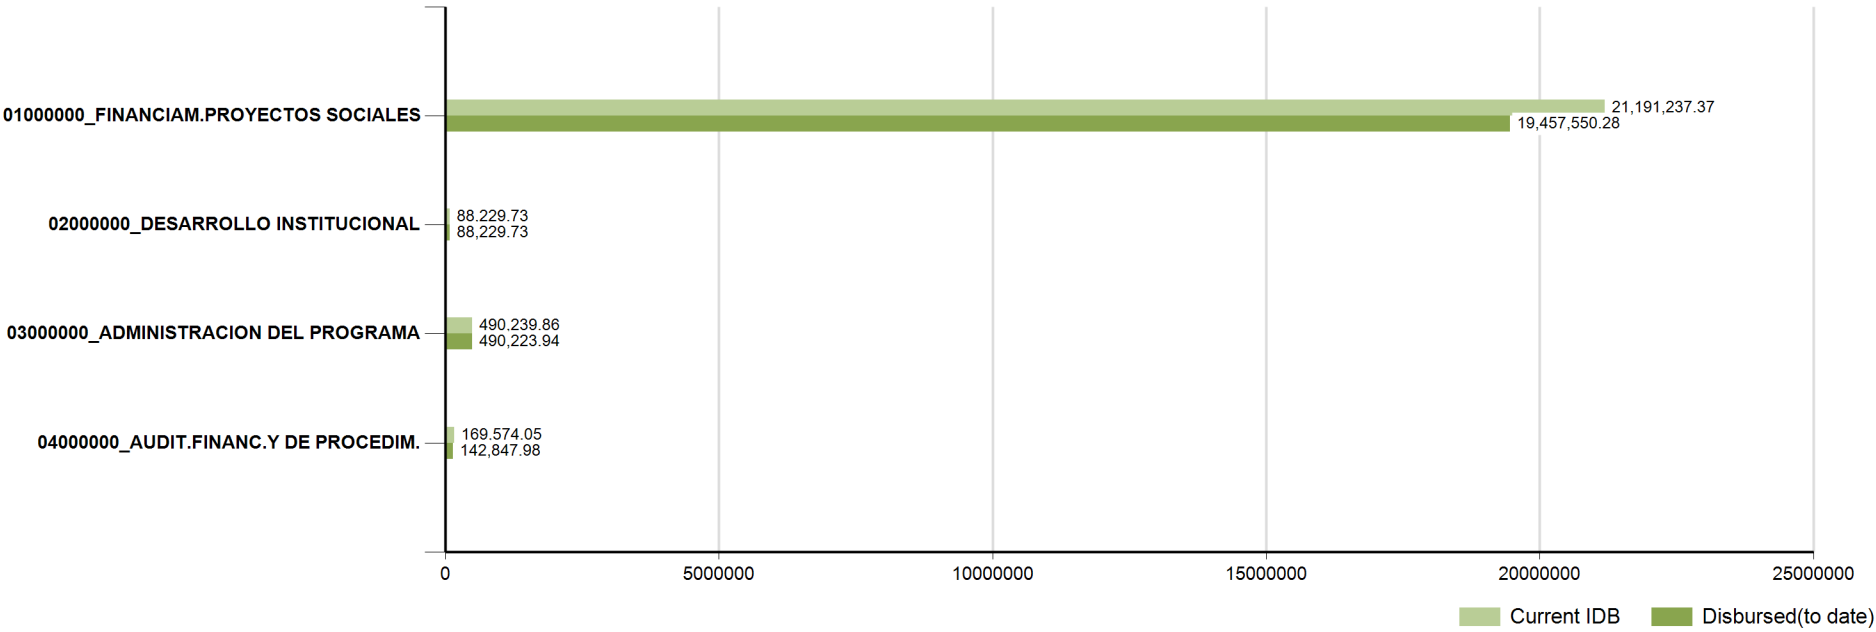

Results Matrix

Impacts

Impact:	1 Inversión social dirigida a sectores de la población en extrema pobreza y vulnerabilidad mejorada								
Observation:									
Indicators	Flags*	Unit of Measure	Baseline	Baseline Year	Means of verification	Observations	2009		EOP
1.1 Retención en el quinto grado de la educación escolar básica.		%	69.00	2005	Sistema Información de Estadística Continua (SIEC) del MEC	No se tiene información a nivel de los distritos beneficiarios, por lo que se tomarán los resultados del nivel nacional.	P	85.70	87.70
	P(a)						85.70	87.70	
	A								
1.2 Mortalidad infantil.		%	18.00	2005	ENDSSR 2008	Se incorpora un nuevo indicador de salud, para el que se tiene información. Se tenía previsto el indicador de desnutrición según peso y talla, pero ni el programa, ni el país cuenta con esta información, y la encuesta del Gabinete Social con UNICEF, pre	P		15.00
	P(a)							15.00	
	A						15.40		



Outcomes

Outcome:	1 Uso de servicios básicos de educación de la población de distritos intervenidos aumentado							
Observation:								
Indicators	Flags*	Unit of Measure	Baseline	Baseline Year	Means of verification	Observations	EOP	
1.1 Matrícula bruta de población entre 6 y 14 años		%	86.00	2006	Base de Datos PROPAIS y sistema de información del MEC.		P	96.00
	P(a)						96.00	
	A							
Outcome:	2 Uso de los servicios básicos de salud pública de menores de 5 años de beneficiarios del programa incrementado							
Observation:								

Indicators	Flags*	Unit of Measure	Baseline	Baseline Year	Means of verification	Observations	EOP	
2.1 Mujeres embarazadas con al menos 4 controles prenatales		%	70.00	2006	Información de PROPAIS y Departamento de Bioestadística del MSPyBS.	La norma del MSPyBS establece un mínimo de 4 controles prenatales, por lo que se cambió la meta de 6 controles prenatales.	P	90.00
							P(a)	90.00
							A	

 RF - RF Indicator

 SI - Sector Indicator

 CI - Country Indicator

 PG - Pro-Gender

 PE - Pro-Ethnicity

Outputs: Annual Physical and Financial Progress

1. Financiamiento de Proyectos Sociales (PS)		Physical Progress			Financial Progress		
Outputs	Unit of Measure	2014		EOP	2014		EOP
Transferencias monetarias condicionadas otorgadas.	Personas	P		242,719.00	P		8,336,747.40
		P(a)		242,719.00	P(a)	0.00	8,349,712.79
		A		242,719.00	A	0.00	8,349,712.79
Proyectos de Mejoramiento de Barrios ejecutados	proyectos	P		4.00	P		2,945,977.42
		P(a)	4.00	4.00	P(a)	226,858.00	2,323,741.83
		A	0.00	0.00	A	25,341.56	2,122,225.39
Proyectos Específicos (PE) ejecutados	proyectos	P		103.00	P		2,073,204.71
		P(a)	103.00	103.00	P(a)	654,372.00	3,089,000.51
		A		0.00	A	117,306.03	2,551,934.54
Preinversion	consultorias	P		20.00	P		227,153.00
		P(a)		20.00	P(a)	0.00	258,980.12
		A		20.00	A	0.00	258,980.12
Planes Integrales de desarrollo ejecutados	proyectos	P		34.00	P		4,000,000.00
		P(a)	34.00	34.00	P(a)	1,592,733.00	6,420,574.02
		A		0.00	A	52,259.29	4,880,100.31
2. Desarrollo Institucional		Physical Progress			Financial Progress		
Outputs	Unit of Measure	2014		EOP	2014		EOP
Documentos de análisis en apoyo a Políticas Sociales elaborados	Documentos	P		2.00	P		26,754.00
		P(a)		2.00	P(a)	0.00	26,754.00
		A		2.00	A	0.00	26,754.00
Eventos de fortalecimiento y Capacitación Profesional realizados	Eventos	P		2.00	P		103,705.74
		P(a)		2.00	P(a)	0.00	103,705.74
		A		2.00	A	0.00	103,705.74
3. Administración del Programa		Physical Progress			Financial Progress		
Outputs	Unit of Measure	2014		EOP	2014		EOP
Sistema de Información, Formulación, Evaluación y Monitoreo de Proyectos (SIFEM) de la SAS instalado, socializado y funcionando	Sistema	P		0.00	P		0.00
		P(a)	0.00	0.00	P(a)	0.00	0.00
		A		0.00	A	0.00	0.00
Consultorías de apoyo a la SAS ejecutadas	Consultorias	P		7.00	P		401,633.00
		P(a)	0.00	6.00	P(a)	0.00	362,009.44
		A		6.00	A	0.00	362,009.44
Equipo y vehículos adquiridos	vehiculos	P		1.01	P		25,285.01
		P(a)	0.00	1.01	P(a)	0.00	25,285.01
		A		1.01	A	0.00	25,285.01
Evaluación de Medio Término y Final	estudios	P		1.00	P		150,000.00
		P(a)		0.00	P(a)	0.00	0.00
		A		0.00	A	0.00	0.00
4. Auditorías externas y de procedimientos y otros		Physical Progress			Financial Progress		
Outputs	Unit of Measure	2014		EOP	2014		EOP
Auditoria	Informe	P		4.00	P		266,409.08
		P(a)	1.00	5.00	P(a)	33,272.73	259,432.03
		A		4.00	A	0.00	226,159.30

Other Cost		2014	Cost
Otras actividades de Administracion	P		\$598,088.28
	P(a)		\$598,088.28
	A	\$0.00	\$598,088.28
Otros costos del Programa	P		\$387,180.00
	P(a)		\$387,180.00
	A	\$0.00	\$387,180.00
Costos Financieros	P		\$758,136.00
	P(a)		\$758,136.00
	A	\$0.00	\$758,136.00
Total Cost		2014	Total Cost
	P		\$20,300,273.64
	P(a)	\$2,507,235.73	\$22,962,599.77
	A	\$194,906.88	\$20,650,270.92

Changes to the Matrix

No information related to this operation.

Please note that the Overall Stage represents the stage of the operation at the time of this report's publication, which might not necessarily match the stage of the operation during the PMR Cycle to which the report pertains.
