

PMR Operational Report

Operation Number	SU-L1020	Chief of Operations Validation Date	04/19/18
Year- PMR Cycle	Second period Jan-Dec 2017	Division Chief Validation Date	04/19/18
Last Update	04/19/18	Country Representative Validation Date	04/19/18
PMR Validation Stage	Validated by Representative		

Basic Data

Operation Profile

Operation Name	Agricultural Competitiveness Program	Loan Number	4097/OC-SU
Executing Agency	MINISTRY OF AGRICULTURE HUSBANDRY, FISHERIES AND FORESTRY	Sector/Subsector	AG-SAN - AGRICULTURE AND RURAL DEVELOPMENT-AGRICULTURAL HEALTH AND FOOD SAFETY
Team Leader	COLLINS, MICHAEL I.	Overall Stage	Disbursing (From eligibility until all the Operations are closed)
Operation Type	Loan Operation	Country	SURINAME
Lending Instrument	Investment Loan	Convergence related Operation(s)	
Borrower	REPUBLIC OF SURINAME		


Environmental and Social Safeguards

Impacts Category	B	Was/Were the objective(s) of this operation reformulated?	NO
Safeguard Performance Rating		Date of approval	
Safeguard Performance Rating - Rationale			

Financial Data

Item	Total Cost and Source					Available Funds (US\$)			
	Original IDB	Current IDB	Local Counterpart	Co-Financing / Country	Total Original Cost	Current IDB	Disb. Amount to Date	% Disb	Undisbursed Amount
SU-L1020	17,500,000	17,500,000	0	0	17,500,000	17,500,000	150,000	0.86%	17,350,000
Aggregated	17,500,000	17,500,000	0	0	17,500,000	17,500,000	150,000	0.86%	17,350,000

Expense Categories by Loan Contract (cumulative values)

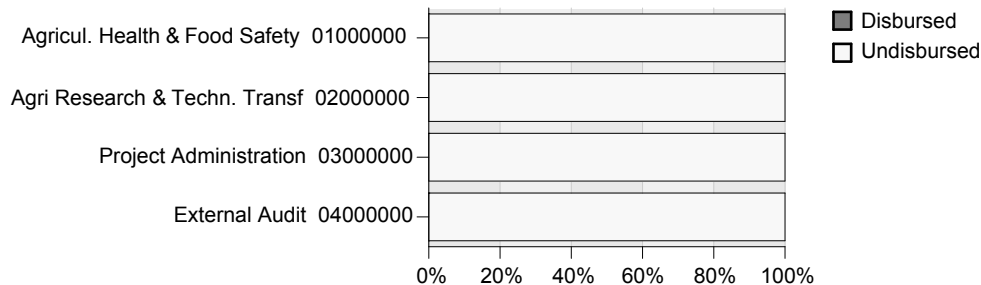

Please note that the Overall Stage represents the stage of the operation at the time of this report's publication, which might not necessarily match the stage of the operation during the PMR Cycle to which the report pertains. Please also note that inactive indicators and outputs are not displayed; totals in the actual cost table may not match the sum of the cost of the outputs displayed, due to the cost of inactive outputs.

PMR Operational Report

RESULTS MATRIX

IMPACTS

Impact Nbr. 0: Increase in agricultural revenue

Observation: The baseline corresponds to a representative group of open field vegetables that will be targeted by the program. The baseline will be re-estimated when the impact evaluation's baseline data is collected using farmers' surveys. The target refers to program beneficiaries.

Indicator		Unit of Measure	Baseline	Baseline Year		2022	EOP 2022
0.0	Value of production per hectare of open field vegetables	SRD	69,336.00	2014	P	77,906.00	77,906.00
					P(a)	77,906.00	77,906.00
					A		
Details							
Means of verification: Impact evaluation and LVV reports.							
Pro-Gender		No	Pro-Ethnicity		No		

PMR Operational Report

RESULTS MATRIX

IMPACTS

Impact Nbr. 1: Increase in agricultural productivity

Observation:

Indicator		Unit of Measure	Baseline	Baseline Year		2022	EOP 2022
1.0	Yields of long yard bean	tons/ha	14.00	2014	P	16.10	16.10
					P(a)	16.10	16.10
					A		

Details

Means of verification: Impact evaluation and LVV reports.

Pro-Gender No **Pro-Ethnicity** No

Indicator		Unit of Measure	Baseline	Baseline Year		2022	EOP 2022
1.1	Yields of oranges	Tons/ha	13.20	2014	P	15.20	15.20
					P(a)	15.20	15.20
					A		

Details

Means of verification: Impact evaluation and LVV reports.

Pro-Gender No **Pro-Ethnicity** No

Indicator		Unit of Measure	Baseline	Baseline Year		2022	EOP 2022
1.2	Yields of passionfruit	Tons/ha	15.40	2014	P	17.70	17.70
					P(a)	17.70	17.70
					A		

Details

Means of verification: Impact evaluation and LVV reports.

Pro-Gender No **Pro-Ethnicity** No

Indicator		Unit of Measure	Baseline	Baseline Year		2022	EOP 2022
1.3	Yields of rice	Tons/ha	4.40	2014	P	4.60	4.60
					P(a)	4.60	4.60
					A		

PMR Operational Report

RESULTS MATRIX

IMPACTS

Details							
Means of verification: Impact evaluation and LVV reports.							
Pro-Gender		No	Pro-Ethnicity		No		
Indicator		Unit of Measure	Baseline	Baseline Year		2022	EOP 2022
1.4	Average weight of slaughtered pigs	Kgs	71.50	2014	P	78.70	78.70
					P(a)	78.70	78.70
					A		
Details							
Means of verification: Impact evaluation and LVV reports.							
Pro-Gender		No	Pro-Ethnicity		No		

PMR Operational Report

RESULTS MATRIX

IMPACTS

Impact Nbr. 2: Increase in agricultural exports

Observation:

Indicator		Unit of Measure	Baseline	Baseline Year		2022	EOP 2022
2.0	Quantity of rice exports	Tons	103,755.00	2014	P	114,131.00	114,131.00
					P(a)	114,131.00	114,131.00
					A		

Details

Means of verification: LVV reports (Agricultural Statistics).

Pro-Gender No **Pro-Ethnicity** No

Indicator		Unit of Measure	Baseline	Baseline Year		2022	EOP 2022
2.1	Quantity of banana exports	Tons	75,261.00	2014	P	82,787.00	82,787.00
					P(a)	82,787.00	82,787.00
					A		

Details

Means of verification: LVV reports (Agricultural Statistics).

Pro-Gender No **Pro-Ethnicity** No

Indicator		Unit of Measure	Baseline	Baseline Year		2022	EOP 2022
2.2	Quantity of vegetable exports	Tons	4,746.00	2014	P	5,221.00	5,221.00
					P(a)	5,221.00	5,221.00
					A		

Details

Means of verification: LVV reports (Agricultural Statistics).

Pro-Gender No **Pro-Ethnicity** No

PMR Operational Report

RESULTS MATRIX

IMPACTS

Impact Nbr. 3: Increase in competitiveness

Observation: Baseline reflects the average position Suriname obtained in the ranking, out of 178 countries. Baseline is average of 2011-2015

Indicator		Unit of Measure	Baseline	Baseline Year		2022	EOP 2022
3.0	Position in the International Trade Centre's General Index Ranking of Export Performance in fresh food	Rank	98.00	2013	P	65.00	65.00
					P(a)	65.00	65.00
					A		
Details							
Means of verification: Report of International Trade Centre							
Pro-Gender		No	Pro-Ethnicity		No		

PMR Operational Report

RESULTS MATRIX

OUTCOMES

Outcome Nbr. 0: Improved use of natural capital

Observation:

Indicator		Unit of Measure	Baseline	Baseline Year		2022	EOP 2022
0.0	Number of beneficiaries of improved management and sustainable use of natural capital	Beneficiaries (#)	0.00	2016	P	15,370.00	15,370.00
					P(a)	15,370.00	15,370.00
					A		
Details							
Means of verification: Records of beneficiaries of LVV services. Ex post evaluation.							
Pro-Gender		No	Pro-Ethnicity		No		
	Women				P	3,074.00	3,074.00
					P(a)	3,074.00	3,074.00
					A		
	Men				P	12,296.00	12,296.00
					P(a)	12,296.00	12,296.00
					A		

Outcome Nbr. 1: Increase in export ability

Observation:

Indicator		Unit of Measure	Baseline	Baseline Year		2022	EOP 2022
1.0	Number of exporting firms.	Firms	9.00	2016	P	15.00	15.00
					P(a)	15.00	15.00
					A		
Details							
Means of verification: LVV data.							
Pro-Gender		No	Pro-Ethnicity		No		

Outcome Nbr. 2: Improved provision of plant health services

Observation:

Indicator		Unit of Measure	Baseline	Baseline Year		2022	EOP 2022
2.0	Percentage of annual notifications of exported crops due to noncompliance with plant health requirements	%	7.00	2014	P	3.50	3.50
					P(a)	3.50	3.50

PMR Operational Report

RESULTS MATRIX

OUTCOMES

2.0	Percentage of annual notifications of exported crops due to noncompliance with plant health requirements	%	7.00	2014	A		
Details							
Means of verification: Europhyt database and data provided by the Netherlands Food and Consumer Product Safety Authority (NVWA).							
Pro-Gender		No			Pro-Ethnicity		No
Indicator		Unit of Measure	Baseline	Baseline Year		2022	EOP 2022
2.1	Average score PVS (Performance Vision and Strategy) developed by IICA	%	28.60	2013	P	43.20	43.20
					P(a)	43.20	43.20
					A		
Details							
Means of verification: IICA independent evaluation							
Pro-Gender		No			Pro-Ethnicity		No
Indicator		Unit of Measure	Baseline	Baseline Year		2022	EOP 2022
2.2	Achievement of Area of Low Pest Prevalence (ALPP) of Carambola Fruit Fly in orange producing area	ALPP	0.00	2016	P	1.00	1.00
					P(a)	1.00	1.00
					A		
Details							
Means of verification: LVV Fruit Fly report.							
Pro-Gender		No			Pro-Ethnicity		No
Indicator		Unit of Measure	Baseline	Baseline Year		2022	EOP 2022
2.3	Masters of Science (MSc) degrees obtained by Plant Health Services employees	degrees	0.00	2016	P	6.00	6.00
					P(a)	6.00	6.00
					A		
Details							
Means of verification: MSc Diplomas							
Pro-Gender		No			Pro-Ethnicity		No
	Women					P	2.00
						P(a)	2.00

PMR Operational Report

RESULTS MATRIX

OUTCOMES

	Women				A		
	Men				P	4.00	4.00
					P(a)	4.00	4.00
					A		

Outcome Nbr. 3: Improved provision of animal health services

Observation:

Indicator		Unit of Measure	Baseline	Baseline Year		2022	EOP 2022
3.0	Average score PVS developed by OIE	Score	1.72	2012	P	2.75	2.75
					P(a)	2.75	2.75
					A		

Details

Means of verification: OIE PVS evaluation.

Pro-Gender	No	Pro-Ethnicity	No
-------------------	----	----------------------	----

Indicator		Unit of Measure	Baseline	Baseline Year		2022	EOP 2022
3.1	OIE Disease Free Status recognition for 3 diseases achieved	Recognitions	0.00	2016	P	3.00	3.00
					P(a)	3.00	3.00
					A		

Details

Means of verification: OIE Certificate

Pro-Gender	No	Pro-Ethnicity	No
-------------------	----	----------------------	----

Indicator		Unit of Measure	Baseline	Baseline Year		2022	EOP 2022
3.2	Self-Declaration to OIE of Disease Free for Tuberculosis and Brucellosis	Self declarations	0.00	2016	P	2.00	2.00
					P(a)	2.00	2.00
					A		

Details

Means of verification: OIE website

Pro-Gender	No	Pro-Ethnicity	No
-------------------	----	----------------------	----

Indicator		Unit of Measure	Baseline	Baseline Year		2022	EOP 2022
-----------	--	-----------------	----------	---------------	--	------	----------

PMR Operational Report

RESULTS MATRIX

OUTCOMES

3.3	Accreditation of the Animal Health Laboratory (ISO 17025)	lab	0.00	2016	P	1.00	1.00
					P(a)	1.00	1.00
					A		

Details

Means of verification: ISO Accreditation certificate

Pro-Gender	No	Pro-Ethnicity	No
-------------------	----	----------------------	----

Indicator		Unit of Measure	Baseline	Baseline Year		2022	EOP 2022
3.4	Online Master's degrees obtained by Head of Units	diplomas	0.00	2016	P	4.00	4.00
					P(a)	4.00	4.00
					A		

Details

Means of verification: Diplomas

Pro-Gender	No	Pro-Ethnicity	No
-------------------	----	----------------------	----

	Women				P	1.00	1.00
					P(a)	1.00	1.00
					A		
	Men				P	3.00	3.00
					P(a)	3.00	3.00
					A		

Outcome Nbr. 4: Improved provision of food safety services

Observation:

Indicator		Unit of Measure	Baseline	Baseline Year		2022	EOP 2022
4.0	Percentage of annual rejections of exported food products to the Netherlands due to noncompliance with Maximum Residue Levels (MRL)	%	20.00	2014	P	10.00	10.00
					P(a)	10.00	10.00
					A		

Details

Means of verification: Independent final evaluation

Pro-Gender	No	Pro-Ethnicity	No
-------------------	----	----------------------	----

Indicator	Unit of	Baseline	Baseline		2022	EOP 2022
-----------	---------	----------	----------	--	------	----------

PMR Operational Report

RESULTS MATRIX

OUTCOMES

		Measure		Year			
4.1	Number of farmers adopting Good Agricultural Practices (GAP) (male headed/female headed)	Farmers	0.00	2016	P	275.00	275.00
					P(a)	275.00	275.00
					A		

Details

Means of verification: LVV reports

Pro-Gender	No	Pro-Ethnicity	No
------------	----	---------------	----

	Female head of household				P	75.00	75.00
					P(a)	75.00	75.00
					A		
	Male head of household				P	200.00	200.00
					P(a)	200.00	200.00
					A		

Indicator	Unit of Measure	Baseline	Baseline Year		2022	EOP 2022
4.2	Number of primary processors approved by LVV for their compliance with the Hygiene Code	Processors	0.00	2016	P	84.00
					P(a)	84.00
					A	

Details

Means of verification: LVV reports

Pro-Gender	No	Pro-Ethnicity	No
------------	----	---------------	----

Indicator	Unit of Measure	Baseline	Baseline Year		2022	EOP 2022
4.3	Accreditation of inspection units (ISO 17020)	Accreditations	0.00	2016	P	2.00
					P(a)	2.00
					A	

Details

Means of verification: Accreditation certificates

Pro-Gender	No	Pro-Ethnicity	No
------------	----	---------------	----

Indicator	Unit of Measure	Baseline	Baseline Year		2022	EOP 2022
-----------	-----------------	----------	---------------	--	------	----------

PMR Operational Report

RESULTS MATRIX

OUTCOMES

4.4	Accreditation of the Food Safety Laboratory (ISO 17025)	Methodologies	0.00	2016	P	3.00	3.00
					P(a)	3.00	3.00
					A		

Details

Means of verification: Accreditation certificates

Pro-Gender	No	Pro-Ethnicity	No
-------------------	----	----------------------	----

Indicator		Unit of Measure	Baseline	Baseline Year		2022	EOP 2022
4.5	Food Safety Unit (FSU) established and operational	unit	0.00	2016	P	1.00	1.00
					P(a)	1.00	1.00
					A		

Details

Means of verification: LVV reports

Pro-Gender	No	Pro-Ethnicity	No
-------------------	----	----------------------	----

Indicator		Unit of Measure	Baseline	Baseline Year		2022	EOP 2022
4.6	Masters of Science degrees in Agri-food safety and quality assurance obtained by civil servants	diplomas	0.00	2016	P	2.00	2.00
					P(a)	2.00	2.00
					A		

Details

Means of verification: Diplomas

Pro-Gender	No	Pro-Ethnicity	No
-------------------	----	----------------------	----

	Women				P	1.00	1.00
					P(a)	1.00	1.00
					A		
	Men				P	1.00	1.00
					P(a)	1.00	1.00
					A		

Outcome Nbr. 5: Improved agricultural research and extension system

Observation:

Indicator	Unit of	Baseline	Baseline		2022	EOP 2022
-----------	---------	----------	----------	--	------	----------

PMR Operational Report

RESULTS MATRIX

OUTCOMES

		Measure		Year			
5.0	Percentage of targeted open field vegetable farmers that adopted best practices recommended by the projects (male headed/female headed)	%	0.00	2016	P	50.00	50.00
					P(a)	50.00	50.00
					A		

Details

Means of verification: impact evaluation

Pro-Gender	No	Pro-Ethnicity	No
-------------------	----	----------------------	----

Indicator	Unit of Measure	Baseline	Baseline Year		2022	EOP 2022
5.1	Amount of chemical pesticides used in the production of rice	SRD	800.00	2016	P	720.00
					P(a)	720.00
					A	

Details

Means of verification: Impact evaluation

Pro-Gender	No	Pro-Ethnicity	No
-------------------	----	----------------------	----

Indicator	Unit of Measure	Baseline	Baseline Year		2022	EOP 2022
5.2	Number of technologies adapted to local conditions	Technologies	0.00	2016	P	28.00
					P(a)	28.00
					A	

Details

Means of verification: LVV research reports

Pro-Gender	No	Pro-Ethnicity	No
-------------------	----	----------------------	----

Indicator	Unit of Measure	Baseline	Baseline Year		2022	EOP 2022
5.3	Tertiary education degrees obtained by research and extension staff	degrees	0.00	2016	P	18.00
					P(a)	18.00
					A	

Details

Means of verification: Project progress report. Diplomas.

Pro-Gender	No	Pro-Ethnicity	No
-------------------	----	----------------------	----

PMR Operational Report

RESULTS MATRIX

OUTCOMES

	Women				P	8.00	8.00
					P(a)	8.00	8.00
					A		
	Men				P	10.00	10.00
					P(a)	10.00	10.00
					A		

RESULTS MATRIX

OUTPUTS: ANNUAL PHYSICAL AND FINANCIAL PROGRESS

Component Nbr. 1 Agricultural health and food safety

	Output	Unit of Measure		PHYSICAL PROGRESS		FINANCIAL PROGRESS	
				2017	EOP 2022	2017	EOP 2022
1.1	Plant health laboratory completed and equipped	lab	P		1		300,000
			P(a)		1		300,000
			A		0		0
1.2	Pest risk analysis (PRA) conducted	number	P		12		557,000
			P(a)		12		557,000
			A		0		0
1.3	Border control points equipped	number	P		5		203,800
			P(a)		5		203,800
			A		0		0
1.4	Operational material developed	documents	P		29		300,000
			P(a)		29		300,000
			A		0		0
1.5	Import and export pest-specific protocols developed	documents	P		18		147,000
			P(a)		18		147,000
			A		0		0
1.6	Tertiary education scholarships financed	staff	P		20		352,115
			P(a)		20		352,115
			A		0		0
1.7	Pesticide management training conducted	number of people	P		500		263,600
			P(a)		500		263,600
			A		0		0
1.8	Traceability system for plant health established	system	P		1		558,000
			P(a)		1		558,000
			A		0		0
1.9	Inputs for ALPP financed	ALPP	P		1		139,600
			P(a)		1		139,600
			A		0		0
1.10	Animal health laboratory equipped	lab	P		1		2,698,940
			P(a)		1		2,698,940
			A		0		0
1.11	Information system installed	system	P		1		410,500
			P(a)		1		410,500
			A		0		0
1.12	Veterinary services staff trained	number of staff	P		45		45,000
			P(a)		45		45,000
			A		0		0
1.13	Risk assessment studies conducted	number of studies	P		6		266,000
			P(a)		6		266,000
			A		0		0
1.14	Awareness campaigns and workshops conducted	number of activities	P		9		145,000
			P(a)		9		145,000
			A		0		0
1.15	Laboratory personnel and inspectors trained	Number of staff	P		40		400,582
			P(a)		40		400,582

RESULTS MATRIX

OUTPUTS: ANNUAL PHYSICAL AND FINANCIAL PROGRESS

	Output	Unit of Measure		PHYSICAL PROGRESS		FINANCIAL PROGRESS	
				2017	EOP 2022	2017	EOP 2022
1.15	Laboratory personnel and inspectors trained	Number of staff	A		0		0
1.16	National Food Safety Policy and implementation plan drafted	document	P		1		33,500
			P(a)		1		33,500
			A		0		0
1.17	Updated food safety regulations drafted	documents	P		1		17,100
			P(a)		1		17,100
			A		0		0
1.18	GAP and hygiene code manuals developed	number of manuals	P		9		31,000
			P(a)		9		31,000
			A		0		0
1.19	Inspector and extension officers trained	number of staff	P		180		1,800
			P(a)		180		1,800
			A		0		0
1.20	Farmers trained in GAP and hygiene code	number of farmers	P		420		279,000
			P(a)		420		279,000
			A		0		0
1.21	Inspectors hired and trained	number of staff	P		23		753,256
			P(a)		23		753,256
			A		0		0
1.22	Food safety laboratory equipped	lab	P		1		361,270
			P(a)		1		361,270
			A		0		0
1.23	Laboratory technicians trained	number of staff	P		56		222,000
			P(a)		56		222,000
			A		0		0
1.24	Surveillance plan for food safety hazards developed	plan	P		1		15,000
			P(a)		1		15,000
			A		0		0
1.25	Consumer food safety awareness campaign conducted	campaign	P		2		64,000
			P(a)		2		64,000
			A		0		0
1.26	Laboratory complex completed	lab	P		1		1,535,000
			P(a)		1		1,535,000
			A		0		0

RESULTS MATRIX

OUTPUTS: ANNUAL PHYSICAL AND FINANCIAL PROGRESS

Component Nbr. 2 Agricultural research and technology transfer

	Output	Unit of Measure		PHYSICAL PROGRESS		FINANCIAL PROGRESS	
				2017	EOP 2022	2017	EOP 2022
2.1	Research projects completed	number of projects	P		30		2,766,937
			P(a)		30		2,766,937
			A		0		0
2.2	Production manuals developed	number of manuals	P		18		27,700
			P(a)		18		27,700
			A		0		0
2.3	YouTube instructional videos produced	videos	P		58		26,500
			P(a)		58		26,500
			A		0		0
2.4	Agricultural innovation training conducted	number of farmers	P		700		191,000
			P(a)		700		191,000
			A		0		0
2.5	On-farm trials and demonstrations conducted	trials	P		30		201,000
			P(a)		30		201,000
			A		0		0
2.6	Media equipment purchased	equipment	P		1		250,000
			P(a)		1		250,000
			A		0		0
2.7	Training events conducted	Number of people	P		45		105,000
			P(a)		45		105,000
			A		0		0
2.8	Tertiary education scholarships financed	number of staff	P		18		656,503
			P(a)		18		656,503
			A		0		0
2.9	Pesticide management facilities upgraded	facilities	P		1		25,000
			P(a)		1		25,000
			A		0		0
2.10	Agricultural innovation projects completed	number of projects	P		20		125,000
			P(a)		20		125,000
			A		0		0
2.11	Cluster laboratory installations completed	laboratory	P		1		1,211,700
			P(a)		1		1,211,700
			A		0		0

Other Cost

	External Audit	P				250,000
		P(a)				250,000
		A				0
	Monitoring and evaluation	P				300,000
		P(a)				300,000
		A				0
	Project management	P				1,263,597
		P(a)				1,263,597
		A				0

Total Cost

	Total Cost	P				17,500,000
		P(a)				17,500,000
		A				0

PMR Operational Report

CHANGES TO THE MATRIX

Section	Name	Type of Change	Reasons	Entered in the System	Agreed with Executing Agency
Output	Information system installed	Modify Output	Include unit of measureA solicitud del JEP se incluye el siguiente comentario: El plazo para acordar la matriz de resultados con el Organismo Ejecutor demoró más de 60 días contados desde la fecha de elegibilidad, razón por la cual se registraron los indicadores de impacto, resultado y productos posterior a dicho plazo, así como los medios de verificación para impactos y resultados. Vale la pena aclarar que los medios de verificación son los mismos presentes en la Propuesta de Préstamo aprobada por el Directorio, por tanto, no son un cambio.	04/10/2018	03/30/2018
Output	Inputs for ALPP financed	Modify Output	Include unit of measureA solicitud del JEP se incluye el siguiente comentario: El plazo para acordar la matriz de resultados con el Organismo Ejecutor demoró más de 60 días contados desde la fecha de elegibilidad, razón por la cual se registraron los indicadores de impacto, resultado y productos posterior a dicho plazo, así como los medios de verificación para impactos y resultados. Vale la pena aclarar que los medios de verificación son los mismos presentes en la Propuesta de Préstamo aprobada por el Directorio, por tanto, no son un cambio.	04/10/2018	03/30/2018
Output	Media equipment purchased	Modify Output	A solicitud del JEP se incluye el siguiente comentario: El plazo para acordar la matriz de resultados con el Organismo Ejecutor demoró más de 60 días contados desde la fecha de elegibilidad, razón por la cual se registraron los indicadores de impacto, resultado y productos posterior a dicho plazo, así como los medios de verificación para impactos y resultados. Vale la pena aclarar que los medios de verificación son los mismos presentes en la Propuesta de Préstamo aprobada por el Directorio, por tanto, no son un cambio.	04/10/2018	03/30/2018
Output	Cluster laboratory installations completed	Modify Output	Include unit of measureA solicitud del JEP se incluye el siguiente comentario: El plazo para acordar la matriz de resultados con el Organismo Ejecutor demoró más de 60 días contados desde la fecha de elegibilidad, razón por la cual se registraron los indicadores de impacto, resultado y productos posterior a dicho plazo, así como los medios de verificación para impactos y resultados. Vale la pena aclarar que los medios de verificación son los mismos presentes en la Propuesta de Préstamo aprobada por el Directorio, por tanto, no son un cambio.	04/10/2018	03/30/2018
Impact	Average weight of slaughtered pigs	Modify Impact Indicator	El plazo para acordar la matriz de resultados con el Organismo Ejecutor demoró más de 60 días contados desde la fecha de elegibilidad, razón por la cual se registraron los indicadores de impacto, resultado y productos posterior a dicho plazo. Vale la pena aclarar que todos los indicadores de impacto, resultado y producto son los mismos presentes en la Propuesta de Préstamo aprobada por el Directorio, por tanto, no son un cambio.	04/18/2018	03/30/2018
Impact	Quantity of rice exports	Modify Impact Indicator	El plazo para acordar la matriz de resultados con el Organismo Ejecutor demoró más de 60 días contados desde la fecha de elegibilidad, razón por la cual se registraron los indicadores de impacto, resultado y productos posterior a dicho plazo. Vale la pena aclarar que todos los indicadores de impacto, resultado y producto son los mismos presentes en la Propuesta de Préstamo aprobada por el Directorio, por tanto, no son un cambio.	04/18/2018	03/30/2018
Impact	Quantity of banana exports	Modify Impact Indicator	El plazo para acordar la matriz de resultados con el Organismo Ejecutor demoró más de 60 días contados desde la fecha de elegibilidad, razón por la cual se registraron los indicadores de impacto, resultado y productos posterior a dicho plazo. Vale la pena aclarar que todos los indicadores de impacto, resultado y producto son los mismos presentes en la Propuesta de Préstamo aprobada por el Directorio, por tanto, no son un cambio.	04/18/2018	03/30/2018
Impact	Quantity of vegetable exports	Modify Impact Indicator	El plazo para acordar la matriz de resultados con el Organismo Ejecutor demoró más de 60 días contados desde la fecha de elegibilidad, razón por la cual se registraron los indicadores de impacto, resultado y productos posterior a dicho plazo. Vale la pena aclarar que todos los indicadores de impacto, resultado y producto son los mismos presentes en la Propuesta de Préstamo aprobada por el Directorio, por tanto, no son un cambio.	04/18/2018	03/30/2018
Impact	Position in the International Trade Centre's General Index Ranking of Export Performance in fresh food	Modify Impact Indicator	El plazo para acordar la matriz de resultados con el Organismo Ejecutor demoró más de 60 días contados desde la fecha de elegibilidad, razón por la cual se registraron los indicadores de impacto, resultado y productos posterior a dicho plazo. Vale la pena aclarar que todos los indicadores de impacto, resultado y producto son los mismos presentes en la Propuesta de Préstamo aprobada por el Directorio, por tanto, no son un cambio.	04/18/2018	03/30/2018
Outcome	Number of beneficiaries of improved management and sustainable use of natural capital	Modify Outcome Indicator	El plazo para acordar la matriz de resultados con el Organismo Ejecutor demoró más de 60 días contados desde la fecha de elegibilidad, razón por la cual se registraron los indicadores de impacto, resultado y productos posterior a dicho plazo. Vale la pena aclarar que todos los indicadores de impacto, resultado y producto son los mismos presentes en la Propuesta de Préstamo aprobada por el Directorio, por tanto, no son un cambio.	04/18/2018	03/30/2018
Outcome	Number of exporting firms.	Modify Outcome Indicator	El plazo para acordar la matriz de resultados con el Organismo Ejecutor demoró más de 60 días contados desde la fecha de elegibilidad, razón por la cual se registraron los indicadores de impacto, resultado y productos posterior a dicho plazo. Vale la pena aclarar que todos los indicadores de impacto, resultado y producto son los mismos presentes en la Propuesta de Préstamo aprobada por el Directorio, por tanto, no son un cambio.	04/18/2018	03/30/2018
Outcome	Percentage of annual notifications of exported crops due to noncompliance with plant health requirements	Modify Outcome Indicator	El plazo para acordar la matriz de resultados con el Organismo Ejecutor demoró más de 60 días contados desde la fecha de elegibilidad, razón por la cual se registraron los indicadores de impacto, resultado y productos posterior a dicho plazo. Vale la pena aclarar que todos los indicadores de impacto, resultado y producto son los mismos presentes en la Propuesta de Préstamo aprobada por el Directorio, por tanto, no son un cambio.	04/18/2018	03/30/2018
Outcome	Achievement of Area of	Modify	El plazo para acordar la matriz de resultados con el Organismo Ejecutor demoró más de 60 días contados desde la fecha de elegibilidad, razón	04/18/2018	03/30/2018

CHANGES TO THE MATRIX

Section	Name	Type of Change	Reasons	Entered in the System	Agreed with Executing Agency
	Low Pest Prevalence (ALPP) of Carambola Fruit Fly in orange producing area	Outcome Indicator	por la cual se registraron los indicadores de impacto, resultado y productos posterior a dicho plazo. Vale la pena aclarar que todos los indicadores de impacto, resultado y producto son los mismos presentes en la Propuesta de Préstamo aprobada por el Directorio, por tanto, no son un cambio.		
Outcome	Masters of Science (MSc) degrees obtained by Plant Health Services employees	Modify Outcome Indicator	El plazo para acordar la matriz de resultados con el Organismo Ejecutor demoró más de 60 días contados desde la fecha de elegibilidad, razón por la cual se registraron los indicadores de impacto, resultado y productos posterior a dicho plazo. Vale la pena aclarar que todos los indicadores de impacto, resultado y producto son los mismos presentes en la Propuesta de Préstamo aprobada por el Directorio, por tanto, no son un cambio.	04/18/2018	03/30/2018
Outcome	Average score PVS developed by OIE	Modify Outcome Indicator	El plazo para acordar la matriz de resultados con el Organismo Ejecutor demoró más de 60 días contados desde la fecha de elegibilidad, razón por la cual se registraron los indicadores de impacto, resultado y productos posterior a dicho plazo. Vale la pena aclarar que todos los indicadores de impacto, resultado y producto son los mismos presentes en la Propuesta de Préstamo aprobada por el Directorio, por tanto, no son un cambio.	04/18/2018	03/30/2018
Outcome	OIE Disease Free Status recognition for 3 diseases achieved	Modify Outcome Indicator	El plazo para acordar la matriz de resultados con el Organismo Ejecutor demoró más de 60 días contados desde la fecha de elegibilidad, razón por la cual se registraron los indicadores de impacto, resultado y productos posterior a dicho plazo. Vale la pena aclarar que todos los indicadores de impacto, resultado y producto son los mismos presentes en la Propuesta de Préstamo aprobada por el Directorio, por tanto, no son un cambio.	04/18/2018	03/30/2018
Outcome	Self-Declaration to OIE of Disease Free for Tuberculosis and Brucellosis	Modify Outcome Indicator	El plazo para acordar la matriz de resultados con el Organismo Ejecutor demoró más de 60 días contados desde la fecha de elegibilidad, razón por la cual se registraron los indicadores de impacto, resultado y productos posterior a dicho plazo. Vale la pena aclarar que todos los indicadores de impacto, resultado y producto son los mismos presentes en la Propuesta de Préstamo aprobada por el Directorio, por tanto, no son un cambio.	04/18/2018	03/30/2018
Outcome	Accreditation of the Animal Health Laboratory (ISO 17025)	Modify Outcome Indicator	El plazo para acordar la matriz de resultados con el Organismo Ejecutor demoró más de 60 días contados desde la fecha de elegibilidad, razón por la cual se registraron los indicadores de impacto, resultado y productos posterior a dicho plazo. Vale la pena aclarar que todos los indicadores de impacto, resultado y producto son los mismos presentes en la Propuesta de Préstamo aprobada por el Directorio, por tanto, no son un cambio.	04/18/2018	03/30/2018
Outcome	Online Master's degrees obtained by Head of Units	Modify Outcome Indicator	El plazo para acordar la matriz de resultados con el Organismo Ejecutor demoró más de 60 días contados desde la fecha de elegibilidad, razón por la cual se registraron los indicadores de impacto, resultado y productos posterior a dicho plazo. Vale la pena aclarar que todos los indicadores de impacto, resultado y producto son los mismos presentes en la Propuesta de Préstamo aprobada por el Directorio, por tanto, no son un cambio.	04/18/2018	03/30/2018
