

PMR Operational Report

Operation Number	JA-L1079	Chief of Operations Validation Date	10/18/19
Year- PMR Cycle	First period Jan-Jun 2019	Division Chief Validation Date	10/30/19
Last Update	10/11/19	Country Representative Validation Date	11/01/19
PMR Validation Stage	Validated by Representative		

Basic Data

Operation Profile

Operation Name	Skills Development for Global Services in Jamaica	Loan Number	4645/OC-JA
Executing Agency	Ministry of Industry, Commerce, Agriculture and Fisheries	Sector/Subsector	IS-VOC - SOCIAL INVESTMENT-VOCATIONAL AND WORKFORCE TRAINING
Team Leader	PAVON, FERNANDO YITZACK	Overall Stage	Disbursing (From eligibility until all the Operations are closed)
Operation Type	Loan Operation	Country	JAMAICA
Lending Instrument	Investment Loan	Convergence related Operation(s)	
Borrower	JAMAICA		


Environmental and Social Safeguards

Impacts Category	C	Was/Were the objective(s) of this operation reformulated?	NO
Safeguard Performance Rating		Date of approval	
Safeguard Performance Rating - Rationale			

Financial Data

Item	Total Cost and Source					Available Funds (US\$)			
	Original IDB	Current IDB	Local Counterpart	Co-Financing / Country	Total Original Cost	Current IDB	Disb. Amount to Date	% Disb	Undisbursed Amount
JA-L1079	15,000,000	15,000,000	0	0	15,000,000	15,000,000	594,300	3.96%	14,405,700
Aggregated	15,000,000	15,000,000	0	0	15,000,000	15,000,000	594,300	3.96%	14,405,700

Expense Categories by Loan Contract (cumulative values)

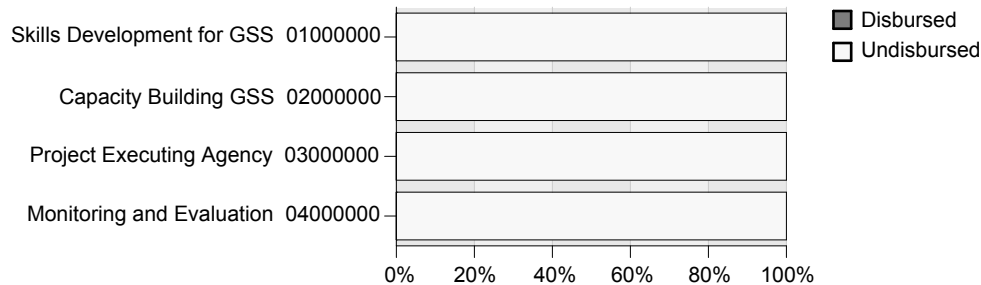

PMR Operational Report

RESULTS MATRIX

IMPACTS

Impact Nbr. 1: Increased growth of the Global Services Sector (GSS) in Jamaica, particularly in higher value-added segments

Observation:

Indicator		Unit of Measure	Baseline	Baseline Year		2023	EOP 2024
1.1	Value of exports of Global Services	US\$ millions	223.00	2016	P	231.00	231.00
					P(a)	231.00	231.00
					A		

Details

Means of verification: IMF Statistics

Observations: Baseline: A proxy of services exports value under the classification "Other business services" for 2016 (IMF BOP and IIP Data) which covers the exports from firms in areas related to global services (e.g. gaming, professional services). Goal: Projected GSS exports volume by 2026 in Jamaica. See Annex Economic Analysis.

Pro-Gender No **Pro-Ethnicity** No

Indicator		Unit of Measure	Baseline	Baseline Year		2023	EOP 2024
1.2	Number of employed individuals in the GSS	Employed Individuals	22,000.00	2016	P	50,000.00	50,000.00
					P(a)	50,000.00	50,000.00
					A		

Details

Means of verification: Heart- Trust/NTA

Observations: Baseline: Heart-Trust/NTA (2017b). Goal: JAMPRO's Corporate Strategic Plan (2018).

Pro-Gender No **Pro-Ethnicity** No

Indicator		Unit of Measure	Baseline	Baseline Year		2023	EOP 2024
1.3	AT Kearney Global Services Location Index	value (in points)	5.00	2017	P	5.06	5.06
					P(a)	5.06	5.06
					A		

Details

Means of verification: AT Kearney Global Indicators

Observations: Baseline: AT Kearney Global Indicators. Goal: Projected in line with the index of Trinidad and Tobago (5.07) –one of Jamaica's main competitors-. Note: Currently, Jamaica ranks 43rd out of 55 countries in this index.

Pro-Gender No **Pro-Ethnicity** No

PMR Operational Report

RESULTS MATRIX

OUTCOMES

Outcome Nbr. 1: Increased supply of skilled workers in the GSS

Observation:

Indicator		Unit of Measure	Baseline	Baseline Year		2021	2023	EOP 2024
1.1	Share of certified graduates from Finishing Schools (FS) with a formal contract in a GSS firm one year after training completion	Percentage points (pp)	0.00	2019	P	2.50	2.50	2.50
					P(a)	2.50	2.50	2.50
					A			

Details

Means of verification: Mid-term/final reports based on follow-up survey

Observations: Definition: Measures formal employment for unemployed beneficiaries. See M&E Arrangements for complete details (Formula, Baseline and Goal).

Pro-Gender	No	Pro-Ethnicity	No
-------------------	----	----------------------	----

Indicator		Unit of Measure	Baseline	Baseline Year		2021	2023	EOP 2024
1.2	Percentage change in the average wage of GSS workers who obtained a Finishing School (FS) certification one year after completing the training	Percentage (%)	0.00	2019	P	6.00	6.00	6.00
					P(a)	6.00	6.00	6.00
					A			

Details

Means of verification: Mid-term/final reports based on follow-up survey

Observations: Definition: This indicator measures improvement in wages for active GSS workers. See M&E Arrangements for complete details (Formula, Baseline and Goal).

Pro-Gender	No	Pro-Ethnicity	No
-------------------	----	----------------------	----

Indicator		Unit of Measure	Baseline	Baseline Year		2021	2023	EOP 2024
1.3	Percentage change in the average wage of GSS workers who obtained an Apprenticeship Programme (AP) certification one year after training completion	Percentage (%)	0.00	2019	P	9.00	9.00	9.00
					P(a)	9.00	9.00	9.00
					A			

Details

Means of verification: Mid-term/final reports based on follow-up survey

Observations: Definition: Measures wages improvement for active GSS workers. See M&E Arrangements for complete details (Formula, Baseline and Goal).

Pro-Gender	No	Pro-Ethnicity	No
-------------------	----	----------------------	----

Outcome Nbr. 2: Increased export volumes and capacity of the sector to attract FDI

Observation:

Indicator	Unit of	Baseline	Baseline		2021	2023	EOP 2024
-----------	---------	----------	----------	--	------	------	----------

PMR Operational Report

RESULTS MATRIX

OUTCOMES

		Measure		Year				
2.1	Percentage change in the value of exports of the GSS sector	Percentage (%)	0.00	2016	P	0.00	1.70	1.70
					P(a)	0.00	1.70	1.70
					A			
Details								
Means of verification: Final report based on follow-up survey								
Observations: Definition: Measures the value of exports of the beneficiary GSS firms. See M&E Arrangements for complete details (Formula, Baseline and Goal).								
Pro-Gender		No	Pro-Ethnicity		No			
Indicator		Unit of Measure	Baseline	Baseline Year		2021	2023	EOP 2024
2.2	Capital expenditure made in Jamaica by the beneficiary GSS firms	US millions	33.40	2017	P	0.00	45.90	45.90
					P(a)	0.00	45.90	45.90
					A			
Details								
Means of verification: Final report based on follow-up survey								
Observations: Definition: Measures the value of investments based on the capital expenditure made by domestic and foreign GSS firms in Jamaica in a particular year. See M&E Arrangements for complete details (Formula, Baseline and Goal).								
Pro-Gender		No	Pro-Ethnicity		No			
Indicator		Unit of Measure	Baseline	Baseline Year		2021	2023	EOP 2024
2.3	Share of high-level sub-segments (higher-value added BPO, KPO- and ITO) that are offered by the beneficiary GSS firms	Percentage (%)	0.00	2017	P	0.00	25.00	25.00
					P(a)	0.00	25.00	25.00
					A			
Details								
Means of verification: Final report based on follow-up survey								
Observations: Definition: Measures the share of high-level sub-segments in GSS firms. High-level subsegments are divided in KPO and ITO. See M&E Arrangements for complete details (Formula, Baseline and Goal) and definition of the segments.								
Pro-Gender		No	Pro-Ethnicity		No			

RESULTS MATRIX

OUTPUTS: ANNUAL PHYSICAL AND FINANCIAL PROGRESS

Component Nbr. 1 Skills Development for the Global Services Industry and Strengthening of the Skills Development System

	Output	Unit of Measure		PHYSICAL PROGRESS		FINANCIAL PROGRESS	
				2019	EOP 2024	2019	EOP 2024
1.1	1. Global Services Sector Skills Board (GSSSB) established and active	# boards	P	0	1	155,698	713,000
			P(a)	0	1	155,698	713,000
			A	1	1	11,632	11,632
1.2	2. Diagnosis for gender imbalances in the industry developed	#diagnoses	P	0	1	55,800	62,000
			P(a)	0	1	55,800	62,000
			A	0	0	0	0
1.3	3. Smart Talent Platform online and functioning	# platforms	P	0	1	79,467	956,000
			P(a)	0	1	79,467	956,000
			A	0	0	0	0
1.4	4. Job readiness curriculum developed and approved	# curricula	P	0	2	0	94,000
			P(a)	0	2	0	94,000
			A	0	0	0	0
1.5	5. Places for training trainers with the Job readiness curriculum available	# places	P	0	1,000	0	966,000
			P(a)	0	1,000	0	966,000
			A	0	0	0	0
1.6	6. Apprenticeships places for the GSS available	# places	P	0	450	0	1,080,000
			P(a)	0	450	0	1,080,000
			A	0	0	0	0
1.7	7. Trainees positions in finishing schools available	# positions	P	0	12,000	0	3,200,000
			P(a)	0	12,000	0	3,200,000
			A	0	0	0	0
1.8	8. Competitive Fund Management set up and active	# funds	P	1	1	38,167	450,000
			P(a)	1	1	38,167	450,000
			A	0	0	415	415
1.9	9. Mechanisms for measuring and improving training provider's performance developed and delivered to the NTA	# mechanisms	P	0	1	15,000	200,000
			P(a)	0	1	15,000	200,000
			A	0	0	0	0
1.10	10. Psychometric assessment tool designed and delivered to the NTA	# tools	P	0	1	0	125,000
			P(a)	0	1	0	125,000
			A	0	0	0	0
1.11	11. Mechanisms for collecting employers' feedback designed and delivered to the NTA	# mechanisms	P	0	1	0	94,000
			P(a)	0	1	0	94,000
			A	0	0	0	0

RESULTS MATRIX

OUTPUTS: ANNUAL PHYSICAL AND FINANCIAL PROGRESS

Component Nbr. 2 Strengthening JAMPRO's institutional capacity to increase investment and promote exports in the GSS

	Output	Unit of Measure		PHYSICAL PROGRESS		FINANCIAL PROGRESS	
				2019	EOP 2024	2019	EOP 2024
2.1	12. Business process re-engineering/change management strategy designed and delivered to JAMPRO	# strategies	P	0	2	0	450,000
			P(a)	0	2	0	450,000
			A	0	0	0	0
2.2	13. Regulatory and incentives framework optimization designed and delivered to JAMPRO	# frameworks	P	1	2	91,694	391,500
			P(a)	1	2	91,694	391,500
			A	0	0	3,394	3,394
2.3	14. Digital Global Services Strategy designed and delivered to JAMPRO	# strategies	P	0	1	78,750	175,000
			P(a)	0	1	78,750	175,000
			A	0	0	0	0
2.4	15. Digital GSS Promotional Activities developed	# activities	P	0	3	0	1,000,000
			P(a)	0	3	0	1,000,000
			A	0	0	0	0
2.5	16. Participation in international and regional investment targeting events	# events participation	P	1	5	83,000	900,000
			P(a)	1	5	83,000	900,000
			A	0	0	64,680	64,680
2.6	17. National Awareness campaign activities executed	# activities	P	0	4	0	795,000
			P(a)	0	4	0	795,000
			A	0	0	0	0
2.7	18. GSS Incubators designed and furnished	# of incubators	P	0	2	0	700,000
			P(a)	0	2	0	700,000
			A	0	0	0	0
2.8	19. Entrepreneurial accelerator programme events (including workshops) delivered	# events	P	0	4	0	361,500
			P(a)	0	4	0	361,500
			A	0	0	0	0
2.9	20. Awards for entrepreneurial accelerator programme events (including workshops) delivered	# licenses	P	0	6	0	140,000
			P(a)	0	6	0	140,000
			A	0	0	0	0
2.10	21. Digital management system active	# systems	P	0	1	0	327,000
			P(a)	0	1	0	327,000
			A	0	0	0	0

Other Cost

Project Management: PEU Staff	P			213,897	1,308,500
	P(a)			213,897	1,308,500
	A			68,498.4	68,498.4
Project Management: Office Equipment	P			30,620	65,000
	P(a)			30,620	65,000
	A			11,334.44	11,334.44
Project Management: Office Space - Lease	P			17,600	102,080
	P(a)			17,600	102,080
	A			0	0
Monitoring and Evaluation: Trainee Surveys	P			0	100,000
	P(a)			0	100,000
	A			0	0
Monitoring and Evaluation: Firm Surveys	P			26,000	100,000

RESULTS MATRIX

OUTPUTS: ANNUAL PHYSICAL AND FINANCIAL PROGRESS

	Monitoring and Evaluation: Firm Surveys	P(a)			26,000	100,000
		A			0	0
	Contingencies	P			0	20,000
		P(a)			0	20,000
		A			0	0
	Audits	P			0	100,000
		P(a)			0	100,000
		A			0	0
	Project Management: Other Expenses	P			4,420	24,420
		P(a)			4,420	24,420
		A			0	0

Total Cost

	Total Cost	P			890,113	15,000,000
		P(a)			890,113	15,000,000
		A			159,953.84	159,953.84

CHANGES TO THE MATRIX

No information available for this section

IMPLEMENTATION STATUS AND LEARNING

No information available for this section
