

PMR Operational Report

| | | | |
|-----------------------------|-----------------------------|---|----------|
| Operation Number | JA-L1072 | Chief of Operations Validation Date | 04/20/20 |
| Year- PMR Cycle | Second period Jan-Dec 2019 | Division Chief Validation Date | 04/21/20 |
| Last Update | 04/15/20 | Country Representative Validation Date | 04/28/20 |
| PMR Validation Stage | Validated by Representative | | |

Basic Data

Operation Profile

| | | | |
|---------------------------|---|---|---|
| Operation Name | Implementation of the National Identification System (NIDS) for Economic Growth | Loan Number | 4437/OC-JA |
| Executing Agency | OFFICE OF THE PRIME MINISTER | Sector/Subsector | RM-REG - REFORM / MODERNIZATION OF THE STATE-CIVIL REGISTRIES |
| Team Leader | DE SIMONE, FRANCESCO | Overall Stage | Disbursing (From eligibility until all the Operations are closed) |
| Operation Type | Loan Operation | Country | Jamaica |
| Lending Instrument | Investment Loan | Convergence related Operation(s) | |
| Borrower | JAMAICA | | |


Environmental and Social Safeguards

| | | | |
|---|---|--|----|
| Impacts Category | C | Was/Were the objective(s) of this operation reformulated? | NO |
| Safeguard Performance Rating | | Date of approval | |
| Safeguard Performance Rating - Rationale | | | |

Financial Data

| Item | Total Cost and Source | | | | | Available Funds (US\$) | | | |
|------------|-----------------------|-------------|-------------------|------------------------|---------------------|------------------------|----------------------|--------|--------------------|
| | Original IDB | Current IDB | Local Counterpart | Co-Financing / Country | Total Original Cost | Current IDB | Disb. Amount to Date | % Disb | Undisbursed Amount |
| JA-L1072 | 68,000,000 | 68,000,000 | 0 | 0 | 68,000,000 | 68,000,000 | 7,088,891 | 10.42% | 60,911,109 |
| Aggregated | 68,000,000 | 68,000,000 | 0 | 0 | 68,000,000 | 68,000,000 | 7,088,891 | 10.42% | 60,911,109 |

Expense Categories by Loan Contract (cumulative values)

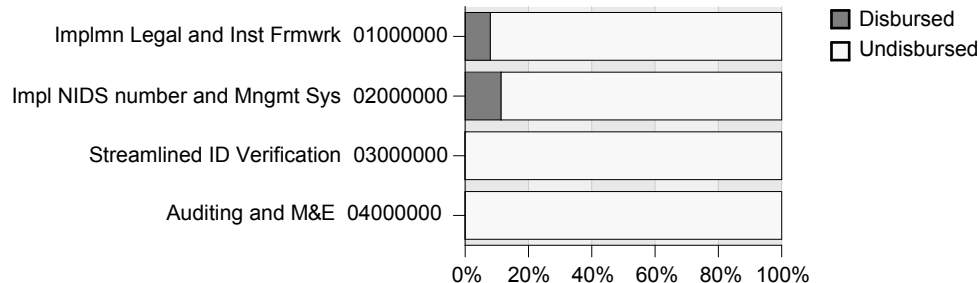

Please note that inactive indicators and outputs are not displayed; totals in the actual cost table may not match the sum of the cost of the outputs displayed, due to the cost of inactive outputs.

PMR Operational Report

RESULTS MATRIX

IMPACTS

Impact Nbr. 0: Reduce the transactional costs associated with identity verification for citizens to access public and private services

Observation:

| Indicator | | Unit of Measure | Baseline | Baseline Year | | 2024 | EOP 2024 |
|-----------|--|-----------------|----------|---------------|------|-------|----------|
| 0.0 | Average cost for citizens to open a bank account | US\$ | 92.86 | 2017 | P | | 0.00 |
| | | | | | P(a) | 19.32 | 19.32 |
| | | | | | A | | 0.00 |

Details

Means of verification: End of Project Report

Pro-Gender No **Pro-Ethnicity** No

| Indicator | | Unit of Measure | Baseline | Baseline Year | | 2024 | EOP 2024 |
|-----------|--|-----------------|----------|---------------|------|-------|----------|
| 0.1 | Average cost for citizens to register a passport application | US\$ | 115.09 | 2017 | P | | 0.00 |
| | | | | | P(a) | 38.64 | 38.64 |
| | | | | | A | | 0.00 |

Details

Means of verification: End of Project Report

Pro-Gender No **Pro-Ethnicity** No

PMR Operational Report

RESULTS MATRIX

OUTCOMES

Outcome Nbr. 0: OUTCOME # 1: Increase in the number of women who register their children through bedside registration

Observation:

| Indicator | | Unit of Measure | Baseline | Baseline Year | | 2018 | 2019 | 2020 | 2021 | 2022 | 2023 | 2024 | EOP 2024 |
|---|---|-----------------|----------|---------------|------|------|------|------|-------|------|------|------|----------|
| 0.0 | Women who register their children through electronic bedside registration | % of women | 30.70 | 2016 | P | 0.00 | 0.00 | 0.00 | 95.00 | 0.00 | 0.00 | 0.00 | 95.00 |
| | | | | | P(a) | 0.00 | 0.00 | 0.00 | 95.00 | 0.00 | 0.00 | 0.00 | 95.00 |
| | | | | | A | 0.00 | | | | | | | 0.00 |
| Details | | | | | | | | | | | | | |
| Means of verification: Annual Reports from NIRA | | | | | | | | | | | | | |
| Pro-Gender | | No | | Pro-Ethnicity | | No | | | | | | | |

Outcome Nbr. 1: Outcome # 2: Reduce the number of persons with special needs without a birth certificate

Observation:

| Indicator | | Unit of Measure | Baseline | Baseline Year | | 2018 | 2019 | 2020 | 2021 | 2022 | 2023 | 2024 | EOP 2024 |
|---|---|---------------------------------|----------|---------------|---------------|------|------|------|------|------|--------|------|----------|
| 1.0 | Persons with special needs registered in the JCPD without a birth certificate | % of persons with special needs | 90.00 | 2017 | P | 0.00 | 0.00 | 0.00 | 0.00 | 0.00 | 100.00 | 0.00 | 100.00 |
| | | | | | P(a) | 0.00 | 0.00 | 0.00 | 0.00 | 0.00 | 100.00 | 0.00 | 100.00 |
| | | | | | A | 0.00 | | | | | | | 0.00 |
| Details | | | | | | | | | | | | | |
| Means of verification: Annual Reports from NIRA | | | | | | | | | | | | | |
| Pro-Gender | | No | | | Pro-Ethnicity | | No | | | | | | |

Outcome Nbr. 2: OUTCOME # 3: Enrollment of the National Identification System (NIDS)

Observation:

| Indicator | | Unit of Measure | Baseline | Baseline Year | | 2018 | 2019 | 2020 | 2021 | 2022 | 2023 | 2024 | EOP 2024 |
|---|---------------|---|---------------|---------------|------|------|------|------|------|------|-------|------|----------|
| 2.0 | NIDS coverage | % of total population with a National Identification Number (NIN) | 0.00 | 2017 | P | 0.00 | 0.00 | 0.00 | 0.00 | 0.00 | 75.00 | 0.00 | 75.00 |
| | | | | | P(a) | 0.00 | 0.00 | 0.00 | 0.00 | 0.00 | 75.00 | 0.00 | 75.00 |
| | | | | | A | 0.00 | | | | | | | 0.00 |
| Details | | | | | | | | | | | | | |
| Means of verification: Annual Reports from NIRA | | | | | | | | | | | | | |
| Pro-Gender | | No | Pro-Ethnicity | | No | | | | | | | | |

Outcome Nbr. 3: OUTCOME # 4: Improvement in the reliability of identification

Observation:

PMR Operational Report

RESULTS MATRIX

OUTCOMES

| Indicator | | Unit of Measure | Baseline | Baseline Year | | 2018 | 2019 | 2020 | 2021 | 2022 | 2023 | 2024 | EOP 2024 |
|---|---|---------------------------------------|---------------|---------------|------|------|------|------|------|------|-------|------|----------|
| 3.0 | Confirmation of identity through the NIDS | % of confirmed identity verifications | 0.00 | 2017 | P | 0.00 | 0.00 | 0.00 | 0.00 | 0.00 | 95.00 | 0.00 | 95.00 |
| | | | | | P(a) | 0.00 | 0.00 | 0.00 | 0.00 | 0.00 | 95.00 | 0.00 | 95.00 |
| | | | | | A | 0.00 | | | | | | | 0.00 |
| Details | | | | | | | | | | | | | |
| Means of verification: Annual Reports from NIRA | | | | | | | | | | | | | |
| Pro-Gender | | No | Pro-Ethnicity | | No | | | | | | | | |

Outcome Nbr. 4: OUTCOME #5: Improvement in identity verification services through the NIDS

Observation:

| Indicator | | Unit of Measure | Baseline | Baseline Year | | 2018 | 2019 | 2020 | 2021 | 2022 | 2023 | 2024 | EOP 2024 |
|---|---|---|---------------|---------------|------|------|------|------|------|------|-----------|------|-----------|
| 4.0 | Identity Verification requests to the NIDS per year | # of identity verification requests to the NIDS | 0.00 | 2017 | P | 0.00 | 0.00 | 0.00 | 0.00 | 0.00 | 19,200.00 | 0.00 | 19,200.00 |
| | | | | | P(a) | 0.00 | 0.00 | 0.00 | 0.00 | 0.00 | 19,200.00 | 0.00 | 19,200.00 |
| | | | | | A | 0.00 | | | | | | | 0.00 |
| Details | | | | | | | | | | | | | |
| Means of verification: Annual Reports from NIRA | | | | | | | | | | | | | |
| Pro-Gender | | No | Pro-Ethnicity | | No | | | | | | | | |

Outcome Nbr. 5: OUTCOME #6: Reduction in the transactional costs associated with identity verification for public and private service providers and citizens

Observation:

| Indicator | | Unit of Measure | Baseline | Baseline Year | | 2018 | 2019 | 2020 | 2021 | 2022 | 2023 | 2024 | EOP 2024 |
|--|---|-----------------|----------|---------------|------|------|------|------|------|------|------|------|----------|
| 5.0 | Average cost for a ban to open a bank account | US\$ | 4.40 | 2017 | P | 0.00 | 0.00 | 0.00 | 0.00 | 0.00 | 0.00 | 0.88 | 0.88 |
| | | | | | P(a) | 0.00 | 0.00 | 0.00 | 0.00 | 0.00 | 0.00 | 0.88 | 0.88 |
| | | | | | A | 0.00 | | | | | | | 0.00 |
| Details | | | | | | | | | | | | | |
| Means of verification: End of Project Report | | | | | | | | | | | | | |
| Pro-Gender | | No | | Pro-Ethnicity | | No | | | | | | | |

RESULTS MATRIX

OUTPUTS: ANNUAL PHYSICAL AND FINANCIAL PROGRESS

Component Nbr. 1 Component # 1: Implementation of the legal and institutional framework for the NIDS

| | Output | Unit of Measure | | PHYSICAL PROGRESS | | FINANCIAL PROGRESS | |
|-----|--|--------------------------------|------|-------------------|-----------|--------------------|--------------|
| | | | | 2019 | EOP 2024 | 2019 | EOP 2024 |
| 1.1 | NIRA fully staffed and operating | Government agencies (#) | P | | 1 | 1,795,897.16 | 9,915,163.16 |
| | | | P(a) | | 1 | 1,313,207.91 | 9,915,163.16 |
| | | | A | 0 | 0 | 704,821.61 | 1,105,990.78 |
| 1.2 | Civil Records Digitized available in database | # of civil records in database | P | | 2,550,000 | 1,397,000 | 3,515,000 |
| | | | P(a) | | 2,550,000 | 279,400 | 3,515,000 |
| | | | A | 0 | 0 | 0 | 0 |
| 1.3 | Mobile workstations for birth registration functioning | # of mobile workstations | P | | 160 | 36,000 | 72,000 |
| | | | P(a) | | 160 | 36,000 | 72,000 |
| | | | A | 0 | 0 | 0 | 0 |
| 1.4 | Communications and Behaviourial Change Plan for the NIDS implemented | # of communications plans | P | | 1 | 508,915.22 | 2,401,339.55 |
| | | | P(a) | | 1 | 438,760.28 | 2,401,339.55 |
| | | | A | 0 | 0 | 528,949.03 | 613,208.35 |

Component Nbr. 2 Component # 2: Implementation of a unique National Identification Number and National Identification Management System

| | Output | Unit of Measure | | PHYSICAL PROGRESS | | FINANCIAL PROGRESS | |
|-----|--|--------------------------------|------|-------------------|----------|--------------------|---------------|
| | | | | 2019 | EOP 2024 | 2019 | EOP 2024 |
| 2.1 | Data center for the NIDS operating | Government agencies (#) | P | | 1 | 2,924,692.58 | 19,890,304.65 |
| | | | P(a) | | 1 | 2,424,692.58 | 19,890,304.65 |
| | | | A | 0 | 0 | 220,963.26 | 398,709.06 |
| 2.2 | Enrollment sites fully staffed, delivering cards | # of enrollment sites | P | | 43 | 784,235.67 | 4,385,937.59 |
| | | | P(a) | | 43 | 685,753.78 | 4,385,937.59 |
| | | | A | 0 | 0 | 41,372.69 | 48,536.47 |
| 2.3 | Card production site producing cards | # of card production sites | P | | 1 | 800,000 | 8,000,000 |
| | | | P(a) | | 1 | 800,000 | 8,000,000 |
| | | | A | 0 | 0 | 1,794,249 | 1,794,249 |
| 2.4 | Identity Management System Operating | # of identity management syste | P | | 1 | 1,110,000 | 11,100,000 |
| | | | P(a) | | 1 | 1,110,000 | 11,100,000 |
| | | | A | 0 | 0 | 2,829,146.14 | 2,829,146.14 |

Component Nbr. 3 Component # 3: Streamlined identity verification for public and private sector

| | Output | Unit of Measure | | PHYSICAL PROGRESS | | FINANCIAL PROGRESS | |
|-----|---|-----------------|------|-------------------|----------|--------------------|--------------|
| | | | | 2019 | EOP 2024 | 2019 | EOP 2024 |
| 3.1 | Financial Regulatory entities with employees trained in identity verification | # of trainings | P | | 3 | 95,000 | 95,000 |
| | | | P(a) | | 3 | 40,000 | 95,000 |
| | | | A | 0 | 0 | 0 | 0 |
| 3.2 | Databases integrating the NIN | # of databases | P | | 6 | 1,881,250 | 4,449,833.33 |
| | | | P(a) | | 6 | 1,281,250 | 4,449,833.33 |
| | | | A | 0 | 0 | 3,123.2 | 3,123.2 |
| 3.3 | MDAs' employees trained in identity verification | # of trainings | P | | 6 | 140,000 | 230,000 |
| | | | P(a) | | 6 | 140,000 | 230,000 |
| | | | A | 0 | 0 | 0 | 0 |

Other Cost

| | | | | | | |
|--|----------------------------------|------|--|--|-----------|-----------|
| | Audit, Monitoring and Evaluation | P | | | 87,000 | 454,000 |
| | | P(a) | | | 87,000 | 454,000 |
| | | A | | | 20,089.78 | 20,267.02 |

RESULTS MATRIX

OUTPUTS: ANNUAL PHYSICAL AND FINANCIAL PROGRESS

| | | | | | | |
|--|-------------|------|--|--|---|--------------|
| | Contingency | P | | | | 3,491,421.72 |
| | | P(a) | | | 0 | 3,491,421.72 |
| | | A | | | 0 | 0 |

Total Cost

| | | | | | | |
|--|------------|------|--|--|---------------|--------------|
| | Total Cost | P | | | 11,559,990.63 | 68,000,000 |
| | | P(a) | | | 8,636,064.55 | 68,000,000 |
| | | A | | | 6,142,714.71 | 6,813,230.02 |

PMR Operational Report

CHANGES TO THE MATRIX

| Section | Name | Reasons | Type of Change | Subtype | Modified By | Entered in the System |
|---------|--|---------------------------------|----------------|---|-------------|-----------------------|
| Output | Civil Records Digitized available in database | correcting some rounding errors | Modify Output | Modify Financial EOP P(a) value - caused by a change in the Financial P(a). | FRANDESCOD | 03/31/2020 |
| | Communications and Behaviourial Change Plan for the NIDS implemented | correcting some rounding errors | Modify Output | Modify Financial EOP P(a) value - caused by a change in the Financial P(a). | FRANDESCOD | 03/18/2020 |
| | Enrollment sites fully staffed, delivering cards | correcting some rounding errors | Modify Output | Modify Financial EOP P(a) value - caused by a change in the Financial P(a). | FRANDESCOD | 03/31/2020 |

PMR Operational Report

IMPLEMENTATION STATUS AND LEARNING

| Lesson Learned - Categories |
|-----------------------------|
| Project Design |
| Project Management Capacity |
