

# PMR Public Report

<b>Operation Number</b>	GU-L1163	<b>Chief of Operations Validation Date</b>	10/01/21
<b>Year- PMR Cycle</b>	First period Jan-Jun 2021	<b>Division Chief Validation Date</b>	
<b>Last Update</b>	10/01/21	<b>Country Representative Validation Date</b>	
<b>PMR Validation Stage</b>	Validated by Chief of Operations		

## Basic Data

### Operation Profile

<b>Operation Name</b>	Program to Strengthen the Institutional Healthcare Service Network (PRORISS)	<b>Loan Number</b>	4791/OC-GU
<b>Executing Agency</b>	MINISTERIO DE SALUD PUBLICA Y ASISTENCIA SOCIAL	<b>Sector/Subsector</b>	HEALTH-PRIMARY HEALTH CARE
<b>Team Leader</b>	ASTORGA, IGNACIO JOSE	<b>Overall Stage</b>	Disbursing (From eligibility until all the Operations are closed)
<b>Operation Type</b>	Loan Operation	<b>Country</b>	Guatemala
<b>Lending Instrument</b>	Investment Loan	<b>Convergence related Operation(s)</b>	
<b>Borrower</b>	REPUBLICA DE GUATEMALA		


## Environmental and Social Safeguards

<b>Impacts Category</b>	B	<b>Was/Were the objective(s) of this operation reformulated?</b>	NO
<b>Safeguard Performance Rating</b>	Satisfactory	<b>Date of approval</b>	
<b>Safeguard Performance Rating - Rationale</b>	La ejecución de esta operación está en una etapa incipiente donde aún se está conformando la AE con el personal técnico que se requiere para ejecutar el préstamo. Durante el proceso de supervisión no se encontró incumplimientos de las políticas y salvaguardas ambientales y sociales del Banco		

## Financial Data

Item	Total Cost and Source					Available Funds (US\$)			
	Original IDB	Current IDB	Local Counterpart	Co-Financing / Country	Total Original Cost	Current IDB	Disb. Amount to Date	% Disb	Undisbursed Amount
GU-L1163	100,000,000	100,000,000	0	0	100,000,000	100,000,000	1,926,041	1.93%	98,073,959
<b>Aggregated</b>	<b>100,000,000</b>	<b>100,000,000</b>	<b>0</b>	<b>0</b>	<b>100,000,000</b>	<b>100,000,000</b>	<b>1,926,041</b>	<b>1.93%</b>	<b>98,073,959</b>

## Expense Categories by Loan Contract (cumulative values)

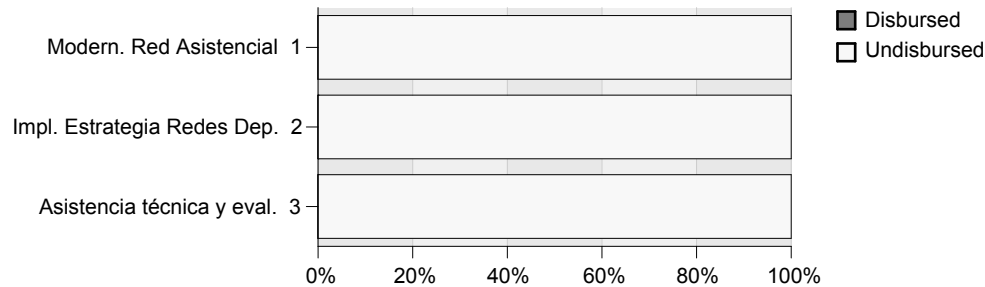

## PMR Public Report

### RESULTS MATRIX

#### General Development Objectives

**General Development Objectives Nbr. 1:** Razón de Mortalidad Materna Huehuetenango y San Marcos

**Observation:** Pro-gender

	Indicator	Unit of Measure	Baseline	Baseline Year	Expected Year of Achievement		Target
1.1	Razón de Mortalidad Materna Huehuetenango y San Marcos	Razón	137.20	2016	2026	P	110.00
						A	0.00

#### Details

**Means of verification:** Informe de Vigilancia de Morbilidad Materna MSPAS

**Observations:** Valor ponderado de Mujeres fallecidas cada 100.000 nacidos vivos

**Pro-Gender** No **Pro-Ethnicity** No

The General Development  
bjective indicator target is  
expected to be observed by  
the operation's "Fully  
Justified" date  
inConvergence (CO)

**General Development Objectives Nbr. 2:** Tasa de Mortalidad Infantil Huehuetenango y San Marcos

**Observation:** Se estima que en Huehuetenango existe sub registro de niños fallecidos por un 30% por lo que la mejora del control puede incrementar inicialmente la tasa

	Indicator	Unit of Measure	Baseline	Baseline Year	Expected Year of Achievement		Target
2.0	Tasa de Mortalidad Infantil Huehuetenango y San Marcos	Tasa	14.80	2016	2026	P	13.00
						A	0.00

#### Details

**Means of verification:** INE

**Observations:** Se estima que en Huehuetenango existe subregistro de niños fallecidos en un 30%, por lo que la mejora del control puede incrementar inicialmente la tasa

**Pro-Gender** No **Pro-Ethnicity** No

The General Development  
bjective indicator target is  
expected to be observed by  
the operation's "Fully  
Justified" date  
inConvergence (CO)

## PMR Public Report

### RESULTS MATRIX

#### Specific Development Objectives

**Specific Development Objectives Nbr. 1:** Resultado 1: Cobertura de servicios materno infantil mejorada en Huehuetenango y San Marcos

**Observation:** Los denominadores con base poblacional pueden variar al contar con datos oficiales del Censo Nacional 2018

Indicator		Unit of Measure	Baseline	Baseline Year		2024	2025	2026	EOP 2026
1.0	Cobertura de atención prenatal oportuna	%	34.72	2017	P	34.72	42.00		50.00
					A				0.00
Details									
Means of verification: SIGSA (MSPAS e INE)									
Observations: No. embarazadas con control prenatal antes de las 12 semanas/ No. embarazos esperados									
Pro-Gender		No			Pro-Ethnicity		No		

Indicator		Unit of Measure	Baseline	Baseline Year		2024	2025	2026	EOP 2026
1.2	Cobertura parto institucional	%	46.66	2016	P	46.66	58.00		104.66
					A				0.00
Details									
Means of verification: INE									
Observations: No. de parto en servicio de salud /No. total de partos									
Pro-Gender		No	Pro-Ethnicity		No				

Indicator		Unit of Measure	Baseline	Baseline Year		2024	2025	2026	EOP 2026
1.3	Cobertura de monitoreo de crecimiento en niños/niñas menores de 24 meses	%	29.00	2017	P	35.00	43.00		50.00
					A				0.00
Details									
Means of verification: SIGSA (MSPAS)									
Observations: No. niños/as menores 24 meses en control de monitoreo de crecimiento según norma/ No. niños/as menores de 24 meses									
Pro-Gender		No			Pro-Ethnicity		No		

**Specific Development Objectives Nbr. 2:** Resultado 2: Calidad de servicio mejorada en Huehuetenango y San Marcos

**Observation:** Los denominadores con base poblacional pueden variar al contar con datos oficiales del Censo Nacional 2018. El indicador 2.4 corresponde a un valor agregado

Indicator		Unit of Measure	Baseline	Baseline Year		2024	2025	2026	EOP 2026
2.0	Partos atendidos según norma	%	36.10	2015	P	40.00	50.00		60.00
					A				0.00

## PMR Public Report

### RESULTS MATRIX

#### Specific Development Objectives

Details									
Means of verification: Auditoria Expedientes Sistema de Información MSPAS desde año tres en adelante									
Observations: No. Partos atendidos según norma /Total partos institucionales									
Pro-Gender		No			Pro-Ethnicity		No		
Indicator		Unit of Measure	Baseline	Baseline Year		2024	2025	2026	EOP 2026
2.2	Recién nacidos atendidos según norma	%	18.60	2017	P	24.00	33.00		53.00
					A				0.00
Details									
Means of verification: Auditoria Expedientes Sistema de Información MSPAS desde año tres en adelante									
Observations: No. Recién Nacidos atendidos según norma /Total partos institucionales									
Pro-Gender		No			Pro-Ethnicity		No		
Indicator		Unit of Measure	Baseline	Baseline Year		2024	2025	2026	EOP 2026
2.3	Hacinamiento de hospitalización obstétrica en Hospital de Malacatán	%	111.00	2016	P	80.00	80.00		80.00
					A				0.00
Details									
Means of verification: SIGSA (MSPAS)									
Observations: Dias Cama Ocupados Obstetricia/Dias Cama Disponibles Obstetricia Hospital Malacatán									
Pro-Gender		No			Pro-Ethnicity		No		
Indicator		Unit of Measure	Baseline	Baseline Year		2024	2025	2026	EOP 2026
2.4	Hospitales que aplican protocolo de Violencia contra la Mujer (VCM)	#	0.00	2018	P	1.00	5.00		5.00
					A				0.00
Details									
Means of verification: Informe Unidad de Género MSPAS									
Pro-Gender		No			Pro-Ethnicity		No		
Indicator		Unit of Measure	Baseline	Baseline Year		2024	2025	2026	EOP 2026
2.5	Cobertura de embarazadas con exámenes de laboratorio en control prenatal	%	53.00	2017	P	65.00	75.00		85.00
					A				0.00
Details									

## PMR Public Report

### RESULTS MATRIX

#### Specific Development Objectives

**Means of verification:** Auditoria Expedientes

**Observations:** No. Embarazadas en control prenatal con exámenes de laboratorio según norma/ No. Embarazadas en control prenatal

**Pro-Gender** No **Pro-Ethnicity** No

**Specific Development Objectives Nbr. 3:** Resultado 3: Eficiencia Productiva Mejorada

**Observation:**

Indicator		Unit of Measure	Baseline	Baseline Year		2024	2025	2026	EOP 2026
3.0	Número de Bancos de Sangre procesadores a nivel nacional MSPAS	#	27.00	2018	P	22.00	18.00		14.00
					A				0.00

#### Details

**Means of verification:** Informe MSPAS

**Pro-Gender** No **Pro-Ethnicity** No

Indicator		Unit of Measure	Baseline	Baseline Year		2024	2025	2026	EOP 2026
3.2	Número de Laboratorios de rutina en APS Huehuetenango y San Marcos operando	#	66.00	2018	P	30.00	15.00		6.00
					A				0.00

#### Details

**Means of verification:** Informe DAS Departamentales

**Pro-Gender** No **Pro-Ethnicity** No

## RESULTS MATRIX

## OUTPUTS: ANNUAL PHYSICAL AND FINANCIAL PROGRESS

Component Nbr. 1 Componente 1: Modernización de la Red Asistencial bajo la estrategia de redes de salud a nivel nacional

	Output	Unit of Measure		PHYSICAL PROGRESS		FINANCIAL PROGRESS	
				2021	EOP 2026	2021	EOP 2026
1.1	1.1.1. Normas materno infantil complementadas y aprobadas	#	P	0	4	0	150,000
			P(a)	0	4	0	150,000
			A	0	0	0	0
1.2	1.1.2. Metodología de planificación Red Asistencial Departamental publicada	#	P	0	1	15,000	100,000
			P(a)	0	1	15,000	100,000
			A	0	0	0	0
1.3	1.1.3. Manual Gestión Integral de Red aprobado	#	P	0	1	15,000	100,000
			P(a)	0	1	15,000	100,000
			A	0	0	0	0
1.4	1.1.4. Propuesta de acción sobre interculturalidad implementado	#	P	0	1	0	300,000
			P(a)	0	1	0	300,000
			A	0	0	0	0
1.5	1.1.5. Propuesta de atención a la violencia contra la mujer implementada	#	P	0	1	0	150,000
			P(a)	0	1	0	150,000
			A	0	0	0	0
1.6	1.2.1. Metodologías de preparación de proyectos de inversión aprobadas	#	P	0	4	0	550,000
			P(a)	0	4	0	550,000
			A	0	0	0	0
1.7	1.2.2. Estudios de prefactibilidad APS aprobados	#	P	0	15	0	170,000
			P(a)	0	15	0	170,000
			A	0	0	0	0
1.8	1.2.3. Estudios de prefactibilidad Hospitales aprobados	#	P	0	2	0	300,000
			P(a)	0	2	0	300,000
			A	0	0	0	0
1.9	1.2.4. Estudio factibilidad Hospital aprobado	#	P	0	2	14,480	595,087
			P(a)	0	2	14,480	595,087
			A	0	0	0	0
1.10	1.2.5. Propuesta de Organización y Gestión de Hospitales aprobado	#	P	0	1	0	100,000
			P(a)	0	1	0	100,000
			A	0	0	0	0
1.11	1.2.6. Propuesta Organización y Gestión de CS/CAP CAIMI aprobado	#	P	0	1	0	50,000
			P(a)	0	1	0	50,000
			A	0	0	0	0
1.12	1.3.1. Plan de Gestión de la Red de Urgencia aprobado	#	P	0	1	0	100,000
			P(a)	0	1	0	100,000
			A	0	0	0	0
1.13	1.3.2. Centro Regulador de la Red de Urgencia Nacional operativo	#	P	0	1	1,590,667	2,610,982
			P(a)	0	1	1,590,667	2,610,982
			A	0	0	0	0
1.14	1.3.3. Propuesta de Organización y Gestión de la Red Electiva aprobado	#	P	0	1	20,000	100,000
			P(a)	0	1	20,000	100,000
			A	0	0	0	0
1.15	1.4.1. Propuesta de regionalización de Bancos de Sangre aprobado	#	P	0	1	0	100,000
			P(a)	0	1	0	100,000

## RESULTS MATRIX

## OUTPUTS: ANNUAL PHYSICAL AND FINANCIAL PROGRESS

	Output	Unit of Measure		PHYSICAL PROGRESS		FINANCIAL PROGRESS	
				2021	EOP 2026	2021	EOP 2026
1.15	1.4.1. Propuesta de regionalización de Bancos de Sangre aprobado	#	A	0	0	0	0
1.16	1.4.2. Hemocentro operativo	#	P	0	1	14,794	5,785,080
			P(a)	0	1	14,794	5,785,080
			A	0	0	0	0
1.17	1.4.3. Plan de regionalización de Laboratorios de Rutina aprobado	#	P	0	1	0	100,000
			P(a)	0	1	0	100,000
			A	0	0	0	0
1.18	1.4.4. Estrategia de Mantenimiento implementada	#	P	0	1	0	868,049
			P(a)	0	1	0	868,049
			A	0	0	0	0
1.19	1.4.5. Plan de Gestión Logística de Medicamentos e Insumos implementado	#	P	0	1	0	220,000
			P(a)	0	1	0	220,000
			A	0	0	0	0
1.20	1.4.6. Propuesta Sistema TIC de Salud implementada	#	P	0	1	552,000	6,391,803
			P(a)	0	1	552,000	6,391,803
			A	0	0	0	0

## RESULTS MATRIX

## OUTPUTS: ANNUAL PHYSICAL AND FINANCIAL PROGRESS

Component Nbr. 2 Componente 2: Implementación de la Estrategia Redes de Salud departamental

	Output	Unit of Measure		PHYSICAL PROGRESS		FINANCIAL PROGRESS	
				2021	EOP 2026	2021	EOP 2026
2.1	2.1.1. Unidades administrativas de la Red Departamental implementadas	#	P	0	2	347	100,347
			P(a)	0	2	347	100,347
			A	0	0	0	0
2.2	2.1.2. Estudio de Red Departamental aprobado	#	P	0	2	0	200,000
			P(a)	0	2	0	200,000
			A	0	0	0	0
2.3	2.2.1. Puestos de Salud construidos operativos	#	P	0	75	46,643	11,947,082
			P(a)	0	75	46,643	11,947,082
			A	0	0	4,478	4,478
2.4	2.2.2. Puestos de Salud mejorados / remozados operativos	#	P	0	63	19,845	3,937,845
			P(a)	0	63	19,845	3,937,845
			A	0	0	0	0
2.5	2.2.3. CAP construidos operativos	#	P	0	1	315	1,231,154
			P(a)	0	1	315	1,231,154
			A	0	0	0	0
2.6	2.2.4. CS / CAP / CAIMI mejorados / remozados operativos	#	P	0	12	39,398	4,906,645
			P(a)	0	12	39,398	4,906,645
			A	0	0	4,478	4,478
2.7	2.2.5. Hospitales Huehuetenango, Malacatán y San Marcos normalizados operativos	#	P	0	3	945	26,053,658
			P(a)	0	3	945	26,053,658
			A	0	0	0	0
2.8	2.2.6. Hospital Barillas mejorado operativo	#	P	0	1	35,933	2,539,378
			P(a)	0	1	35,933	2,539,378
			A	0	0	4,478	4,478
2.9	2.2.7. PS / CS / CAP / CAIMI equipados	#	P	0	127	0	3,584,034
			P(a)	0	127	0	3,584,034
			A	0	0	0	0
2.10	2.2.8. Hospitales distritales construidos operativos	#	P	0	2	36,248	16,380,184
			P(a)	0	2	36,248	16,380,184
			A	0	0	4,478	4,478
2.11	2.2.9. Auxiliares Enfermería formadas	#	P	0	600	0	600,000
			P(a)	0	600	0	600,000
			A	0	0	0	0
2.12	2.2.10. Equipos capacitados en Planificación y Gestión de la Red	#	P	0	71	0	100,000
			P(a)	0	71	0	100,000
			A	0	0	0	0
2.13	2.2.11. Funcionarios capacitados en Gestión Hospitalaria	#	P	0	60	0	100,000
			P(a)	0	60	0	100,000
			A	0	0	0	0
2.14	2.2.12. Equipos de APS capacitados	#	P	0	64	0	100,000
			P(a)	0	64	0	100,000
			A	0	0	0	0
2.15	2.3.1. Departamentos con Sistema de Coordinación de Urgencia operando	#	P	0	2	224,520	357,143
			P(a)	0	2	224,520	357,143



## RESULTS MATRIX

## OUTPUTS: ANNUAL PHYSICAL AND FINANCIAL PROGRESS

	Output	Unit of Measure		PHYSICAL PROGRESS		FINANCIAL PROGRESS	
				2021	EOP 2026	2021	EOP 2026
2.15	2.3.1. Departamentos con Sistema de Coordinación de Urgencia operando	#	A	0	0	0	0
2.16	2.3.2. Departamentos con Sistema de Referencia / Contrarreferencia funcionando	#	P	0	2	0	132,623
			P(a)	0	2	0	132,623
			A	0	0	0	0
2.17	2.4.1. Departamentos con Red de Laboratorios de rutina funcionando	#	P	0	2	0	395,613
			P(a)	0	2	0	395,613
			A	0	0	0	0
2.18	2.4.2. Departamentos con Red de Sangre funcionando	#	P	0	2	0	357,494
			P(a)	0	2	0	357,494
			A	0	0	0	0
2.19	2.4.3. Departamentos con Sistema Logístico funcionando	#	P	0	2	0	239,802
			P(a)	0	2	0	239,802
			A	0	0	0	0
2.20	2.4.4. Departamentos con Sistema de Mantenimiento funcionando	#	P	0	2	0	220,741
			P(a)	0	2	0	220,741
			A	0	0	0	0
2.21	2.4.5. Municipios de Huehuetenango y San Marcos con Tecnologías de la Información funcionando	#	P	0	64	0	1,938,614
			P(a)	0	64	0	1,938,614
			A	0	0	0	0

## Other Cost

	Evaluación y Administración	P			771,432	5,736,642
		P(a)			771,432	5,736,642
		A			42,700	42,700

## Total Cost

	Total Cost	P			3,397,567	100,000,000
		P(a)			3,397,567	100,000,000
		A			60,612	60,612

**CHANGES TO THE MATRIX**

No information available for this section

## RISKS AND PLANNED RESPONSES

Risk ID	Risk Status		Risk Taxonomy
1	Active		Legal Environment
	Response actions		
	1.0	Management Strategy	Status
		-	
Risk ID	Risk Status		Risk Taxonomy
2	Active		Organizational Structure
	Response actions		
	2.1	Management Strategy	Status
		MITIGATE	ACTIVE
Risk ID	Risk Status		Risk Taxonomy
3	Active		Internal Processes
	Response actions		
	3.1	Management Strategy	Status
		MITIGATE	ACTIVE
Risk ID	Risk Status		Risk Taxonomy
4	Active		Governance Framework
	Response actions		
	4.1	Management Strategy	Status
		ENHANCE	ACTIVE
	4.2	Management Strategy	Status
		MITIGATE	ACTIVE

# PMR Public Report

## IMPLEMENTATION STATUS AND LEARNING

Lesson Learned - Categories
Cost and Budgetary Aspects
Project Management Capacity
